PETRA General Contractors

Meridian, ID - 2026.04.09 - UP05

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Name	% Complete	Duration	Start	Finish
1	**GENERAL REQUIREMENTS AND CONDITIONS**	**77%**	**231 days**	**Mon 9/8/25**	**Tue 8/4/26**
12	Submittals (numerous)	57%	150 days	Tue 10/14/25	Fri 5/15/26
13	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG B	25%	124 days	Thu 10/23/25	Mon 4/20/26
14	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG A	76%	108 days	Thu 11/6/25	Fri 4/10/26
21	**TWENTY WORKING DAYS OF WEATHER DELAY**	0%	10 days	Wed 7/22/26	Tue 8/4/26
27	**Substantial Completion**	**0%**	**0 days**	**Tue 8/4/26**	**Tue 8/4/26**
28	Clean Up and Project Close Out	0%	5 days	Tue 6/30/26	Tue 7/7/26
29	Demobilize	0%	3 days	Wed 7/8/26	Fri 7/10/26
30	**SITEWORK**	**50%**	**212 days**	**Mon 9/8/25**	**Wed 7/8/26**
31	**Level of Effort**	**42%**	**131 days**	**Mon 9/8/25**	**Fri 3/13/26**
33	Inspections and Testing	0%	100 days	Fri 9/12/25	Fri 2/13/26
34	Maintain Erosion Control	50%	120 days	Tue 9/23/25	Fri 3/13/26
53	**FRAGNET - Site - Drive Aisle Unsuitable Soils**	**74%**	**74 days**	**Tue 2/3/26**	**Fri 5/15/26**
62	FRAGNET - Site - Partial Soft Spot Repair Examination of Pit Run to Proceed. If failed, provide geo grid per RFI 33	0%	3 days	Tue 5/5/26	Thu 5/7/26
63	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Start	0%	1 day	Fri 5/8/26	Fri 5/8/26
64	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld A	0%	5 days	Mon 5/11/26	Fri 5/15/26
65	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld B	0%	5 days	Mon 5/11/26	Fri 5/15/26
69	Storm Drain Lines and Devices - South of Buildings (E-W)	0%	7 days	Wed 4/15/26	Thu 4/23/26
70	Site - Flatwork Sidewalk Prep (E-W)	0%	8 days	Wed 4/15/26	Fri 4/24/26
71	Storm Drain Lines and Devices - North of Buildings (E-W)	0%	7 days	Fri 4/24/26	Mon 5/4/26
72	Site Concrete Flatwork and Curb and Gutter - (E-W) at Buildings	0%	15 days	Mon 4/27/26	Fri 5/15/26
73	Site - Base Course Asphalt Prep	0%	8 days	Mon 5/18/26	Thu 5/28/26
74	Site - Curb and Gutter Prep	0%	8 days	Fri 5/29/26	Tue 6/9/26
75	Site - Fine Grade Asphalt Prep	0%	3 days	Wed 6/10/26	Fri 6/12/26
76	Asphalt Paving	0%	2 days	Mon 6/15/26	Tue 6/16/26
77	Pavement Markings, Signage & Bumpers	0%	2 days	Wed 6/17/26	Thu 6/18/26
78	Site Fencing Chainlink	0%	5 days	Wed 5/20/26	Wed 5/27/26
79	Gravel Road Finish Grading	0%	5 days	Wed 6/10/26	Tue 6/16/26
80	Landscaping and Irrigation	0%	15 days	Wed 6/17/26	Wed 7/8/26
81	Site Fencing Vinyl	0%	10 days	Wed 6/17/26	Tue 6/30/26
82	Site Fencing Rod Iron and Gates	0%	5 days	Wed 6/17/26	Tue 6/23/26
83	**BUILDING B**	**44%**	**162 days**	**Wed 10/29/25**	**Thu 6/18/26**
94	**STEEL AND METALS**	**63%**	**76 days**	**Mon 1/12/26**	**Mon 4/27/26**
98	Perimeter Panel Interior Walls (JANUS)	0%	20 days	Tue 3/31/26	Mon 4/27/26
99	**WOOD & FRP**	**0%**	**5 days**	**Thu 4/9/26**	**Wed 4/15/26**
100	Misc Finish Carpentry	0%	5 days	Thu 4/9/26	Wed 4/15/26
101	**ROOF & SIDING**	**54%**	**78 days**	**Fri 1/30/26**	**Tue 5/19/26**
106	Rigid Insulation Behind CMU	0%	5 days	Wed 4/8/26	Tue 4/14/26
107	Rigid Insulation Behind Metal Panels	0%	3 days	Wed 4/15/26	Fri 4/17/26
108	CMU Veneer Remaining	0%	15 days	Wed 4/15/26	Tue 5/5/26
109	Exterior Metal Panels (JANUS)	0%	10 days	Wed 5/6/26	Tue 5/19/26
112	**DOORS & WINDOWS**	**0%**	**41 days**	**Mon 4/13/26**	**Tue 6/9/26**

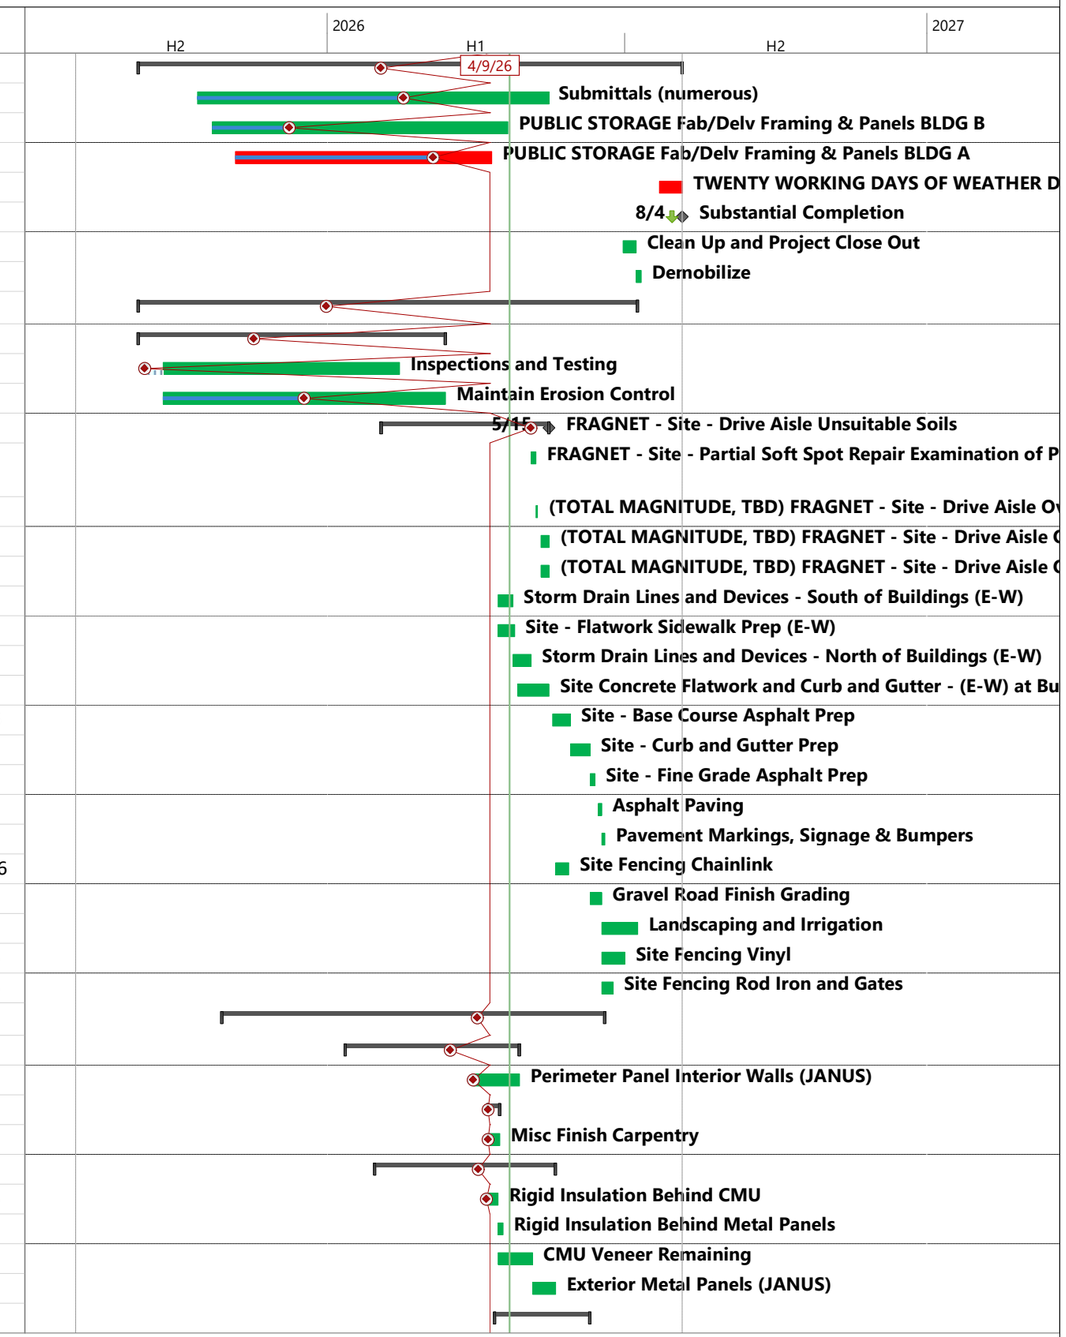

Printed: Wed 4/22/26 3:01 PM

PETRA General Contractors

Meridian, ID - 2026.04.09 - UP05

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Name	% Complete	Duration	Start	Finish
113	F&I HM Doors and Hardware (JANUS)	0%	5 days	Mon 4/13/26	Fri 4/17/26
114	F&I Storage Unit Doors (JANUS)	0%	30 days	Tue 4/28/26	Tue 6/9/26
115	Install Security Mesh (JANUS)	0%	10 days	Mon 5/18/26	Mon 6/1/26
116	**FINISHES**	**0%**	**30 days**	**Thu 3/26/26**	**Wed 5/6/26**
117	Install Gypsum Board	0%	10 days	Thu 3/26/26	Wed 4/8/26
118	Flooring Polished Concrete	0%	5 days	Thu 4/9/26	Wed 4/15/26
119	FRP / Vinyl Base	0%	5 days	Thu 4/16/26	Wed 4/22/26
120	Painting	0%	10 days	Thu 4/23/26	Wed 5/6/26
121	**SPECIALTIES**	**0%**	**23 days**	**Thu 4/9/26**	**Mon 5/11/26**
122	Install Misc Equipment & Lockers	0%	20 days	Thu 4/9/26	Wed 5/6/26
123	Bathroom Accessories	0%	2 days	Thu 4/16/26	Fri 4/17/26
124	Building Interior Signage	0%	3 days	Thu 5/7/26	Mon 5/11/26
128	**PLUMBING**	**31%**	**104 days**	**Thu 11/20/25**	**Mon 4/20/26**
130	Drains, Water, Sewer Lines	25%	15 days	Thu 3/26/26	Wed 4/15/26
131	Bathroom Fixtures	0%	3 days	Thu 4/16/26	Mon 4/20/26
132	Other Plumbing Fixtures	0%	3 days	Thu 4/16/26	Mon 4/20/26
133	**HVAC**	**22%**	**63 days**	**Mon 3/16/26**	**Thu 6/11/26**
135	**FRAGNET - RFI 38 Condenser Unit Relocations**	**20%**	**55 days**	**Mon 3/23/26**	**Mon 6/8/26**
138	FRAGNET - RFI 38 - Procurement, Re-Route Electrical	0%	8 days	Mon 4/13/26	Wed 4/22/26
139	**TBD FRAGNET - RFI 38 - HVAC Set Units, Duct Procurement & Install**	**0%**	**0 days**	**Thu 4/9/26**	**Thu 4/9/26**
140	TBD FRAGNET - RFI 38 - Screen Wall Procurement and Install	0%	40 days	Mon 4/13/26	Mon 6/8/26
141	**FRAGNET - RFI 37 - Duct Conflicts**	**35%**	**29 days**	**Mon 3/16/26**	**Thu 4/23/26**
144	RFI 37 - Review and Responsed, Close as Directed	10%	5 days	Fri 4/3/26	Thu 4/9/26
145	TBD RFI 37 - Cost Impact Collection and Submission	0%	10 days	Fri 4/10/26	Thu 4/23/26
146	TBD RFI 37 - Procure Remaining Duct Materials	0%	5 days	Fri 4/10/26	Thu 4/16/26
147	HVAC Installation - Remaining	0%	21 days	Fri 4/17/26	Fri 5/15/26
148	HVAC Commisioning & T&B	0%	5 days	Fri 6/5/26	Thu 6/11/26
149	**ELECTRICAL**	**42%**	**146 days**	**Thu 11/20/25**	**Thu 6/18/26**
153	Install Wire & Inspect - Remaining	0%	5 days	Thu 4/23/26	Wed 4/29/26
154	Install and Wire Panels	0%	3 days	Thu 4/30/26	Mon 5/4/26
155	**Permanent Power On**	**0%**	**0 days**	**Thu 6/4/26**	**Thu 6/4/26**
157	Electric Lights, Devices and Trim	25%	55 days	Wed 3/25/26	Thu 6/11/26
158	Fire Alarm System	0%	3 days	Mon 5/18/26	Wed 5/20/26
159	Electrical Commissioning	0%	5 days	Fri 6/12/26	Thu 6/18/26
160	**BUILDING A**	**23%**	**125 days**	**Mon 1/26/26**	**Tue 7/21/26**
183	**CONCRETE WORK**	**84%**	**50 days**	**Wed 2/4/26**	**Tue 4/14/26**
189	BLDG A Slab On Grade (West)	25%	10 days	Wed 4/1/26	Tue 4/14/26
190	**BLDG A Slab On Grade Complete**	**0%**	**0 days**	**Tue 4/14/26**	**Tue 4/14/26**
191	**STEEL AND METALS**	**0%**	**57 days**	**Mon 4/13/26**	**Wed 7/1/26**
192	Frame Load Bearing, Shear Walls, Partition & Corridor (JANUS)	0%	15 days	Mon 4/13/26	Fri 5/1/26
193	Panel Shear Wall, Interior Partition, & Corridor Walls (JANUS)	0%	10 days	Mon 5/4/26	Fri 5/15/26
194	Perimeter Panel Interior Walls (JANUS)	0%	15 days	Thu 6/11/26	Wed 7/1/26
195	Canopy Install	0%	8 days	Mon 5/4/26	Wed 5/13/26

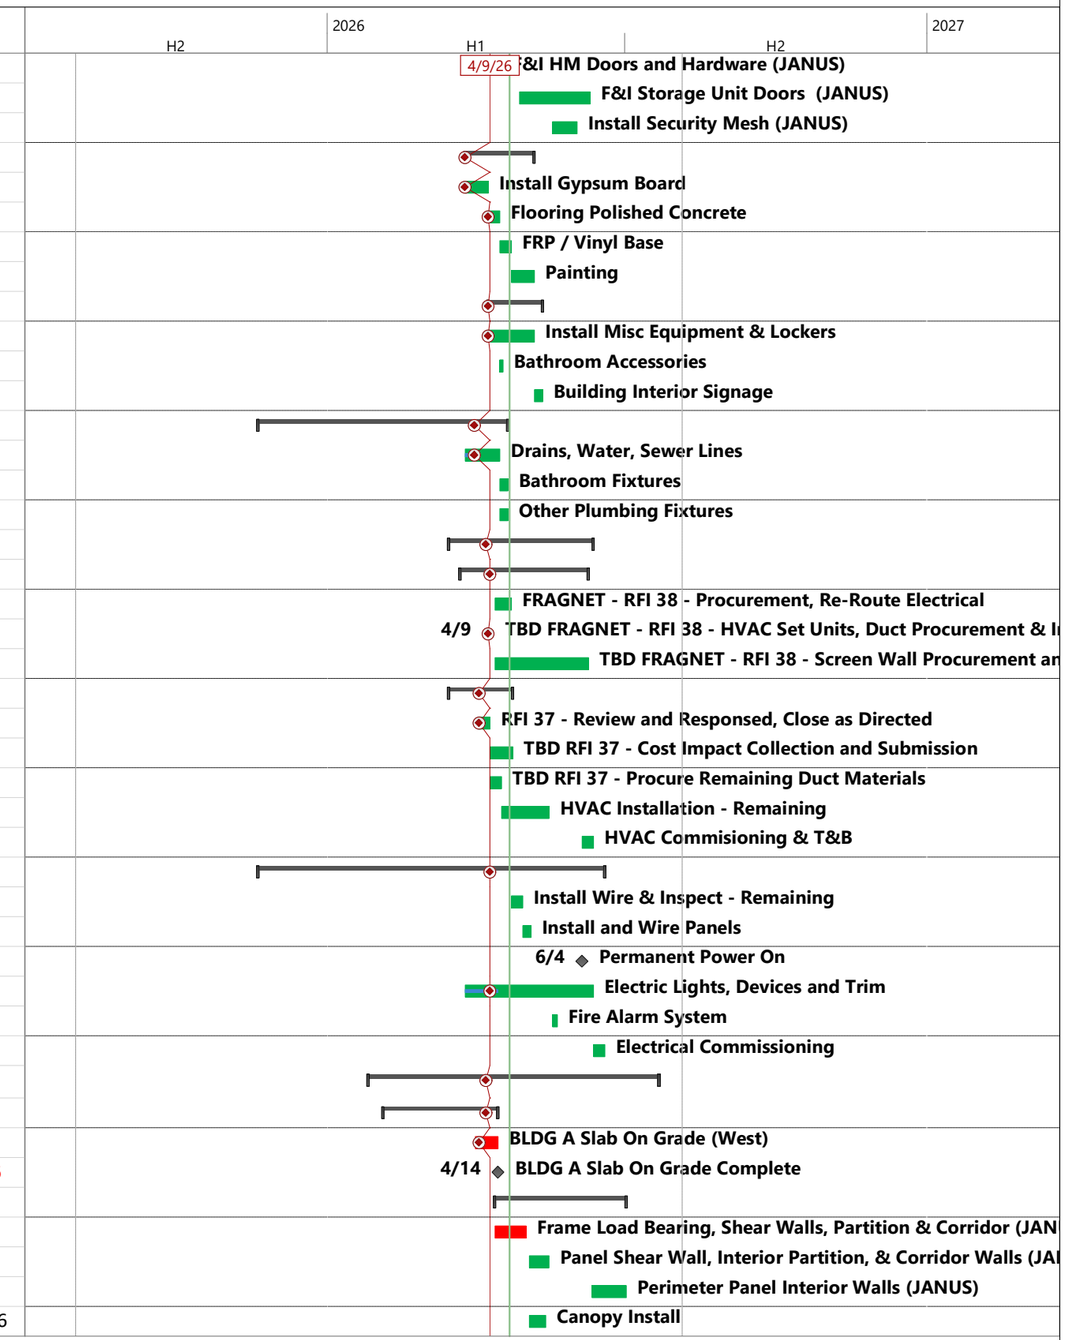

Printed: Wed 4/22/26 3:01 PM

PETRA General Contractors

Meridian, ID - 2026.04.09 - UP05

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Name	% Complete	Duration	Start	Finish
196	**WOOD & FRP**	**0%**	**5 days**	**Tue 6/2/26**	**Mon 6/8/26**
197	Misc Finish Carpentry	0%	5 days	Tue 6/2/26	Mon 6/8/26
198	**ROOF & SIDING**	**0%**	**40 days**	**Mon 4/20/26**	**Mon 6/15/26**
199	Exterior Sheathing	0%	10 days	Mon 4/20/26	Fri 5/1/26
200	Exterior Sheathing, Weather Barrier & Rigid Insulation - Building A	0%	10 days	Mon 4/27/26	Fri 5/8/26
201	Rigid Insulation Behind Metal Panels	0%	3 days	Mon 5/11/26	Wed 5/13/26
202	Rigid Insulation Behind CMU	0%	5 days	Mon 5/11/26	Fri 5/15/26
203	CMU Veneer	0%	15 days	Mon 5/18/26	Mon 6/8/26
204	Exterior Metal Panels (JANUS)	0%	10 days	Tue 6/2/26	Mon 6/15/26
205	Install Roof & Roof Insulation (JANUS)	0%	10 days	Mon 5/4/26	Fri 5/15/26
206	BLDG A Roofing Complete	0%	0 days	Fri 5/15/26	Fri 5/15/26
207	**DOORS & WINDOWS**	**0%**	**25 days**	**Tue 6/16/26**	**Tue 7/21/26**
208	F&I Storage Unit Doors (JANUS)	0%	25 days	Tue 6/16/26	Tue 7/21/26
209	F&I HM Doors and Hardware (JANUS)	0%	5 days	Tue 6/16/26	Mon 6/22/26
210	Install Security Mesh (JANUS)	0%	10 days	Tue 6/16/26	Mon 6/29/26
211	**FINISHES**	**0%**	**30 days**	**Mon 5/18/26**	**Mon 6/29/26**
212	Install Gypsum Board	0%	10 days	Mon 5/18/26	Mon 6/1/26
213	Painting	0%	10 days	Tue 6/2/26	Mon 6/15/26
214	Flooring Polished Conc.	0%	5 days	Tue 6/16/26	Mon 6/22/26
215	FRP & Vinyl Base	0%	5 days	Tue 6/23/26	Mon 6/29/26
216	**SPECIALTIES**	**0%**	**22 days**	**Tue 6/2/26**	**Wed 7/1/26**
217	Install Misc Equipment & Lockers	0%	20 days	Tue 6/2/26	Mon 6/29/26
218	Bathroom Accessories- Building A	0%	2 days	Tue 6/30/26	Wed 7/1/26
219	Building Interior Signage	0%	3 days	Tue 6/16/26	Thu 6/18/26
220	**FIRE SPRINKLERS**	**0%**	**30 days**	**Mon 5/18/26**	**Mon 6/29/26**
221	Fire Sprinkler System Rough In	0%	15 days	Mon 5/18/26	Mon 6/8/26
222	Fire Sprinkler System Trim Out	0%	15 days	Tue 6/9/26	Mon 6/29/26
223	**PLUMBING**	**10%**	**85 days**	**Mon 3/9/26**	**Tue 7/7/26**
225	Drains, Water, Sewer Lines	0%	15 days	Mon 5/18/26	Mon 6/8/26
226	Bathroom Fixtures- Building A	0%	10 days	Tue 6/9/26	Mon 6/22/26
227	Other Plumbing Fixtures	0%	10 days	Tue 6/23/26	Tue 7/7/26
228	**HVAC**	**0%**	**30 days**	**Mon 5/18/26**	**Mon 6/29/26**
229	HVAC Installation	0%	20 days	Mon 5/18/26	Mon 6/15/26
230	HVAC Commisioning - Building A	0%	10 days	Tue 6/16/26	Mon 6/29/26
231	**ELECTRICAL**	**4%**	**69 days**	**Tue 3/24/26**	**Mon 6/29/26**
233	Electrical Rough-In	0%	25 days	Wed 5/6/26	Wed 6/10/26
234	New Service Equipment Install, Wire & Inspect	0%	10 days	Mon 5/18/26	Mon 6/1/26
235	Install and Wire Panels	0%	3 days	Tue 6/2/26	Thu 6/4/26
236	**Permanent Power On- Building A**	**0%**	**0 days**	**Thu 6/4/26**	**Thu 6/4/26**
237	Electric Lights, Devices and Trim	0%	20 days	Wed 5/20/26	Wed 6/17/26
238	Fire Alarm System	0%	5 days	Tue 6/16/26	Mon 6/22/26
239	Electrical Commissioning	0%	5 days	Tue 6/23/26	Mon 6/29/26

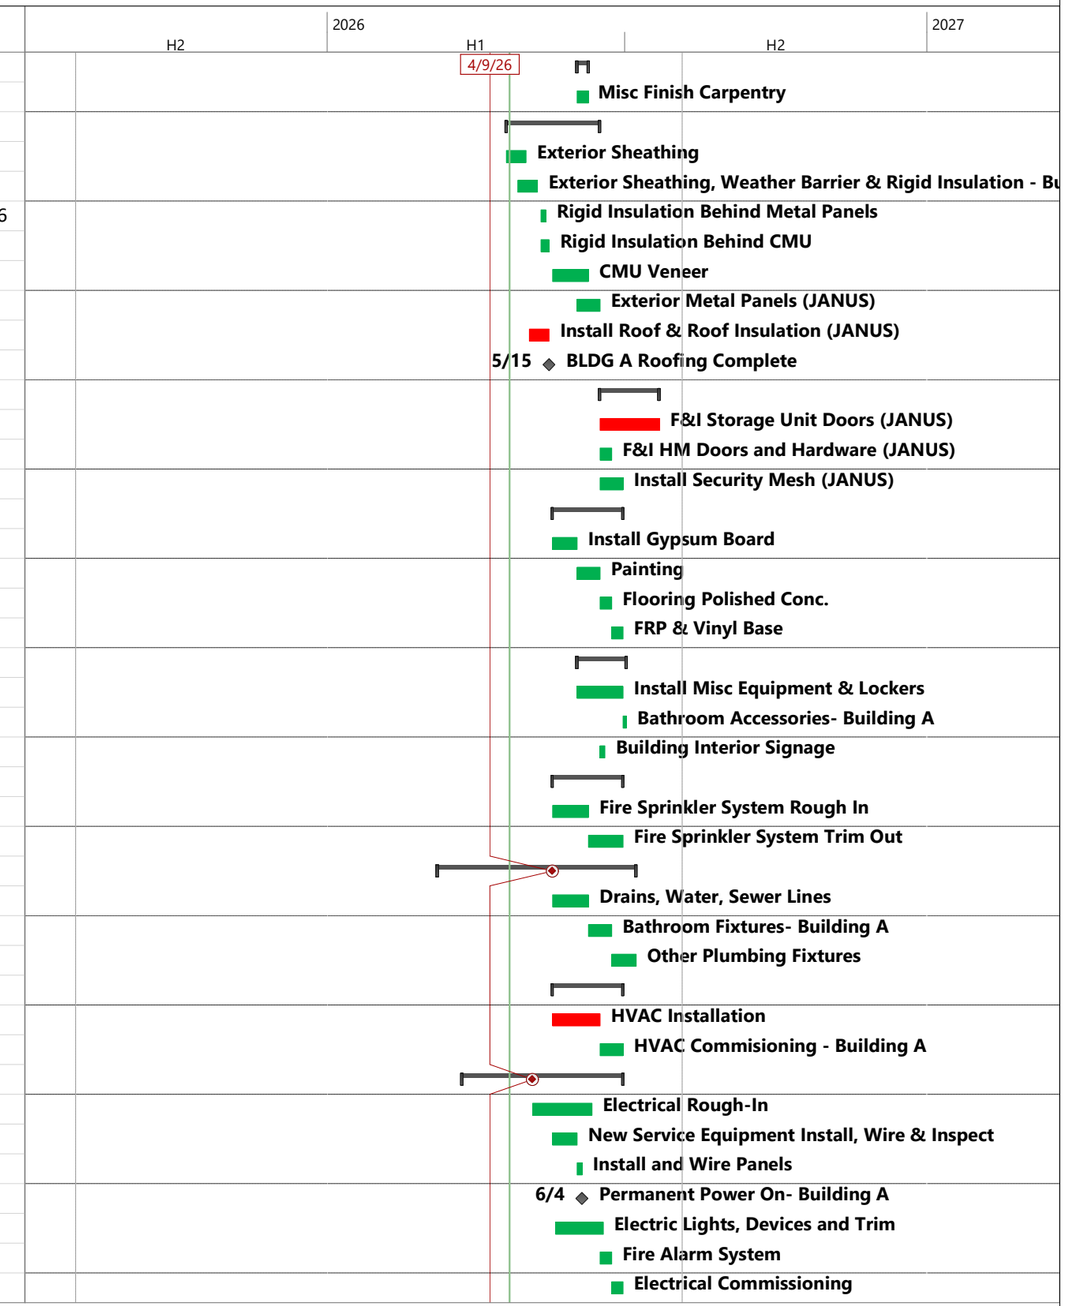

Printed: Wed 4/22/26 3:01 PM
