	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**GENERAL REQUIREMENTS AND CONDITIONS**	**255 days**	**259 days**	**-4d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Mon 9/7/26**	**Fri 9/11/26**	**-4d**
2	Notice to Proceed	1 day	1 day	0d	Mon 9/8/25	Mon 9/8/25	0d	Mon 9/8/25	Mon 9/8/25	0d
3	DELAY - PERMIT DELAY	32 days	32 days	0d	Tue 9/9/25	Tue 9/9/25	0d	Wed 10/22/25	Wed 10/22/25	0d
4	Obtain Building Permit	0 days	0 days	0d	Wed 10/22/25	Wed 10/22/25	0d	Wed 10/22/25	Wed 10/22/25	0d
5	ACHD ROW Permit	0 days	0 days	0d	Wed 10/29/25	Wed 10/29/25	0d	Wed 10/29/25	Wed 10/29/25	0d
6	Obtain LDIR Approval to Proceed	0 days	0 days	0d	Mon 10/27/25	Mon 10/27/25	0d	Mon 10/27/25	Mon 10/27/25	0d
7	Receive CAD Base Files from Public Storage	10 days	10 days	0d	Tue 9/9/25	Tue 9/9/25	0d	Mon 9/22/25	Mon 9/22/25	0d
8	Procure Early Work Subcontractors	5 days	5 days	0d	Tue 9/9/25	Tue 9/9/25	0d	Mon 9/15/25	Mon 9/15/25	0d
9	Procure Remaining Subcontractors	20 days	20 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Mon 10/13/25	Mon 10/13/25	0d
10	Submittals (SWPPP/NOI)	10 days	10 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Mon 9/29/25	Mon 9/29/25	0d
11	Submittals (SES /Switchgear)	125 days	125 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Fri 3/13/26	Fri 3/13/26	0d
12	Submittals (numerous)	150 days	90 days	60d	Tue 10/14/25	Tue 10/14/25	0d	Fri 5/15/26	Fri 2/20/26	60d
13	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG B	124 days	40 days	84d	Thu 10/23/25	Thu 10/23/25	0d	Mon 4/20/26	Fri 12/19/25	86d
14	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG A	110 days	40 days	70d	Thu 11/6/25	Thu 11/6/25	0d	Tue 4/14/26	Tue 1/6/26	70d
15	Procure SES's/Switchgears (6 mos ~ 130 WD)	56 days	56 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Fri 1/23/26	Fri 1/23/26	0d
16	Light Fixture Submittal Review and Approval	10 days	10 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Fri 2/6/26	Fri 2/6/26	0d
17	Light Fixture Package Alternate - Fab and Deliver	10 days	10 days	0d	Mon 2/9/26	Mon 2/9/26	0d	Fri 2/20/26	Fri 2/20/26	0d
18	Fire Sprinkler Design and Approval	78 days	78 days	0d	Tue 10/14/25	Tue 10/14/25	0d	Wed 2/4/26	Wed 2/4/26	0d
19	Fire Alarm System Design and Approval	40 days	40 days	0d	Tue 10/14/25	Tue 10/14/25	0d	Wed 12/10/25	Wed 12/10/25	0d
20	ASPHALT BATCH PLANT SHUTDOWN	70 days	70 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Thu 2/26/26	Thu 2/26/26	0d
21	TWENTY WORKING DAYS OF WEATHER DELAY	10 days	10 days	0d	Tue 8/25/26	Mon 8/31/26	-4d	Mon 9/7/26	Fri 9/11/26	-4d
22	WEATHER DELAY - Rain and High Winds - Imapct SOG B	2 days	2 days	0d	Wed 12/17/25	Wed 12/17/25	0d	Thu 12/18/25	Thu 12/18/25	0d
23	WEATHER DELAY - Rain - Impact SOG B	1 day	1 day	0d	Mon 12/22/25	Mon 12/22/25	0d	Mon 12/22/25	Mon 12/22/25	0d
24	WEATHER DELAY - Rain - Impact SOG B	3 days	3 days	0d	Thu 1/8/26	Thu 1/8/26	0d	Mon 1/12/26	Mon 1/12/26	0d
25	WEATHER DELAY - Rain - Impact Footing Bldg A	2 days	2 days	0d	Tue 2/17/26	Tue 2/17/26	0d	Wed 2/18/26	Wed 2/18/26	0d
26	WEATHER DELAY - Rain - Impact Footing Bldg A	2 days	2 days	0d	Tue 2/24/26	Tue 2/24/26	0d	Wed 2/25/26	Wed 2/25/26	0d
27	Substantial Completion	0 days	0 days	0d	Mon 9/7/26	Fri 9/11/26	-4d	Mon 9/7/26	Fri 9/11/26	-4d
28	Clean Up and Project Close Out	5 days	5 days	0d	Thu 8/13/26	Wed 8/19/26	-4d	Wed 8/19/26	Tue 8/25/26	-4d
29	Demobilize	3 days	3 days	0d	Thu 8/20/26	Wed 8/26/26	-4d	Mon 8/24/26	Fri 8/28/26	-4d
30	**SITEWORK**	**219 days**	**219 days**	**0d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Fri 7/17/26**	**Fri 7/17/26**	**0d**
31	**Level of Effort**	**131 days**	**131 days**	**0d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Fri 3/13/26**	**Fri 3/13/26**	**0d**
32	Construction Staking & Surveying	90 days	90 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Fri 1/16/26	Fri 1/16/26	0d
33	Inspections and Testing	100 days	100 days	0d	Fri 9/12/25	Fri 9/12/25	0d	Fri 2/13/26	Fri 2/13/26	0d
34	Maintain Erosion Control	120 days	120 days	0d	Tue 9/23/25	Tue 9/23/25	0d	Fri 3/13/26	Fri 3/13/26	0d
35	Erosion Control & SWPP	5 days	5 days	0d	Tue 9/16/25	Tue 9/16/25	0d	Mon 9/22/25	Mon 9/22/25	0d
36	Mobilization	5 days	5 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Mon 9/15/25	Mon 9/15/25	0d
37	Site Demolition (Trees,Sawcut, Asphalt, Base)	0 days	0 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Fri 9/12/25	Fri 9/12/25	0d
38	Clear/Grub & Overlot Grading	12 days	12 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Tue 9/23/25	Tue 9/23/25	0d
39	Structure Demo (Partial Building & RV Storage)	5 days	5 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Fri 11/7/25	Fri 11/7/25	0d
40	Re-Mobilization	4 days	4 days	0d	Thu 10/23/25	Thu 10/23/25	0d	Tue 10/28/25	Tue 10/28/25	0d
41	FRAGNET - CITY PRE-CON & 7 DAY NOTICE	7 days	7 days	0d	Wed 10/29/25	Wed 10/29/25	0d	Thu 11/6/25	Thu 11/6/25	0d
42	Site - Water Line Ten Mile Tie-In	2 days	2 days	0d	Sat 11/8/25	Sat 11/8/25	0d	Tue 11/11/25	Tue 11/11/25	0d
43	Work Week Restriction	5 days	5 days	0d	Fri 11/7/25	Fri 11/7/25	0d	Thu 11/13/25	Thu 11/13/25	0d
44	Site - Sewer Lines and Devices/Ten Mile Tie-In	13 days	13 days	0d	Fri 11/14/25	Fri 11/14/25	0d	Thu 12/4/25	Thu 12/4/25	0d
45	DELAY - GIRR License Agreement Approval to Proceed	6 days	6 days	0d	Fri 12/5/25	Fri 12/5/25	0d	Fri 12/12/25	Fri 12/12/25	0d
46	DELAY - RFI #14 - GIRR Separation	4 days	4 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Thu 12/18/25	Thu 12/18/25	0d
47	Storm Drain Lines South	6 days	6 days	0d	Mon 12/22/25	Mon 12/22/25	0d	Tue 12/30/25	Tue 12/30/25	0d
48	Site - Water Line & Fire Lines/Hydrants and Devices Remaining	18 days	18 days	0d	Mon 1/5/26	Mon 1/5/26	0d	Wed 1/28/26	Wed 1/28/26	0d
49	Site - GIRR Piping & Devices	16 days	16 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 2/2/26	Mon 2/2/26	0d
50	TP DELAY - Site - GIRR Box Delivery and Placement	6 days	6 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Mon 2/2/26	Mon 2/2/26	0d
51	Complete UG Utility Lines, SD Turn Ups, to Building A	1 day	1 day	0d	Fri 3/27/26	Tue 3/31/26	-2d	Fri 3/27/26	Tue 3/31/26	-2d
52	Gravel Road Rough Grade Prep	8 days	8 days	0d	Mon 12/8/25	Mon 12/8/25	0d	Wed 12/17/25	Wed 12/17/25	0d
53	**FRAGNET - Site - Drive Aisle Unsuitable Soils**	**74 days**	**74 days**	**0d**	**Tue 2/3/26**	**Tue 2/3/26**	**0d**	**Fri 5/15/26**	**Fri 5/15/26**	**0d**
54	FRAGNET - Site - Drive Aisle Over Ex Unsuitable Soil Identified	1 day	1 day	0d	Tue 2/3/26	Tue 2/3/26	0d	Tue 2/3/26	Tue 2/3/26	0d
55	FRAGNET - Site - Drive Aisle Over Ex Discussion and Confirmation	2 days	2 days	0d	Wed 2/4/26	Wed 2/4/26	0d	Thu 2/5/26	Thu 2/5/26	0d
56	FRAGNET - Site - Idaho Power - Pivot to Moblize and Peform the	15 days	15 days	0d	Fri 2/6/26	Fri 2/6/26	0d	Thu 2/26/26	Thu 2/26/26	0d
57	FRAGNET - Site - Owner Review of Impact and Discussion with Ge	5 days	5 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Wed 2/25/26	Wed 2/25/26	0d
58	FRAGNET - Prepare and Submit Pricing for Approval	13 days	13 days	0d	Fri 2/27/26	Fri 2/27/26	0d	Tue 3/17/26	Tue 3/17/26	0d
59	FRAGNET - Owner Issued CCD 07 Directive for Driveisle and Soft	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
60	FRAGNET - Mobilize Crew, Rough Grade Prep, Scarify and Air Dry	2 days	1 day	1d	Fri 3/20/26	Fri 3/20/26	0d	Mon 3/23/26	Fri 3/20/26	1d

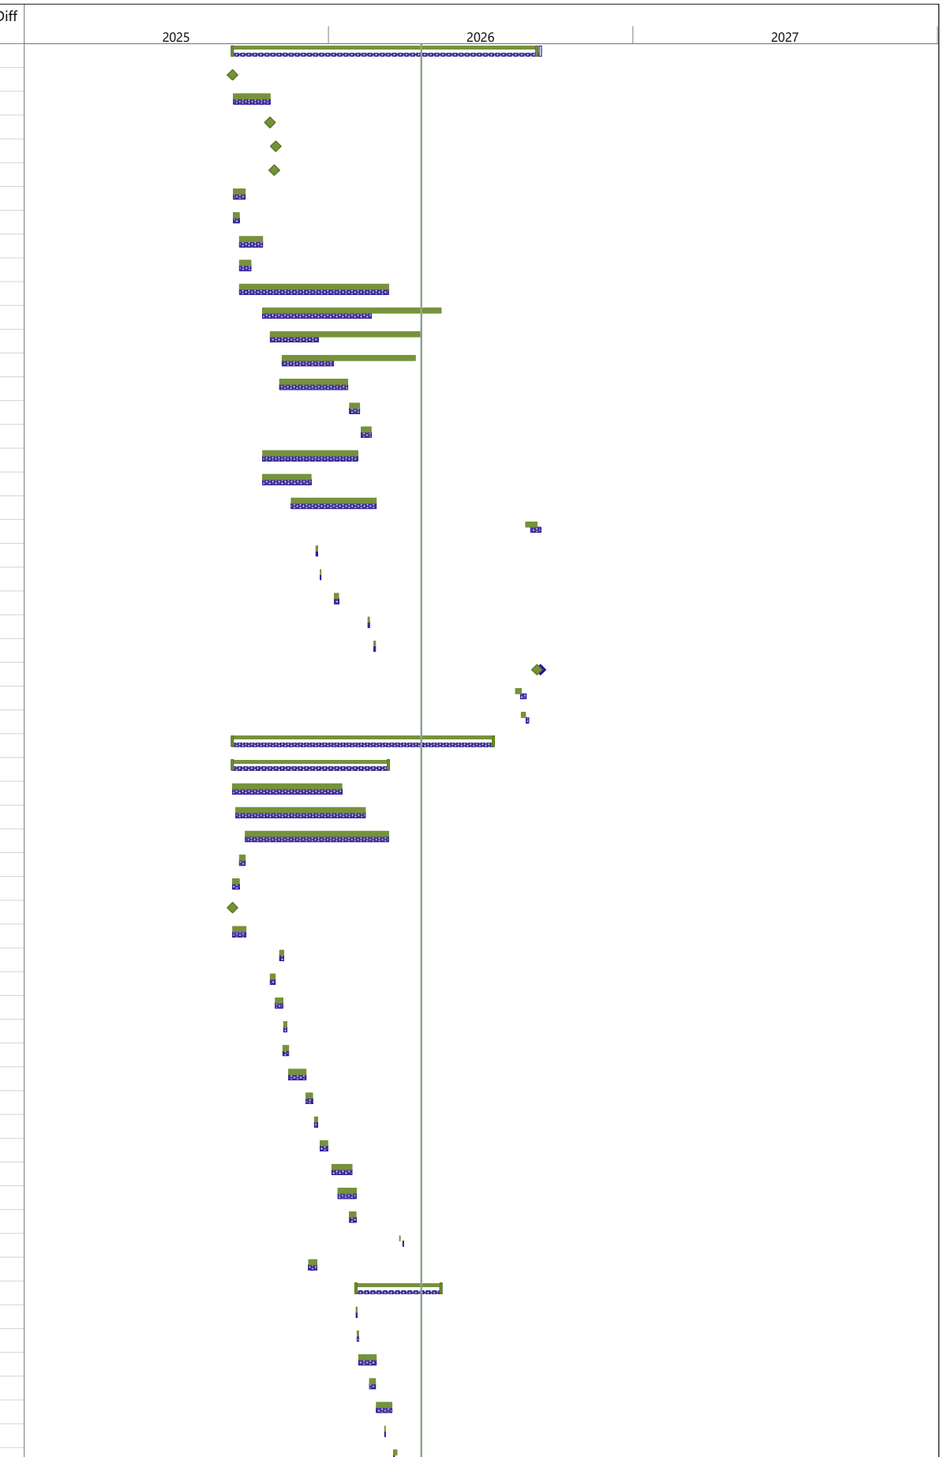

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
61	FRAGNET - Re-Prep, Proof Roll, Confirm Soft Spot Magnitude	1 day	1 day	0d	Mon 3/23/26	Mon 3/23/26	0d	Mon 3/23/26	Mon 3/23/26	0d
62	FRAGNET - Site - Partial Soft Spot Repair Examination of Pit Run t	3 days	3 days	0d	Tue 5/5/26	Tue 5/5/26	0d	Thu 5/7/26	Thu 5/7/26	0d
63	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex S	1 day	1 day	0d	Fri 5/8/26	Fri 5/8/26	0d	Fri 5/8/26	Fri 5/8/26	0d
64	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex F	5 days	5 days	0d	Mon 5/11/26	Mon 5/11/26	0d	Fri 5/15/26	Fri 5/15/26	0d
65	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex F	5 days	5 days	0d	Mon 5/11/26	Mon 5/11/26	0d	Fri 5/15/26	Fri 5/15/26	0d
66	Site - Idaho Power Boring	2 days	2 days	0d	Thu 2/26/26	Thu 2/26/26	0d	Fri 2/27/26	Fri 2/27/26	0d
67	Site - Idaho Power Trench, Conduit and Backfill	5 days	5 days	0d	Mon 3/9/26	Mon 3/9/26	0d	Fri 3/13/26	Fri 3/13/26	0d
68	Site - Idaho Power Transformer Set and Make Live	0 days	0 days	0d	Fri 3/13/26	Fri 3/13/26	0d	Fri 3/13/26	Fri 3/13/26	0d
69	Storm Drain Lines and Devices - South of Buildings (E-W)	7 days	7 days	0d	Wed 4/15/26	Wed 4/15/26	0d	Thu 4/23/26	Thu 4/23/26	0d
70	Site - Flatwork Sidewalk Prep	8 days	8 days	0d	Wed 4/15/26	Wed 4/15/26	0d	Fri 4/24/26	Fri 4/24/26	0d
71	Storm Drain Lines and Devices - North of Buildings (E-W)	7 days	7 days	0d	Fri 4/24/26	Fri 4/24/26	0d	Mon 5/4/26	Mon 5/4/26	0d
72	Site - Curb and Gutter Prep	8 days	8 days	0d	Mon 5/18/26	Mon 5/18/26	0d	Thu 5/28/26	Thu 5/28/26	0d
73	Site - Base Course Asphalt Prep	8 days	8 days	0d	Mon 5/18/26	Mon 5/18/26	0d	Thu 5/28/26	Thu 5/28/26	0d
74	Site Flatwork and Curb and Gutter - (E-W)	15 days	15 days	0d	Fri 5/29/26	Fri 5/29/26	0d	Thu 6/18/26	Thu 6/18/26	0d
75	Site - Fine Grade Asphalt Prep	3 days	3 days	0d	Fri 6/19/26	Fri 6/19/26	0d	Tue 6/23/26	Tue 6/23/26	0d
76	Asphalt Paving	2 days	2 days	0d	Wed 6/24/26	Wed 6/24/26	0d	Thu 6/25/26	Thu 6/25/26	0d
77	Pavement Markings, Signage & Bumpers	2 days	2 days	0d	Fri 6/26/26	Fri 6/26/26	0d	Mon 6/29/26	Mon 6/29/26	0d
78	Site Fencing Chainlink	5 days	5 days	0d	Wed 5/20/26	Wed 5/20/26	0d	Wed 5/27/26	Wed 5/27/26	0d
79	Gravel Road Finish Grading	5 days	5 days	0d	Thu 5/28/26	Thu 5/28/26	0d	Wed 6/3/26	Wed 6/3/26	0d
80	Landscaping and Irrigation	15 days	15 days	0d	Fri 6/26/26	Fri 6/26/26	0d	Fri 7/17/26	Fri 7/17/26	0d
81	Site Fencing Vinyl	10 days	10 days	0d	Fri 6/26/26	Fri 6/26/26	0d	Fri 7/10/26	Fri 7/10/26	0d
82	Site Fencing Rod Iron and Gates	5 days	5 days	0d	Fri 6/26/26	Fri 6/26/26	0d	Thu 7/2/26	Thu 7/2/26	0d
83	**BUILDING B**	**191 days**	**195 days**	**-4d**	**Wed 10/29/25**	**Wed 10/29/25**	**0d**	**Thu 7/30/26**	**Wed 8/5/26**	**-4d**
84	BLDG B Foundation Excavation	6 days	6 days	0d	Wed 10/29/25	Wed 10/29/25	0d	Wed 11/5/25	Wed 11/5/25	0d
85	DELAY - BLDG B FOOTING OVER-EX	4 days	4 days	0d	Fri 10/31/25	Fri 10/31/25	0d	Wed 11/5/25	Wed 11/5/25	0d
86	BLDG B SOG Prep	5 days	5 days	0d	Wed 11/26/25	Wed 11/26/25	0d	Thu 12/4/25	Thu 12/4/25	0d
87	FRAGNET - Bldg B Soft Spot Repair	8 days	8 days	0d	Thu 12/4/25	Thu 12/4/25	0d	Mon 12/15/25	Mon 12/15/25	0d
88	BLDG B Backfill Foundations	18 days	18 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Fri 1/9/26	Fri 1/9/26	0d
89	**CONCRETE WORK**	**44 days**	**44 days**	**0d**	**Thu 11/6/25**	**Thu 11/6/25**	**0d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**
90	BLDG B Foundation	14 days	14 days	0d	Thu 11/6/25	Thu 11/6/25	0d	Tue 11/25/25	Tue 11/25/25	0d
91	BLDG B Dampproofing	1 day	1 day	0d	Tue 11/18/25	Tue 11/18/25	0d	Wed 11/26/25	Wed 11/26/25	0d
92	BLDG B Slab On Grade	19 days	19 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Mon 1/12/26	Mon 1/12/26	0d
93	BLDG B Slab On Grade Complete	0 days	0 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 1/12/26	Mon 1/12/26	0d
94	**STEEL AND METALS**	**76 days**	**82 days**	**-6d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Mon 4/27/26**	**Tue 5/5/26**	**-6d**
95	Frame Load Bearing Shear Walls, Interior Partitions, & Corridors	20 days	20 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 2/9/26	Mon 2/9/26	0d
96	FRAGNET - Extended Shear Wall Durations (JANUS)	12 days	12 days	0d	Tue 2/10/26	Tue 2/10/26	0d	Wed 2/25/26	Wed 2/25/26	0d
97	Panel Shear Walls, Interior Partition, & Corridor Walls (JANUS)	20 days	20 days	0d	Thu 2/26/26	Thu 2/26/26	0d	Wed 3/25/26	Wed 3/25/26	0d
98	Perimeter Panel Interior Walls (JANUS)	20 days	20 days	0d	Tue 3/31/26	Wed 4/8/26	-6d	Mon 4/27/26	Tue 5/5/26	-6d
99	**WOOD & FRP**	**5 days**	**5 days**	**0d**	**Thu 4/9/26**	**Tue 4/14/26**	**-3d**	**Wed 4/15/26**	**Mon 4/20/26**	**-3d**
100	Misc Finish Carpentry	5 days	5 days	0d	Thu 4/9/26	Tue 4/14/26	-3d	Wed 4/15/26	Mon 4/20/26	-3d
101	**ROOF & SIDING**	**78 days**	**78 days**	**0d**	**Fri 1/30/26**	**Fri 1/30/26**	**0d**	**Tue 5/19/26**	**Tue 5/19/26**	**0d**
102	Exterior Sheathing	0 days	0 days	0d	Fri 1/30/26	Fri 1/30/26	0d	Mon 2/16/26	Mon 2/16/26	0d
103	Weather Barrier Fluid Applied	8 days	8 days	0d	Fri 2/6/26	Fri 2/6/26	0d	Thu 2/19/26	Thu 2/19/26	0d
104	Weather Barrier Tyvek	10 days	10 days	0d	Wed 3/4/26	Wed 3/4/26	0d	Tue 3/17/26	Tue 3/17/26	0d
105	CMU Veneer Base Course & Grout	15 days	15 days	0d	Tue 3/3/26	Tue 3/3/26	0d	Tue 4/7/26	Tue 4/7/26	0d
106	Rigid Insulation Behind CMU	5 days	5 days	0d	Wed 4/8/26	Wed 4/8/26	0d	Tue 4/14/26	Tue 4/14/26	0d
107	Rigid Insulation Behind Metal Panels	3 days	3 days	0d	Wed 4/15/26	Wed 4/15/26	0d	Fri 4/17/26	Fri 4/17/26	0d
108	CMU Veneer Remaining	15 days	15 days	0d	Wed 4/15/26	Wed 4/15/26	0d	Tue 5/5/26	Tue 5/5/26	0d
109	Exterior Metal Panels (JANUS)	10 days	10 days	0d	Wed 5/6/26	Wed 5/6/26	0d	Tue 5/19/26	Tue 5/19/26	0d
110	Install Roof & Roof Insulation (JANUS)	12 days	15 days	-3d	Wed 2/25/26	Wed 2/25/26	0d	Wed 3/25/26	Mon 3/30/26	-3d
111	BLDG B Roofing Complete	0 days	0 days	0d	Wed 3/25/26	Mon 3/30/26	-3d	Wed 3/25/26	Mon 3/30/26	-3d
112	**DOORS & WINDOWS**	**20 days**	**20 days**	**0d**	**Thu 7/2/26**	**Thu 7/9/26**	**-5d**	**Thu 7/30/26**	**Wed 8/5/26**	**-4d**
113	F&I Storage Unit Doors (JANUS)	20 days	20 days	0d	Thu 7/2/26	Thu 7/9/26	-5d	Thu 7/30/26	Wed 8/5/26	-4d
114	F&I HM Doors and Hardware (JANUS)	15 days	15 days	0d	Thu 7/2/26	Thu 7/9/26	-5d	Thu 7/23/26	Wed 7/29/26	-4d
115	**FINISHES**	**30 days**	**30 days**	**0d**	**Thu 3/26/26**	**Tue 3/31/26**	**-3d**	**Wed 5/6/26**	**Mon 5/11/26**	**-3d**
116	Install Gypsum Board	10 days	10 days	0d	Thu 3/26/26	Tue 3/31/26	-3d	Wed 4/8/26	Mon 4/13/26	-3d
117	Flooring Polished Concrete	5 days	5 days	0d	Thu 4/9/26	Tue 4/14/26	-3d	Wed 4/15/26	Mon 4/20/26	-3d
118	FRP / Vinyl Base	5 days	5 days	0d	Thu 4/16/26	Tue 4/21/26	-3d	Wed 4/22/26	Mon 4/27/26	-3d
119	Painting	10 days	10 days	0d	Thu 4/23/26	Tue 4/28/26	-3d	Wed 5/6/26	Mon 5/11/26	-3d
120	**SPECIALTIES**	**23 days**	**23 days**	**0d**	**Thu 4/9/26**	**Tue 4/14/26**	**-3d**	**Mon 5/11/26**	**Thu 5/14/26**	**-3d**

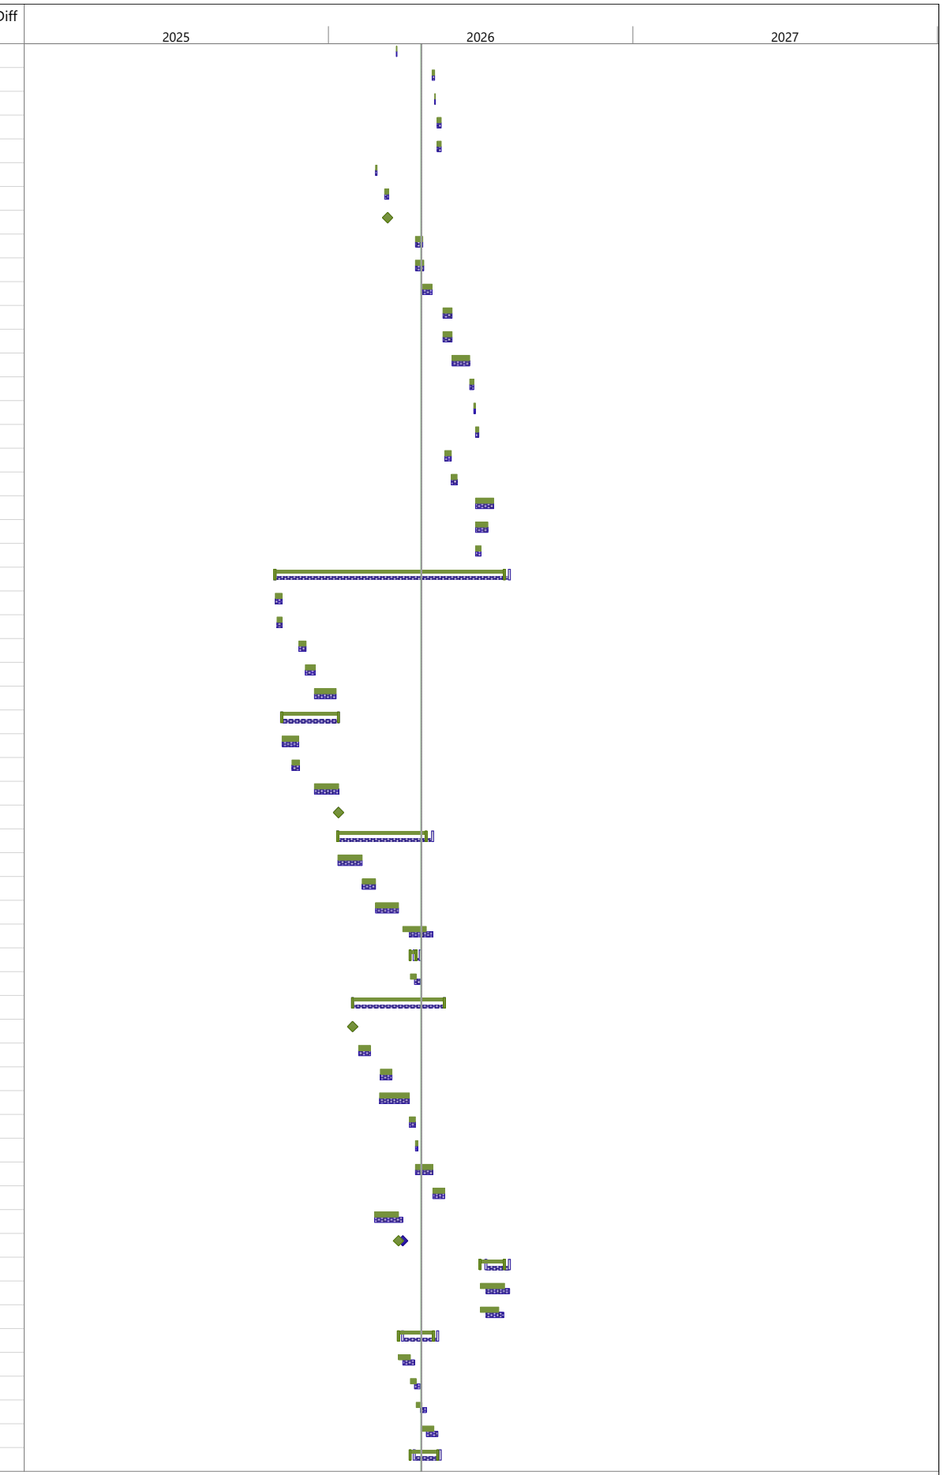

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
121	Install Misc Equipment & Lockers	20 days	20 days	0d	Thu 4/9/26	Tue 4/14/26	-3d	Wed 5/6/26	Mon 5/11/26	-3d
122	Bathroom Accessories	2 days	2 days	0d	Thu 4/16/26	Tue 4/21/26	-3d	Fri 4/17/26	Wed 4/22/26	-3d
123	Building Interior Signage	3 days	3 days	0d	Thu 5/7/26	Tue 5/12/26	-3d	Mon 5/11/26	Thu 5/14/26	-3d
124	**FIRE SPRINKLERS**	**36.25 days**	**50 days**	**-13.75d**	**Mon 2/23/26**	**Mon 2/23/26**	**0d**	**Tue 4/14/26**	**Fri 5/1/26**	**-13.75d**
125	Fire Sprinkler System Rough In	18 days	28 days	-10d	Mon 2/23/26	Mon 2/23/26	0d	Fri 3/27/26	Fri 4/10/26	-10d
126	Fire Sprinkler System Trim Out	15 days	15 days	0d	Mon 3/2/26	Mon 4/13/26	-30d	Tue 4/14/26	Fri 5/1/26	-13.75d
127	**PLUMBING**	**104 days**	**107 days**	**-3d**	**Thu 11/20/25**	**Thu 11/20/25**	**0d**	**Mon 4/20/26**	**Thu 4/23/26**	**-3d**
128	Plumbing Rough-in Underground	4 days	4 days	0d	Thu 11/20/25	Thu 11/20/25	0d	Tue 11/25/25	Tue 11/25/25	0d
129	Drains, Water, Sewer Lines	15 days	15 days	0d	Thu 3/26/26	Tue 3/31/26	-3d	Wed 4/15/26	Mon 4/20/26	-3d
130	Bathroom Fixtures	3 days	3 days	0d	Thu 4/16/26	Tue 4/21/26	-3d	Mon 4/20/26	Thu 4/23/26	-3d
131	Other Plumbing Fixtures	3 days	3 days	0d	Thu 4/16/26	Tue 4/21/26	-3d	Mon 4/20/26	Thu 4/23/26	-3d
132	**HVAC**	**94 days**	**30 days**	**64d**	**Mon 3/16/26**	**Tue 3/31/26**	**-11d**	**Mon 7/27/26**	**Mon 5/11/26**	**55d**
133	HVAC Installation - Start/Partial	4 days			Mon 3/23/26			Tue 3/31/26		
134	**FRAGNET - RFI 38 Condenser Unit Relocations**	**63 days**			**Mon 3/23/26**			**Thu 6/18/26**		
135	FRAGNET - RFI 38 Submitted, Reviewed, Responded, Confirme	10 days			Mon 3/23/26			Wed 4/8/26		
136	FRAGNET - RFI 38 - Cost Impact, Collect, Submit, Confirm CO	10 days			Thu 4/9/26			Wed 4/22/26		
137	FRAGNET - RFI 38 - Procurement, Re-Route Electrical	15 days			Thu 4/23/26			Wed 5/13/26		
138	TBD FRAGNET - RFI 38 - HVAC Set Units, Duct Procurement & I	40 days			Thu 4/23/26			Thu 6/18/26		
139	TBD FRAGNET - RFI 38 - Screen Wall Procurement and Install	40 days			Thu 4/23/26			Thu 6/18/26		
140	**FRAGNET - RFI 37 - Duct Conflicts**	**57 days**	**25 days**	**32d**	**Mon 3/16/26**	**Tue 3/31/26**	**-11d**	**Wed 6/3/26**	**Mon 5/4/26**	**22d**
141	RFI 37 - Initiated and Responded	8 days			Mon 3/16/26			Wed 3/25/26		
142	RFI 37 - Further Clarification Required, Caught Design Decrepe	2 days			Wed 4/1/26			Thu 4/2/26		
143	RFI 37 - Review and Responsed, Close as Directed	3 days			Fri 4/3/26			Tue 4/7/26		
144	TBD RFI 37 - Cost Impact Collection and Submission	10 days			Wed 4/8/26			Tue 4/21/26		
145	TBD RFI 37 - Procure Additional Matierals?	30 days			Wed 4/22/26			Wed 6/3/26		
146	HVAC Installation - Remaining	21 days			Fri 6/19/26			Mon 7/20/26		
147	HVAC Commisioning & T&B	5 days	5 days	0d	Tue 7/21/26	Tue 5/5/26	55d	Mon 7/27/26	Mon 5/11/26	55d
148	**ELECTRICAL**	**175 days**	**149 days**	**26d**	**Thu 11/20/25**	**Thu 11/20/25**	**0d**	**Thu 7/30/26**	**Tue 6/23/26**	**27d**
149	Building Rough-in Underground	0 days	0 days	0d	Thu 11/20/25	Thu 11/20/25	0d	Tue 11/25/25	Tue 11/25/25	0d
150	Elect Rough-In		25 days			Mon 3/2/26			Tue 4/7/26	
151	Elect Rough-In Start/Partial	19 days			Mon 3/2/26			Mon 3/30/26		
152	Install, Wire & Inspect - Start/Partial	5 days			Wed 3/25/26			Wed 4/1/26		
153	Install Wire & Inspect - Remaining	5 days	10 days	-5d	Thu 5/14/26	Tue 3/31/26	32d	Wed 5/20/26	Mon 4/13/26	27d
154	Install and Wire Panels	3 days	15 days	-12d	Fri 6/19/26	Tue 4/14/26	48d	Tue 6/23/26	Mon 5/4/26	36d
155	Permanent Power On	0 days	0 days	0d	Tue 6/23/26	Mon 5/4/26	36d	Tue 6/23/26	Mon 5/4/26	36d
156	FRAGNET - RFI 35 - Light Fixture Mounting Height Clarification Su	3 days	3 days	0d	Fri 3/13/26	Fri 3/13/26	0d	Tue 3/17/26	Tue 3/17/26	0d
157	Electric Lights, Devices and Trim	55 days	55 days	0d	Wed 3/25/26	Tue 3/31/26	-4d	Thu 6/11/26	Tue 6/16/26	-3d
158	Fire Alarm System	3 days	3 days	0d	Tue 7/21/26	Tue 5/5/26	55d	Thu 7/23/26	Thu 5/7/26	55d
159	Electrical Commissioning	5 days	5 days	0d	Fri 7/24/26	Wed 6/17/26	27d	Thu 7/30/26	Tue 6/23/26	27d
160	**BUILDING A**	**141 days**	**145 days**	**-4d**	**Mon 1/26/26**	**Mon 1/26/26**	**0d**	**Wed 8/12/26**	**Tue 8/18/26**	**-4d**
161	BLDG A Foundation Excavation	24 days	24 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Thu 2/26/26	Thu 2/26/26	0d
162	FRAGNET - BLDG A Footing Seepage Bed Over Ex.	1 day	1 day	0d	Mon 2/2/26	Mon 2/2/26	0d	Mon 2/2/26	Mon 2/2/26	0d
163	BLDG A - Interoir Backfill Foundations	2 days	2 days	0d	Thu 2/26/26	Thu 2/26/26	0d	Tue 3/3/26	Tue 3/3/26	0d
164	**FRAGNET - BLDG A Seepage Bed Pad Over Ex.**	**11 days**	**11 days**	**0d**	**Thu 2/26/26**	**Thu 2/26/26**	**0d**	**Thu 3/12/26**	**Thu 3/12/26**	**0d**
165	FRAGNET -Proposed direction received from Owner to perform E	1 day	1 day	0d	Thu 2/26/26	Thu 2/26/26	0d	Thu 2/26/26	Thu 2/26/26	0d
166	FRAGNET - Prepare and Submit Pricing for Approval	8 days	8 days	0d	Fri 2/27/26	Fri 2/27/26	0d	Tue 3/10/26	Tue 3/10/26	0d
167	FRAGNET - Owner Issued CCD 06 on Seepage Bed Cost Impact	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
168	FRAGNET - Mobilize Crew for BLDG A Seepage Bed Pad Over Ex.	1 day	1 day	0d	Tue 3/10/26	Tue 3/10/26	0d	Tue 3/10/26	Tue 3/10/26	0d
169	FRAGNET - Start BLDG A Seepage Bed Pad Over Ex.	1 day	1 day	0d	Wed 3/11/26	Wed 3/11/26	0d	Wed 3/11/26	Wed 3/11/26	0d
170	FRAGNET - Finish BLDG A Seepage Bed Pad Over Ex.	1 day	1 day	0d	Thu 3/12/26	Thu 3/12/26	0d	Thu 3/12/26	Thu 3/12/26	0d
171	BLDG A - Exterior Backfill Foundations	2 days	2 days	0d	Tue 3/10/26	Tue 3/10/26	0d	Wed 3/11/26	Wed 3/11/26	0d
172	BLDG A SOG Rough Grade Prep	2 days	2 days	0d	Wed 3/18/26	Wed 3/18/26	0d	Thu 3/19/26	Thu 3/19/26	0d
173	**FRAGNET - BLDG A Soft Spot Over Ex**	**20 days**	**20 days**	**0d**	**Thu 2/26/26**	**Thu 2/26/26**	**0d**	**Wed 3/25/26**	**Wed 3/25/26**	**0d**
174	FRAGNET - Proposed direction received from Owner to perform	1 day	1 day	0d	Thu 2/26/26	Thu 2/26/26	0d	Thu 2/26/26	Thu 2/26/26	0d
175	FRAGNET - Prepare and Submit Pricing for Approval	13 days	13 days	0d	Fri 2/27/26	Fri 2/27/26	0d	Tue 3/17/26	Tue 3/17/26	0d
176	FRAGNET - Owner Issued CCD 07 Directive for Driveisle and Soft	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
177	FRAGNET - Mobilize Crew, SOG Rough Grade Prep, Scarify, Air Dr	5 days	5 days	0d	Fri 3/13/26	Fri 3/13/26	0d	Thu 3/19/26	Thu 3/19/26	0d
178	FRAGNET - Air Dry Pad A, Re-Prep, Proof Roll to Idendify Soft Spc	2 days	2 days	0d	Fri 3/20/26	Fri 3/20/26	0d	Mon 3/23/26	Mon 3/23/26	0d
179	FRAGNET - Start Soft Spot Repairs	0 days	0 days	0d	Mon 3/23/26	Mon 3/23/26	0d	Mon 3/23/26	Mon 3/23/26	0d
180	FRAGNET - Test and Review Compaction Results for Soft Spot - If	1 day	1 day	0d	Tue 3/24/26	Tue 3/24/26	0d	Tue 3/24/26	Tue 3/24/26	0d

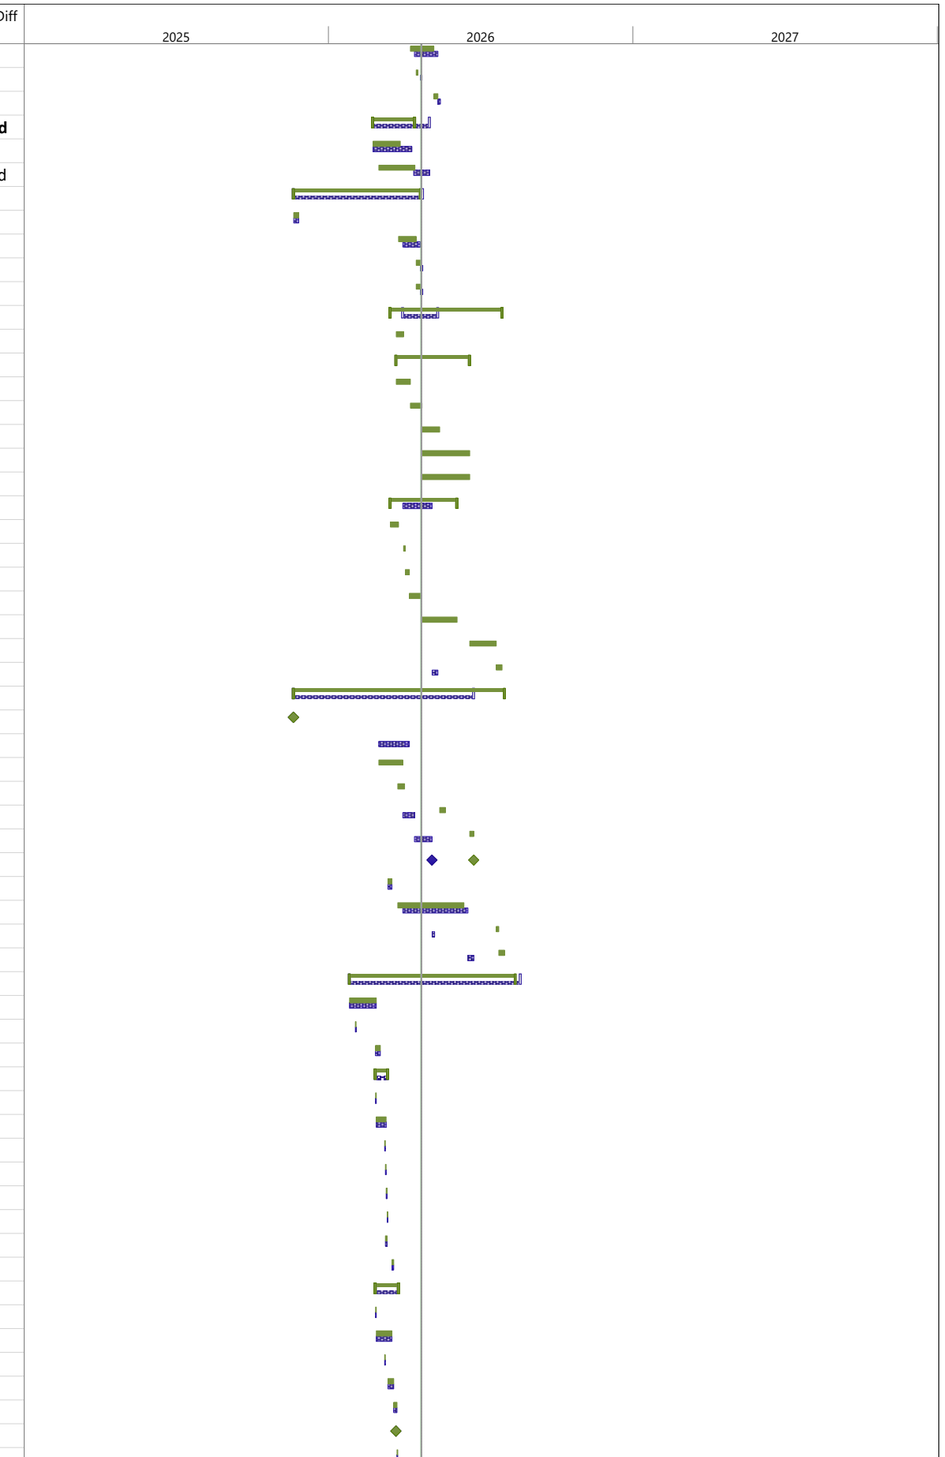
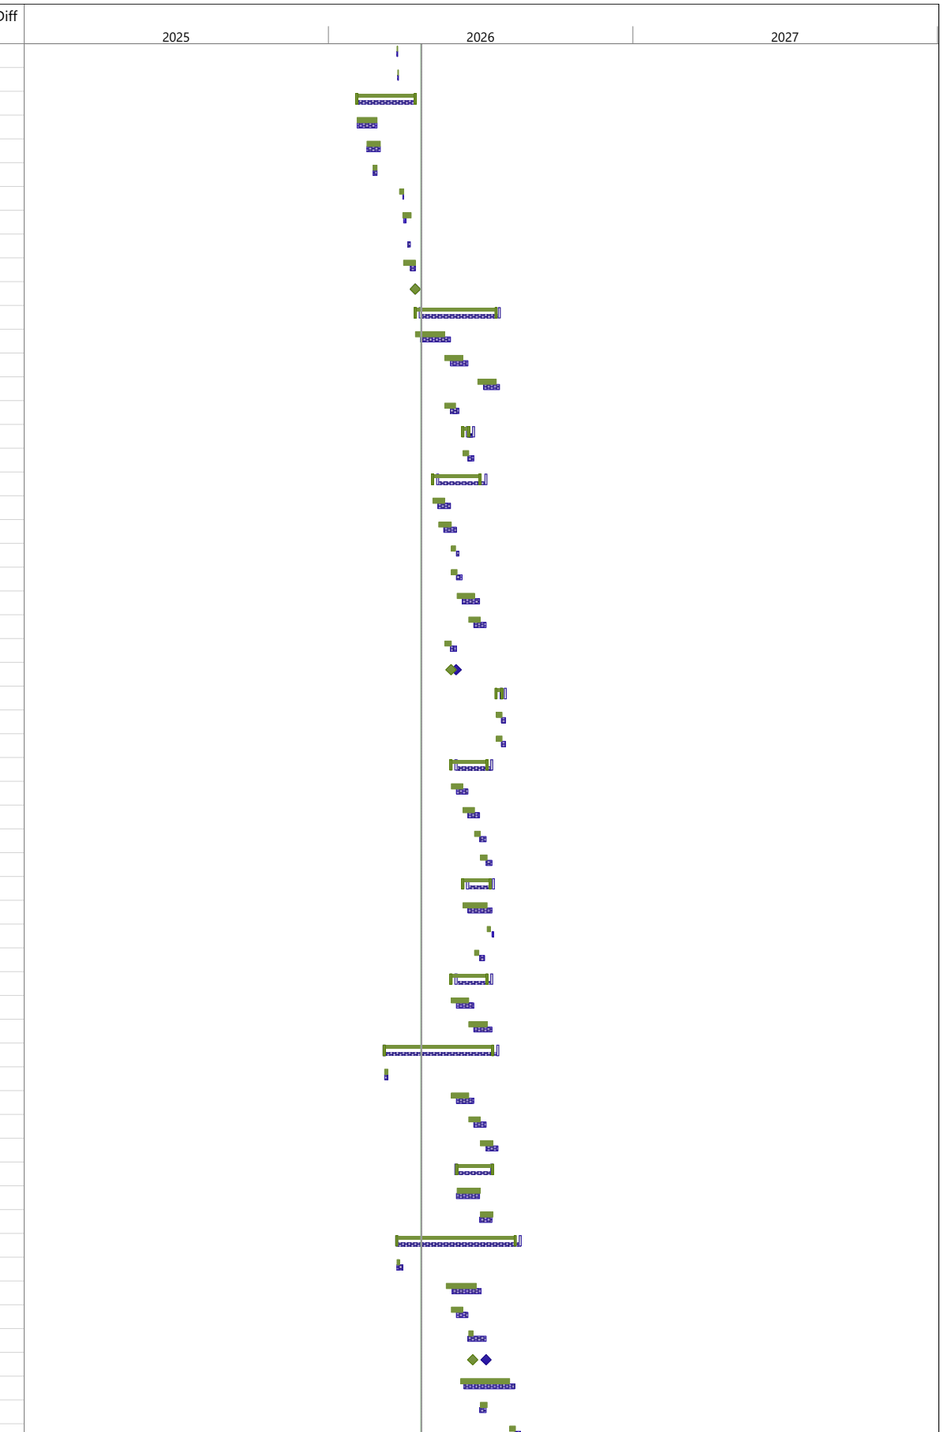
	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
181	FRAGNET - Soft Spot Repairs East Area	1 day	1 day	0d	Tue 3/24/26	Tue 3/24/26	0d	Tue 3/24/26	Tue 3/24/26	0d
182	FRAGNET - Soft Spot Repairs West Area	1 day	1 day	0d	Wed 3/25/26	Wed 3/25/26	0d	Wed 3/25/26	Wed 3/25/26	0d
183	**CONCRETE WORK**	**50 days**	**50 days**	**0d**	**Wed 2/4/26**	**Wed 2/4/26**	**0d**	**Tue 4/14/26**	**Tue 4/14/26**	**0d**
184	BLDG A Foundation	18 days	18 days	0d	Wed 2/4/26	Wed 2/4/26	0d	Fri 2/27/26	Fri 2/27/26	0d
185	BLDG A Dampproofing	4 days	4 days	0d	Mon 2/16/26	Mon 2/16/26	0d	Tue 3/3/26	Tue 3/3/26	0d
186	BLDG A Exterior Footing Insulation	5 days	5 days	0d	Mon 2/23/26	Mon 2/23/26	0d	Fri 2/27/26	Fri 2/27/26	0d
187	BLDG A SOG Fine Prep	3 days	1 day	2d	Fri 3/27/26	Tue 3/31/26	-2d	Tue 3/31/26	Tue 3/31/26	0d
188	BLDG A Slab On Grade (East)	7 days	3 days	4d	Tue 3/31/26	Wed 4/1/26	-1d	Thu 4/9/26	Fri 4/3/26	4d
189	BLDG A Slab On Grade (Center)		3 days			Mon 4/6/26			Wed 4/8/26	
190	BLDG A Slab On Grade (West)	10 days	4 days	6d	Wed 4/1/26	Thu 4/9/26	-6d	Tue 4/14/26	Tue 4/14/26	0d
191	BLDG A Slab On Grade Complete	0 days	0 days	0d	Tue 4/14/26	Tue 4/14/26	0d	Tue 4/14/26	Tue 4/14/26	0d
192	**STEEL AND METALS**	**67 days**	**67 days**	**0d**	**Wed 4/15/26**	**Tue 4/21/26**	**-4d**	**Mon 7/20/26**	**Fri 7/24/26**	**-4d**
193	Frame Load Bearing, Shear Walls, Partition & Corridor (JANUS)	25 days	25 days	0d	Wed 4/15/26	Tue 4/21/26	-4d	Tue 5/19/26	Tue 5/26/26	-5d
194	Panel Shear Wall, Interior Partition, & Corridor Walls (JANUS)	15 days	15 days	0d	Wed 5/20/26	Wed 5/27/26	-5d	Wed 6/10/26	Tue 6/16/26	-4d
195	Perimeter Panel Interior Walls (JANUS)	15 days	15 days	0d	Mon 6/29/26	Mon 7/6/26	-5d	Mon 7/20/26	Fri 7/24/26	-4d
196	Canopy Install	8 days	8 days	0d	Wed 5/20/26	Wed 5/27/26	-5d	Mon 6/1/26	Fri 6/5/26	-4d
197	**WOOD & FRP**	**5 days**	**5 days**	**0d**	**Thu 6/11/26**	**Wed 6/17/26**	**-4d**	**Wed 6/17/26**	**Tue 6/23/26**	**-4d**
198	Misc Finish Carpentry	5 days	5 days	0d	Thu 6/11/26	Wed 6/17/26	-4d	Wed 6/17/26	Tue 6/23/26	-4d
199	**ROOF & SIDING**	**40 days**	**40 days**	**0d**	**Wed 5/6/26**	**Tue 5/12/26**	**-4d**	**Wed 7/1/26**	**Wed 7/8/26**	**-5d**
200	Exterior Sheathing	10 days	10 days	0d	Wed 5/6/26	Tue 5/12/26	-4d	Tue 5/19/26	Tue 5/26/26	-5d
201	Exterior Sheathing, Weather Barrier & Rigid Insulation - Building	10 days	10 days	0d	Wed 5/13/26	Tue 5/19/26	-4d	Wed 5/27/26	Tue 6/2/26	-4d
202	Rigid Insulation Behind Metal Panels	3 days	3 days	0d	Thu 5/28/26	Wed 6/3/26	-4d	Mon 6/1/26	Fri 6/5/26	-4d
203	Rigid Insulation Behind CMU	5 days	5 days	0d	Thu 5/28/26	Wed 6/3/26	-4d	Wed 6/3/26	Tue 6/9/26	-4d
204	CMU Veneer	15 days	15 days	0d	Thu 6/4/26	Wed 6/10/26	-4d	Wed 6/24/26	Tue 6/30/26	-4d
205	Exterior Metal Panels (JANUS)	10 days	10 days	0d	Thu 6/18/26	Wed 6/24/26	-4d	Wed 7/1/26	Wed 7/8/26	-5d
206	Install Roof & Roof Insulation (JANUS)	5 days	5 days	0d	Wed 5/20/26	Wed 5/27/26	-5d	Wed 5/27/26	Tue 6/2/26	-4d
207	BLDG A Roofing Complete	0 days	0 days	0d	Wed 5/27/26	Tue 6/2/26	-4d	Wed 5/27/26	Tue 6/2/26	-4d
208	**DOORS & WINDOWS**	**5 days**	**5 days**	**0d**	**Tue 7/21/26**	**Mon 7/27/26**	**-4d**	**Mon 7/27/26**	**Fri 7/31/26**	**-4d**
209	F&I Storage Unit Doors (JANUS)	5 days	5 days	0d	Tue 7/21/26	Mon 7/27/26	-4d	Mon 7/27/26	Fri 7/31/26	-4d
210	F&I HM Doors and Hardware (JANUS)	5 days	5 days	0d	Tue 7/21/26	Mon 7/27/26	-4d	Mon 7/27/26	Fri 7/31/26	-4d
211	**FINISHES**	**30 days**	**30 days**	**0d**	**Thu 5/28/26**	**Wed 6/3/26**	**-4d**	**Thu 7/9/26**	**Wed 7/15/26**	**-4d**
212	Install Gypsum Board	10 days	10 days	0d	Thu 5/28/26	Wed 6/3/26	-4d	Wed 6/10/26	Tue 6/16/26	-4d
213	Painting	10 days	10 days	0d	Thu 6/11/26	Wed 6/17/26	-4d	Wed 6/24/26	Tue 6/30/26	-4d
214	Flooring Polished Conc.	5 days	5 days	0d	Thu 6/25/26	Wed 7/1/26	-4d	Wed 7/1/26	Wed 7/8/26	-5d
215	FRP & Vinyl Base	5 days	5 days	0d	Thu 7/2/26	Thu 7/9/26	-5d	Thu 7/9/26	Wed 7/15/26	-4d
216	**SPECIALTIES**	**22 days**	**22 days**	**0d**	**Thu 6/11/26**	**Wed 6/17/26**	**-4d**	**Mon 7/13/26**	**Fri 7/17/26**	**-4d**
217	Install Misc Equipment & Lockers	20 days	20 days	0d	Thu 6/11/26	Wed 6/17/26	-4d	Thu 7/9/26	Wed 7/15/26	-4d
218	Bathroom Accessories- Building A	2 days	2 days	0d	Fri 7/10/26	Thu 7/16/26	-4d	Mon 7/13/26	Fri 7/17/26	-4d
219	Building Interior Signage	3 days	3 days	0d	Thu 6/25/26	Wed 7/1/26	-4d	Mon 6/29/26	Mon 7/6/26	-5d
220	**FIRE SPRINKLERS**	**30 days**	**30 days**	**0d**	**Thu 5/28/26**	**Wed 6/3/26**	**-4d**	**Thu 7/9/26**	**Wed 7/15/26**	**-4d**
221	Fire Sprinkler System Rough In	15 days	15 days	0d	Thu 5/28/26	Wed 6/3/26	-4d	Wed 6/17/26	Tue 6/23/26	-4d
222	Fire Sprinkler System Trim Out	15 days	15 days	0d	Thu 6/18/26	Wed 6/24/26	-4d	Thu 7/9/26	Wed 7/15/26	-4d
223	**PLUMBING**	**92 days**	**96 days**	**-4d**	**Mon 3/9/26**	**Mon 3/9/26**	**0d**	**Thu 7/16/26**	**Wed 7/22/26**	**-4d**
224	Plumbing Rough-in Underground	4 days	4 days	0d	Mon 3/9/26	Mon 3/9/26	0d	Thu 3/12/26	Thu 3/12/26	0d
225	Drains, Water, Sewer Lines	15 days	15 days	0d	Thu 5/28/26	Wed 6/3/26	-4d	Wed 6/17/26	Tue 6/23/26	-4d
226	Bathroom Fixtures- Building A	10 days	10 days	0d	Thu 6/18/26	Wed 6/24/26	-4d	Wed 7/1/26	Wed 7/8/26	-5d
227	Other Plumbing Fixtures	10 days	10 days	0d	Thu 7/2/26	Thu 7/9/26	-5d	Thu 7/16/26	Wed 7/22/26	-4d
228	**HVAC**	**30 days**	**30 days**	**0d**	**Thu 6/4/26**	**Wed 6/3/26**	**1d**	**Thu 7/16/26**	**Wed 7/15/26**	**1d**
229	HVAC Installation	20 days	20 days	0d	Thu 6/4/26	Wed 6/3/26	1d	Wed 7/1/26	Tue 6/30/26	1d
230	HVAC Commisioning - Building A	10 days	10 days	0d	Thu 7/2/26	Wed 7/1/26	1d	Thu 7/16/26	Wed 7/15/26	1d
231	**ELECTRICAL**	**100 days**	**104 days**	**-4d**	**Tue 3/24/26**	**Tue 3/24/26**	**0d**	**Wed 8/12/26**	**Tue 8/18/26**	**-4d**
232	Building Rough-in Underground	3 days	5 days	-2d	Tue 3/24/26	Tue 3/24/26	0d	Thu 3/26/26	Mon 3/30/26	-2d
233	Electrical Rough-In	25 days	25 days	0d	Fri 5/22/26	Fri 5/29/26	-5d	Fri 6/26/26	Thu 7/2/26	-4d
234	New Service Equipment Install, Wire & Inspect	10 days	10 days	0d	Thu 5/28/26	Wed 6/3/26	-4d	Wed 6/10/26	Tue 6/16/26	-4d
235	Install and Wire Panels	3 days	15 days	-12d	Thu 6/18/26	Wed 6/17/26	1d	Mon 6/22/26	Wed 7/8/26	-12d
236	Permanent Power On- Building A	0 days	0 days	0d	Mon 6/22/26	Wed 7/8/26	-12d	Mon 6/22/26	Wed 7/8/26	-12d
237	Electric Lights, Devices and Trim	42 days	42 days	0d	Mon 6/8/26	Fri 6/12/26	-4d	Wed 8/5/26	Tue 8/11/26	-4d
238	Fire Alarm System	5 days	5 days	0d	Thu 7/2/26	Wed 7/1/26	1d	Thu 7/9/26	Wed 7/8/26	1d
239	Electrical Commissioning	5 days	5 days	0d	Thu 8/6/26	Wed 8/12/26	-4d	Wed 8/12/26	Tue 8/18/26	-4d
