PETRA GENERAL CONTRACTORS

Meridian, ID - 2026.04.02 - UP04

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Name	% Complete	Duration	Start	Finish
1	**GENERAL REQUIREMENTS AND CONDITIONS**	**67%**	**255 days**	**Mon 9/8/25**	**Mon 9/7/26**
12	Submittals (numerous)	57%	150 days	Tue 10/14/25	Fri 5/15/26
13	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG B	16%	124 days	Thu 10/23/25	Mon 4/20/26
14	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG A	9%	110 days	Thu 11/6/25	Tue 4/14/26
21	**TWENTY WORKING DAYS OF WEATHER DELAY**	0%	10 days	Tue 8/25/26	Mon 9/7/26
27	**Substantial Completion**	**0%**	**0 days**	**Mon 9/7/26**	**Mon 9/7/26**
28	Clean Up and Project Close Out	0%	5 days	Thu 8/13/26	Wed 8/19/26
29	Demobilize	0%	3 days	Thu 8/20/26	Mon 8/24/26
30	**SITEWORK**	**50%**	**219 days**	**Mon 9/8/25**	**Fri 7/17/26**
31	**Level of Effort**	**42%**	**131 days**	**Mon 9/8/25**	**Fri 3/13/26**
32	Construction Staking & Surveying	75%	90 days	Mon 9/8/25	Fri 1/16/26
33	Inspections and Testing	0%	100 days	Fri 9/12/25	Fri 2/13/26
34	Maintain Erosion Control	50%	120 days	Tue 9/23/25	Fri 3/13/26
51	Complete UG Utility Lines, SD Turn Ups, to Building A	0%	1 day	Fri 3/27/26	Fri 3/27/26
53	**FRAGNET - Site - Drive Aisle Unsuitable Soils**	**74%**	**74 days**	**Tue 2/3/26**	**Fri 5/15/26**
62	FRAGNET - Site - Partial Soft Spot Repair Examination of Pit Run to Proceed. If failed,	0%	3 days	Tue 5/5/26	Thu 5/7/26
63	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Start	0%	1 day	Fri 5/8/26	Fri 5/8/26
64	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld A	0%	5 days	Mon 5/11/26	Fri 5/15/26
65	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld B	0%	5 days	Mon 5/11/26	Fri 5/15/26
69	Storm Drain Lines and Devices - South of Buildings (E-W)	0%	7 days	Wed 4/15/26	Thu 4/23/26
70	Site - Flatwork Sidewalk Prep	0%	8 days	Wed 4/15/26	Fri 4/24/26
71	Storm Drain Lines and Devices - North of Buildings (E-W)	0%	7 days	Fri 4/24/26	Mon 5/4/26
72	Site - Curb and Gutter Prep	0%	8 days	Mon 5/18/26	Thu 5/28/26
73	Site - Base Course Asphalt Prep	0%	8 days	Mon 5/18/26	Thu 5/28/26
74	Site Flatwork and Curb and Gutter - (E-W)	0%	15 days	Fri 5/29/26	Thu 6/18/26
75	Site - Fine Grade Asphalt Prep	0%	3 days	Fri 6/19/26	Tue 6/23/26
76	Asphalt Paving	0%	2 days	Wed 6/24/26	Thu 6/25/26
77	Pavement Markings, Signage & Bumpers	0%	2 days	Fri 6/26/26	Mon 6/29/26
78	Site Fencing Chainlink	0%	5 days	Wed 5/20/26	Wed 5/27/26
79	Gravel Road Finish Grading	0%	5 days	Thu 5/28/26	Wed 6/3/26
80	Landscaping and Irrigation	0%	15 days	Fri 6/26/26	Fri 7/17/26
81	Site Fencing Vinyl	0%	10 days	Fri 6/26/26	Fri 7/10/26
82	Site Fencing Rod Iron and Gates	0%	5 days	Fri 6/26/26	Thu 7/2/26
83	**BUILDING B**	**37%**	**191 days**	**Wed 10/29/25**	**Thu 7/30/26**
94	**STEEL AND METALS**	**63%**	**76 days**	**Mon 1/12/26**	**Mon 4/27/26**
97	Panel Shear Walls, Interior Partition, & Corridor Walls (JANUS)	65%	20 days	Thu 2/26/26	Wed 3/25/26
98	Perimeter Panel Interior Walls (JANUS)	0%	20 days	Tue 3/31/26	Mon 4/27/26
99	**WOOD & FRP**	**0%**	**5 days**	**Thu 4/9/26**	**Wed 4/15/26**
100	Misc Finish Carpentry	0%	5 days	Thu 4/9/26	Wed 4/15/26
101	**ROOF & SIDING**	**54%**	**78 days**	**Fri 1/30/26**	**Tue 5/19/26**
105	CMU Veneer Base Course & Grout	80%	15 days	Tue 3/3/26	Tue 4/7/26
106	Rigid Insulation Behind CMU	0%	5 days	Wed 4/8/26	Tue 4/14/26
107	Rigid Insulation Behind Metal Panels	0%	3 days	Wed 4/15/26	Fri 4/17/26
108	CMU Veneer Remaining	0%	15 days	Wed 4/15/26	Tue 5/5/26
109	Exterior Metal Panels (JANUS)	0%	10 days	Wed 5/6/26	Tue 5/19/26

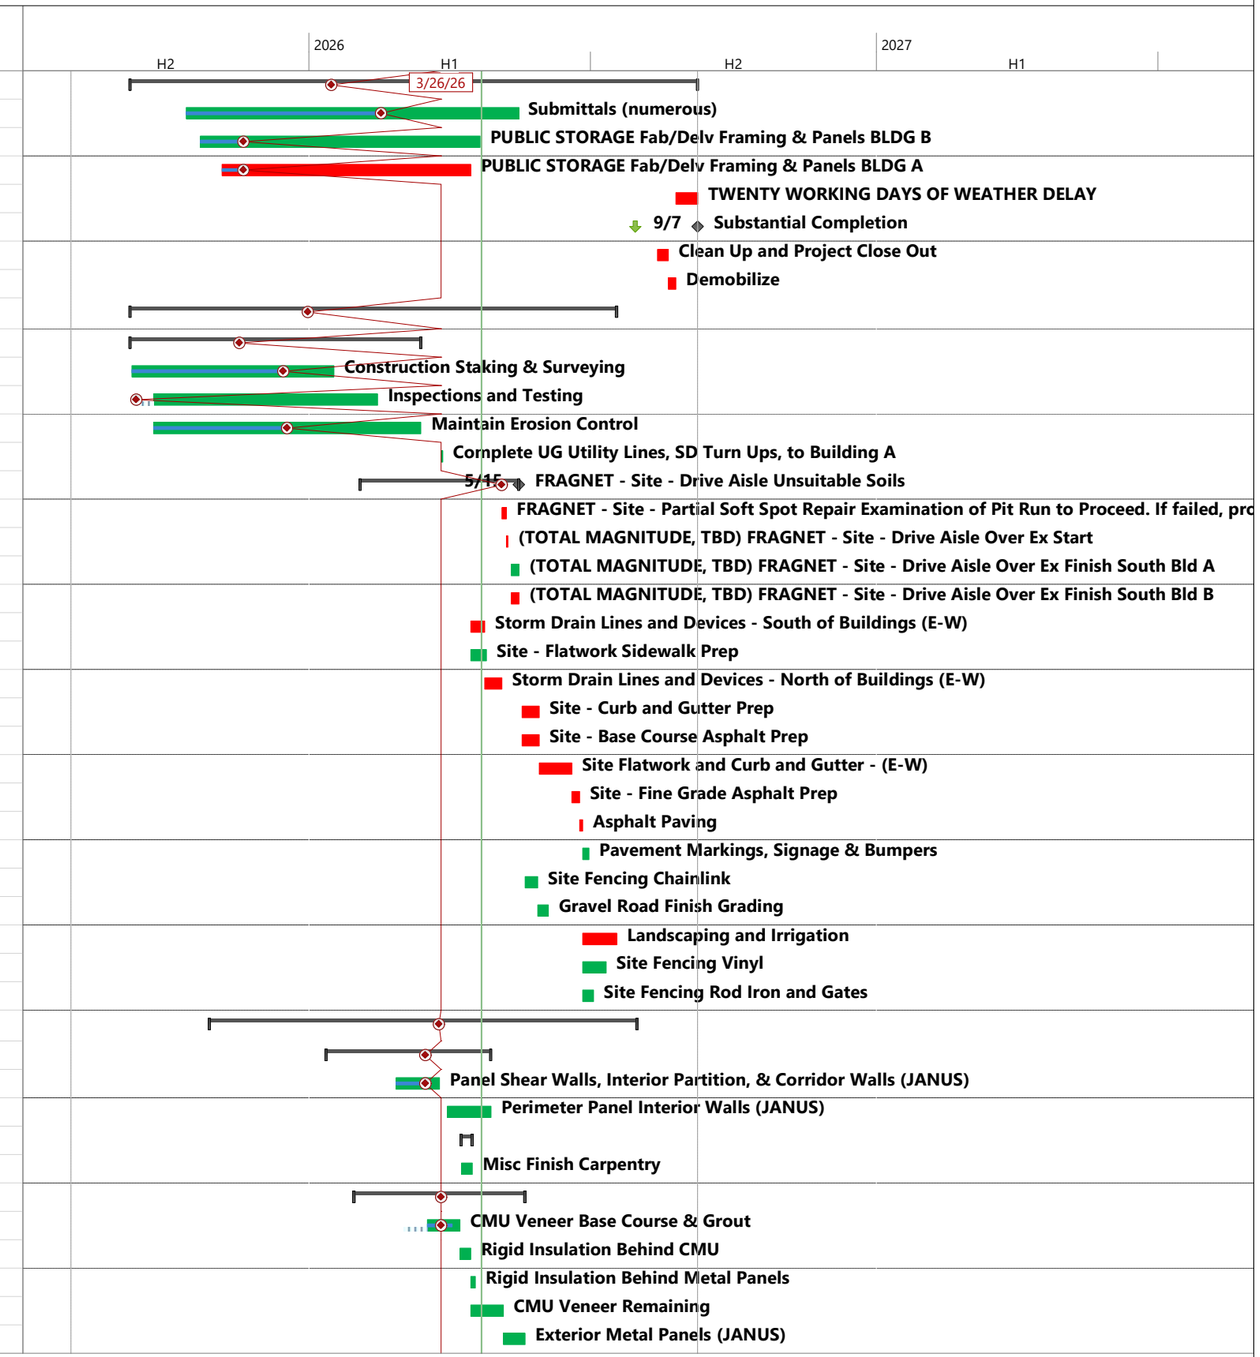

Printed: Wed 4/22/26 2:26 PM

PETRA General Contractors

Meridian, ID - 2026.04.02 - UP04

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Name	% Complete	Duration	Start	Finish
112	**DOORS & WINDOWS**	**0%**	**20 days**	**Thu 7/2/26**	**Thu 7/30/26**
113	F&I Storage Unit Doors (JANUS)	0%	20 days	Thu 7/2/26	Thu 7/30/26
114	F&I HM Doors and Hardware (JANUS)	0%	15 days	Thu 7/2/26	Thu 7/23/26
115	**FINISHES**	**0%**	**30 days**	**Thu 3/26/26**	**Wed 5/6/26**
116	Install Gypsum Board	0%	10 days	Thu 3/26/26	Wed 4/8/26
117	Flooring Polished Concrete	0%	5 days	Thu 4/9/26	Wed 4/15/26
118	FRP / Vinyl Base	0%	5 days	Thu 4/16/26	Wed 4/22/26
119	Painting	0%	10 days	Thu 4/23/26	Wed 5/6/26
120	**SPECIALTIES**	**0%**	**23 days**	**Thu 4/9/26**	**Mon 5/11/26**
121	Install Misc Equipment & Lockers	0%	20 days	Thu 4/9/26	Wed 5/6/26
122	Bathroom Accessories	0%	2 days	Thu 4/16/26	Fri 4/17/26
123	Building Interior Signage	0%	3 days	Thu 5/7/26	Mon 5/11/26
124	**FIRE SPRINKLERS**	**89%**	**36.25 days**	**Mon 2/23/26**	**Tue 4/14/26**
126	Fire Sprinkler System Trim Out	75%	15 days	Mon 3/2/26	Tue 4/14/26
127	**PLUMBING**	**16%**	**104 days**	**Thu 11/20/25**	**Mon 4/20/26**
129	Drains, Water, Sewer Lines	0%	15 days	Thu 3/26/26	Wed 4/15/26
130	Bathroom Fixtures	0%	3 days	Thu 4/16/26	Mon 4/20/26
131	Other Plumbing Fixtures	0%	3 days	Thu 4/16/26	Mon 4/20/26
132	**HVAC**	**9%**	**94 days**	**Mon 3/16/26**	**Mon 7/27/26**
134	**FRAGNET - RFI 38 Condenser Unit Relocations**	**3%**	**63 days**	**Mon 3/23/26**	**Thu 6/18/26**
135	FRAGNET - RFI 38 Submitted, Reviewed, Responded, Confirmed Direction	40%	10 days	Mon 3/23/26	Wed 4/8/26
136	FRAGNET - RFI 38 - Cost Impact, Collect, Submit, Confirm CO	0%	10 days	Thu 4/9/26	Wed 4/22/26
137	FRAGNET - RFI 38 - Procurement, Re-Route Electrical	0%	15 days	Thu 4/23/26	Wed 5/13/26
138	TBD FRAGNET - RFI 38 - HVAC Set Units, Duct Procurement & Install	0%	40 days	Thu 4/23/26	Thu 6/18/26
139	TBD FRAGNET - RFI 38 - Screen Wall Procurement and Install	0%	40 days	Thu 4/23/26	Thu 6/18/26
140	**FRAGNET - RFI 37 - Duct Conflicts**	**20%**	**57 days**	**Mon 3/16/26**	**Wed 6/3/26**
143	RFI 37 - Review and Responsed, Close as Directed	17%	3 days	Fri 4/3/26	Tue 4/7/26
144	TBD RFI 37 - Cost Impact Collection and Submission	0%	10 days	Wed 4/8/26	Tue 4/21/26
145	TBD RFI 37 - Procure Additional Matierals?	0%	30 days	Wed 4/22/26	Wed 6/3/26
146	HVAC Installation - Remaining	0%	21 days	Fri 6/19/26	Mon 7/20/26
147	HVAC Commisioning & T&B	0%	5 days	Tue 7/21/26	Mon 7/27/26
148	**ELECTRICAL**	**39%**	**175 days**	**Thu 11/20/25**	**Thu 7/30/26**
152	Install Wire & Inspect - Remaining	0%	5 days	Thu 5/14/26	Wed 5/20/26
153	Install and Wire Panels	0%	3 days	Fri 6/19/26	Tue 6/23/26
154	**Permanent Power On**	**0%**	**0 days**	**Tue 6/23/26**	**Tue 6/23/26**
156	Electric Lights, Devices and Trim	20%	55 days	Wed 3/25/26	Thu 6/11/26
157	Fire Alarm System	0%	3 days	Tue 7/21/26	Thu 7/23/26
158	Electrical Commissioning	0%	5 days	Fri 7/24/26	Thu 7/30/26
159	**BUILDING A**	**22%**	**141 days**	**Mon 1/26/26**	**Wed 8/12/26**
182	**CONCRETE WORK**	**77%**	**50 days**	**Wed 2/4/26**	**Tue 4/14/26**
187	BLDG A Slab On Grade (East)	50%	7 days	Tue 3/31/26	Thu 4/9/26
188	BLDG A Slab On Grade (West)	25%	10 days	Wed 4/1/26	Tue 4/14/26
189	**BLDG A Slab On Grade Complete**	**0%**	**0 days**	**Tue 4/14/26**	**Tue 4/14/26**
190	**STEEL AND METALS**	**0%**	**67 days**	**Wed 4/15/26**	**Mon 7/20/26**
191	Frame Load Bearing, Shear Walls, Partition & Corridor (JANUS)	0%	25 days	Wed 4/15/26	Tue 5/19/26

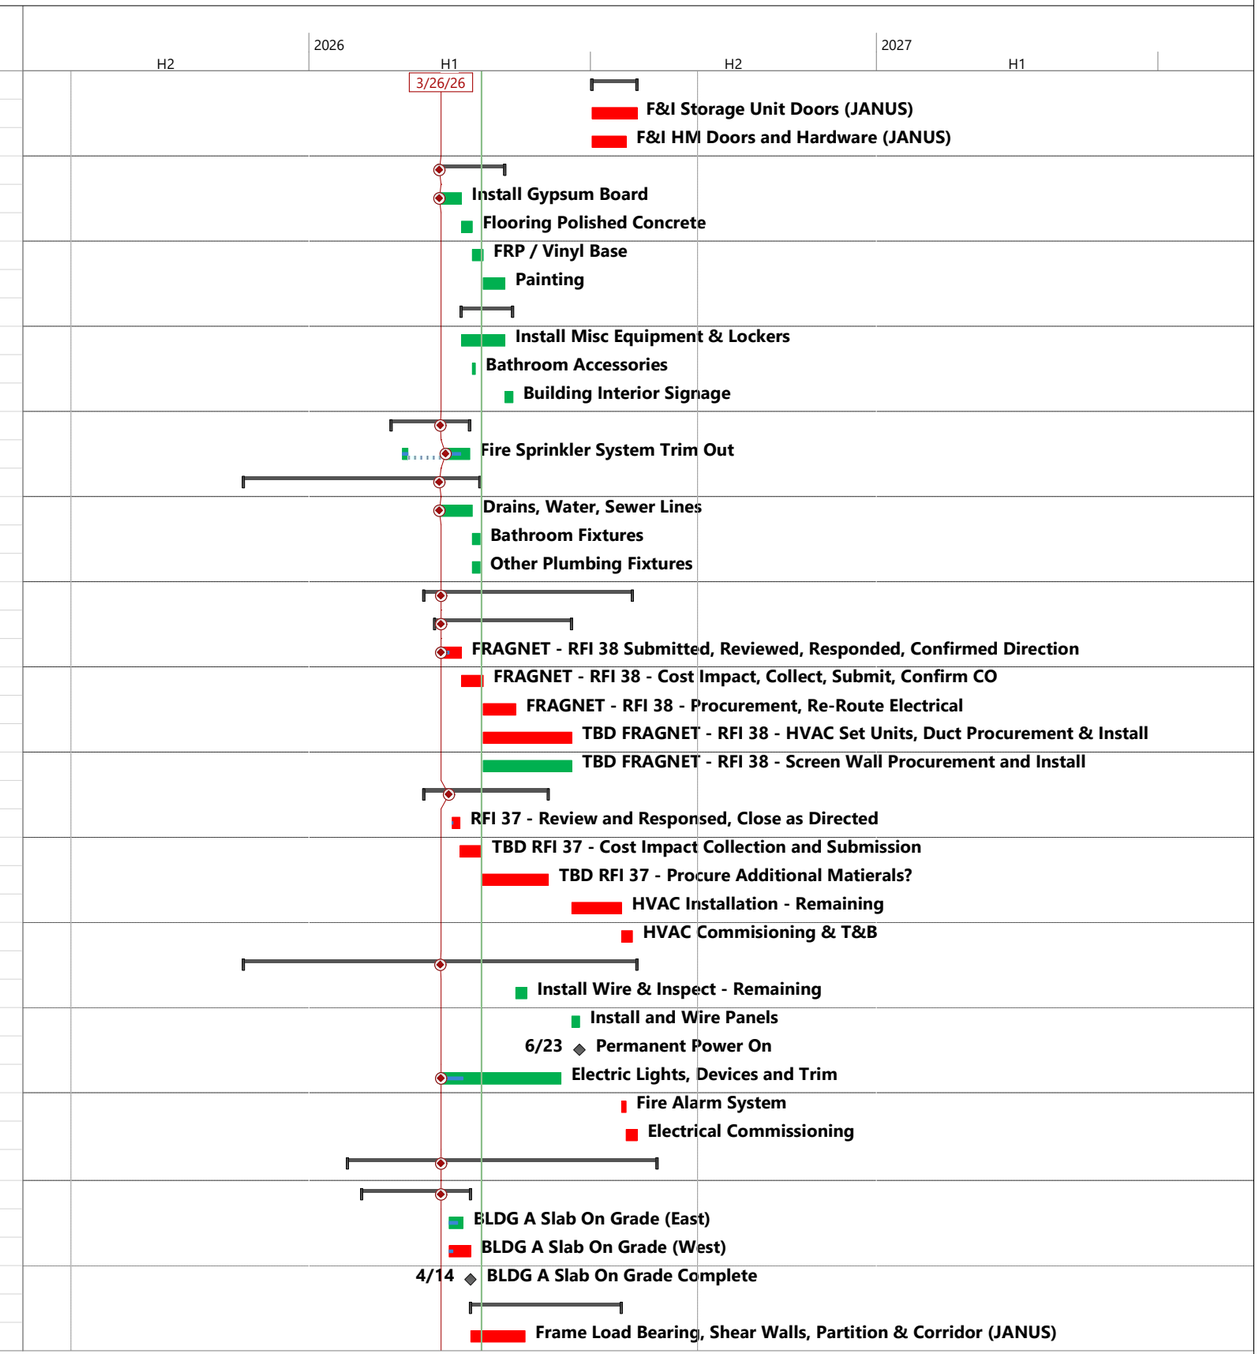

Printed: Wed 4/22/26 2:26 PM

PETRA General Contractors

Meridian, ID - 2026.04.02 - UP04

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Name	% Complete	Duration	Start	Finish
192	Panel Shear Wall, Interior Partition, & Corridor Walls (JANUS)	0%	15 days	Wed 5/20/26	Wed 6/10/26
193	Perimeter Panel Interior Walls (JANUS)	0%	15 days	Mon 6/29/26	Mon 7/20/26
194	Canopy Install	0%	8 days	Wed 5/20/26	Mon 6/1/26
195	**WOOD & FRP**	**0%**	**5 days**	**Thu 6/11/26**	**Wed 6/17/26**
196	Misc Finish Carpentry	0%	5 days	Thu 6/11/26	Wed 6/17/26
197	**ROOF & SIDING**	**0%**	**40 days**	**Wed 5/6/26**	**Wed 7/1/26**
198	Exterior Sheathing	0%	10 days	Wed 5/6/26	Tue 5/19/26
199	Exterior Sheathing, Weather Barrier & Rigid Insulation - Building A	0%	10 days	Wed 5/13/26	Wed 5/27/26
200	Rigid Insulation Behind Metal Panels	0%	3 days	Thu 5/28/26	Mon 6/1/26
201	Rigid Insulation Behind CMU	0%	5 days	Thu 5/28/26	Wed 6/3/26
202	CMU Veneer	0%	15 days	Thu 6/4/26	Wed 6/24/26
203	Exterior Metal Panels (JANUS)	0%	10 days	Thu 6/18/26	Wed 7/1/26
204	Install Roof & Roof Insulation (JANUS)	0%	5 days	Wed 5/20/26	Wed 5/27/26
205	**BLDG A Roofing Complete**	**0%**	**0 days**	**Wed 5/27/26**	**Wed 5/27/26**
206	**DOORS & WINDOWS**	**0%**	**5 days**	**Tue 7/21/26**	**Mon 7/27/26**
207	F&I Storage Unit Doors (JANUS)	0%	5 days	Tue 7/21/26	Mon 7/27/26
208	F&I HM Doors and Hardware (JANUS)	0%	5 days	Tue 7/21/26	Mon 7/27/26
209	**FINISHES**	**0%**	**30 days**	**Thu 5/28/26**	**Thu 7/9/26**
210	Install Gypsum Board	0%	10 days	Thu 5/28/26	Wed 6/10/26
211	Painting	0%	10 days	Thu 6/11/26	Wed 6/24/26
212	Flooring Polished Conc.	0%	5 days	Thu 6/25/26	Wed 7/1/26
213	FRP & Vinyl Base	0%	5 days	Thu 7/2/26	Thu 7/9/26
214	**SPECIALTIES**	**0%**	**22 days**	**Thu 6/11/26**	**Mon 7/13/26**
215	Install Misc Equipment & Lockers	0%	20 days	Thu 6/11/26	Thu 7/9/26
216	Bathroom Accessories- Building A	0%	2 days	Fri 7/10/26	Mon 7/13/26
217	Building Interior Signage	0%	3 days	Thu 6/25/26	Mon 6/29/26
218	**FIRE SPRINKLERS**	**0%**	**30 days**	**Thu 5/28/26**	**Thu 7/9/26**
219	Fire Sprinkler System Rough In	0%	15 days	Thu 5/28/26	Wed 6/17/26
220	Fire Sprinkler System Trim Out	0%	15 days	Thu 6/18/26	Thu 7/9/26
221	**PLUMBING**	**10%**	**92 days**	**Mon 3/9/26**	**Thu 7/16/26**
223	Drains, Water, Sewer Lines	0%	15 days	Thu 5/28/26	Wed 6/17/26
224	Bathroom Fixtures- Building A	0%	10 days	Thu 6/18/26	Wed 7/1/26
225	Other Plumbing Fixtures	0%	10 days	Thu 7/2/26	Thu 7/16/26
226	**HVAC**	**0%**	**30 days**	**Thu 6/4/26**	**Thu 7/16/26**
227	HVAC Installation	0%	20 days	Thu 6/4/26	Wed 7/1/26
228	HVAC Commisioning - Building A	0%	10 days	Thu 7/2/26	Thu 7/16/26
229	**ELECTRICAL**	**3%**	**100 days**	**Tue 3/24/26**	**Wed 8/12/26**
231	Electrical Rough-In	0%	25 days	Fri 5/22/26	Fri 6/26/26
232	New Service Equipment Install, Wire & Inspect	0%	10 days	Thu 5/28/26	Wed 6/10/26
233	Install and Wire Panels	0%	3 days	Thu 6/18/26	Mon 6/22/26
234	**Permanent Power On- Building A**	**0%**	**0 days**	**Mon 6/22/26**	**Mon 6/22/26**
235	Electric Lights, Devices and Trim	0%	42 days	Mon 6/8/26	Wed 8/5/26
236	Fire Alarm System	0%	5 days	Thu 7/2/26	Thu 7/9/26
237	Electrical Commissioning	0%	5 days	Thu 8/6/26	Wed 8/12/26

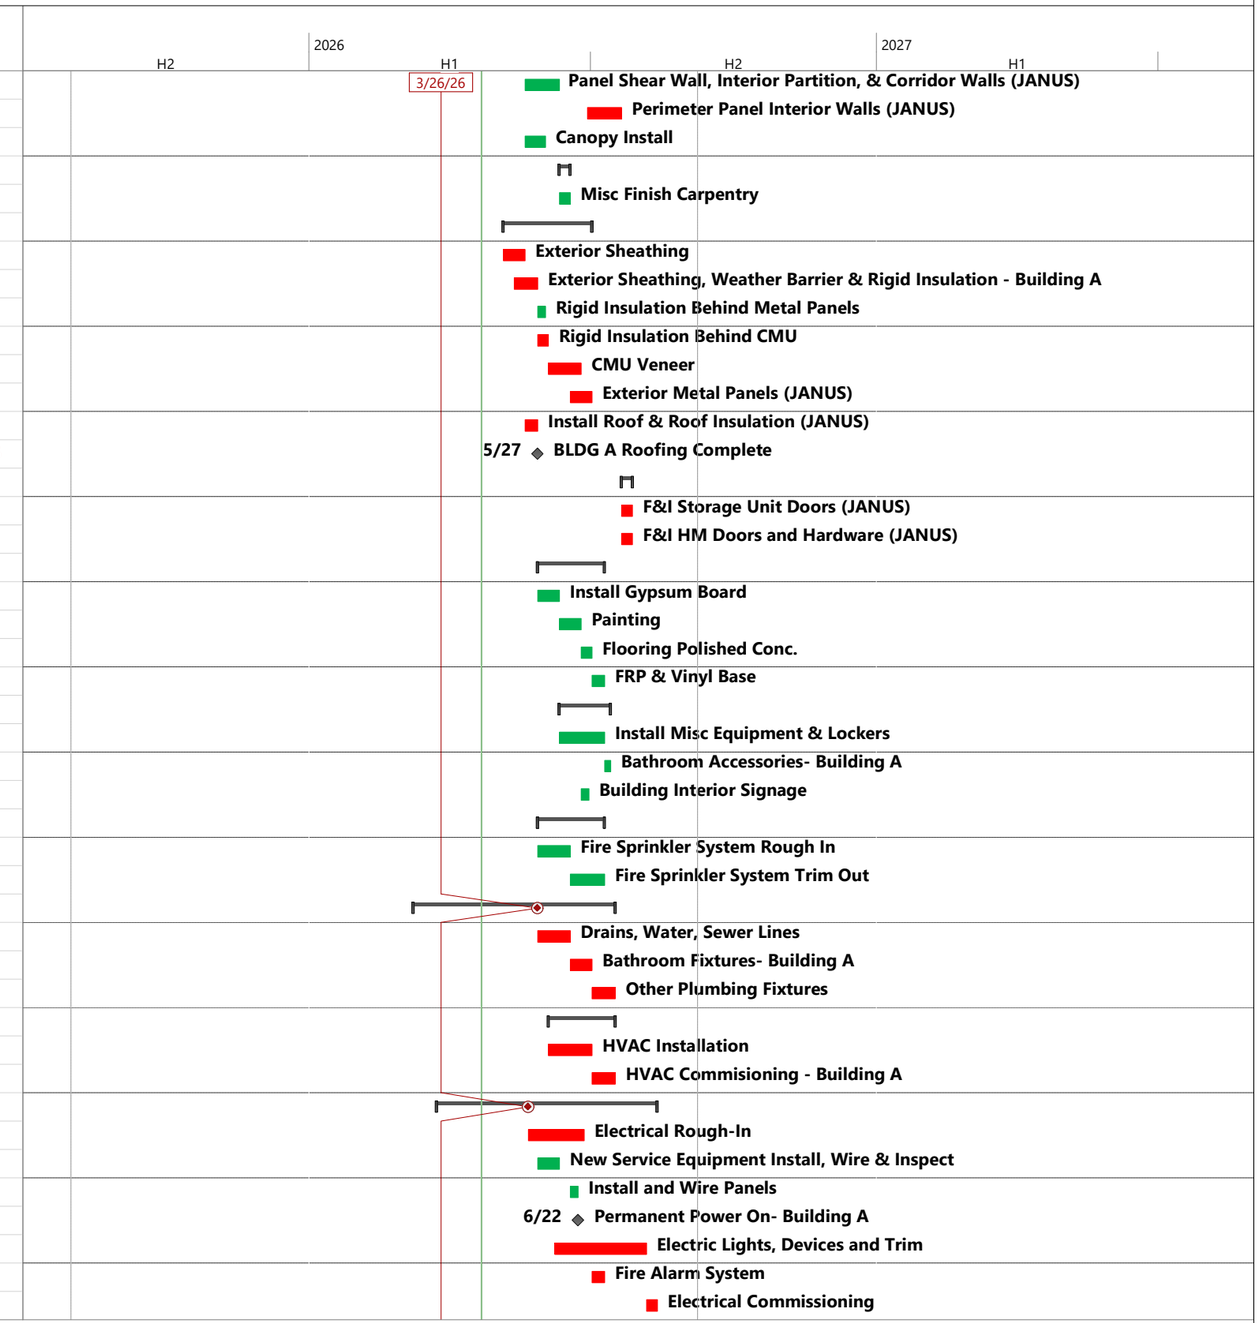

Printed: Wed 4/22/26 2:26 PM
