| Activity ID | Activity Name | Remaining Duration | Schedule % Complete | Start | Finish | Total Float | BL Project Start | BL Project Finish | Variance - BL Project Finish Date |
|---|---|---|---|---|---|---|---|---|---|
| **TN23676 - Mt. Juliet - Golden Bear (land) - TBA-2026.03.26 UP08** | | 429 | 0% | 12-Dec-25A | 18-Nov-27 | 0 | 12-Dec-25 | 12-Nov-27 | -4 |
| **Project Summary** | | 108 | 0% | 08-Jul-26 | 07-Dec-26 | 248 | 01-Jul-26 | 07-Dec-26 | 0 |
| **Contract Milestones** | | 13 | 0% | 18-Nov-26 | 07-Dec-26 | 248 | 12-Nov-26 | 07-Dec-26 | 0 |
| PS-CMIL-1010 | Project Substantial Completion | 0 | 0% | | 18-Nov-26 | 0 | | 12-Nov-26 | -4 |
| PS-CMIL-1150 | Contractual Substantial Completion Date | 0 | 0% | | 07-Dec-26 | 240 | | 07-Dec-26 | 0 |
| PS-CMIL-1160 | Remaining Weather Allowance (Originally 20 Days) | 11 | 0% | 19-Nov-26 | 07-Dec-26 | 0 | 13-Nov-26 | 01-Dec-26 | -4 |
| PS-CMIL-1170 | Project Substantial Completion with Weather Projection | 0 | 0% | | 07-Dec-26 | 0 | | 01-Dec-26 | -4 |
| PS-CMIL-1190 | Public Storage Final Acceptance | 0 | 0% | | 07-Dec-26 | 35 | | 01-Dec-26 | -4 |
| **Construction Milestones** | | 86 | 0% | 08-Jul-26 | 06-Nov-26 | 7 | 01-Jul-26 | 02-Nov-26 | -4 |
| PS-CMIL-1120 | Structure Complete | 0 | 0% | | 08-Jul-26 | 93 | | 01-Jul-26 | -4 |
| PS-CMIL-1130 | Building Dry In | 0 | 0% | | 14-Aug-26 | 66 | | 10-Aug-26 | -4 |
| PS-CMIL-1110 | Exterior Work Complete | 0 | 0% | | 06-Nov-26 | 7 | | 02-Nov-26 | -4 |
| PS-CMIL-1140 | Landscape & Hardscape Complete | 0 | 0% | | 06-Nov-26 | 7 | | 02-Nov-26 | -4 |
| **Pre-Construction** | | 90 | 0% | 12-Dec-25A | 31-Jul-26 | 71 | 12-Dec-25 | 29-Jun-26 | -24 |
| **Procurement** | | 90 | 0% | 12-Dec-25A | 31-Jul-26 | 71 | 12-Dec-25 | 29-Jun-26 | -24 |
| PS-PROC-1080 | Submit and Approve Plumbing Fixtures | 5 | 100% | 12-Dec-25A | 03-Apr-26 | 129 | 12-Dec-25 | 09-Mar-26 | -19 |
| PS-PROC-1110 | Submit and Approve Drywall / Ceilings | 5 | 100% | 02-Feb-26A | 03-Apr-26 | 119 | 02-Feb-26 | 02-Mar-26 | -24 |
| PS-PROC-1150 | Submit and Approve D/F/HW | 5 | 100% | 12-Feb-26A | 03-Apr-26 | 55 | 12-Feb-26 | 02-Mar-26 | -24 |
| PS-PROC-1130 | Submit and Approve Roofing | 10 | 100% | 16-Feb-26A | 10-Apr-26 | 61 | 16-Feb-26 | 09-Mar-26 | -24 |
| PS-PROC-1300 | Submit and Approve Brick Veneer | 10 | 100% | 12-Jan-26A | 10-Apr-26 | 10 | 12-Jan-26 | 09-Mar-26 | -24 |
| PS-PROC-1120 | Submit and Approve Floor Finishes | 15 | 60% | 30-Mar-26 | 17-Apr-26 | 110 | 17-Mar-26 | 06-Apr-26 | -9 |
| PS-PROC-1160 | Submit and Approve Toilet Accessories | 15 | 100% | 30-Mar-26 | 17-Apr-26 | 126 | 03-Mar-26 | 23-Mar-26 | -19 |
| PS-PROC-1170 | Submit and Approve Specialties | 15 | 100% | 30-Mar-26 | 17-Apr-26 | 121 | 03-Mar-26 | 23-Mar-26 | -19 |
| PS-PROC-1190 | Submit and Approve Appliances | 15 | 60% | 30-Mar-26 | 17-Apr-26 | 120 | 17-Mar-26 | 06-Apr-26 | -9 |
| PS-PROC-1340 | Procure Fireproofing / Intumescent | 15 | 100% | 30-Mar-26 | 17-Apr-26 | 103 | 27-Feb-26 | 19-Mar-26 | -21 |
| PS-PROC-1260 | Procure Roofing | 15 | 93.33% | 13-Apr-26 | 01-May-26 | 61 | 10-Mar-26 | 30-Mar-26 | -24 |
| PS-PROC-1020 | Procure Electric Room MDP | 30 | 78.67% | 05-Jan-26A | 08-May-26 | 99 | 05-Jan-26 | 20-Apr-26 | -14 |
| PS-PROC-1220 | Procure Light Fixtures | 30 | 71.93% | 30-Jan-26A | 08-May-26 | 122 | 30-Jan-26 | 20-Apr-26 | -14 |
| PS-PROC-1350 | Procure Plumbing Fixtures | 25 | 56% | 06-Apr-26 | 08-May-26 | 129 | 10-Mar-26 | 13-Apr-26 | -19 |
| PS-PROC-1360 | Procure Ceilings | 25 | 76% | 06-Apr-26 | 08-May-26 | 119 | 03-Mar-26 | 06-Apr-26 | -24 |
| PS-PROC-1280 | Procure D/F/HW | 30 | 63.33% | 06-Apr-26 | 15-May-26 | 55 | 03-Mar-26 | 13-Apr-26 | -24 |
| PS-PROC-1310 | Procure Toilet Accessories | 20 | 20% | 20-Apr-26 | 15-May-26 | 126 | 24-Mar-26 | 20-Apr-26 | -19 |
| PS-PROC-1320 | Procure Specialties | 20 | 20% | 20-Apr-26 | 15-May-26 | 121 | 24-Mar-26 | 20-Apr-26 | -19 |
| PS-PROC-1330 | Procure Appliances | 20 | 0% | 20-Apr-26 | 15-May-26 | 120 | 07-Apr-26 | 04-May-26 | -9 |
| PS-PROC-1230 | Procure HVAC Equipment and Fab Ductwork | 40 | 47.27% | 20-Feb-26A | 22-May-26 | 55 | 20-Feb-26 | 07-May-26 | -11 |
| PS-PROC-1270 | Procure Storefront / Glazing | 40 | 60% | 30-Mar-26 | 22-May-26 | 57 | 24-Feb-26 | 20-Apr-26 | -24 |
| PS-PROC-1290 | Procure Finishes | 25 | 0% | 20-Apr-26 | 22-May-26 | 110 | 07-Apr-26 | 11-May-26 | -9 |
| PS-PROC-1370 | Procure Brick Veneer | 80 | 17.5% | 13-Apr-26 | 31-Jul-26 | 10 | 10-Mar-26 | 29-Jun-26 | -24 |
| **Construction** | | 168 | 0% | 06-Jan-26A | 18-Nov-26 | 48 | 06-Jan-26 | 12-Nov-26 | -4 |
| **Mobilization** | | 0 | 0% | | | 0 | | | |
| **Sitework & Utilities** | | 40 | 0% | 25-Mar-26A | 22-May-26 | 52 | 24-Feb-26 | 13-Apr-26 | -29 |
| **Sitework** | | 22 | 0% | 23-Apr-26 | 22-May-26 | 50 | 13-Mar-26 | 13-Apr-26 | -29 |
| SU-STWK-1050 | Install Site Stone Base | 6 | 100% | 23-Apr-26 | 30-Apr-26 | 50 | 13-Mar-26 | 20-Mar-26 | -29 |
| SU-STWK-1060 | Install Prime Coat, Binder, & Tack Coat | 3 | 100% | 01-May-26 | 05-May-26 | 50 | 23-Mar-26 | 25-Mar-26 | -29 |
| SU-STWK-1070 | Install Asphalt (Wearing Course) | 1 | 100% | 06-May-26 | 06-May-26 | 50 | 26-Mar-26 | 26-Mar-26 | -29 |
| SU-STWK-1080 | Form & Reinforce Curb & Gutter | 5 | 20% | 07-May-26 | 13-May-26 | 50 | 27-Mar-26 | 02-Apr-26 | -29 |
| SU-STWK-1090 | Pour Curb & Gutter | 2 | 0% | 14-May-26 | 15-May-26 | 50 | 03-Apr-26 | 06-Apr-26 | -29 |
| SU-STWK-1100 | Rough Grade Site | 5 | 0% | 18-May-26 | 22-May-26 | 50 | 07-Apr-26 | 13-Apr-26 | -29 |
| **Site Utilities** | | 18 | 0% | 25-Mar-26A | 22-Apr-26 | 51 | 24-Feb-26 | 12-Mar-26 | -29 |
| *SU-SUTL-1060 | West Wilson Precon & Procurement | 5 | 0% | 25-Mar-26A | 03-Apr-26 | 51 | | | |
| SU-SUTL-1050 | Install U.G. Fire Water & Domestic | 10 | 100% | 06-Apr-26 | 17-Apr-26 | 50 | 24-Feb-26 | 09-Mar-26 | -29 |
| SU-SUTL-1010 | Install Irrigation Sleeves | 3 | 100% | 20-Apr-26 | 22-Apr-26 | 50 | 10-Mar-26 | 12-Mar-26 | -29 |
| **Foundation & Structural** | | 73 | 0% | 06-Jan-26A | 08-Jul-26 | 48 | 06-Jan-26 | 01-Jul-26 | -5 |
| **Level 1** | | 18 | 0% | 06-Jan-26A | 22-Apr-26 | 103 | 06-Jan-26 | 01-Apr-26 | -15 |
| FS-LVL1-1010 | Underground MEPF Install (Pre-Pour) | 2 | 100% | 06-Jan-26A | 31-Mar-26 | 0 | 06-Jan-26 | 04-Mar-26 | -19 |
| FS-LVL1-1080 | North Footings & Foundations | 3 | 0% | 30-Mar-26A | 01-Apr-26 | 0 | | | |
| FS-LVL1-1070 | Slab Prep & Pour (Pour A3) | 2 | 0% | 02-Apr-26 | 03-Apr-26 | 0 | | | |
| FS-LVL1-1050 | Steel Erection (Columns & Beams) | 8 | 100% | 26-Mar-26A | 08-Apr-26 | 0 | 16-Mar-26 | 27-Mar-26 | -8 |
| FS-LVL1-1060 | Fireproofing | 3 | 0% | 20-Apr-26 | 22-Apr-26 | 100 | 30-Mar-26 | 01-Apr-26 | -15 |
| **Level 2** | | 20 | 0% | 06-Apr-26 | 01-May-26 | 0 | 24-Mar-26 | 27-Apr-26 | -4 |
| FS-LVL2-1000 | Install Metal Decking | 4 | 100% | 06-Apr-26 | 09-Apr-26 | 0 | 24-Mar-26 | 27-Mar-26 | -9 |
| FS-LVL2-1010 | MEPF Rough-In (Pre-Pour) | 5 | 50% | 08-Apr-26 | 13-Apr-26 | 0 | 26-Mar-26 | 01-Apr-26 | -10 |
| FS-LVL2-1020 | FRP Metal Deck Slab (Pour A1) | 5 | 0% | 10-Apr-26 | 15-Apr-26 | 0 | 02-Apr-26 | 08-Apr-26 | -6 |
| FS-LVL2-1030 | FRP Metal Deck Slab (Pour A2) | 3 | 0% | 16-Apr-26 | 18-Apr-26 | 0 | 09-Apr-26 | 13-Apr-26 | -5 |
| FS-LVL2-1040 | Layout & Erect Load Bearing Framing | 10 | 0% | 20-Apr-26 | 01-May-26 | 0 | 14-Apr-26 | 27-Apr-26 | -4 |
| **Level 3** | | 25 | 0% | 28-Apr-26 | 02-Jun-26 | 0 | 22-Apr-26 | 27-May-26 | -4 |
| FS-LVL3-1000 | Install Metal Decking | 4 | 0% | 28-Apr-26 | 01-May-26 | 0 | 22-Apr-26 | 27-Apr-26 | -4 |
| FS-LVL3-1010 | MEPF Rough-In (Pre-Pour) | 5 | 0% | 30-Apr-26 | 06-May-26 | 0 | 24-Apr-26 | 30-Apr-26 | -4 |
| FS-LVL3-1020 | FRP Metal Deck Slab (Pour A1) | 5 | 0% | 07-May-26 | 13-May-26 | 0 | 01-May-26 | 07-May-26 | -4 |
| FS-LVL3-1030 | FRP Metal Deck Slab (Pour A2) | 3 | 0% | 14-May-26 | 18-May-26 | 0 | 08-May-26 | 12-May-26 | -4 |

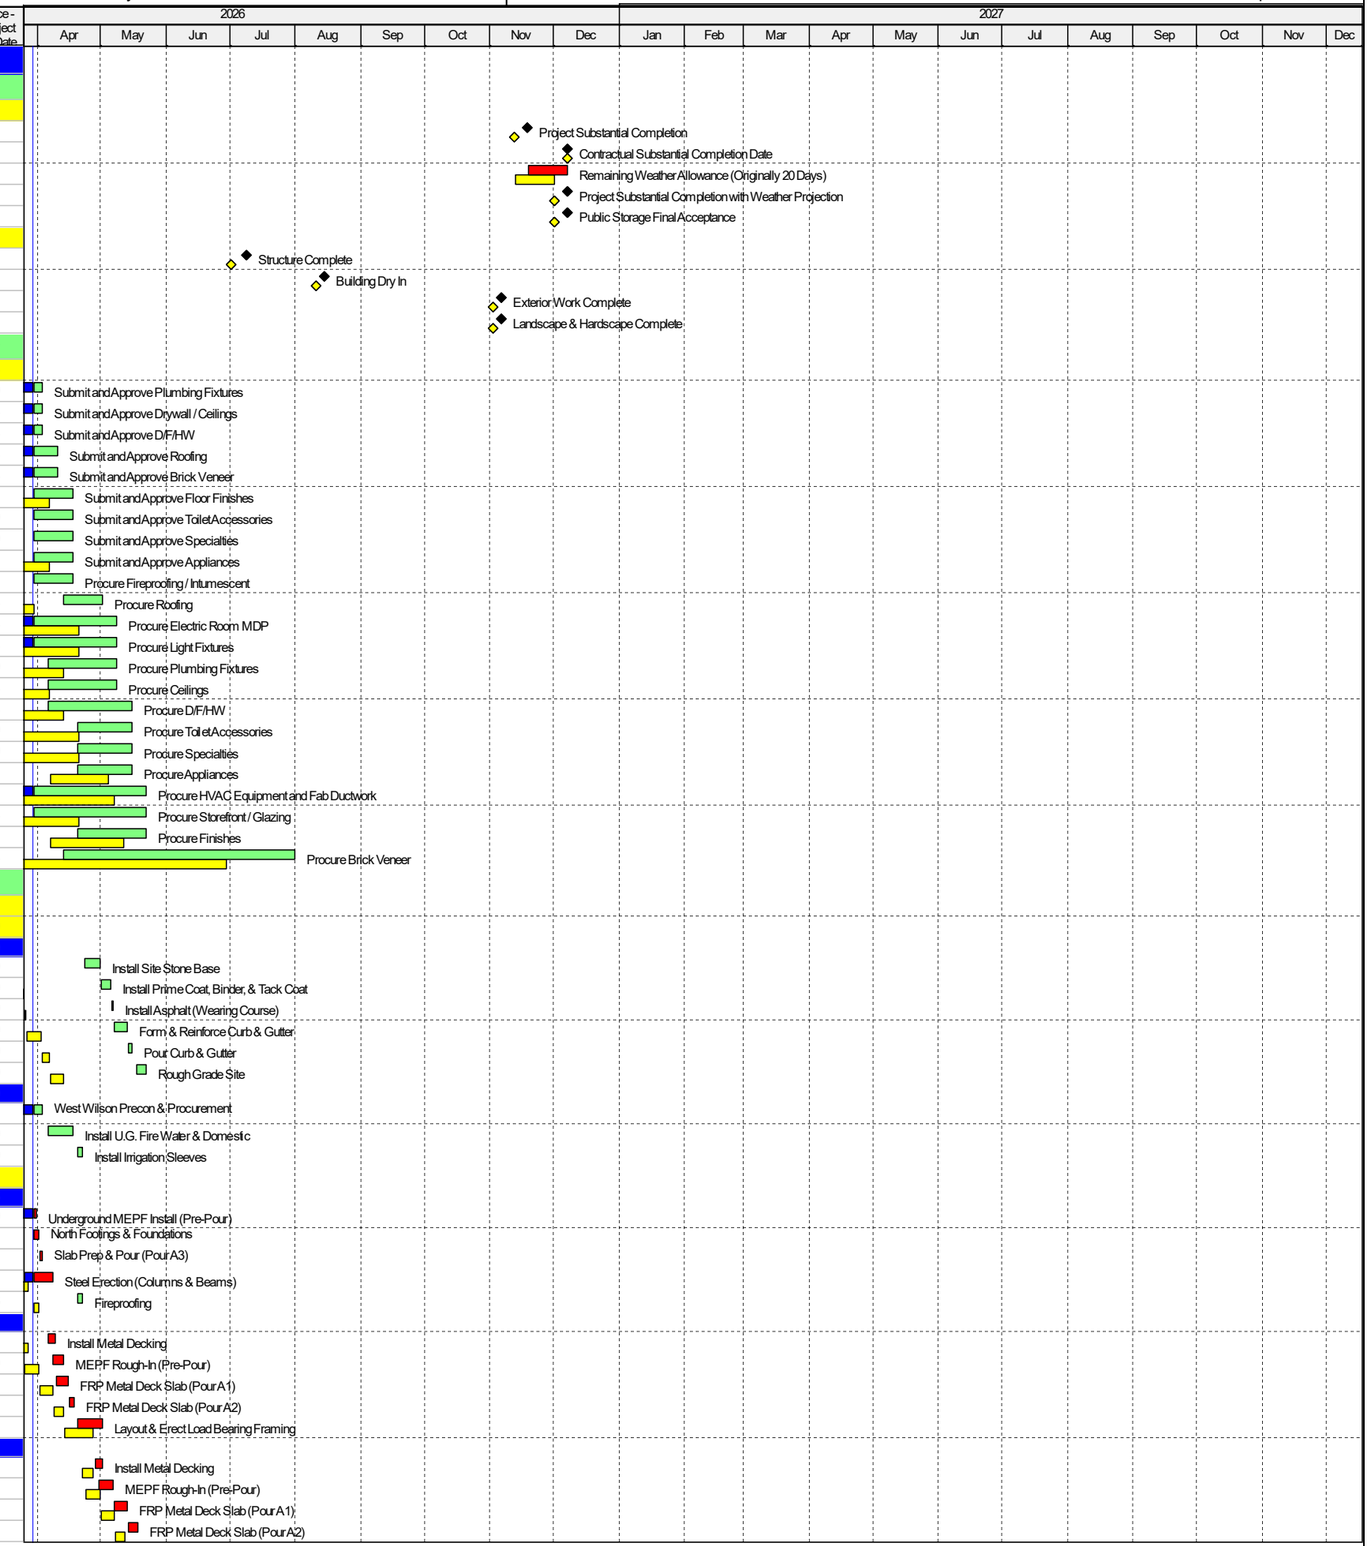


Project Baseline Bar | Remaining Work | ◇ Baseline Milestone
Actual Work | Critical Remaining Work | ◆ Milestone



TASK filter: Remaining .

© Oracle Corporation

| Activity ID | Activity Name | Remaining Duration | Schedule % Complete | Start | Finish | Total Float | BL Project Start | BL Project Finish | Variance - BL Project Finish Date |
|---|---|---|---|---|---|---|---|---|---|
| FS-LVL3-1040 | Layout & Erect Load Bearing Framing | 10 | 0% | 19-May-26 | 02-Jun-26 | 0 | 13-May-26 | 27-May-26 | -4 |
| **Level 4** | | 25 | 0% | 28-May-26 | 01-Jul-26 | 0 | 21-May-26 | 25-Jun-26 | -4 |
| FS-LVL4-1000 | Install Metal Decking | 4 | 0% | 28-May-26 | 02-Jun-26 | 0 | 21-May-26 | 27-May-26 | -4 |
| FS-LVL4-1010 | MEPF Rough-In (Pre-Pour) | 5 | 0% | 01-Jun-26 | 05-Jun-26 | 0 | 26-May-26 | 01-Jun-26 | -4 |
| FS-LVL4-1020 | FRP Metal Deck Slab (Pour A1) | 5 | 0% | 08-Jun-26 | 12-Jun-26 | 0 | 02-Jun-26 | 08-Jun-26 | -4 |
| FS-LVL4-1030 | FRP Metal Deck Slab (Pour A2) | 3 | 0% | 15-Jun-26 | 17-Jun-26 | 0 | 09-Jun-26 | 11-Jun-26 | -4 |
| FS-LVL4-1040 | Layout & Erect Load Bearing Framing | 10 | 0% | 18-Jun-26 | 01-Jul-26 | 0 | 12-Jun-26 | 25-Jun-26 | -4 |
| **Roof** | | 8 | 0% | 26-Jun-26 | 08-Jul-26 | 0 | 22-Jun-26 | 01-Jul-26 | -4 |
| FS-ROOF-1000 | Install Metal Decking | 4 | 0% | 26-Jun-26 | 01-Jul-26 | 0 | 22-Jun-26 | 25-Jun-26 | -4 |
| FS-ROOF-1010 | MEPF Rough-In (Stubups) | 3 | 0% | 30-Jun-26 | 02-Jul-26 | 0 | 24-Jun-26 | 26-Jun-26 | -4 |
| FS-ROOF-1020 | Layout & Frame Parapets | 3 | 0% | 06-Jul-26 | 08-Jul-26 | 0 | 29-Jun-26 | 01-Jul-26 | -4 |
| **Envelope & Exterior** | | 108 | 0% | 18-Jun-26 | 18-Nov-26 | 41 | 12-Jun-26 | 12-Nov-26 | -4 |
| **North Elevation** | | 77 | 0% | 18-Jun-26 | 06-Oct-26 | 72 | 12-Jun-26 | 30-Sep-26 | -4 |
| EE-NRTH-1000 | Layout & Exterior Framing (Level 1) | 5 | 0% | 18-Jun-26 | 24-Jun-26 | 10 | 12-Jun-26 | 18-Jun-26 | -4 |
| EE-NRTH-1010 | City Inspection (Rough Framing) | 1 | 0% | 25-Jun-26 | 25-Jun-26 | 10 | 19-Jun-26 | 19-Jun-26 | -4 |
| EE-NRTH-1020 | Electrical Rough-In | 5 | 0% | 09-Jul-26 | 15-Jul-26 | 2 | 02-Jul-26 | 09-Jul-26 | -4 |
| EE-NRTH-1030 | City Inspection (Electrical) | 1 | 0% | 16-Jul-26 | 16-Jul-26 | 2 | 10-Jul-26 | 10-Jul-26 | -4 |
| EE-NRTH-1040 | Install Exterior Sheathing | 5 | 0% | 17-Jul-26 | 23-Jul-26 | 2 | 13-Jul-26 | 17-Jul-26 | -4 |
| EE-NRTH-1050 | City Inspection (Screw Inspection) | 1 | 0% | 24-Jul-26 | 24-Jul-26 | 2 | 20-Jul-26 | 20-Jul-26 | -4 |
| EE-NRTH-1060 | Weather Barrier & Flashing | 5 | 0% | 27-Jul-26 | 31-Jul-26 | 2 | 21-Jul-26 | 27-Jul-26 | -4 |
| EE-NRTH-1070 | Install Rigid Insulation | 5 | 0% | 03-Aug-26 | 07-Aug-26 | 2 | 28-Jul-26 | 03-Aug-26 | -4 |
| EE-NRTH-1080 | Storefront, Windows & Metals | 3 | 0% | 10-Aug-26 | 12-Aug-26 | 2 | 04-Aug-26 | 06-Aug-26 | -4 |
| EE-NRTH-1090 | Install Brick Veneer | 15 | 0% | 13-Aug-26 | 02-Sep-26 | 2 | 07-Aug-26 | 27-Aug-26 | -4 |
| EE-NRTH-1100 | Install Canopies & Trim | 3 | 0% | 03-Sep-26 | 08-Sep-26 | 35 | 28-Aug-26 | 01-Sep-26 | -4 |
| EE-NRTH-1110 | Install Lighting Fixtures | 3 | 0% | 09-Sep-26 | 11-Sep-26 | 35 | 02-Sep-26 | 04-Sep-26 | -4 |
| EE-NRTH-1120 | Install Signage | 1 | 0% | 14-Sep-26 | 14-Sep-26 | 35 | 08-Sep-26 | 08-Sep-26 | -4 |
| EE-NRTH-1130 | Install Doors & Hardware | 2 | 0% | 15-Sep-26 | 16-Sep-26 | 35 | 09-Sep-26 | 10-Sep-26 | -4 |
| EE-NRTH-1140 | Install Downspouts | 1 | 0% | 17-Sep-26 | 17-Sep-26 | 35 | 11-Sep-26 | 11-Sep-26 | -4 |
| EE-NRTH-1150 | Final Paint | 3 | 0% | 18-Sep-26 | 22-Sep-26 | 35 | 14-Sep-26 | 16-Sep-26 | -4 |
| EE-NRTH-1160 | Punch List & Corrections | 5 | 0% | 23-Sep-26 | 29-Sep-26 | 35 | 17-Sep-26 | 23-Sep-26 | -4 |
| EE-NRTH-1170 | Final Owner Walk (Punch List & Corrections) | 5 | 0% | 30-Sep-26 | 06-Oct-26 | 72 | 24-Sep-26 | 30-Sep-26 | -4 |
| **East Elevation** | | 75 | 0% | 25-Jun-26 | 09-Oct-26 | 69 | 19-Jun-26 | 05-Oct-26 | -4 |
| EE-EAST-1000 | Layout & Exterior Framing (Level 1) | 5 | 0% | 25-Jun-26 | 01-Jul-26 | 13 | 19-Jun-26 | 25-Jun-26 | -4 |
| EE-EAST-1010 | City Inspection (Rough Framing) | 1 | 0% | 02-Jul-26 | 02-Jul-26 | 20 | 26-Jun-26 | 26-Jun-26 | -4 |
| EE-EAST-1020 | Electrical Rough-In | 5 | 0% | 16-Jul-26 | 22-Jul-26 | 12 | 10-Jul-26 | 16-Jul-26 | -4 |
| EE-EAST-1030 | City Inspection (Electrical) | 1 | 0% | 23-Jul-26 | 23-Jul-26 | 12 | 17-Jul-26 | 17-Jul-26 | -4 |
| EE-EAST-1040 | Install Exterior Sheathing | 5 | 0% | 24-Jul-26 | 30-Jul-26 | 12 | 20-Jul-26 | 24-Jul-26 | -4 |
| EE-EAST-1050 | City Inspection (Screw Inspection) | 1 | 0% | 31-Jul-26 | 31-Jul-26 | 12 | 27-Jul-26 | 27-Jul-26 | -4 |
| EE-EAST-1060 | Weather Barrier & Flashing | 5 | 0% | 03-Aug-26 | 07-Aug-26 | 12 | 28-Jul-26 | 03-Aug-26 | -4 |
| EE-EAST-1070 | Install Rigid Insulation | 5 | 0% | 10-Aug-26 | 14-Aug-26 | 12 | 04-Aug-26 | 10-Aug-26 | -4 |
| EE-EAST-1080 | Install Windows & Metals | 3 | 0% | 17-Aug-26 | 19-Aug-26 | 12 | 11-Aug-26 | 13-Aug-26 | -4 |
| EE-EAST-1090 | Install Brick Veneer | 15 | 0% | 03-Sep-26 | 24-Sep-26 | 2 | 28-Aug-26 | 18-Sep-26 | -4 |
| EE-EAST-1100 | Install Signage | 1 | 0% | 25-Sep-26 | 25-Sep-26 | 32 | 21-Sep-26 | 21-Sep-26 | -4 |
| EE-EAST-1110 | Punch List & Corrections | 5 | 0% | 28-Sep-26 | 02-Oct-26 | 32 | 22-Sep-26 | 28-Sep-26 | -4 |
| EE-EAST-1120 | Final Owner Walk (Punch List & Corrections) | 5 | 0% | 05-Oct-26 | 09-Oct-26 | 69 | 29-Sep-26 | 05-Oct-26 | -4 |
| **South Elevation** | | 90 | 0% | 02-Jul-26 | 06-Nov-26 | 49 | 26-Jun-26 | 02-Nov-26 | -4 |
| EE-SOTH-1000 | Layout & Exterior Framing (Level 1) | 5 | 0% | 02-Jul-26 | 09-Jul-26 | 13 | 26-Jun-26 | 02-Jul-26 | -4 |
| EE-SOTH-1010 | City Inspection (Rough Framing) | 1 | 0% | 10-Jul-26 | 10-Jul-26 | 33 | 06-Jul-26 | 06-Jul-26 | -4 |
| EE-SOTH-1020 | Electrical Rough-In | 5 | 0% | 23-Jul-26 | 29-Jul-26 | 25 | 17-Jul-26 | 23-Jul-26 | -4 |
| EE-SOTH-1030 | City Inspection (Electrical) | 1 | 0% | 30-Jul-26 | 30-Jul-26 | 25 | 24-Jul-26 | 24-Jul-26 | -4 |
| EE-SOTH-1040 | Install Exterior Sheathing | 5 | 0% | 31-Jul-26 | 06-Aug-26 | 25 | 27-Jul-26 | 31-Jul-26 | -4 |
| EE-SOTH-1050 | City Inspection (Screw Inspection) | 1 | 0% | 07-Aug-26 | 07-Aug-26 | 25 | 03-Aug-26 | 03-Aug-26 | -4 |
| EE-SOTH-1060 | Weather Barrier & Flashing | 5 | 0% | 10-Aug-26 | 14-Aug-26 | 25 | 04-Aug-26 | 10-Aug-26 | -4 |
| EE-SOTH-1070 | Install Rigid Insulation | 5 | 0% | 17-Aug-26 | 21-Aug-26 | 25 | 11-Aug-26 | 17-Aug-26 | -4 |
| EE-SOTH-1080 | Install Brick Veneer | 15 | 0% | 25-Sep-26 | 15-Oct-26 | 2 | 21-Sep-26 | 09-Oct-26 | -4 |
| EE-SOTH-1090 | Install Signage | 1 | 0% | 16-Oct-26 | 16-Oct-26 | 12 | 12-Oct-26 | 12-Oct-26 | -4 |
| EE-SOTH-1100 | Install Doors & Hardware | 1 | 0% | 19-Oct-26 | 19-Oct-26 | 12 | 13-Oct-26 | 13-Oct-26 | -4 |
| EE-SOTH-1110 | Install Downspouts | 2 | 0% | 20-Oct-26 | 21-Oct-26 | 12 | 14-Oct-26 | 15-Oct-26 | -4 |
| EE-SOTH-1120 | Final Paint | 2 | 0% | 22-Oct-26 | 23-Oct-26 | 12 | 16-Oct-26 | 19-Oct-26 | -4 |
| EE-SOTH-1130 | Punch List & Corrections | 5 | 0% | 26-Oct-26 | 30-Oct-26 | 12 | 20-Oct-26 | 26-Oct-26 | -4 |
| EE-SOTH-1140 | Final Owner Walk (Punch List & Corrections) | 5 | 0% | 02-Nov-26 | 06-Nov-26 | 49 | 27-Oct-26 | 02-Nov-26 | -4 |
| **West Elevation** | | 93 | 0% | 10-Jul-26 | 18-Nov-26 | 41 | 06-Jul-26 | 12-Nov-26 | -4 |
| EE-WEST-1000 | Layout & Exterior Framing (Level 1) | 5 | 0% | 10-Jul-26 | 16-Jul-26 | 13 | 06-Jul-26 | 10-Jul-26 | -4 |
| EE-WEST-1010 | City Inspection (Rough Framing) | 1 | 0% | 17-Jul-26 | 17-Jul-26 | 40 | 13-Jul-26 | 13-Jul-26 | -4 |
| EE-WEST-1020 | Electrical Rough-In | 5 | 0% | 30-Jul-26 | 05-Aug-26 | 32 | 24-Jul-26 | 30-Jul-26 | -4 |
| EE-WEST-1030 | City Inspection (Electrical) | 1 | 0% | 06-Aug-26 | 06-Aug-26 | 32 | 31-Jul-26 | 31-Jul-26 | -4 |
| EE-WEST-1040 | Install Exterior Sheathing | 5 | 0% | 07-Aug-26 | 13-Aug-26 | 32 | 03-Aug-26 | 07-Aug-26 | -4 |
| EE-WEST-1050 | City Inspection (Screw Inspection) | 1 | 0% | 14-Aug-26 | 14-Aug-26 | 32 | 10-Aug-26 | 10-Aug-26 | -4 |
| EE-WEST-1060 | Weather Barrier & Flashing | 5 | 0% | 17-Aug-26 | 21-Aug-26 | 32 | 11-Aug-26 | 17-Aug-26 | -4 |
| EE-WEST-1070 | Install Rigid Insulation | 5 | 0% | 24-Aug-26 | 28-Aug-26 | 32 | 18-Aug-26 | 24-Aug-26 | -4 |
| EE-WEST-1080 | Install Windows & Metals | 3 | 0% | 31-Aug-26 | 02-Sep-26 | 32 | 25-Aug-26 | 27-Aug-26 | -4 |

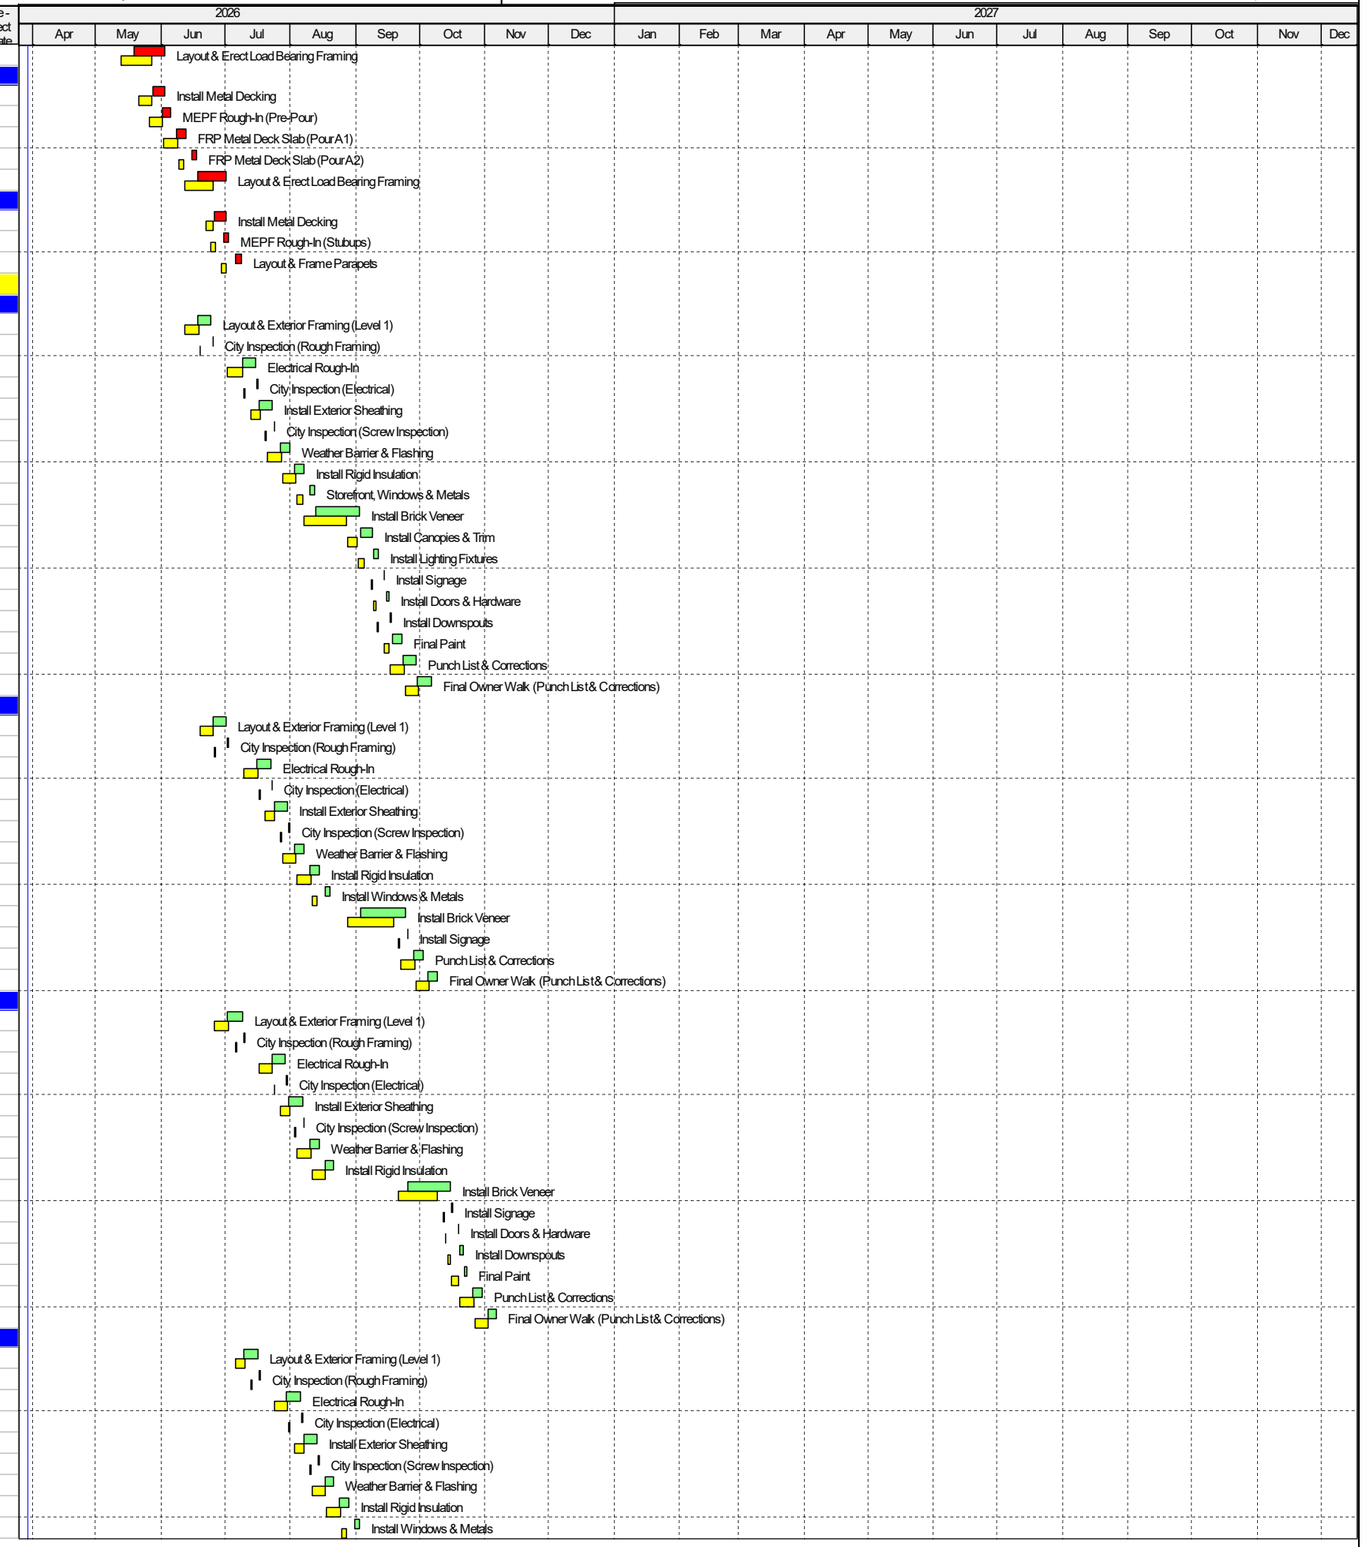


Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone



TASK filter: Remaining .

© Oracle Corporation

| Activity ID | Activity Name | Remaining Duration | Schedule % Complete | Start | Finish | Total Float | BL Project Start | BL Project Finish | Variance - BL Project Finish Date |
|---|---|---|---|---|---|---|---|---|---|
| EE-WEST-1090 | Install Brick Veneer | 15 | 0% | 16-Oct-26 | 05-Nov-26 | 2 | 12-Oct-26 | 30-Oct-26 | -4 |
| EE-WEST-1100 | Install Signage | 1 | 0% | 06-Nov-26 | 06-Nov-26 | 2 | 02-Nov-26 | 02-Nov-26 | -4 |
| EE-WEST-1110 | Punch List & Corrections | 5 | 0% | 09-Nov-26 | 13-Nov-26 | 2 | 03-Nov-26 | 09-Nov-26 | -4 |
| EE-WEST-1120 | Final Owner Walk (Punch List & Corrections) | 3 | 0% | 16-Nov-26 | 18-Nov-26 | 41 | 10-Nov-26 | 12-Nov-26 | -4 |
| **Roof** | | 80 | 0% | 09-Jul-26 | 29-Oct-26 | 13 | 02-Jul-26 | 23-Oct-26 | -4 |
| EE-ROOF-1000 | Clean & Prep Metal Deck | 2 | 0% | 09-Jul-26 | 10-Jul-26 | 0 | 02-Jul-26 | 06-Jul-26 | -4 |
| EE-ROOF-1010 | Stage Materials & Solar Rails (Crane) | 2 | 0% | 13-Jul-26 | 14-Jul-26 | 0 | 07-Jul-26 | 08-Jul-26 | -4 |
| EE-ROOF-1020 | Layout for Penetrations, Curb Blocking, Edge Metal | 2 | 0% | 15-Jul-26 | 16-Jul-26 | 0 | 09-Jul-26 | 10-Jul-26 | -4 |
| EE-ROOF-1030 | Install Blocking & Equipment Curbs | 3 | 0% | 17-Jul-26 | 21-Jul-26 | 0 | 13-Jul-26 | 15-Jul-26 | -4 |
| EE-ROOF-1040 | Install Rigid Insulation | 4 | 0% | 22-Jul-26 | 27-Jul-26 | 0 | 16-Jul-26 | 21-Jul-26 | -4 |
| EE-ROOF-1050 | Install Cover Board | 4 | 0% | 28-Jul-26 | 31-Jul-26 | 0 | 22-Jul-26 | 27-Jul-26 | -4 |
| EE-ROOF-1060 | Install TPO Roofing System (incl. boots, termination bars) | 10 | 0% | 03-Aug-26 | 14-Aug-26 | 0 | 28-Jul-26 | 10-Aug-26 | -4 |
| EE-ROOF-1070 | Install Edge Metal, Coping, Trim | 5 | 0% | 17-Aug-26 | 21-Aug-26 | 13 | 11-Aug-26 | 17-Aug-26 | -4 |
| EE-ROOF-1080 | Install Roof Drains, Vents, Mechanical Curbs | 5 | 0% | 24-Aug-26 | 28-Aug-26 | 13 | 18-Aug-26 | 24-Aug-26 | -4 |
| EE-ROOF-1140 | Set Rooftop Units (RTU's & Splits) | 1 | 0% | 31-Aug-26 | 31-Aug-26 | 34 | 25-Aug-26 | 25-Aug-26 | -4 |
| EE-ROOF-1150 | Install Duct/Condensate/Vent Tie-Ins & Flashing | 3 | 0% | 01-Sep-26 | 03-Sep-26 | 34 | 26-Aug-26 | 28-Aug-26 | -4 |
| EE-ROOF-1090 | Install Electrical Conduit & Roof Mounted Boxes | 5 | 0% | 31-Aug-26 | 04-Sep-26 | 13 | 25-Aug-26 | 31-Aug-26 | -4 |
| EE-ROOF-1160 | Startup/Controls/Balancing Prep | 3 | 0% | 04-Sep-26 | 09-Sep-26 | 34 | 31-Aug-26 | 02-Sep-26 | -4 |
| EE-ROOF-1100 | Install Solar Mounting Rails & Racking | 3 | 0% | 08-Sep-26 | 10-Sep-26 | 13 | 01-Sep-26 | 03-Sep-26 | -4 |
| EE-ROOF-1170 | Water Test / Leak Test | 1 | 0% | 10-Sep-26 | 10-Sep-26 | 34 | 03-Sep-26 | 03-Sep-26 | -4 |
| EE-ROOF-1180 | Roof Patches (If Any) | 1 | 0% | 11-Sep-26 | 11-Sep-26 | 34 | 04-Sep-26 | 04-Sep-26 | -4 |
| EE-ROOF-1190 | Punch List & Corrections | 3 | 0% | 14-Sep-26 | 16-Sep-26 | 34 | 08-Sep-26 | 10-Sep-26 | -4 |
| EE-ROOF-1110 | Mount Solar Panels | 15 | 0% | 11-Sep-26 | 01-Oct-26 | 13 | 04-Sep-26 | 25-Sep-26 | -4 |
| EE-ROOF-1120 | Run Electrical Conduit & Inverters to Roof | 5 | 0% | 02-Oct-26 | 08-Oct-26 | 13 | 28-Sep-26 | 02-Oct-26 | -4 |
| EE-ROOF-1130 | Final Electrical Tie-In (Solar Panels) | 5 | 0% | 09-Oct-26 | 15-Oct-26 | 13 | 05-Oct-26 | 09-Oct-26 | -4 |
| EE-ROOF-1200 | Final Owner Walk (Punch List & Corrections) | 10 | 0% | 16-Oct-26 | 29-Oct-26 | 13 | 12-Oct-26 | 23-Oct-26 | -4 |
| **Interior Build-Out** | | 159 | 0% | 09-Apr-26 | 17-Nov-26 | 49 | 03-Mar-26 | 11-Nov-26 | -4 |
| **Level 2 Interior** | | 67 | 0% | 02-Jul-26 | 02-Oct-26 | 81 | 26-Jun-26 | 28-Sep-26 | -4 |
| IB-L2IN-1000 | Layout & Framing (incl. backing, door frames) | 5 | 0% | 02-Jul-26 | 09-Jul-26 | 21 | 26-Jun-26 | 02-Jul-26 | -4 |
| IB-L2IN-1010 | Electrical Rough-In | 5 | 0% | 10-Jul-26 | 16-Jul-26 | 21 | 06-Jul-26 | 10-Jul-26 | -4 |
| IB-L2IN-1020 | Mechanical Rough-In | 5 | 0% | 10-Jul-26 | 16-Jul-26 | 21 | 06-Jul-26 | 10-Jul-26 | -4 |
| IB-L2IN-1030 | Plumbing Rough-In | 5 | 0% | 10-Jul-26 | 16-Jul-26 | 21 | 06-Jul-26 | 10-Jul-26 | -4 |
| IB-L2IN-1040 | Fire Supression Rough-In | 5 | 0% | 10-Jul-26 | 16-Jul-26 | 21 | 06-Jul-26 | 10-Jul-26 | -4 |
| IB-L2IN-1050 | Install Insulation | 2 | 0% | 17-Aug-26 | 18-Aug-26 | 0 | 11-Aug-26 | 12-Aug-26 | -4 |
| IB-L2IN-1060 | Install Drywall | 4 | 0% | 19-Aug-26 | 24-Aug-26 | 0 | 13-Aug-26 | 18-Aug-26 | -4 |
| IB-L2IN-1070 | Tape & Mud Drywall | 5 | 0% | 25-Aug-26 | 31-Aug-26 | 37 | 19-Aug-26 | 25-Aug-26 | -4 |
| IB-L2IN-1080 | Prep & Paint | 3 | 0% | 01-Sep-26 | 03-Sep-26 | 37 | 26-Aug-26 | 28-Aug-26 | -4 |
| IB-L2IN-1090 | MEPF Trim-Out | 5 | 0% | 04-Sep-26 | 11-Sep-26 | 37 | 31-Aug-26 | 04-Sep-26 | -4 |
| IB-L2IN-1100 | Install Storage Doors & Hardware | 5 | 0% | 14-Sep-26 | 18-Sep-26 | 37 | 08-Sep-26 | 14-Sep-26 | -4 |
| IB-L2IN-1110 | Final Clean and Punchlist | 5 | 0% | 21-Sep-26 | 25-Sep-26 | 37 | 15-Sep-26 | 21-Sep-26 | -4 |
| IB-L2IN-1120 | Punchlist Completion and Signoff | 5 | 0% | 28-Sep-26 | 02-Oct-26 | 81 | 22-Sep-26 | 28-Sep-26 | -4 |
| **Level 3 Interior** | | 58 | 0% | 10-Jul-26 | 29-Sep-26 | 84 | 06-Jul-26 | 23-Sep-26 | -4 |
| IB-L3IN-1000 | Layout & Framing (incl. backing, door frames) | 5 | 0% | 10-Jul-26 | 16-Jul-26 | 36 | 06-Jul-26 | 10-Jul-26 | -4 |
| IB-L3IN-1010 | Electrical Rough-In | 5 | 0% | 17-Jul-26 | 23-Jul-26 | 56 | 13-Jul-26 | 17-Jul-26 | -4 |
| IB-L3IN-1020 | Mechanical Rough-In | 5 | 0% | 17-Jul-26 | 23-Jul-26 | 56 | 13-Jul-26 | 17-Jul-26 | -4 |
| IB-L3IN-1030 | Plumbing Rough-In | 5 | 0% | 17-Jul-26 | 23-Jul-26 | 56 | 13-Jul-26 | 17-Jul-26 | -4 |
| IB-L3IN-1040 | Fire Supression Rough-In | 5 | 0% | 17-Jul-26 | 23-Jul-26 | 56 | 13-Jul-26 | 17-Jul-26 | -4 |
| IB-L3IN-1050 | Install Insulation | 2 | 0% | 17-Aug-26 | 18-Aug-26 | 40 | 11-Aug-26 | 12-Aug-26 | -4 |
| IB-L3IN-1060 | Install Drywall | 4 | 0% | 19-Aug-26 | 24-Aug-26 | 40 | 13-Aug-26 | 18-Aug-26 | -4 |
| IB-L3IN-1070 | Tape & Mud Drywall | 5 | 0% | 25-Aug-26 | 31-Aug-26 | 40 | 19-Aug-26 | 25-Aug-26 | -4 |
| IB-L3IN-1080 | Prep & Paint | 3 | 0% | 01-Sep-26 | 03-Sep-26 | 40 | 26-Aug-26 | 28-Aug-26 | -4 |
| IB-L3IN-1090 | MEPF Trim-Out | 5 | 0% | 04-Sep-26 | 11-Sep-26 | 40 | 31-Aug-26 | 04-Sep-26 | -4 |
| IB-L3IN-1100 | Install Storage Doors & Hardware | 5 | 0% | 14-Sep-26 | 18-Sep-26 | 40 | 08-Sep-26 | 14-Sep-26 | -4 |
| IB-L3IN-1110 | Final Clean and Punchlist | 2 | 0% | 21-Sep-26 | 22-Sep-26 | 40 | 15-Sep-26 | 16-Sep-26 | -4 |
| IB-L3IN-1120 | Punchlist Completion and Signoff | 5 | 0% | 23-Sep-26 | 29-Sep-26 | 84 | 17-Sep-26 | 23-Sep-26 | -4 |
| **Unisex Restroom** | | 28 | 0% | 17-Jul-26 | 25-Aug-26 | 109 | 13-Jul-26 | 19-Aug-26 | -4 |
| IB-L3UN-1000 | Framing (Metal Studs, Blocking) | 3 | 0% | 17-Jul-26 | 21-Jul-26 | 43 | 13-Jul-26 | 15-Jul-26 | -4 |
| IB-L3UN-1010 | MEPF Rough-In | 3 | 0% | 22-Jul-26 | 24-Jul-26 | 56 | 16-Jul-26 | 20-Jul-26 | -4 |
| IB-L3UN-1020 | City Inspection (Framing & MEPF Rough) | 1 | 0% | 27-Jul-26 | 27-Jul-26 | 57 | 21-Jul-26 | 21-Jul-26 | -4 |
| IB-L3UN-1030 | Install Insulation | 1 | 0% | 28-Jul-26 | 28-Jul-26 | 57 | 22-Jul-26 | 22-Jul-26 | -4 |
| IB-L3UN-1040 | Install Drywall | 2 | 0% | 29-Jul-26 | 30-Jul-26 | 57 | 23-Jul-26 | 24-Jul-26 | -4 |
| IB-L3UN-1050 | Tape & Mud Drywall | 3 | 0% | 31-Jul-26 | 04-Aug-26 | 64 | 27-Jul-26 | 29-Jul-26 | -4 |
| IB-L3UN-1060 | Painting | 2 | 0% | 05-Aug-26 | 06-Aug-26 | 64 | 30-Jul-26 | 31-Jul-26 | -4 |
| IB-L3UN-1070 | Install Restroom Fixtures & Partitions | 2 | 0% | 07-Aug-26 | 10-Aug-26 | 64 | 03-Aug-26 | 04-Aug-26 | -4 |
| IB-L3UN-1080 | Install Accessories (Grab Bars, Mirrors, Signs) | 2 | 0% | 11-Aug-26 | 12-Aug-26 | 64 | 05-Aug-26 | 06-Aug-26 | -4 |
| IB-L3UN-1090 | Final MEP Trim-Out | 2 | 0% | 13-Aug-26 | 14-Aug-26 | 64 | 07-Aug-26 | 10-Aug-26 | -4 |
| IB-L3UN-1100 | Final Clean and Punchlist | 2 | 0% | 17-Aug-26 | 18-Aug-26 | 64 | 11-Aug-26 | 12-Aug-26 | -4 |
| IB-L3UN-1110 | Punchlist Completion and Signoff | 5 | 0% | 19-Aug-26 | 25-Aug-26 | 109 | 13-Aug-26 | 19-Aug-26 | -4 |
| **Level 4 Interior** | | 53 | 0% | 17-Jul-26 | 29-Sep-26 | 84 | 13-Jul-26 | 23-Sep-26 | -4 |
| IB-L4IN-1000 | Layout & Framing (incl. backing, door frames) | 5 | 0% | 17-Jul-26 | 23-Jul-26 | 36 | 13-Jul-26 | 17-Jul-26 | -4 |
| IB-L4IN-1010 | Electrical Rough-In | 5 | 0% | 24-Jul-26 | 30-Jul-26 | 43 | 20-Jul-26 | 24-Jul-26 | -4 |

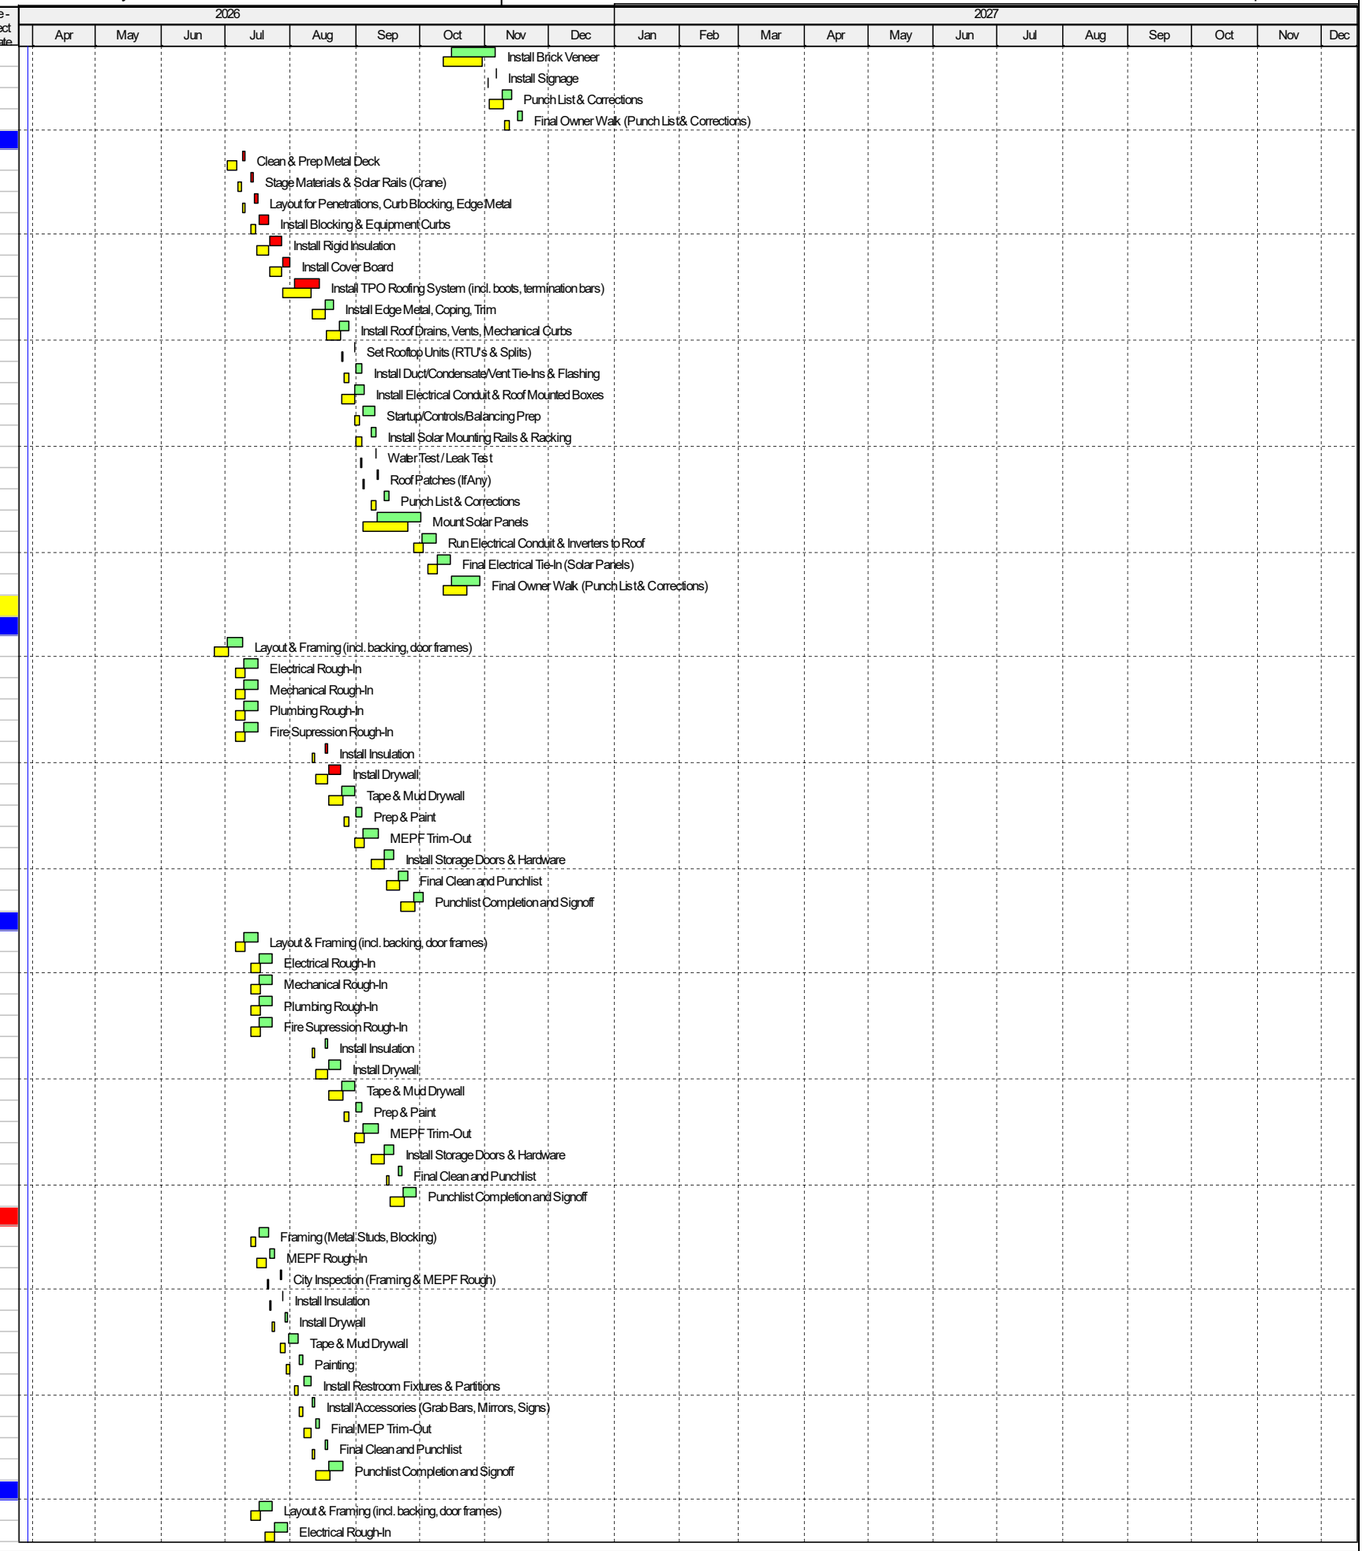


Project Baseline Bar | Remaining Work | ◇ Baseline Milestone
Actual Work | Critical Remaining Work | ◆ Milestone



TASK filter: Remaining .

© Oracle Corporation

| Activity ID | Activity Name | Remaining Duration | Schedule % Complete | Start | Finish | Total Float | BL Project Start | BL Project Finish | Variance - BL Project Finish Date |
|---|---|---|---|---|---|---|---|---|---|
| IB-L4IN-1020 | Mechanical Rough-In | 5 | 0% | 24-Jul-26 | 30-Jul-26 | 43 | 20-Jul-26 | 24-Jul-26 | -4 |
| IB-L4IN-1030 | Plumbing Rough-In | 5 | 0% | 24-Jul-26 | 30-Jul-26 | 43 | 20-Jul-26 | 24-Jul-26 | -4 |
| IB-L4IN-1040 | Fire Supression Rough-In | 5 | 0% | 24-Jul-26 | 30-Jul-26 | 43 | 20-Jul-26 | 24-Jul-26 | -4 |
| IB-L4IN-1050 | Install Insulation | 2 | 0% | 17-Aug-26 | 18-Aug-26 | 32 | 11-Aug-26 | 12-Aug-26 | -4 |
| IB-L4IN-1060 | Install Drywall | 4 | 0% | 19-Aug-26 | 24-Aug-26 | 32 | 13-Aug-26 | 18-Aug-26 | -4 |
| IB-L4IN-1070 | Tape & Mud Drywall | 5 | 0% | 25-Aug-26 | 31-Aug-26 | 32 | 19-Aug-26 | 25-Aug-26 | -4 |
| IB-L4IN-1080 | Prep & Paint | 3 | 0% | 01-Sep-26 | 03-Sep-26 | 32 | 26-Aug-26 | 28-Aug-26 | -4 |
| IB-L4IN-1090 | MEPF Trim-Out | 5 | 0% | 04-Sep-26 | 11-Sep-26 | 32 | 31-Aug-26 | 04-Sep-26 | -4 |
| IB-L4IN-1100 | Install Storage Doors & Hardware | 5 | 0% | 14-Sep-26 | 18-Sep-26 | 40 | 08-Sep-26 | 14-Sep-26 | -4 |
| IB-L4IN-1110 | Final Clean and Punchlist | 2 | 0% | 21-Sep-26 | 22-Sep-26 | 40 | 15-Sep-26 | 16-Sep-26 | -4 |
| IB-L4IN-1120 | Punchlist Completion and Signoff | 5 | 0% | 23-Sep-26 | 29-Sep-26 | 84 | 17-Sep-26 | 23-Sep-26 | -4 |
| **Level 1 Interior** | | **44** | **0%** | **17-Aug-26** | **15-Oct-26** | **72** | **11-Aug-26** | **09-Oct-26** | **-4** |
| IB-L1IN-1000 | Layout & Framing (incl. backing, door frames) | 5 | 0% | 17-Aug-26 | 21-Aug-26 | 20 | 11-Aug-26 | 17-Aug-26 | -4 |
| IB-L1IN-1010 | Electrical Rough-In | 5 | 0% | 24-Aug-26 | 28-Aug-26 | 30 | 18-Aug-26 | 24-Aug-26 | -4 |
| IB-L1IN-1020 | Mechanical Rough-In | 5 | 0% | 24-Aug-26 | 28-Aug-26 | 30 | 18-Aug-26 | 24-Aug-26 | -4 |
| IB-L1IN-1030 | Plumbing Rough-In | 5 | 0% | 24-Aug-26 | 28-Aug-26 | 30 | 18-Aug-26 | 24-Aug-26 | -4 |
| IB-L1IN-1040 | Fire Supression Rough-In | 5 | 0% | 24-Aug-26 | 28-Aug-26 | 30 | 18-Aug-26 | 24-Aug-26 | -4 |
| IB-L1IN-1050 | Install Insulation | 2 | 0% | 31-Aug-26 | 01-Sep-26 | 30 | 25-Aug-26 | 26-Aug-26 | -4 |
| IB-L1IN-1060 | Install Drywall | 4 | 0% | 02-Sep-26 | 08-Sep-26 | 30 | 27-Aug-26 | 01-Sep-26 | -4 |
| IB-L1IN-1070 | Tape & Mud Drywall | 5 | 0% | 09-Sep-26 | 15-Sep-26 | 30 | 02-Sep-26 | 09-Sep-26 | -4 |
| IB-L1IN-1080 | Prep & Paint | 3 | 0% | 16-Sep-26 | 18-Sep-26 | 30 | 10-Sep-26 | 14-Sep-26 | -4 |
| IB-L1IN-1090 | MEPF Trim-Out | 5 | 0% | 21-Sep-26 | 25-Sep-26 | 30 | 15-Sep-26 | 21-Sep-26 | -4 |
| IB-L1IN-1100 | Install Storage Doors & Hardware | 5 | 0% | 28-Sep-26 | 02-Oct-26 | 30 | 22-Sep-26 | 28-Sep-26 | -4 |
| IB-L1IN-1110 | Final Clean and Punchlist | 2 | 0% | 05-Oct-26 | 06-Oct-26 | 30 | 29-Sep-26 | 30-Sep-26 | -4 |
| IB-L1IN-1120 | Punchlist Completion and Signoff | 5 | 0% | 07-Oct-26 | 13-Oct-26 | 74 | 01-Oct-26 | 07-Oct-26 | -4 |
| **Restrooms (Mens & Womens)** | | **29** | **0%** | **24-Aug-26** | **01-Oct-26** | **33** | **18-Aug-26** | **25-Sep-26** | **-4** |
| IB-L1RR-1000 | Framing (Metal Studs, Blocking) | 3 | 0% | 24-Aug-26 | 26-Aug-26 | 20 | 18-Aug-26 | 20-Aug-26 | -4 |
| IB-L1RR-1010 | MEPF Rough-In | 3 | 0% | 27-Aug-26 | 31-Aug-26 | 33 | 21-Aug-26 | 25-Aug-26 | -4 |
| IB-L1RR-1020 | City Inspection (Framing & MEPF Rough) | 1 | 0% | 01-Sep-26 | 01-Sep-26 | 33 | 26-Aug-26 | 26-Aug-26 | -4 |
| IB-L1RR-1030 | Install Insulation | 1 | 0% | 02-Sep-26 | 02-Sep-26 | 33 | 27-Aug-26 | 27-Aug-26 | -4 |
| IB-L1RR-1040 | Install Drywall | 2 | 0% | 03-Sep-26 | 04-Sep-26 | 33 | 28-Aug-26 | 31-Aug-26 | -4 |
| IB-L1RR-1050 | Tape & Mud Drywall | 3 | 0% | 08-Sep-26 | 10-Sep-26 | 33 | 01-Sep-26 | 03-Sep-26 | -4 |
| IB-L1RR-1060 | Painting | 2 | 0% | 11-Sep-26 | 14-Sep-26 | 33 | 04-Sep-26 | 08-Sep-26 | -4 |
| IB-L1RR-1070 | Install Restroom Fixtures & Partitions | 2 | 0% | 15-Sep-26 | 16-Sep-26 | 33 | 09-Sep-26 | 10-Sep-26 | -4 |
| IB-L1RR-1080 | Install Accessories (Grab Bars, Mirrors, Signs) | 2 | 0% | 17-Sep-26 | 18-Sep-26 | 33 | 11-Sep-26 | 14-Sep-26 | -4 |
| IB-L1RR-1090 | Final MEP Trim-Out | 2 | 0% | 21-Sep-26 | 22-Sep-26 | 33 | 15-Sep-26 | 16-Sep-26 | -4 |
| IB-L1RR-1100 | Final Clean and Punclist | 2 | 0% | 23-Sep-26 | 24-Sep-26 | 33 | 17-Sep-26 | 18-Sep-26 | -4 |
| IB-L1RR-1110 | Punchlist Completion and Signoff | 5 | 0% | 25-Sep-26 | 01-Oct-26 | 33 | 21-Sep-26 | 25-Sep-26 | -4 |
| **Management Spaces (Rental Office, Storage, Break Room)** | | **36** | **0%** | **27-Aug-26** | **15-Oct-26** | **23** | **21-Aug-26** | **09-Oct-26** | **-4** |
| IB-L1M\S-1000 | Layout & Framing (incl. backing, door frames) | 3 | 0% | 27-Aug-26 | 31-Aug-26 | 20 | 21-Aug-26 | 25-Aug-26 | -4 |
| IB-L1M\S-1010 | MEPF Rough-In | 3 | 0% | 01-Sep-26 | 03-Sep-26 | 23 | 26-Aug-26 | 28-Aug-26 | -4 |
| IB-L1M\S-1020 | City Inspection (Framing & MEPF) | 1 | 0% | 04-Sep-26 | 04-Sep-26 | 23 | 31-Aug-26 | 31-Aug-26 | -4 |
| IB-L1M\S-1030 | Install Insulation | 2 | 0% | 08-Sep-26 | 09-Sep-26 | 23 | 01-Sep-26 | 02-Sep-26 | -4 |
| IB-L1M\S-1040 | Install Drywall | 2 | 0% | 10-Sep-26 | 11-Sep-26 | 23 | 03-Sep-26 | 04-Sep-26 | -4 |
| IB-L1M\S-1050 | Tape & Mud Drywall | 3 | 0% | 14-Sep-26 | 16-Sep-26 | 23 | 08-Sep-26 | 10-Sep-26 | -4 |
| IB-L1M\S-1060 | Painting | 3 | 0% | 17-Sep-26 | 21-Sep-26 | 23 | 11-Sep-26 | 15-Sep-26 | -4 |
| IB-L1M\S-1070 | Install Ceiling Grid (Break Room) | 1 | 0% | 22-Sep-26 | 22-Sep-26 | 23 | 16-Sep-26 | 16-Sep-26 | -4 |
| IB-L1M\S-1080 | Install Base Trim | 1 | 0% | 23-Sep-26 | 23-Sep-26 | 23 | 17-Sep-26 | 17-Sep-26 | -4 |
| IB-L1M\S-1090 | Install Cabinets & Countertops (Break Room & Office) | 3 | 0% | 24-Sep-26 | 28-Sep-26 | 23 | 18-Sep-26 | 22-Sep-26 | -4 |
| IB-L1M\S-1100 | Install Sink & Faucests (Break Room) | 1 | 0% | 29-Sep-26 | 29-Sep-26 | 23 | 23-Sep-26 | 23-Sep-26 | -4 |
| IB-L1M\S-1110 | Appliances (Microwave & Fridge) | 1 | 0% | 30-Sep-26 | 30-Sep-26 | 23 | 24-Sep-26 | 24-Sep-26 | -4 |
| IB-L1M\S-1120 | Interior Signage | 1 | 0% | 01-Oct-26 | 01-Oct-26 | 23 | 25-Sep-26 | 25-Sep-26 | -4 |
| IB-L1M\S-1130 | MEPF Trim-Out | 3 | 0% | 02-Oct-26 | 06-Oct-26 | 23 | 28-Sep-26 | 30-Sep-26 | -4 |
| IB-L1M\S-1140 | Final Clean and Punchlist | 2 | 0% | 07-Oct-26 | 08-Oct-26 | 23 | 01-Oct-26 | 02-Oct-26 | -4 |
| IB-L1M\S-1150 | Punchlist Completion and Signoff | 5 | 0% | 09-Oct-26 | 15-Oct-26 | 23 | 05-Oct-26 | 09-Oct-26 | -4 |
| **Janus Scope** | | **60** | **0%** | **25-Aug-26** | **17-Nov-26** | **0** | **19-Aug-26** | **11-Nov-26** | **-4** |
| IB-JNUS-1000 | Level 2 Install (Diamond Plate, Turkey Wire, Misc.) | 15 | 0% | 25-Aug-26 | 15-Sep-26 | 0 | 19-Aug-26 | 09-Sep-26 | -4 |
| IB-JNUS-1010 | Level 3 Install (Diamond Plate, Turkey Wire, Misc.) | 15 | 0% | 16-Sep-26 | 06-Oct-26 | 0 | 10-Sep-26 | 30-Sep-26 | -4 |
| IB-JNUS-1020 | Level 4 Install (Diamond Plate, Turkey Wire, Misc.) | 15 | 0% | 07-Oct-26 | 27-Oct-26 | 0 | 01-Oct-26 | 21-Oct-26 | -4 |
| IB-JNUS-1030 | Level 1 Install (Diamond Plate, Turkey Wire, Misc.) | 15 | 0% | 28-Oct-26 | 17-Nov-26 | 0 | 22-Oct-26 | 11-Nov-26 | -4 |
| **Elevator Installation** | | **35** | **0%** | **01-Sep-26** | **20-Oct-26** | **20** | **26-Aug-26** | **14-Oct-26** | **-4** |
| EL-INST-1000 | Evelvator Installation (incl. Equipment Room Buildout) | 35 | 0% | 01-Sep-26 | 20-Oct-26 | 20 | 26-Aug-26 | 14-Oct-26 | -4 |
| **Stairwells** | | **46** | **0%** | **09-Apr-26** | **11-Jun-26** | **162** | **03-Mar-26** | **05-May-26** | **-27** |
| IB-STAR-1000 | Install Stairs & Railings | 20 | 95% | 09-Apr-26 | 06-May-26 | 60 | 03-Mar-26 | 30-Mar-26 | -27 |
| IB-STAR-1010 | Install Signage & Lighting | 7 | 0% | 07-May-26 | 15-May-26 | 115 | 31-Mar-26 | 08-Apr-26 | -27 |
| IB-STAR-1020 | Install Doors & Hardware | 4 | 0% | 18-May-26 | 21-May-26 | 115 | 09-Apr-26 | 14-Apr-26 | -27 |
| IB-STAR-1030 | Paint Stairs and Railings | 5 | 0% | 22-May-26 | 28-May-26 | 118 | 15-Apr-26 | 21-Apr-26 | -27 |
| IB-STAR-1040 | Clean Stairwells and Punchlist | 5 | 0% | 29-May-26 | 04-Jun-26 | 118 | 22-Apr-26 | 28-Apr-26 | -27 |
| IB-STAR-1050 | Punchlist and Signoff on Stairwells | 5 | 0% | 05-Jun-26 | 11-Jun-26 | 162 | 29-Apr-26 | 05-May-26 | -27 |
| **Outside Primary Footprint** | | **81** | **0%** | **17-Jul-26** | **09-Nov-26** | **48** | **13-Jul-26** | **03-Nov-26** | **-4** |
| **Sitework Finishes** | | **62** | **0%** | **17-Jul-26** | **13-Oct-26** | **67** | **13-Jul-26** | **07-Oct-26** | **-4** |

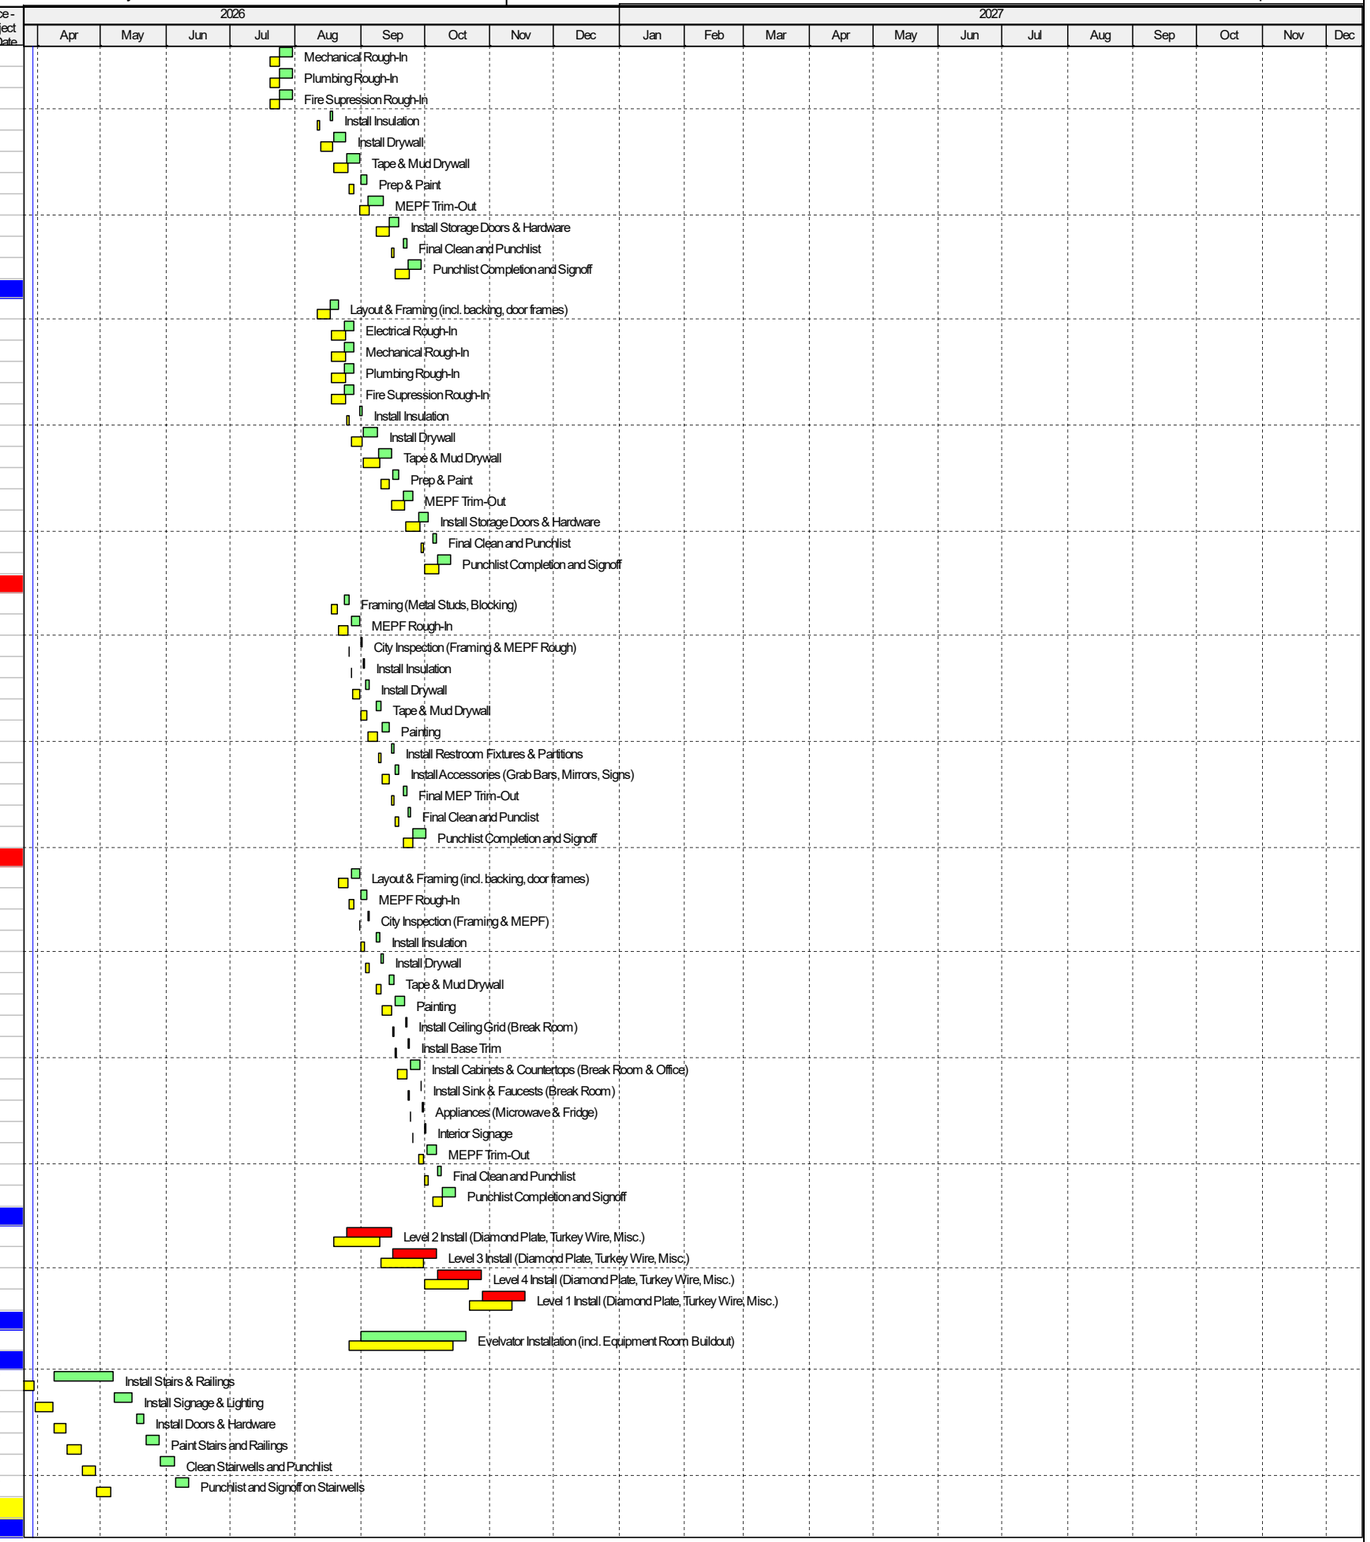


Project Baseline Bar | Remaining Work | ◇ Baseline Milestone
Actual Work | Critical Remaining Work | ◆ Milestone



TASK filter: Remaining .

© Oracle Corporation

| Activity ID | Activity Name | Remaining Duration | Schedule % Complete | Start | Finish | Total Float | BL Project Start | BL Project Finish | Variance - BL Project Finish Date |
|---|---|---|---|---|---|---|---|---|---|
| SW-FIN-1040 | Finish Grade Site (incl. bio ponds) | 5 | 0% | 17-Jul-26 | 23-Jul-26 | 13 | 13-Jul-26 | 17-Jul-26 | -4 |
| SW-FIN-1050 | Install Irrigation Sleeves (inc. bio ponds) | 2 | 0% | 24-Jul-26 | 27-Jul-26 | 13 | 20-Jul-26 | 21-Jul-26 | -4 |
| SW-FIN-1060 | Electrical Rough (Light Poles) | 5 | 0% | 28-Jul-26 | 03-Aug-26 | 13 | 22-Jul-26 | 28-Jul-26 | -4 |
| SW-FIN-1100 | Install Bollards (including footings) | 5 | 0% | 04-Aug-26 | 10-Aug-26 | 13 | 29-Jul-26 | 04-Aug-26 | -4 |
| SW-FIN-1130 | FRP Concrete (Hardscape & Sidewalks) | 7 | 0% | 11-Aug-26 | 19-Aug-26 | 13 | 05-Aug-26 | 13-Aug-26 | -4 |
| SW-FIN-1140 | Install Irrigation | 10 | 0% | 20-Aug-26 | 02-Sep-26 | 28 | 14-Aug-26 | 27-Aug-26 | -4 |
| SW-FIN-1150 | Install Asphalt (Final Coat) | 1 | 0% | 03-Sep-26 | 03-Sep-26 | 28 | 28-Aug-26 | 28-Aug-26 | -4 |
| SW-FIN-1170 | Planting | 10 | 0% | 04-Sep-26 | 18-Sep-26 | 28 | 31-Aug-26 | 14-Sep-26 | -4 |
| SW-FIN-1171 | FRP Dumpster Enclosure | 7 | 0% | 21-Sep-26 | 29-Sep-26 | 28 | 15-Sep-26 | 23-Sep-26 | -4 |
| SW-FIN-1180 | Site Furnishings & Signage | 5 | 0% | 30-Sep-26 | 06-Oct-26 | 28 | 24-Sep-26 | 30-Sep-26 | -4 |
| SW-FIN-1190 | Final Clean and Punchlist Sitework | 2 | 0% | 07-Oct-26 | 08-Oct-26 | 28 | 01-Oct-26 | 02-Oct-26 | -4 |
| SW-FIN-1200 | Punch List Completion and Signoff | 3 | 0% | 09-Oct-26 | 13-Oct-26 | 67 | 05-Oct-26 | 07-Oct-26 | -4 |
| **Rutland Drive Improvements** | | 62 | 0% | 13-Aug-26 | 09-Nov-26 | 48 | 07-Aug-26 | 03-Nov-26 | -4 |
| SW-RTLN-1000 | EPSC Install (Silt Fence, Inlet Protection) | 3 | 0% | 13-Aug-26 | 17-Aug-26 | 13 | 07-Aug-26 | 11-Aug-26 | -4 |
| SW-RTLN-1010 | Sawcut Asphalt & Demo Existing Curb | 3 | 0% | 18-Aug-26 | 20-Aug-26 | 13 | 12-Aug-26 | 14-Aug-26 | -4 |
| SW-RTLN-1020 | Temp Traffic Control Setup | 3 | 0% | 21-Aug-26 | 25-Aug-26 | 13 | 17-Aug-26 | 19-Aug-26 | -4 |
| SW-RTLN-1030 | Relocate Mailbox / Signs / Remove Conflicts | 2 | 0% | 26-Aug-26 | 27-Aug-26 | 13 | 20-Aug-26 | 21-Aug-26 | -4 |
| SW-RTLN-1040 | Trench & Install Storm Pipe | 8 | 0% | 28-Aug-26 | 09-Sep-26 | 13 | 24-Aug-26 | 02-Sep-26 | -4 |
| SW-RTLN-1050 | Set Curb Inlets, Junction Boxes, Headwalls | 6 | 0% | 10-Sep-26 | 17-Sep-26 | 13 | 03-Sep-26 | 11-Sep-26 | -4 |
| SW-RTLN-1060 | Backfill / Compact Drain Trenches | 3 | 0% | 18-Sep-26 | 22-Sep-26 | 13 | 14-Sep-26 | 16-Sep-26 | -4 |
| SW-RTLN-1070 | Subgrade Proofrool & Undercut / Backfill (if needed) | 3 | 0% | 23-Sep-26 | 25-Sep-26 | 13 | 17-Sep-26 | 21-Sep-26 | -4 |
| SW-RTLN-1080 | Place Aggregate Base | 4 | 0% | 28-Sep-26 | 01-Oct-26 | 13 | 22-Sep-26 | 25-Sep-26 | -4 |
| SW-RTLN-1090 | City Inspections (Proofrool, Storm, Curbs) | 2 | 0% | 02-Oct-26 | 05-Oct-26 | 13 | 28-Sep-26 | 29-Sep-26 | -4 |
| SW-RTLN-1100 | Install Curb & Gutter | 5 | 0% | 06-Oct-26 | 12-Oct-26 | 13 | 30-Sep-26 | 06-Oct-26 | -4 |
| SW-RTLN-1110 | Sidewalks & ADA Ramps | 4 | 0% | 13-Oct-26 | 16-Oct-26 | 13 | 07-Oct-26 | 12-Oct-26 | -4 |
| SW-RTLN-1120 | First Lift Asphalt (Binder Course) | 2 | 0% | 19-Oct-26 | 20-Oct-26 | 13 | 13-Oct-26 | 14-Oct-26 | -4 |
| SW-RTLN-1130 | Final Grading | 2 | 0% | 21-Oct-26 | 22-Oct-26 | 13 | 15-Oct-26 | 16-Oct-26 | -4 |
| SW-RTLN-1140 | Final Asphalt Surface Course | 1 | 0% | 23-Oct-26 | 23-Oct-26 | 13 | 19-Oct-26 | 19-Oct-26 | -4 |
| SW-RTLN-1150 | Permanent Signs & Striping | 2 | 0% | 26-Oct-26 | 27-Oct-26 | 13 | 20-Oct-26 | 21-Oct-26 | -4 |
| SW-RTLN-1160 | Site Cleanup & Final EPSC Removal | 2 | 0% | 28-Oct-26 | 29-Oct-26 | 13 | 22-Oct-26 | 23-Oct-26 | -4 |
| SW-RTLN-1170 | Rutland Drive Punchlist Walk | 2 | 0% | 30-Oct-26 | 02-Nov-26 | 48 | 26-Oct-26 | 27-Oct-26 | -4 |
| SW-RTLN-1180 | Rutland Drive Punchlist Completion and Signoff | 5 | 0% | 03-Nov-26 | 09-Nov-26 | 48 | 28-Oct-26 | 03-Nov-26 | -4 |
| **Closeout** | | 78 | 0% | 31-Jul-26 | 18-Nov-26 | 0 | 27-Jul-26 | 12-Nov-26 | -4 |
| **Commissioning** | | 10 | 0% | 14-Sep-26 | 25-Sep-26 | 32 | 08-Sep-26 | 21-Sep-26 | -4 |
| CO-CM-1000 | Start-Up & Testing | 10 | 0% | 14-Sep-26 | 25-Sep-26 | 32 | 08-Sep-26 | 21-Sep-26 | -4 |
| **Building Finals** | | 78 | 0% | 31-Jul-26 | 18-Nov-26 | 0 | 27-Jul-26 | 12-Nov-26 | -4 |
| CO-BF-1000 | Rough Fire Sprinkler Inspection | 1 | 0% | 31-Jul-26 | 31-Jul-26 | 71 | 27-Jul-26 | 27-Jul-26 | -4 |
| CO-BF-1010 | Final Fire Sprinkler Inspection | 1 | 0% | 28-Sep-26 | 28-Sep-26 | 32 | 22-Sep-26 | 22-Sep-26 | -4 |
| CO-BF-1020 | Electrical Final Inspection | 1 | 0% | 29-Sep-26 | 29-Sep-26 | 32 | 23-Sep-26 | 23-Sep-26 | -4 |
| CO-BF-1030 | Plumbing Final Inspection | 1 | 0% | 30-Sep-26 | 30-Sep-26 | 32 | 24-Sep-26 | 24-Sep-26 | -4 |
| CO-BF-1040 | Mechanical Final Inspection | 1 | 0% | 01-Oct-26 | 01-Oct-26 | 32 | 25-Sep-26 | 25-Sep-26 | -4 |
| CO-BF-1050 | Fire Alarm Final Inspection | 1 | 0% | 02-Oct-26 | 02-Oct-26 | 32 | 28-Sep-26 | 28-Sep-26 | -4 |
| CO-BF-1060 | Building Final Occupancy Inspection (Substantial Completion) | 1 | 0% | 18-Nov-26 | 18-Nov-26 | 0 | 12-Nov-26 | 12-Nov-26 | -4 |
| **Warranty Work** | | 240 | 0% | 08-Dec-26 | 18-Nov-27 | 0 | 02-Dec-26 | 12-Nov-27 | -4 |
| WW-WARR-1000 | 1st Quarter HVAC Maintenance | 60 | 0% | 08-Dec-26 | 08-Mar-27 | 0 | 02-Dec-26 | 02-Mar-27 | -4 |
| WW-WARR-1010 | 1st Quarter Landscape Maintenance | 60 | 0% | 08-Dec-26 | 08-Mar-27 | 0 | 02-Dec-26 | 02-Mar-27 | -4 |
| WW-WARR-1030 | 2nd Quarter HVAC Maintenance | 60 | 0% | 09-Mar-27 | 01-Jun-27 | 0 | 03-Mar-27 | 25-May-27 | -4 |
| WW-WARR-1040 | 2nd Quarter Landscape Maintenance | 60 | 0% | 09-Mar-27 | 01-Jun-27 | 0 | 03-Mar-27 | 25-May-27 | -4 |
| WW-WARR-1050 | 3rd Quarter HVAC Maintenance | 60 | 0% | 02-Jun-27 | 25-Aug-27 | 0 | 26-May-27 | 19-Aug-27 | -4 |
| WW-WARR-1060 | 3rd Quarter Landscape Maintenance | 60 | 0% | 02-Jun-27 | 25-Aug-27 | 0 | 26-May-27 | 19-Aug-27 | -4 |
| WW-WARR-1020 | 11-Month Warranty Walk | 5 | 0% | 07-Oct-27 | 13-Oct-27 | 26 | 01-Oct-27 | 07-Oct-27 | -4 |
| WW-WARR-1070 | 4th Quarter HVAC Maintenance | 60 | 0% | 26-Aug-27 | 18-Nov-27 | 0 | 20-Aug-27 | 12-Nov-27 | -4 |
| WW-WARR-1080 | 4th Quarter Landscape Maintenance | 60 | 0% | 26-Aug-27 | 18-Nov-27 | 0 | 20-Aug-27 | 12-Nov-27 | -4 |
| **Weather Impacts & Delays** | | 0 | 0% | | | 0 | | | |

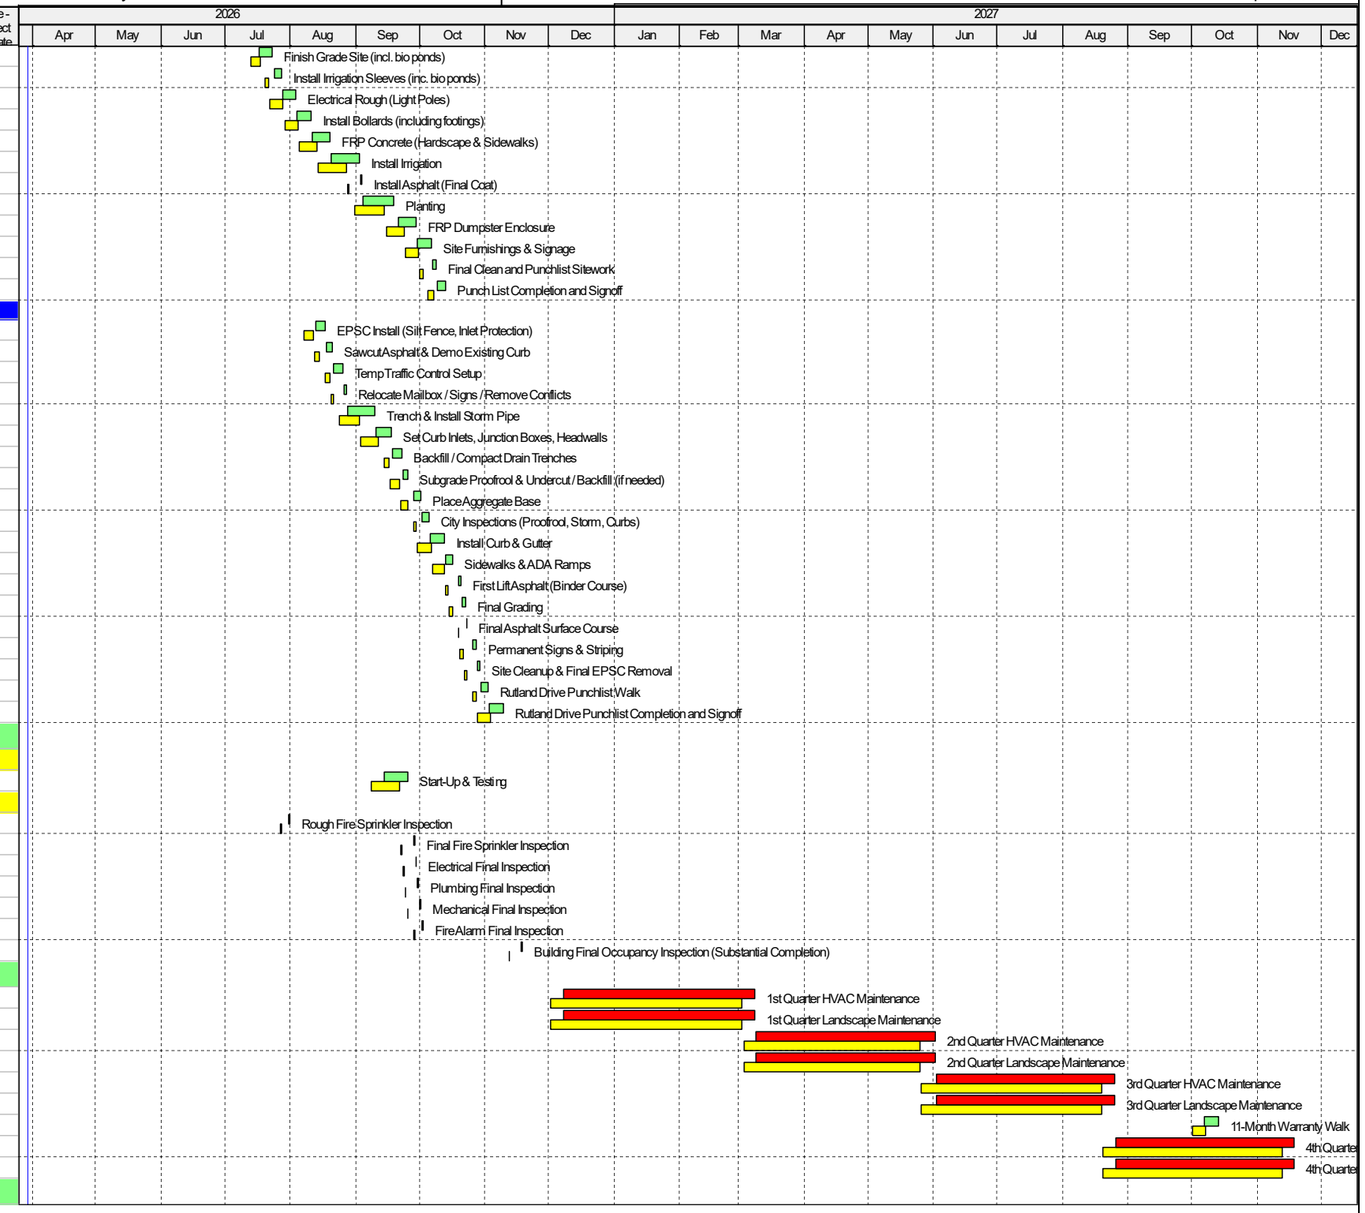


Project Baseline Bar | Remaining Work | ◇ Baseline Milestone
Actual Work | Critical Remaining Work | ◆ Milestone



TASK filter: Remaining .

© Oracle Corporation
