	Name	Duration: Current	Duration: Previous	Durati Diff	Contract Start: Current	Contract Start: Previous	Contrac Start: Diff	Contract Finish: Current	Contract Finish: Previous
1	**Overall Project Duration Public Storage - Aventura**	**443 days**	**428 days**	**15d**	**Wed 10/30/24**	**Wed 10/30/24**	**Equal**	**6/17/2026**	**6/17/2026**
6	**SUBMITTALS**	**342 days**	**328 days**	**14d**	**Tue 12/10/24**	**Tue 12/10/24**	**Equal**	**Mon 9/8/25**	**Mon 9/8/25**
23	**Storefront & Window Shop drawings**	**305 days**	**212 days**	**93d**	**Tue 12/24/24**	**Tue 12/24/24**	**Equal**	**Mon 4/14/25**	**Mon 4/14/25**
31	Fabricate and Deliver	45 days	35 days	10d	Tue 2/25/25	Tue 2/25/25	Equal	Mon 4/14/25	Mon 4/14/25
58				**0d**			**Equal**		
59	**Construction**	**394 days**	**379 days**	**15d**	**Mon 3/17/25**	**Mon 3/17/25**	**Equal**	**Fri 6/12/26**	**Fri 6/12/26**
61	**Overall Site Work Construction**	**367 days**	**359 days**	**8d**	**Mon 3/17/25**	**Mon 3/17/25**	**Equal**	**Fri 4/3/26**	**Fri 4/3/26**
69	**Strom Drainage**	**316 days**	**302 days**	**14d**	**Tue 5/27/25**	**Tue 5/27/25**	**Equal**	**Mon 9/1/25**	**Mon 9/1/25**
76	Complete Install of Storm Pipping	20 days	15 days	5d	Tue 7/8/25	Tue 7/8/25	Equal	Mon 9/1/25	Mon 9/1/25
77	Install Drainage Wells	50 days	3 wks	35d	Tue 6/24/25	Tue 6/24/25	Equal	Mon 7/7/25	Mon 7/7/25
78	**Domestic Water Service**	**304 days**	**57 days**	**247d**	**Mon 12/8/25**	**Mon 12/8/25**	**Equal**	**Fri 1/30/26**	**Fri 1/30/26**
88	Water Main installation	10 days	15 days	-5d	Mon 12/8/25	Mon 12/8/25	Equal	Fri 1/2/26	Fri 1/2/26
89	Building Water Services	2 days	5 days	-3d	Mon 1/5/26	Mon 1/5/26	Equal	Fri 1/9/26	Fri 1/9/26
90	Fire Line Underground w/ DDCV& FDC	3 days	10 days	-7d	Mon 1/12/26	Mon 1/12/26	Equal	Fri 1/23/26	Fri 1/23/26
91	Tie-in to Existing Water Main	3 days	5 days	-2d	Mon 1/26/26	Mon 1/26/26	Equal	Fri 1/30/26	Fri 1/30/26
95	**Hardscape& Misc. Site Work**	**193 days**	**193 days**	**0d**	**Mon 11/24/25**	**Mon 11/24/25**	**Equal**	**Fri 4/3/26**	**Fri 4/3/26**
98	Fill Balance of Site & excavate Retention Areas	5 days	12 days	-7d	Mon 11/24/25	Mon 11/24/25	Equal	Fri 12/12/25	Fri 12/12/25
99	Irrigation and ancillary conduit sleeves	4 days	10 days	-6d	Mon 12/8/25	Mon 12/8/25	Equal	Fri 12/19/25	Fri 12/19/25
100	Sub-base	4 days	5 days	-1d	Mon 1/19/26	Mon 1/19/26	Equal	Fri 1/23/26	Fri 1/23/26
101	Base	5 days	8 days	-3d	Mon 1/26/26	Mon 1/26/26	Equal	Fri 2/6/26	Fri 2/6/26
102	Concrete Curbs	5 days	5 days	0d	Mon 2/2/26	Mon 2/2/26	Equal	Wed 2/11/26	Wed 2/11/26
103	Asphalt (first lift)	3 days	4 days	-1d	Mon 2/9/26	Mon 2/9/26	Equal	Wed 2/18/26	Wed 2/18/26
104	Sidewalks	5 days	5 days	0d	Thu 2/19/26	Thu 2/19/26	Equal	Wed 2/25/26	Wed 2/25/26
105	Landscape& Irrigation Installation	15 days	15 days	0d	Thu 2/19/26	Thu 2/19/26	Equal	Wed 3/11/26	Wed 3/11/26
106	Permanent Fence Install	15 days	15 days	0d	N/A	N/A	Equal	N/A	N/A
107	Final Lift Asphalt & Restoration	5 days	6 days	-1d	Thu 3/12/26	Thu 3/12/26	Equal	Wed 3/25/26	Wed 3/25/26
108	Pavement Marking & Striping	5 days	6 days	-1d	Fri 3/20/26	Fri 3/20/26	Equal	Tue 3/31/26	Tue 3/31/26
109	Jet Vac	3 days	3 days	0d	Wed 4/1/26	Wed 4/1/26	Equal	Fri 4/3/26	Fri 4/3/26
110	**CONVEYANCE PROCESS**	**43 days**	**49 days**	**-6d**	**Fri 1/9/26**	**Fri 1/9/26**	**Equal**	**Wed 3/25/26**	**Wed 3/25/26**
111	Water (Flush & Pressure Testing)	5 days	5 days	0d	Mon 1/12/26	Mon 1/12/26	Equal	Fri 1/16/26	Fri 1/16/26

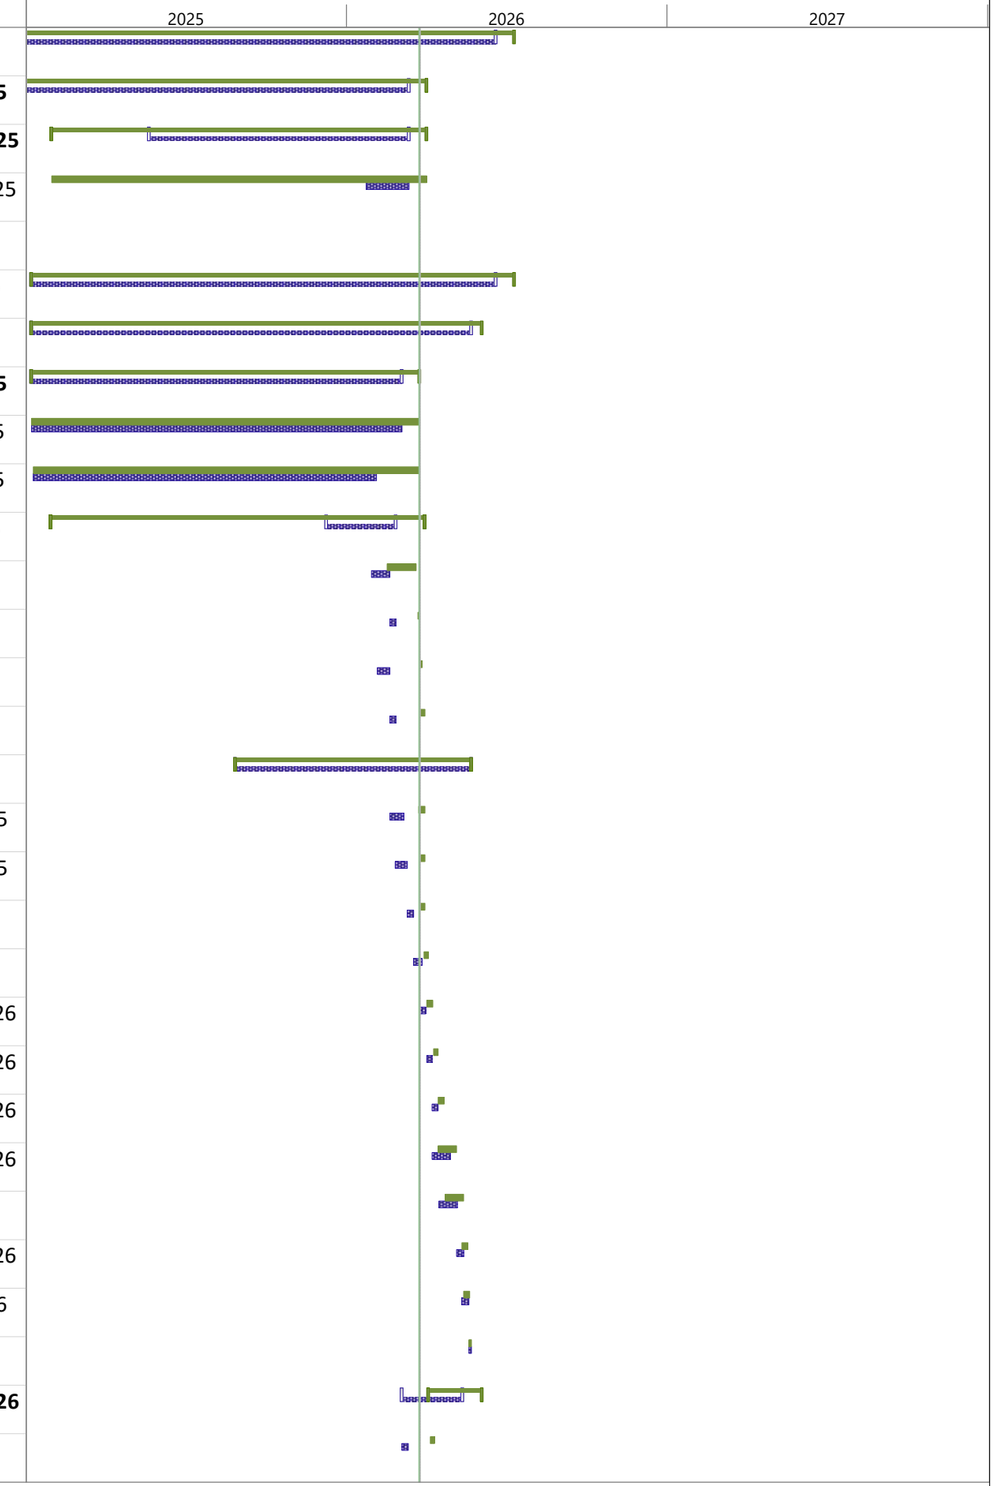

	Name	Duration: Current	Duration: Previous	Durati Diff	Contract Start: Current	Contract Start: Previous	Contrac Start: Diff	Contract Finish: Current	Contract Finish: Previous
112	Water Asbuilts (Partial HRS)	0 days	0 days	0d	Fri 1/9/26	Fri 1/9/26	Equal	Fri 1/9/26	Fri 1/9/26
113	Sewer (Leakage & Lamping)	5 days	5 days	0d	Thu 2/19/26	Thu 2/19/26	Equal	Wed 2/25/26	Wed 2/25/26
114	Sewer As-Builts	0 days	0 days	0d	Fri 1/16/26	Fri 1/16/26	Equal	Fri 1/16/26	Fri 1/16/26
115	Testing (Bacti Samples / Desity Tests)	10 days	10 days	0d	Mon 1/19/26	Mon 1/19/26	Equal	Fri 1/30/26	Fri 1/30/26
116	Release of Lien	1 day	1 day	0d	Mon 1/19/26	Mon 1/19/26	Equal	Mon 1/19/26	Mon 1/19/26
117	HRS Certification (Submission)	4 wks	4 wks	0d	Mon 2/2/26	Mon 2/2/26	Equal	Fri 2/27/26	Fri 2/27/26
118	DERM Certification (Submittion)	4 wks	4 wks	0d	Thu 2/26/26	Thu 2/26/26	Equal	Wed 3/25/26	Wed 3/25/26
119	Water Meter Installation /Owner	3 days	3 days	0d	Mon 3/2/26	Mon 3/2/26	Equal	Wed 3/4/26	Wed 3/4/26
120	Final Asbuilts (For Close-outs)	5 days	5 days	0d	Thu 3/5/26	Thu 3/5/26	Equal	Wed 3/11/26	Wed 3/11/26
121	**Shell Construction**	**320 days**	**374 days**	**-54d**	**Mon 6/2/25**	**Mon 6/2/25**	**Equal**	**Fri 6/12/26**	**Fri 6/12/26**
146	Fireproofing - 5th Floor Deck & Steel Members	18 days	3 wks	3d	N/A	N/A	Equal	N/A	N/A
147	Exterior Finishes	50 days	50 days	0d	Mon 2/2/26	Mon 2/2/26	Equal	Fri 4/10/26	Fri 4/10/26
149	Hallway System (By Owner)	18 wks	18 wks	0d	Thu 11/6/25	Thu 11/6/25	Equal	Wed 4/29/26	Wed 4/29/26
151	HVAC Ductwork	16 wks	16 wks	0d	N/A		Differe	N/A	
153	Install Elevators	10 wks	12 wks	-10d	Fri 2/13/26	Fri 2/13/26	Equal	Thu 4/23/26	Thu 4/23/26
154	Install electrical OH fixtures	30 days	30 days	0d	Thu 3/5/26	Thu 3/5/26	Equal	Wed 4/29/26	Wed 4/29/26
155	Install Rooftop Units	10 days	15 days	-5d	Tue 2/10/26	Tue 2/10/26	Equal	Mon 2/23/26	Mon 2/23/26
156	Install FA System	35 days	35 days	0d	Thu 3/12/26	Thu 3/12/26	Equal	Wed 4/29/26	Wed 4/29/26
157	Exterior Storefront& Windows, & Louvers	25 days	25 days	0d	Mon 2/16/26	Mon 2/16/26	Equal	Fri 3/20/26	Fri 3/20/26
158	Misc. Exterior Items	25 days	25 days	0d	Mon 3/30/26	Mon 3/30/26	Equal	Fri 5/1/26	Fri 5/1/26
159	Delay - FPL Tranformer (On Going)	125 days	80 days	45d	N/A	N/A	Equal	N/A	N/A
160	Install Transformer (Owner)	5 days	5 days	0d	Mon 12/1/25	Mon 12/1/25	Equal	Fri 12/5/25	Fri 12/5/25
161	Temp For Test	5 days	5 days	0d	Thu 3/5/26	Thu 3/5/26	Equal	Wed 3/11/26	Wed 3/11/26
162	Install Electric Meter	1 day	1 day	0d	Thu 3/19/26	Thu 3/19/26	Equal	Thu 3/19/26	Thu 3/19/26
163	Shell Completion	0 days	0 days	0d	Fri 5/1/26	Fri 5/1/26	Equal	Fri 5/1/26	Fri 5/1/26
164	**Offices**	**202 days**	**169 days**	**33d**	**Mon 9/8/25**	**Mon 9/8/25**	**Equal**	**Wed 3/11/26**	**Wed 3/11/26**
167	Start-Up RTUs	0 days	0 days	0d	Wed 3/11/26	Wed 3/11/26	Equal	Wed 3/11/26	Wed 3/11/26
168	T&B	3 days	3 days	0d	N/A	N/A	Equal	N/A	N/A
179	Double Side walls	15 days	10 days	5d	Tue 1/6/26	Tue 1/6/26	Equal	Mon 1/19/26	Mon 1/19/26
180	Tape / Finish Walls	15 days	10 days	5d	Tue 1/13/26	Tue 1/13/26	Equal	Mon 1/26/26	Mon 1/26/26

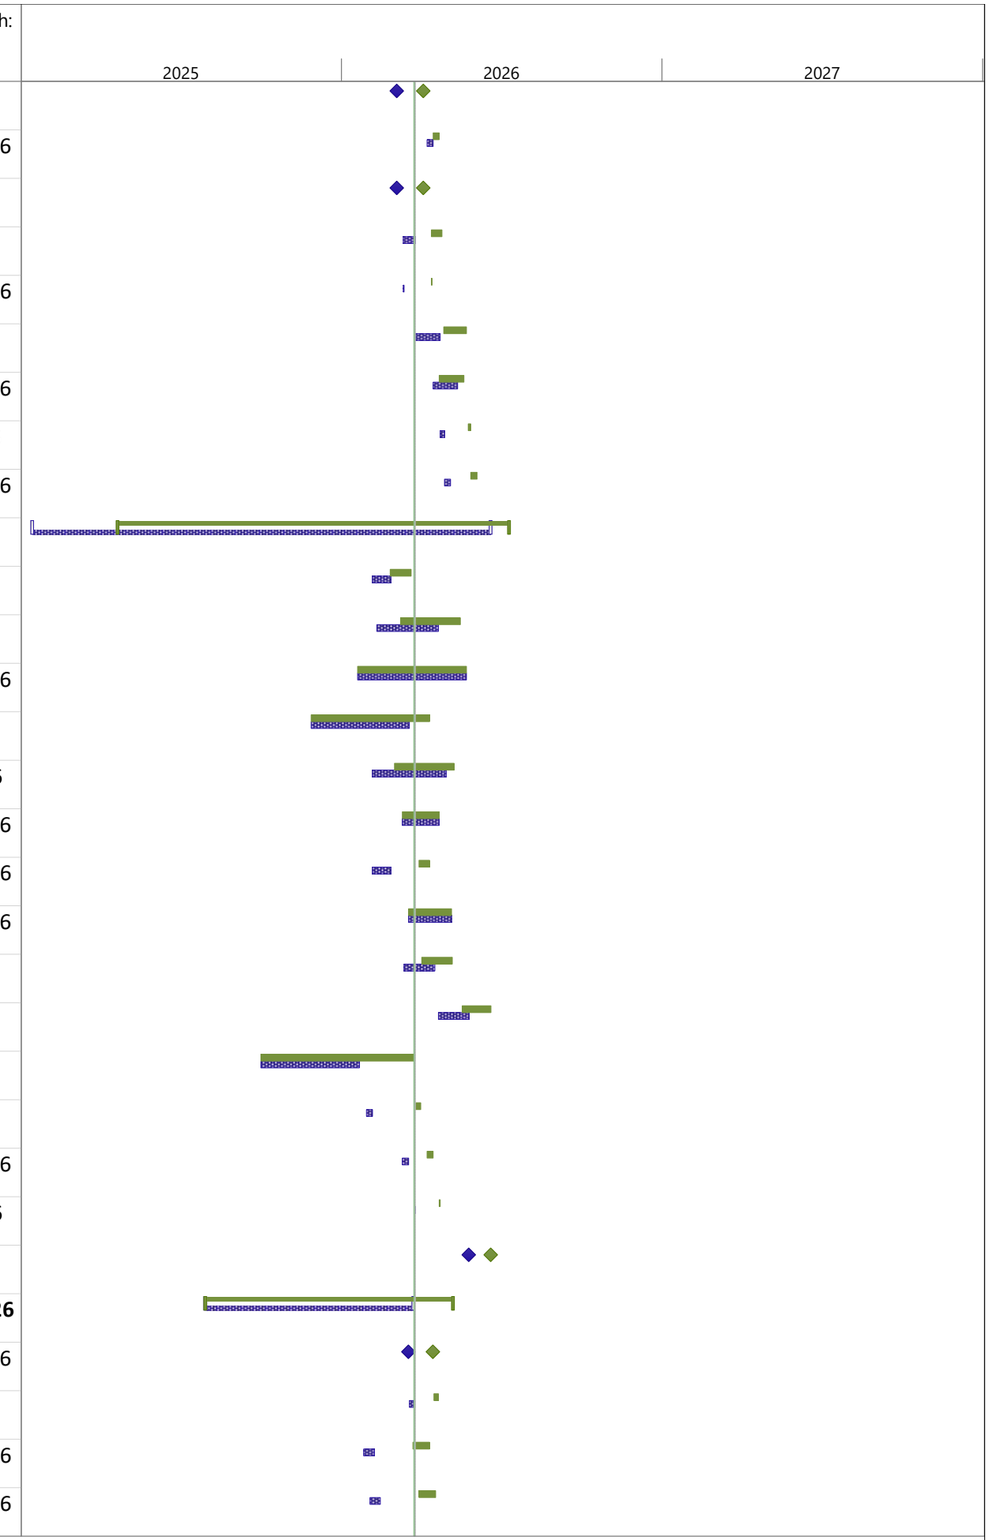
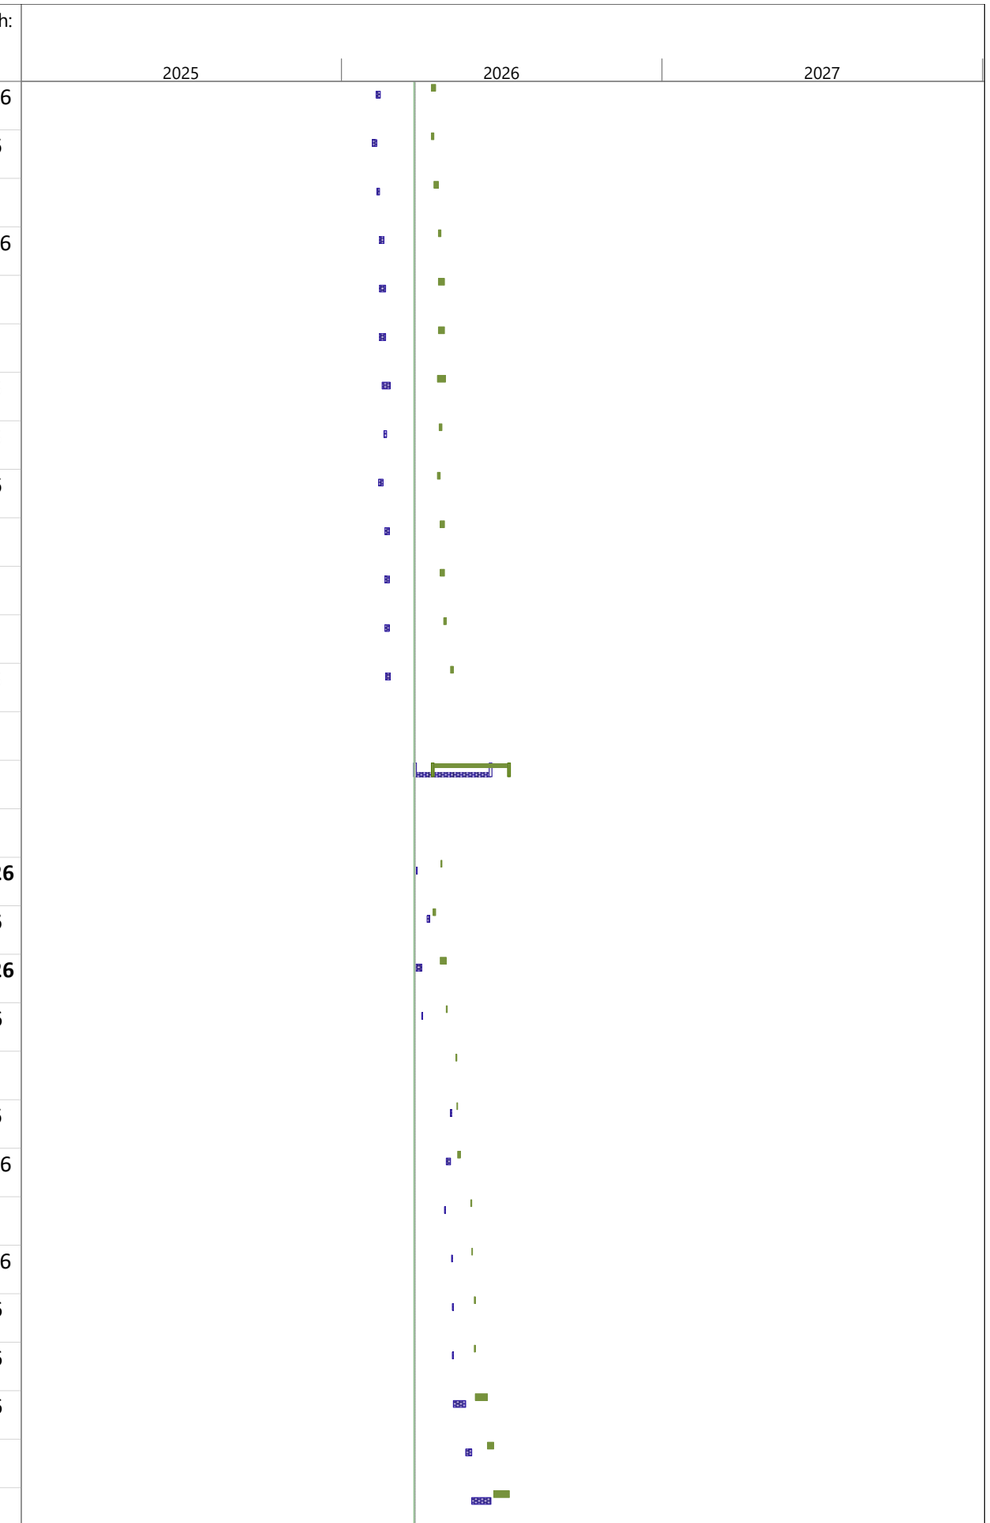
	Name	Duration: Current	Duration: Previous	Durati Diff	Contract Start: Current	Contract Start: Previous	Contrac Start: Diff	Contract Finish: Current	Contract Finish: Previous
181	Install Door Frames	5 days	5 days	0d	Tue 1/20/26	Tue 1/20/26	Equal	Mon 1/26/26	Mon 1/26/26
182	Paint walls (Prime)	3 days	3 days	0d	Fri 1/16/26	Fri 1/16/26	Equal	Tue 1/20/26	Tue 1/20/26
183	Ceiling Grid	3 days	3 days	0d	Wed 1/21/26	Wed 1/21/26	Equal	Fri 1/23/26	Fri 1/23/26
184	Final Paint	3 days	3 days	0d	Mon 1/26/26	Mon 1/26/26	Equal	Wed 1/28/26	Wed 1/28/26
185	Fire Sprinkler Drops	5 days	5 days	0d	Mon 1/26/26	Mon 1/26/26	Equal	Fri 1/30/26	Fri 1/30/26
186	Install Lights	5 days	5 days	0d	Mon 1/26/26	Mon 1/26/26	Equal	Fri 1/30/26	Fri 1/30/26
187	Flooring	7 days	7 days	0d	Tue 1/27/26	Tue 1/27/26	Equal	Wed 2/4/26	Wed 2/4/26
188	Install Millwork	3 days	3 days	0d	Thu 1/29/26	Thu 1/29/26	Equal	Mon 2/2/26	Mon 2/2/26
189	MEP Trim Out	3 days	3 days	0d	Fri 1/23/26	Fri 1/23/26	Equal	Tue 1/27/26	Tue 1/27/26
190	Install Plumbing Fixtures	3 days	3 days	0d	Fri 1/30/26	Fri 1/30/26	Equal	Tue 2/3/26	Tue 2/3/26
191	Install Doors & Hardware	3 days	3 days	0d	Fri 1/30/26	Fri 1/30/26	Equal	Tue 2/3/26	Tue 2/3/26
192	Drop Ceiling tile	3 days	3 days	0d	Fri 1/30/26	Fri 1/30/26	Equal	Tue 2/3/26	Tue 2/3/26
193	Install Toilet Partitions	3 days	3 days	0d	Mon 2/2/26	Mon 2/2/26	Equal	Wed 2/4/26	Wed 2/4/26
194				**0d**			**Equal**		
195	Final Inspections	63 days	62 days	1d	Wed 1/28/26	Wed 1/28/26	Equal	Fri 6/19/26	Fri 6/19/26
196				**0d**			**Equal**		
197	**Final Mechanical**	**1 day**	**1 day**	**0d**	**Wed 1/28/26**	**Wed 1/28/26**	**Equal**	**Wed 1/28/26**	**Wed 1/28/26**
198	**Photometric Inspection / Certification**	**3 days**	**3 days**	**0d**	**Mon 5/4/26**	**Mon 5/4/26**	**Equal**	**Wed 5/6/26**	**Wed 5/6/26**
199	**Fire Pump Certification**	**5 days**	**5 days**	**0d**	**Thu 3/12/26**	**Thu 3/12/26**	**Equal**	**Wed 3/18/26**	**Wed 3/18/26**
200	Final Sprinkler	1 day	1 day	0d	Thu 3/19/26	Thu 3/19/26	Equal	Thu 3/19/26	Thu 3/19/26
201	Final Fire Alarm	1 day			N/A			N/A	
202	Final Fire	1 day	1 day	0d	Tue 5/12/26	Tue 5/12/26	Equal	Tue 5/12/26	Tue 5/12/26
203	Final Electrical - (Fire Life Safety Approval Requie	3 days	3 days	0d	Thu 5/7/26	Thu 5/7/26	Equal	Mon 5/11/26	Mon 5/11/26
204	Final Plumbing	1 day	1 day	0d	Tue 4/7/26	Tue 4/7/26	Equal	Tue 4/7/26	Tue 4/7/26
205	Final Building	1 day	1 day	0d	Wed 5/13/26	Wed 5/13/26	Equal	Wed 5/13/26	Wed 5/13/26
206	Final Zoning	1 day	1 day	0d	Thu 5/14/26	Thu 5/14/26	Equal	Thu 5/14/26	Thu 5/14/26
207	Public Works Release (DERM)	1 day	1 day	0d	Thu 5/14/26	Thu 5/14/26	Equal	Thu 5/14/26	Thu 5/14/26
208	Obtain Certificate of Completion	10 days	10 days	0d	Fri 5/15/26	Fri 5/15/26	Equal	Thu 5/28/26	Thu 5/28/26
209	PCCO #009 - Veneer Window Attachment Chang	5 days	5 days	0d	05/29/2026	05/29/2026	Equal	06/05/2026	06/05/2026
210	Weather Delay Allowance	14 days	16 days	-2d	06/08/2026	06/08/2026	Equal	06/24/2026	06/24/2026
