RYCON Construction Inc.

Construction Schedule
Public Storage - Aventura

Public Storage

Wed 3/25/26

ID	Task Name	% Complete	Duration	Contract Start
1	**Overall Project Duration Public Storage - Aventura**	**79%**	**443 days**	**Wed 10/30/24**
6	**SUBMITTALS**	**99%**	**342 days**	**Tue 12/10/24**
23	**Storefront & Window Shop drawings**	**98%**	**305 days**	**Tue 12/24/24**
31	Fabricate and Deliver	90%	45 days	Tue 2/25/25
59	**Construction**	**63%**	**394 days**	**Mon 3/17/25**
61	**Overall Site Work Construction**	**63%**	**367 days**	**Mon 3/17/25**
69	**Strom Drainage**	**92%**	**316 days**	**Tue 5/27/25**
76	**Complete Install of Storm Pipping**	**95%**	**20 days**	**Tue 7/8/25**
77	Install Drainage Wells	80%	50 days	Tue 6/24/25
78	**Domestic Water Service**	**82%**	**304 days**	**Mon 12/8/25**
88	Water Main installation	30%	10 days	Mon 12/8/25
89	Building Water Services	0%	2 days	Mon 1/5/26
90	Fire Line Underground w/ DDCV& FDC	0%	3 days	Mon 1/12/26
91	Tie-in to Existing Water Main	0%	3 days	Mon 1/26/26
95	**Hardscape& Misc. Site Work**	**12%**	**193 days**	**Mon 11/24/25**
98	Fill Balance of Site & excavate Retention Areas	0%	5 days	Mon 11/24/25
99	Irrigation and ancillary conduit sleeves	0%	4 days	Mon 12/8/25
100	Sub-base	0%	4 days	Mon 1/19/26
101	Base	0%	5 days	Mon 1/26/26
102	Concrete Curbs	0%	5 days	Mon 2/2/26
103	Asphalt (first lift)	0%	3 days	Mon 2/9/26
104	Sidewalks	0%	5 days	Thu 2/19/26
105	Landscape& Irrigation Installation	0%	15 days	Thu 2/19/26
106	Permanent Fence Install	0%	15 days	N/A
107	Final Lift Asphalt & Restoration	0%	5 days	Thu 3/12/26
108	Pavement Marking & Striping	0%	5 days	Fri 3/20/26
109	Jet Vac	0%	3 days	Wed 4/1/26
110	**CONVEYANCE PROCESS**	**0%**	**43 days**	**Fri 1/9/26**
111	Water (Flush & Pressure Testing)	0%	5 days	Mon 1/12/26

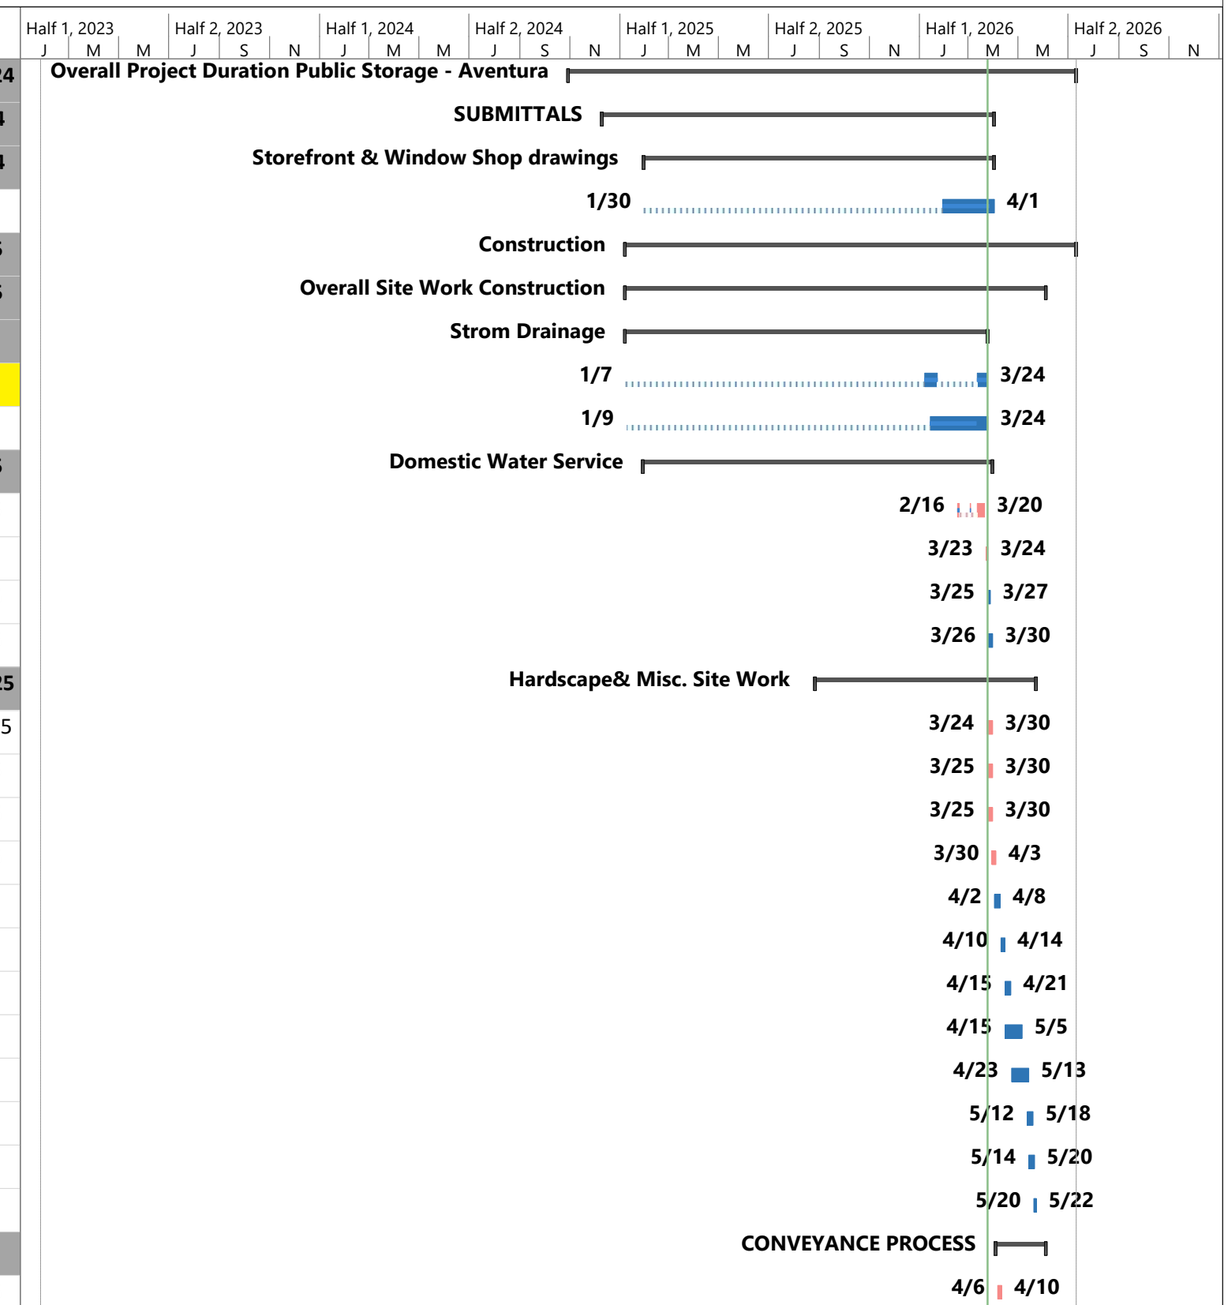

RYCON Construction Inc.

Construction Schedule
Public Storage - Aventura

Public Storage

Wed 3/25/26

ID	Task Name	% Complete	Duration	Contract Start
112	Water Asbuilts (Partial HRS)	0%	0 days	Fri 1/9/26
113	Sewer (Leakage & Lamping)	0%	5 days	Thu 2/19/26
114	Sewer As-Builts	0%	0 days	Fri 1/16/26
115	Testing (Bacti Samples / Desity Tests)	0%	10 days	Mon 1/19/26
116	Release of Lien	0%	1 day	Mon 1/19/26
117	HRS Certification (Submission)	0%	4 wks	Mon 2/2/26
118	DERM Certification (Submittion)	0%	4 wks	Thu 2/26/26
119	Water Meter Installation /Owner	0%	3 days	Mon 3/2/26
120	Final Asbuilts (For Close-outs)	0%	5 days	Thu 3/5/26
121	**Shell Construction**	**63%**	**320 days**	**Mon 6/2/25**
146	Fireproofing - 5th Floor Deck & Steel Members	80%	18 days	N/A
147	Exterior Finishes	0%	50 days	Mon 2/2/26
149	**Hallway System (By Owner)**	**35%**	**18 wks**	**Thu 11/6/25**
151	HVAC Ductwork	80%	16 wks	N/A
153	Install Elevators	40%	10 wks	Fri 2/13/26
154	Install electrical OH fixtures	60%	30 days	Thu 3/5/26
155	Install Rooftop Units	0%	10 days	Tue 2/10/26
156	Install FA System	0%	35 days	Thu 3/12/26
157	Exterior Storefront& Windows, & Louvers	0%	25 days	Mon 2/16/26
158	Misc. Exterior Items	0%	25 days	Mon 3/30/26
159	**Delay - FPL Tranformer (On Going)**	**0%**	**125 days**	**N/A**
160	Install Transformer (Owner)	0%	5 days	Mon 12/1/25
161	**Temp For Test**	**0%**	**5 days**	**Thu 3/5/26**
162	Install Electric Meter	0%	1 day	Thu 3/19/26
163	**Shell Completion**	**0%**	**0 days**	**Fri 5/1/26**
164	**Offices**	**53%**	**202 days**	**Mon 9/8/25**
167	Start-Up RTUs	0%	0 days	Wed 3/11/26
168	T&B	0%	3 days	N/A
179	Double Side walls	0%	15 days	Tue 1/6/26

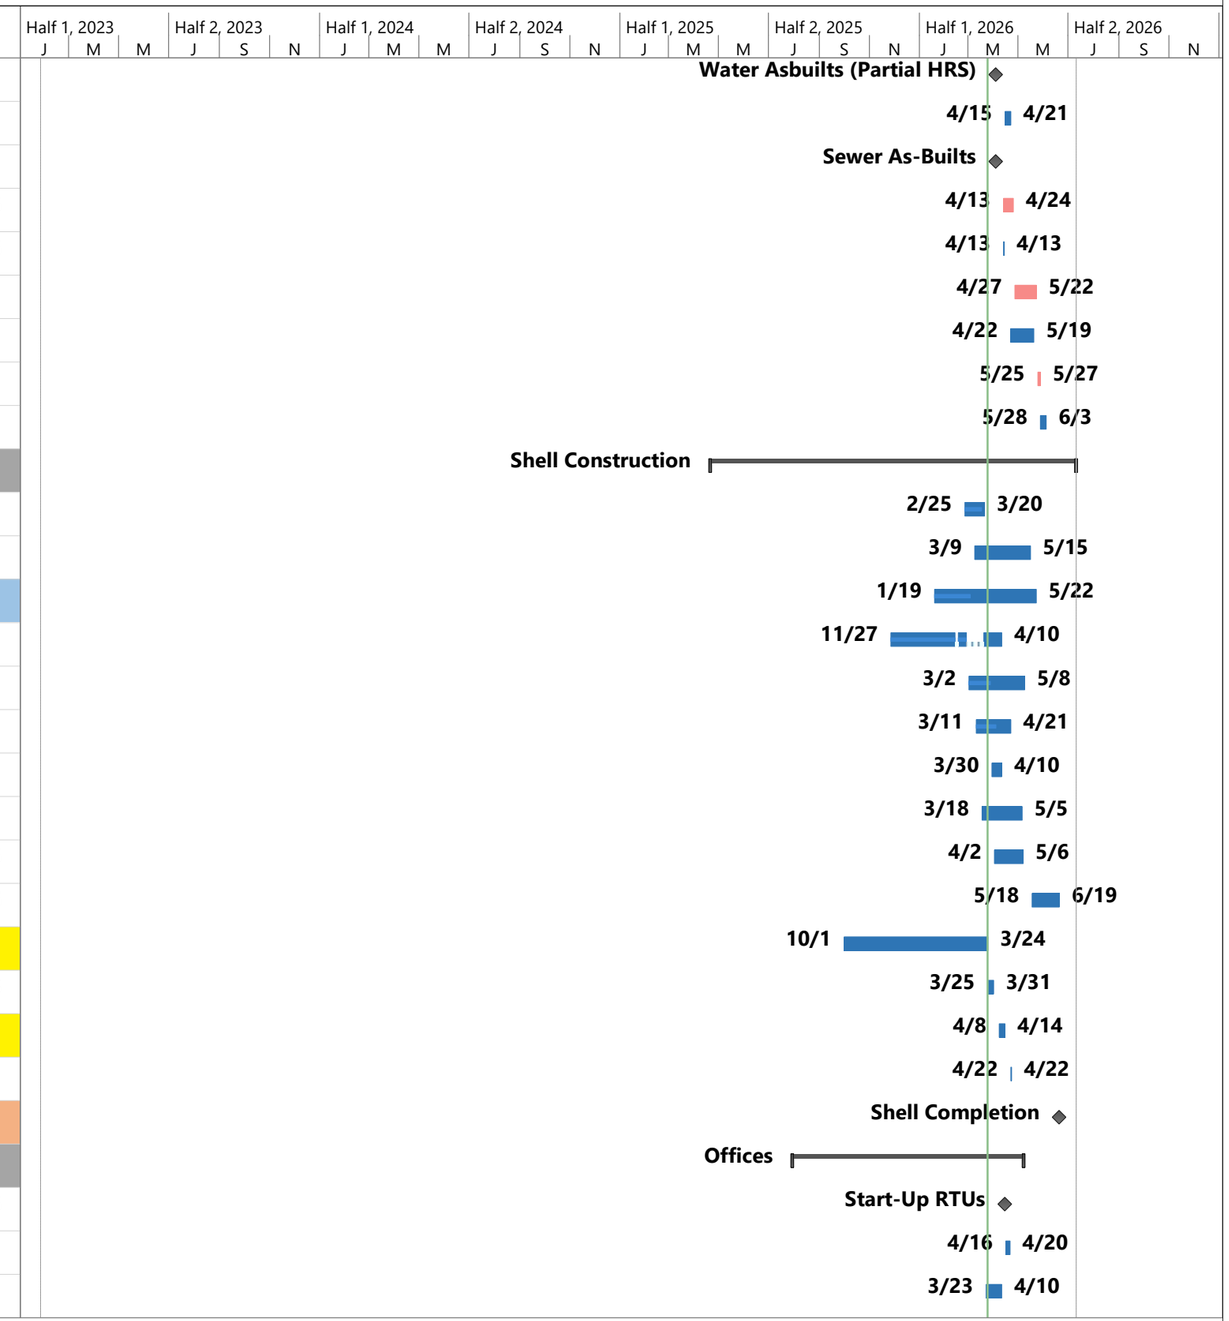

RYCON Construction Inc.

Construction Schedule
Public Storage - Aventura

Public Storage

Wed 3/25/26
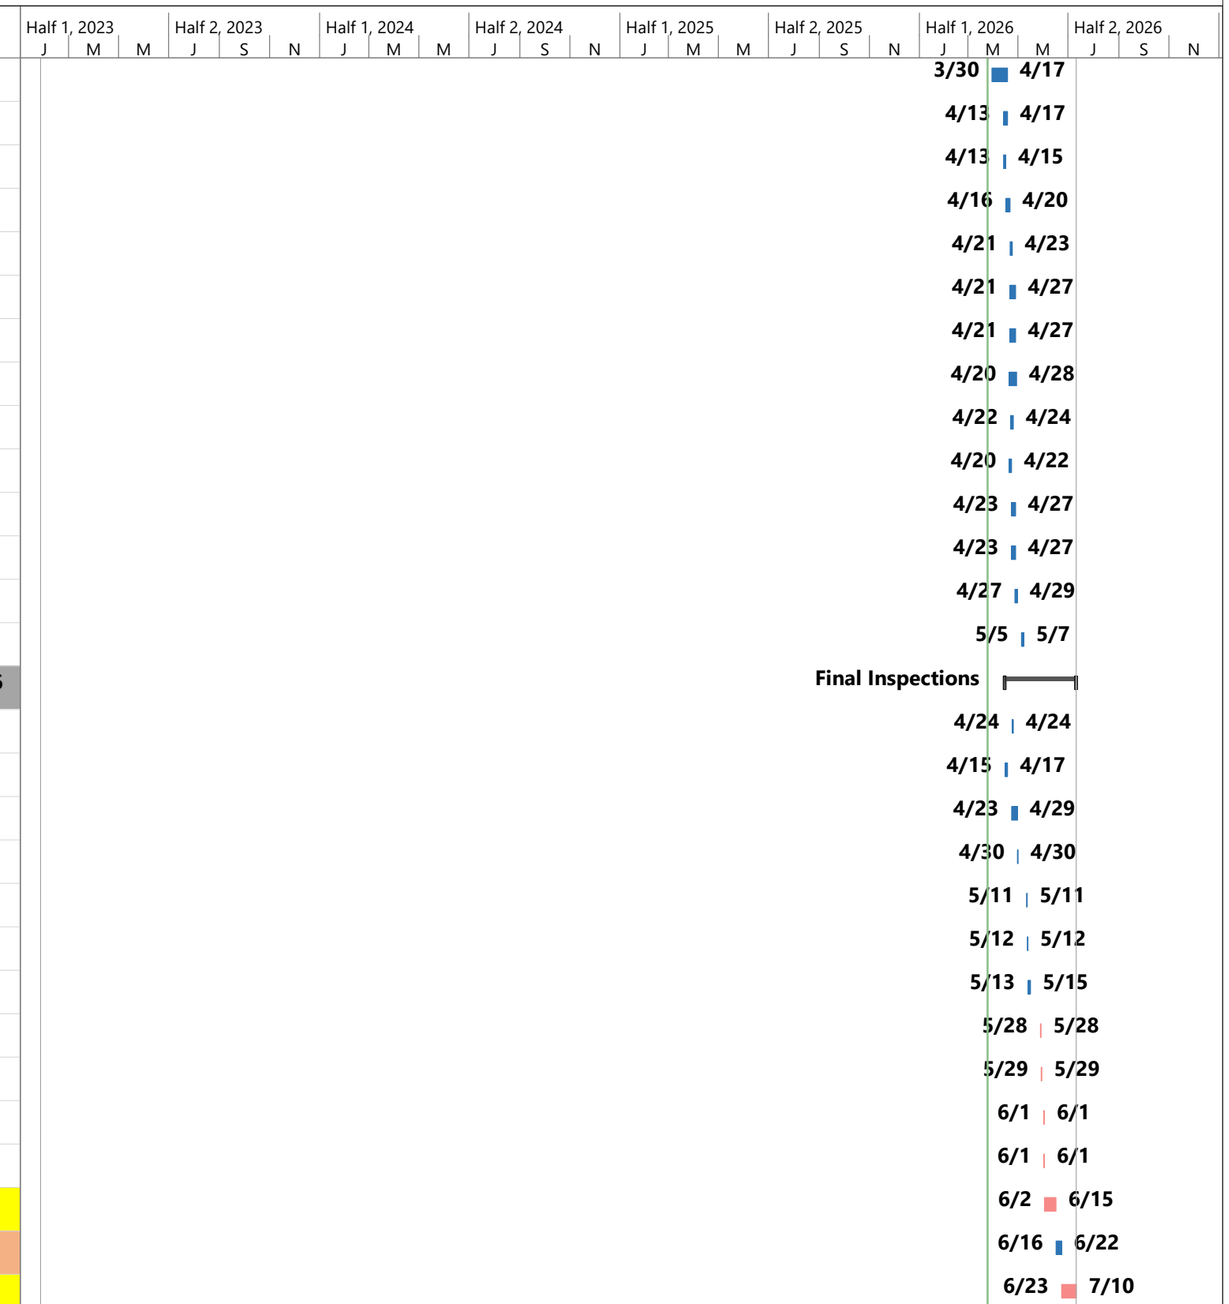
ID	Task Name	% Complete	Duration	Contract Start
180	Tape / Finish Walls	0%	15 days	Tue 1/13/26
181	Install Door Frames	0%	5 days	Tue 1/20/26
182	Paint walls (Prime)	0%	3 days	Fri 1/16/26
183	Ceiling Grid	0%	3 days	Wed 1/21/26
184	Final Paint	0%	3 days	Mon 1/26/26
185	Fire Sprinkler Drops	0%	5 days	Mon 1/26/26
186	Install Lights	0%	5 days	Mon 1/26/26
187	Flooring	0%	7 days	Tue 1/27/26
188	Install Millwork	0%	3 days	Thu 1/29/26
189	MEP Trim Out	0%	3 days	Fri 1/23/26
190	Install Plumbing Fixtures	0%	3 days	Fri 1/30/26
191	Install Doors & Hardware	0%	3 days	Fri 1/30/26
192	Drop Ceiling tile	0%	3 days	Fri 1/30/26
193	Install Toilet Partitions	0%	3 days	Mon 2/2/26
195	**Final Inspections**	**0%**	**63 days**	**Wed 1/28/26**
197	Final Mechanical	0%	1 day	Wed 1/28/26
198	Photometric Inspection / Certification	0%	3 days	Mon 5/4/26
199	Fire Pump Certification	0%	5 days	Thu 3/12/26
200	Final Sprinkler	0%	1 day	Thu 3/19/26
201	Final Fire Alarm	0%	1 day	N/A
202	Final Fire	0%	1 day	Tue 5/12/26
203	Final Electrical - (Fire Life Safety Approval Requiered)	0%	3 days	Thu 5/7/26
204	Final Plumbing	0%	1 day	Tue 4/7/26
205	Final Building	0%	1 day	Wed 5/13/26
206	Final Zoning	0%	1 day	Thu 5/14/26
207	Public Works Release (DERM)	0%	1 day	Thu 5/14/26
208	**Obtain Certificate of Completion**	**0%**	**10 days**	**Fri 5/15/26**
209	PCCO #009 - Veneer Window Attachment Changes	0%	5 days	05/29/2026
210	**Weather Delay Allowance**	**0%**	**14 days**	**06/08/2026**
