RYCON Construction Inc.

Construction Schedule
Public Storage - Aventura

Public Storage

Thu 2/12/26

ID	Task Name	Duration	Contract Start	Contract Finish	Projected Start	Projected Finish	% Complete
1	**Overall Project Duration Public Storage - Aventura**	**428 days**	**Wed 10/30/24**	**6/17/2026**	**Wed 10/30/24**	**Fri 6/19/26**	**71%**
2	**DEMO PERMIT ISSUED**	**0 days**	**Tue 3/11/25**	**Tue 3/11/25**	**Tue 3/11/25**	**Tue 3/11/25**	**100%**
3	**BUILDING MASTER PERMIT (ESTIMATED)**	**1 day**	**Mon 4/7/25**	**Mon 4/7/25**	**Tue 4/15/25**	**Tue 4/15/25**	**100%**
4	Executed Contract	29 days	Wed 10/30/24	Mon 12/9/24	Wed 10/30/24	Mon 12/9/24	100%
5	Release of Subcontractors	10 days	Tue 12/10/24	Mon 12/23/24	Tue 12/10/24	Thu 3/6/25	100%
6	**SUBMITTALS**	**328 days**	**Tue 12/10/24**	**Mon 9/8/25**	**Tue 12/10/24**	**Thu 3/12/26**	**96%**
7	**Fire Sprinkler Shop Drawings**	**68 days**	**Tue 12/24/24**	**Fri 4/11/25**	**Tue 5/13/25**	**Thu 8/14/25**	**100%**
8	Request& Receive CAD Files	7 days	Tue 12/24/24	Tue 12/24/24	Tue 5/13/25	Wed 5/21/25	100%
9	Shop Drawing Submittal	29 days	Wed 12/25/24	Tue 1/14/25	Thu 5/22/25	Tue 7/1/25	100%
10	Approval / AOR	9 days	Wed 1/15/25	Tue 1/28/25	Wed 7/2/25	Mon 7/14/25	100%
11	City Submission& Approval Estimated	2.2 wks	Wed 1/29/25	Tue 4/8/25	Wed 7/30/25	Wed 8/13/25	100%
12	Fire Sprinkler Permit	0 days	Fri 4/11/25	Fri 4/11/25	Thu 8/14/25	Thu 8/14/25	100%
13	**Structural Steel Shop Drawings**	**125 days**	**Tue 12/10/24**	**Thu 6/12/25**	**Tue 12/10/24**	**Mon 6/2/25**	**100%**
14	Structural Steel Shop Drawings Submittal	63 days	Tue 12/10/24	Thu 3/6/25	Tue 12/10/24	Thu 3/6/25	100%
15	Approval / AOR	13 days	Fri 3/14/25	Thu 4/3/25	Fri 3/14/25	Tue 4/1/25	100%
16	Fabricate and Deliver Steel	8.4 wks	Fri 4/4/25	Thu 6/12/25	Fri 4/4/25	Mon 6/2/25	100%
17	**Concrete Submittals / Shop Drawings**	**73 days**	**Tue 12/24/24**	**Wed 3/19/25**	**Tue 12/24/24**	**Thu 4/3/25**	**100%**
18	Footing Rebar Submittal	51 days	Tue 12/24/24	Tue 3/4/25	Tue 12/24/24	Tue 3/4/25	100%
19	Approval AOR	20 days	Wed 3/5/25	Wed 3/5/25	Wed 3/5/25	Tue 4/1/25	100%
20	Concrete mix Submittals	50 days	Tue 12/24/24	Mon 3/3/25	Tue 12/24/24	Mon 3/3/25	100%
21	Approval AOR	13 days	Tue 3/4/25	Mon 3/10/25	Tue 3/4/25	Thu 3/20/25	100%
22	Release Rebar	2 days	Thu 3/6/25	Wed 3/19/25	Fri 3/21/25	Thu 4/3/25	100%
23	**Storefront & Window Shop drawings**	**212 days**	**Tue 12/24/24**	**Mon 4/14/25**	**Wed 5/21/25**	**Thu 3/12/26**	**70%**
24	Storefront& Window Submittal	38 days	Tue 12/24/24	Mon 1/13/25	Wed 5/21/25	Fri 7/11/25	100%
25	Approval / AOR	38 days	Tue 1/14/25	Mon 1/27/25	Wed 7/16/25	Fri 9/5/25	100%
26	Storefront & Window Submittal (Rev 1) per revised detail Rev 4&5 - Cost Rejected by Owner	21 days	N/A	N/A	Mon 9/8/25	Mon 10/6/25	100%
27	Approval / AOR	0 days	N/A	N/A	Tue 11/11/25	Tue 11/11/25	100%
28	Storefront & Window Submittal - Per Latest Veneer Window Attachement Detail	16 days			Wed 11/12/25	Wed 12/3/25	100%
29	Approval / AOR	35 days			Thu 12/4/25	Wed 1/21/26	85%
30	City Submission& Approval	20 days	Tue 1/28/25	Mon 2/24/25	Fri 1/23/26	Thu 2/19/26	0%
31	Fabricate and Deliver	35 days	Tue 2/25/25	Mon 4/14/25	Fri 1/23/26	Thu 3/12/26	0%
32	**Roofing**	**258 days**	**Tue 12/24/24**	**Mon 6/30/25**	**Tue 12/24/24**	**Thu 12/18/25**	**100%**
33	Roofing Submittal	114 days	Tue 12/24/24	Mon 1/13/25	Tue 12/24/24	Fri 5/30/25	100%
34	Approval / AOR	13 days	Tue 1/21/25	Mon 2/3/25	Fri 8/8/25	Tue 8/26/25	100%
35	Roofing Material Deliver	16.4 wks	Tue 2/11/25	Mon 6/30/25	Wed 8/27/25	Thu 12/18/25	100%
36	**DIP Water Piping**	**90 days**	**Tue 12/24/24**	**Mon 5/26/25**	**Thu 5/29/25**	**Wed 10/1/25**	**100%**
37	DIP Submittals	6 days	Tue 12/24/24	Mon 1/6/25	Thu 5/29/25	Thu 6/5/25	100%

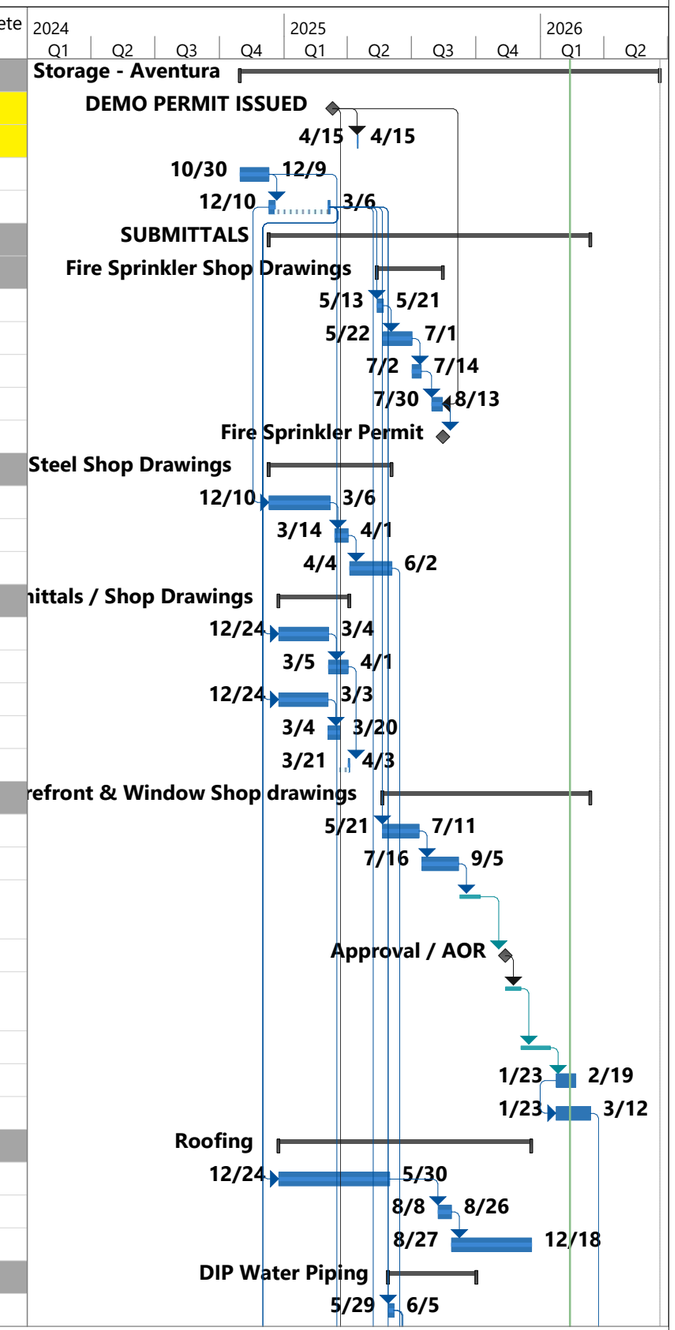

RYCON Construction Inc.

Construction Schedule
Public Storage - Aventura

Public Storage

Thu 2/12/26

ID	Task Name	Duration	Contract Start	Contract Finish	Projected Start	Projected Finish	% Complete
38	Review & Approval (EOR/AOR)	10 days	Tue 1/7/25	Mon 1/20/25	Fri 6/6/25	Thu 6/19/25	100%
39	Fabricate and Deliver	15 wks	Tue 1/7/25	Mon 5/26/25	Thu 6/19/25	Wed 10/1/25	100%
40	**Storm Drainage**	**135 days**	**Tue 12/24/24**	**Mon 3/10/25**	**Thu 5/29/25**	**Wed 12/3/25**	**100%**
41	Storm Drainage& Sewer System Submittals	6 days	Tue 12/24/24	Mon 1/13/25	Thu 5/29/25	Thu 6/5/25	100%
42	Review & Approval (EOR/AOR)	10 days	Tue 1/14/25	Mon 1/27/25	Fri 6/6/25	Thu 6/19/25	100%
43	Fabricate and Deliver Structures	23.8 wks	Tue 1/28/25	Mon 3/10/25	Fri 6/20/25	Wed 12/3/25	100%
44	**HVAC Equipment**	**113 days**	**Tue 12/24/24**	**Mon 9/8/25**	**Thu 5/8/25**	**Mon 10/13/25**	**100%**
45	Submittals	1 day	Tue 12/24/24	Mon 1/13/25	Thu 5/8/25	Thu 5/8/25	100%
46	Review & Approval (EOR/AOR)	10 days	Tue 1/14/25	Mon 1/27/25	Tue 8/26/25	Mon 9/8/25	100%
47	**(ESTIMATED) Fabricate & Deliver**	5 wks	Tue 1/28/25	Mon 9/8/25	Tue 9/9/25	Mon 10/13/25	100%
48	**Switchgear Equipment**	**226 days**	**Tue 12/24/24**	**Mon 7/21/25**	**Tue 12/24/24**	**Tue 11/4/25**	**100%**
49	Submittals	91 days	Tue 12/24/24	Mon 1/13/25	Tue 12/24/24	Tue 4/29/25	100%
50	Review & Approval (EOR/AOR)	10 days	Tue 1/14/25	Mon 1/27/25	Wed 4/30/25	Tue 5/13/25	100%
51	**(Estimated) Fabricate & Deliver Switchgear**	25 wks	Tue 1/28/25	Mon 7/21/25	Wed 5/14/25	Tue 11/4/25	100%
52	**Elevator Equipment**	**281 days**	**Tue 12/24/24**	**Tue 9/2/25**	**Tue 12/24/24**	**Tue 1/20/26**	**99%**
53	Submittals	2.8 wks	Tue 12/24/24	Tue 2/11/25	Tue 12/24/24	Fri 1/10/25	100%
54	Review & Approval (EOR/AOR)	23 days	Wed 2/12/25	Tue 3/4/25	Wed 2/19/25	Fri 3/21/25	100%
55	Revised Submittal	1 day	N/A	N/A	Fri 5/16/25	Fri 5/16/25	100%
56	Review & Approval (EOR/AOR)	120 days	N/A	N/A	Tue 12/24/24	Sun 6/8/25	100%
57	**Released for Fabrication & Deliver Elevator Equipment**	66 days	Wed 3/5/25	Tue 9/2/25	Tue 10/21/25	Tue 1/20/26	95%
58							
59	**Construction**	**379 days**	**Mon 3/17/25**	**Fri 6/12/26**	**Tue 1/7/25**	**Fri 6/19/26**	**50%**
60	Mobilization	5 days	Mon 3/17/25	Fri 3/21/25	Mon 3/17/25	Fri 3/21/25	100%
61	**Overall Site Work Construction**	**359 days**	**Mon 3/17/25**	**Fri 4/3/26**	**Tue 1/7/25**	**Fri 5/22/26**	**36%**
62	**Site Construction**	**40 days**	**Mon 3/17/25**	**Fri 5/30/25**	**Mon 3/17/25**	**Fri 5/9/25**	**100%**
63	Secure / Fence Site	5 days	Mon 3/17/25	Fri 3/21/25	Mon 3/17/25	Fri 3/21/25	100%
64	Locate existing utilities for new tie-in	5 days	Mon 3/31/25	Fri 4/4/25	Mon 3/31/25	Fri 4/4/25	100%
65	Building Site Demolition	30 days	Wed 3/19/25	Fri 5/9/25	Wed 3/19/25	Fri 5/9/25	100%
66	Install protection and erosion control	12 days	Fri 4/4/25	Thu 4/10/25	Fri 4/4/25	Mon 4/21/25	100%
67	Site Survey& Layout	5 days	Mon 5/12/25	Fri 5/16/25	Mon 3/31/25	Fri 4/4/25	100%
68	Construct Building Pad	15 days	Mon 5/12/25	Fri 5/30/25	Mon 3/31/25	Fri 4/18/25	100%
69	**Strom Drainage**	**302 days**	**Tue 5/27/25**	**Mon 9/1/25**	**Tue 1/7/25**	**Wed 3/4/26**	**55%**
70	Install Storm Structures & Well Boxes	22 days	Tue 5/27/25	Mon 6/23/25	Mon 12/8/25	Tue 1/6/26	100%
71	**Delay - Conflict with Existing Drainage Structures - RFI#064 (On Going) - ESTIMATED**	**15 days**	**N/A**	**N/A**	**Thu 1/8/26**	**Wed 1/28/26**	**0%**
72	Install Storm Pipping	15 days	Tue 7/8/25	Mon 9/1/25	Tue 1/7/25	Wed 3/4/26	75%
73	Install Drainage Wells	3 wks	Tue 6/24/25	Mon 7/7/25	Thu 1/9/25	Tue 2/3/26	25%
74	**Domestic Water Service**	**57 days**	**Mon 12/8/25**	**Fri 1/30/26**	**Tue 12/9/25**	**Wed 2/25/26**	**17%**

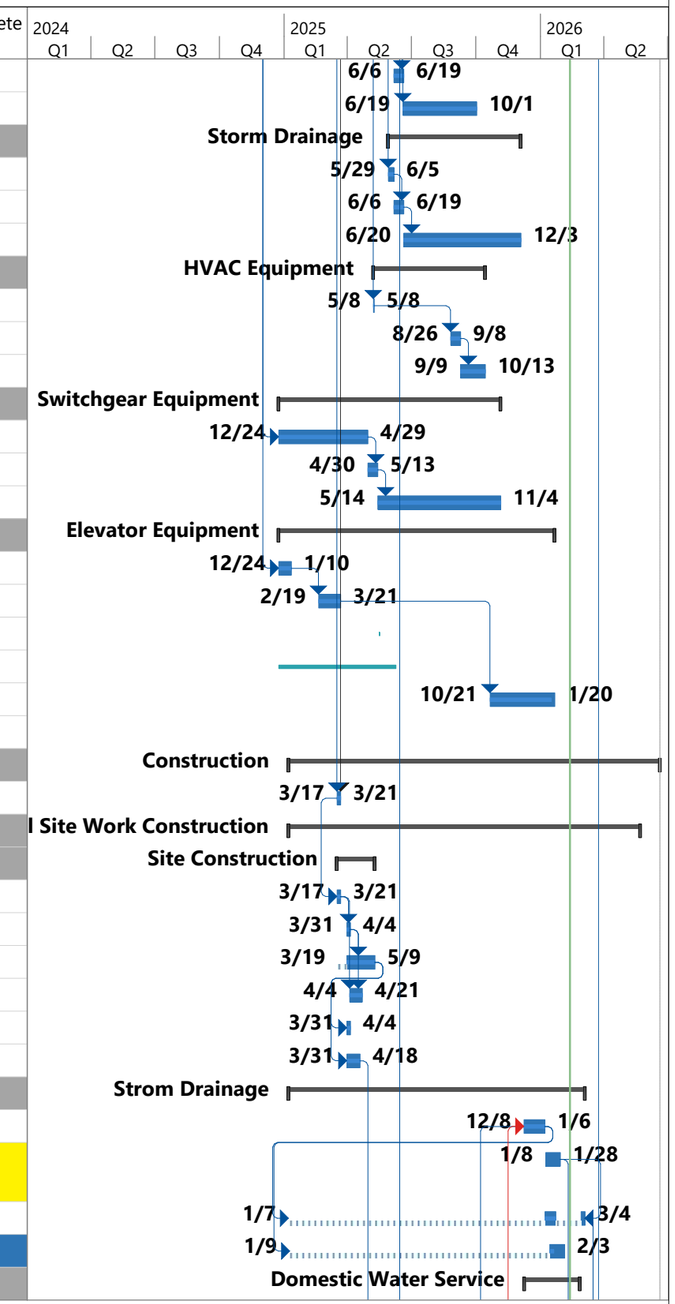

RYCON Construction Inc.

Construction Schedule
Public Storage - Aventura

Public Storage

Thu 2/12/26

ID	Task Name	Duration	Contract Start	Contract Finish	Projected Start	Projected Finish	% Complete
75	**Potential Delay - Temp Access Permit to be Re-Issued & Precon Scheduled (Estimated)**	**35 days**	**N/A**	**N/A**	**Tue 12/9/25**	**Mon 1/26/26**	**34%**
76	Temp Access For Active Building	2 days			Tue 1/27/26	Wed 1/28/26	0%
77	Water Main installation	15 days	Mon 12/8/25	Fri 1/2/26	Thu 1/29/26	Wed 2/18/26	0%
78	Building Water Services	5 days	Mon 1/5/26	Fri 1/9/26	Thu 2/19/26	Wed 2/25/26	0%
79	Fire Line Underground w/ DDCV& FDC	10 days	Mon 1/12/26	Fri 1/23/26	Thu 2/5/26	Wed 2/18/26	0%
80	Tie-in to Existing Water Main	5 days	Mon 1/26/26	Fri 1/30/26	Thu 2/19/26	Wed 2/25/26	0%
81	**Sewer System**	**10 days**	**Mon 1/12/26**	**Fri 1/30/26**	**Thu 10/30/25**	**Wed 11/12/25**	**100%**
82	Tie into Existing Stub as required	5 days	Mon 1/26/26	Fri 1/30/26	Thu 10/30/25	Wed 11/5/25	100%
83	Install Sanitary Piping	5 days	Mon 1/12/26	Fri 1/16/26	Thu 11/6/25	Wed 11/12/25	100%
84	**Hardscape& Misc. Site Work**	**193 days**	**Mon 11/24/25**	**Fri 4/3/26**	**Wed 8/27/25**	**Fri 5/22/26**	**10%**
85	Primary Electrical Conduit	5 days	Mon 11/24/25	Fri 11/28/25	Wed 8/27/25	Tue 9/2/25	100%
86	Site Lighting conduit, brooks boxes,& Fixture Installation	5 days	Mon 12/1/25	Fri 12/5/25	Wed 9/3/25	Tue 9/9/25	100%
87	Fill Balance of Site & excavate Retention Areas	12 days	Mon 11/24/25	Fri 12/12/25	Thu 2/19/26	Fri 3/6/26	0%
88	Irrigation and ancillary conduit sleeves	10 days	Mon 12/8/25	Fri 12/19/25	Wed 2/25/26	Tue 3/10/26	0%
89	Sub-base	5 days	Mon 1/19/26	Fri 1/23/26	Wed 3/11/26	Tue 3/17/26	0%
90	Base	8 days	Mon 1/26/26	Fri 2/6/26	Wed 3/18/26	Fri 3/27/26	0%
91	Concrete Curbs	5 days	Mon 2/2/26	Wed 2/11/26	Wed 3/25/26	Tue 3/31/26	0%
92	Asphalt (first lift)	4 days	Mon 2/9/26	Wed 2/18/26	Thu 4/2/26	Tue 4/7/26	0%
93	Sidewalks	5 days	Thu 2/19/26	Wed 2/25/26	Wed 4/8/26	Tue 4/14/26	0%
94	Landscape& Irrigation Installation	15 days	Thu 2/19/26	Wed 3/11/26	Wed 4/8/26	Tue 4/28/26	0%
95	Permanent Fence Install	15 days	N/A	N/A	Thu 4/16/26	Wed 5/6/26	0%
96	Final Lift Asphalt & Restoration	6 days	Thu 3/12/26	Wed 3/25/26	Wed 5/6/26	Wed 5/13/26	0%
97	Pavement Marking & Striping	6 days	Fri 3/20/26	Tue 3/31/26	Tue 5/12/26	Tue 5/19/26	0%
98	Jet Vac	3 days	Wed 4/1/26	Fri 4/3/26	Wed 5/20/26	Fri 5/22/26	0%
99	**CONVEYANCE PROCESS**	**49 days**	**Fri 1/9/26**	**Wed 3/25/26**	**Wed 3/4/26**	**Tue 5/12/26**	**0%**
100	Water (Flush & Pressure Testing)	5 days	Mon 1/12/26	Fri 1/16/26	Thu 3/5/26	Wed 3/11/26	0%
101	Water Asbuilts (Partial HRS)	0 days	Fri 1/9/26	Fri 1/9/26	Wed 3/4/26	Wed 3/4/26	0%
102	Sewer (Leakage & Lamping)	5 days	Thu 2/19/26	Wed 2/25/26	Wed 4/8/26	Tue 4/14/26	0%
103	Sewer As-Builts	0 days	Fri 1/16/26	Fri 1/16/26	Wed 3/4/26	Wed 3/4/26	0%
104	Testing (Bacti Samples / Desity Tests)	10 days	Mon 1/19/26	Fri 1/30/26	Thu 3/12/26	Wed 3/25/26	0%
105	Release of Lien	1 day	Mon 1/19/26	Mon 1/19/26	Thu 3/12/26	Thu 3/12/26	0%
106	HRS Certification (Submission)	4 wks	Mon 2/2/26	Fri 2/27/26	Thu 3/26/26	Wed 4/22/26	0%
107	DERM Certification (Submittion)	4 wks	Thu 2/26/26	Wed 3/25/26	Wed 4/15/26	Tue 5/12/26	0%
108	Water Meter Installation /Owner	3 days	Mon 3/2/26	Wed 3/4/26	Thu 4/23/26	Mon 4/27/26	0%
109	Final Asbuilts (For Close-outs)	5 days	Thu 3/5/26	Wed 3/11/26	Tue 4/28/26	Mon 5/4/26	0%
110	**Shell Construction**	**374 days**	**Mon 6/2/25**	**Fri 6/12/26**	**Tue 1/14/25**	**Fri 6/19/26**	**53%**
111	Mobilize	3 days	Mon 6/2/25	Wed 6/4/25	Mon 4/21/25	Thu 4/24/25	100%
112	**CONCRETE SCOPE**	**34 days**	**Thu 6/5/25**	**Wed 7/16/25**	**Thu 4/24/25**	**Tue 6/10/25**	**100%**

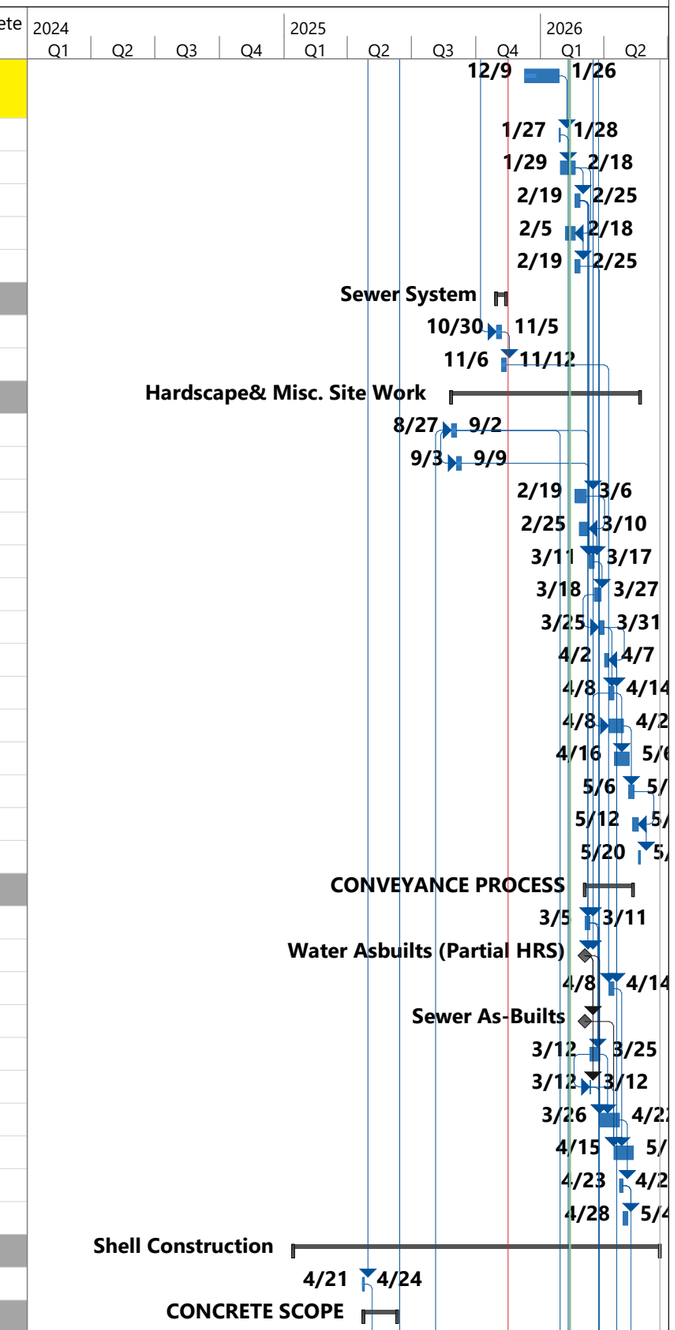

RYCON Construction Inc.

Construction Schedule
Public Storage - Aventura

Public Storage

Thu 2/12/26

ID	Task Name	Duration	Contract Start	Contract Finish	Projected Start	Projected Finish	% Complete
113	Install Footings & Elevator Pits	10 days	Thu 6/5/25	Wed 6/25/25	Thu 4/24/25	Thu 5/8/25	100%
114	Plumbing UG	21 days	N/A	N/A	Thu 4/24/25	Thu 5/22/25	100%
115	Electrical UG	10 days	N/A	N/A	Wed 4/30/25	Tue 5/13/25	100%
116	Elevator Pit Waterproofing	6 days	N/A	N/A	Fri 5/9/25	Fri 5/16/25	100%
117	**Prep and Pour Building Slab With Private Party Inspector**	**17 days**	**Thu 6/26/25**	**Wed 7/16/25**	**Mon 5/19/25**	**Tue 6/10/25**	**100%**
118	**WEATHER DELAY**	**2 days**			**Tue 6/3/25**	**Wed 6/4/25**	**100%**
119	PREP & POUR 1	12 days	Thu 6/26/25	Wed 7/2/25	Mon 5/19/25	Fri 6/6/25	100%
120	PREP & POUR 2	3.8 days	Thu 7/10/25	Wed 7/16/25	Fri 5/30/25	Tue 6/10/25	100%
121	STEEL DELIVERY - Columns	0 days	Thu 6/12/25	Thu 6/12/25	Wed 6/11/25	Wed 6/11/25	100%
122	STEEL DELIVERY - Decking	2 days	N/A	N/A	Tue 6/24/25	Wed 6/25/25	100%
123	Steel Core Erection (Roof, 5th, 4th floor, 3rd floor, 2nd Floor)	22.6 wks	Thu 7/17/25	Wed 12/3/25	Wed 6/11/25	Fri 11/14/25	100%
124	CMU Cores	94 days		Mon 11/10/25	Thu 6/26/25	Wed 11/5/25	100%
125	Pour 2nd , 3rd Floor slabs	19 days	Tue 7/15/25	Fri 12/5/25	Mon 7/21/25	Thu 8/14/25	100%
126	X Bracing and Misc Connections	6 days	Thu 12/4/25	Wed 12/24/25	Thu 7/17/25	Wed 11/26/25	100%
127	Pour 4th, 5th floor slab and roof deck	30 days	Mon 12/8/25	Mon 1/12/26	Wed 9/3/25	Tue 10/14/25	100%
128	Exterior Framing / Sheathing	56 days	Mon 12/8/25	Fri 2/13/26	Fri 8/8/25	Fri 2/6/26	75%
129	**WEATHER DELAY**	**1 day**	**N/A**	**N/A**	**Wed 9/10/25**	**Wed 9/10/25**	**100%**
130	Fireproofing Steel Members Floors 1 - 4	95 days	N/A	N/A	Wed 9/17/25	Tue 1/27/26	100%
131	**WEATHER DELAY**	**1 day**	**N/A**	**N/A**	**Thu 9/18/25**	**Thu 9/18/25**	**100%**
132	Interior LGF Framing	16 wks	Thu 12/4/25	Wed 3/25/26	Thu 7/24/25	Tue 3/10/26	95%
133	Install Roofing	35 days	Tue 1/13/26	Mon 2/9/26	Thu 12/18/25	Wed 2/4/26	50%
134	Fireproofing - 5th Floor Deck & Steel Members	3 wks	N/A	N/A	Thu 2/5/26	Wed 2/25/26	0%
135	Exterior Paint / Finishes	50 days	Mon 2/2/26	Fri 4/10/26	Tue 2/10/26	Mon 4/20/26	0%
136	**Hallway System Material Delivery - 2nd & 3rd Floor**	**2 days**	**N/A**	**N/A**	**Tue 1/14/25**	**Wed 1/15/25**	**100%**
137	**Hallway System (By Owner)**	**18 wks**	**Thu 11/6/25**	**Wed 4/29/26**	**Mon 1/19/26**	**Fri 5/22/26**	**0%**
138	Fire Sprinkler Overhead	16 days	Mon 12/8/25	Fri 1/16/26	Mon 8/4/25	Fri 12/12/25	100%
139	HVAC Ductwork	16 wks			Thu 11/27/25	Wed 3/18/26	70%
140	Install HVAC Units	15 days	Tue 2/10/26	Mon 2/23/26	Thu 2/5/26	Wed 2/25/26	0%
141	Install Elevators	12 wks	Fri 2/13/26	Thu 4/23/26	Thu 2/5/26	Wed 4/29/26	0%
142	Exterior Storefront& Windows, & Louvers	25 days	Mon 2/16/26	Fri 3/20/26	Fri 3/13/26	Thu 4/16/26	0%
143	Install electrical OH fixtures and power to shell	30 days	Thu 3/5/26	Wed 4/29/26	Wed 3/11/26	Tue 4/21/26	0%
144	Install FA System	35 days	Thu 3/12/26	Wed 4/29/26	Wed 3/18/26	Tue 5/5/26	0%
145	Misc. Exterior Items	25 days	Mon 3/30/26	Fri 5/1/26	Tue 4/21/26	Mon 5/25/26	0%
146	**Delay - FPL Tranformer (On Going)**	**80 days**	**N/A**	**N/A**	**Wed 10/1/25**	**Tue 1/20/26**	**0%**
147	Install Transformer (Owner)	5 days	Mon 12/1/25	Fri 12/5/25	Thu 1/29/26	Wed 2/4/26	0%
148	Temp For Test	5 days	Thu 3/5/26	Wed 3/11/26	Wed 3/11/26	Tue 3/17/26	0%
149	Install Electric Meter	1 day	Thu 3/19/26	Thu 3/19/26	Wed 3/25/26	Wed 3/25/26	0%
150	**Shell Completion**	**0 days**	**Fri 5/1/26**	**Fri 5/1/26**	**Mon 5/25/26**	**Mon 5/25/26**	**0%**
151	**Offices**	**169 days**	**Mon 9/8/25**	**Wed 3/11/26**	**Wed 7/30/25**	**Mon 3/23/26**	**50%**

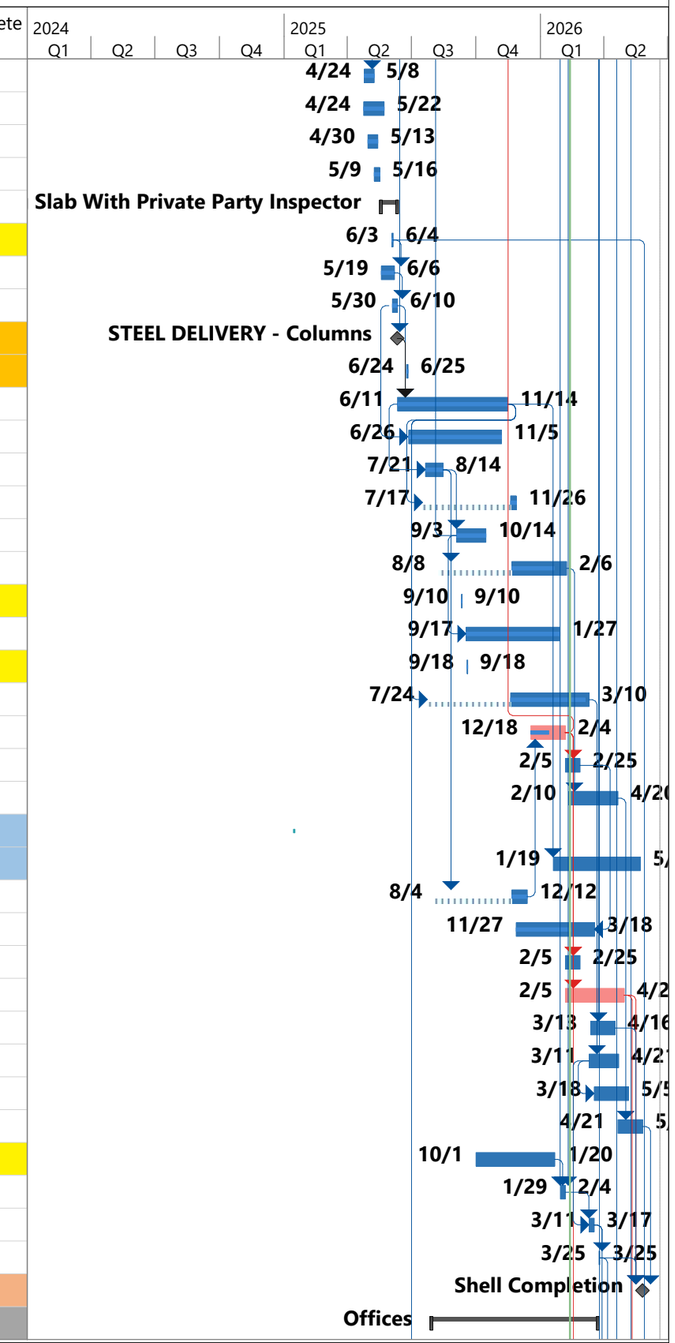

RYCON Construction Inc.

Construction Schedule
Public Storage - Aventura

Public Storage

Thu 2/12/26

ID	Task Name	Duration	Contract Start	Contract Finish	Projected Start	Projected Finish	% Complete
152	Install of HVAC & Fans	0 days	Mon 9/8/25	Mon 9/8/25	Thu 2/5/26	Thu 2/5/26	0%
153	MEP HookUp HVAC Units	10 days	Tue 9/9/25	Mon 9/22/25	Fri 2/6/26	Thu 2/19/26	0%
154	Start-Up RTUs	0 days	Wed 3/11/26	Wed 3/11/26	Tue 3/17/26	Tue 3/17/26	0%
155	T&B	3 days	N/A	N/A	Thu 3/19/26	Mon 3/23/26	0%
156	Layout Walls	0 days	Thu 12/4/25	Fri 12/5/25	Wed 7/30/25	Fri 8/1/25	100%
157	Trench Slab	3 days	Mon 12/8/25	Wed 12/10/25	Mon 8/4/25	Wed 8/6/25	100%
158	Plumbing & Electrical UG	5 days	Thu 12/11/25	Wed 12/17/25	Thu 8/7/25	Wed 8/13/25	100%
159	Trench Pourback	3 days	Thu 12/18/25	Mon 12/22/25	Thu 8/14/25	Mon 8/18/25	100%
160	Framing	10 days	Tue 12/23/25	Mon 1/5/26	Tue 8/19/25	Mon 9/1/25	100%
161	Electrical Rough	5 days	Tue 12/30/25	Mon 1/5/26	Tue 8/26/25	Mon 9/1/25	100%
162	Rough Plumbing	5 days	Tue 12/30/25	Mon 1/5/26	Tue 8/26/25	Mon 9/1/25	100%
163	Overhead MEP Rough	45 days	Mon 12/8/25	Fri 12/19/25	Mon 8/4/25	Fri 10/24/25	100%
164	MEP In-wall Rough	5 days	Tue 12/30/25	Mon 1/5/26	Mon 8/4/25	Fri 12/19/25	100%
165	Inwall Inspection	0 days	Mon 1/5/26	Mon 1/5/26	Fri 1/23/26	Fri 1/23/26	0%
166	Double Side walls	10 days	Tue 1/6/26	Mon 1/19/26	Mon 1/26/26	Fri 2/6/26	0%
167	Tape / Finish Walls	10 days	Tue 1/13/26	Mon 1/26/26	Mon 2/2/26	Fri 2/13/26	0%
168	Install Door Frames	5 days	Tue 1/20/26	Mon 1/26/26	Mon 2/9/26	Fri 2/13/26	0%
169	Paint walls (Prime)	3 days	Fri 1/16/26	Tue 1/20/26	Thu 2/5/26	Mon 2/9/26	0%
170	Ceiling Grid	3 days	Wed 1/21/26	Fri 1/23/26	Tue 2/10/26	Thu 2/12/26	0%
171	Final Paint	3 days	Mon 1/26/26	Wed 1/28/26	Fri 2/13/26	Tue 2/17/26	0%
172	Fire Sprinkler Drops	5 days	Mon 1/26/26	Fri 1/30/26	Fri 2/13/26	Thu 2/19/26	0%
173	Install Lights	5 days	Mon 1/26/26	Fri 1/30/26	Fri 2/13/26	Thu 2/19/26	0%
174	Drop Ceiling tile	3 days	Fri 1/30/26	Tue 2/3/26	Thu 2/19/26	Mon 2/23/26	0%
175	Install Flooring	7 days	Tue 1/27/26	Wed 2/4/26	Mon 2/16/26	Tue 2/24/26	0%
176	Install Millwork	3 days	Thu 1/29/26	Mon 2/2/26	Wed 2/18/26	Fri 2/20/26	0%
177	Install Plumbing Fixtures	3 days	Fri 1/30/26	Tue 2/3/26	Thu 2/19/26	Mon 2/23/26	0%
178	Install Toilet Partitions	3 days	Mon 2/2/26	Wed 2/4/26	Fri 2/20/26	Tue 2/24/26	0%
179	MEP Trim Out	3 days	Fri 1/23/26	Tue 1/27/26	Thu 2/12/26	Mon 2/16/26	0%
180	Install Doors & Hardware	3 days	Fri 1/30/26	Tue 2/3/26	Thu 2/19/26	Mon 2/23/26	0%
181							
182	**Final Inspections**	**62 days**	**Wed 1/28/26**	**Fri 6/19/26**	**Thu 3/26/26**	**Fri 6/19/26**	**0%**
183							
184	Photometric Inspection / Certification	3 days	Mon 5/4/26	Wed 5/6/26	Wed 4/8/26	Fri 4/10/26	0%
185	Final Mechanical	1 day	Wed 1/28/26	Wed 1/28/26	Fri 3/27/26	Fri 3/27/26	0%
186	Fire Pump Certification	5 days	Thu 3/12/26	Wed 3/18/26	Thu 3/26/26	Wed 4/1/26	0%
187	Final Sprinkler	1 day	Thu 3/19/26	Thu 3/19/26	Thu 4/2/26	Thu 4/2/26	0%
188	Final Plumbing	1 day	Tue 4/7/26	Tue 4/7/26	Tue 4/28/26	Tue 4/28/26	0%
189	Final Electrical & Fire Alarm	3 days	Thu 5/7/26	Mon 5/11/26	Thu 4/30/26	Mon 5/4/26	0%
190	Final Fire	1 day	Tue 5/12/26	Tue 5/12/26	Tue 5/5/26	Tue 5/5/26	0%

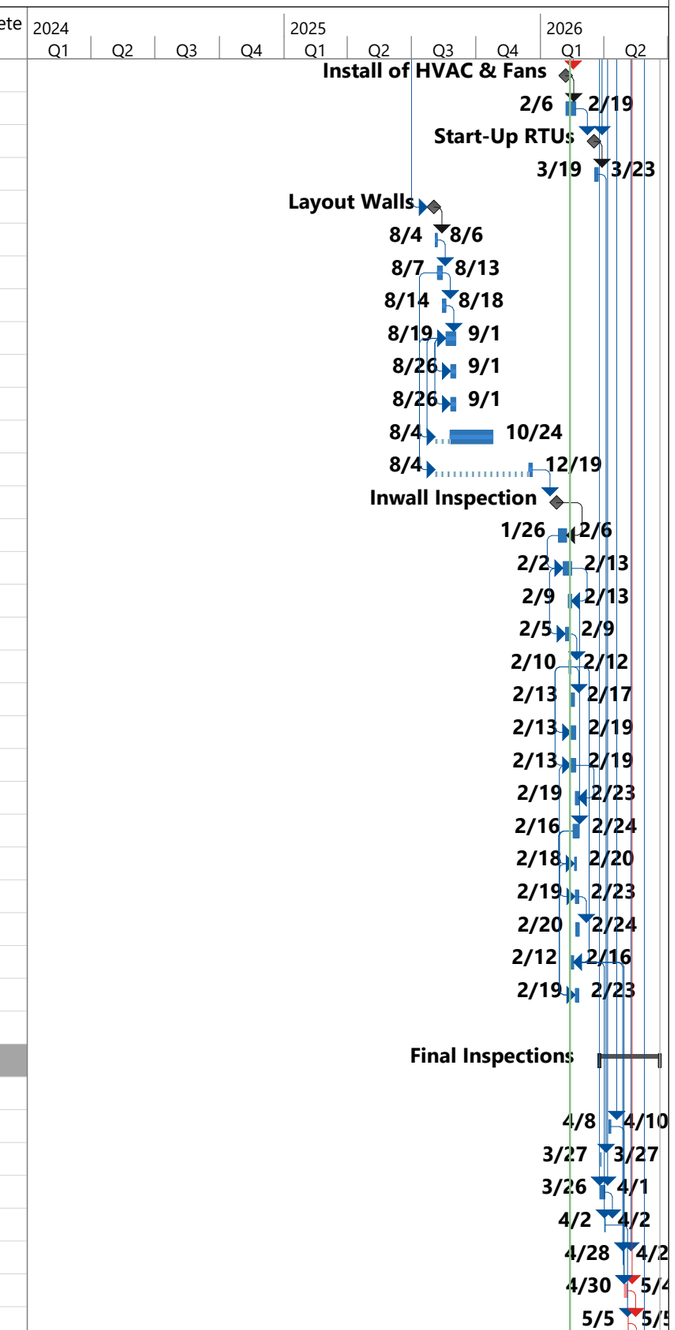

RYCON Construction Inc.

Construction Schedule
Public Storage - Aventura

Public Storage

Thu 2/12/26
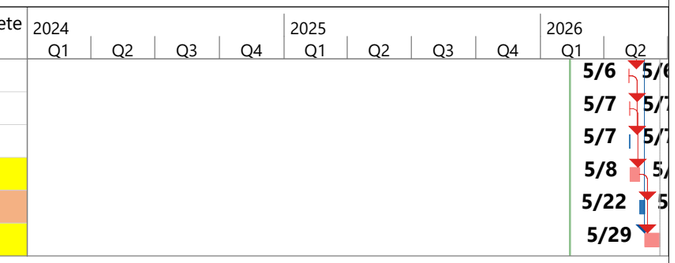
ID	Task Name	Duration	Contract Start	Contract Finish	Projected Start	Projected Finish	% Complete
191	Final Building	1 day	Wed 5/13/26	Wed 5/13/26	Wed 5/6/26	Wed 5/6/26	0%
192	Final Zoning	1 day	Thu 5/14/26	Thu 5/14/26	Thu 5/7/26	Thu 5/7/26	0%
193	Public Works Release (DERM)	1 day	Thu 5/14/26	Thu 5/14/26	Thu 5/7/26	Thu 5/7/26	0%
194	**Obtain Certificate of Completion**	**10 days**	**Fri 5/15/26**	**Thu 5/28/26**	**Fri 5/8/26**	**Thu 5/21/26**	**0%**
195	PCCO #009 - Veneer Window Attachment Changes	5 days	05/29/2026	06/05/2026	Fri 5/22/26	Thu 5/28/26	0%
196	**Weather Delay Allowance**	**16 days**	**06/08/2026**	**06/24/2026**	**Fri 5/29/26**	**Fri 6/19/26**	**0%**
