Public Storage
Davenport

ID	Task Name	Duration	Start	Finish	Remaining Duration	Physical % Complete	Actual Start	Actual Finish
0	**Overall Construction Schedule**	**343 days**	**Wed 7/9/25**	**Fri 10/30/26**	**284.67 days**	**0%**	**Wed 7/9/25**	**NA**
1	**Contract Administration**	**40 days**	**Wed 7/9/25**	**Tue 9/2/25**	**0 days**	**0%**	**Wed 7/9/25**	**Tue 9/2/25**
2	Notice to Proceed	34 days	Wed 7/9/25	Mon 8/25/25	0 days	100%	Wed 7/9/25	Mon 8/25/25
3	Mobilization	1 day	Tue 8/26/25	Tue 9/2/25	0 days	100%	Tue 8/26/25	Tue 9/2/25
4	**Procurement**	**291 days**	**Thu 8/7/25**	**Thu 9/17/26**	**239.1 days**	**0%**	**Thu 8/7/25**	**NA**
313	**Pre-Installation Meetings**	**157 days**	**Tue 9/23/25**	**Wed 4/29/26**	**143.92 days**	**0%**	**Tue 9/23/25**	**NA**
314	Preinstallation Meeting for CIP Concrete	0 days	Tue 9/23/25	Thu 10/23/25	0 days	100%	Tue 9/23/25	Thu 10/23/25
315	Preinstallation Meeting, Cold Formed Metal Framing	1 day	Tue 12/16/25	Tue 12/16/25	0 days	100%	Tue 12/16/25	Tue 12/16/25
316	Preinstallation Meeting, Bituminous and Self-Adhering Waterproofing	0 days	Tue 9/23/25	Tue 9/23/25	0 days	100%	Tue 9/23/25	Tue 9/23/25
317	Preinstallation Meeting, Cold Fluid Applied Waterproofing	1 day	Tue 4/21/26	Tue 4/21/26	1 day	0%	NA	NA
318	Preinstallation Meeting, Hollow Metal Doors and Frames	1 day	Tue 3/24/26	Tue 3/24/26	1 day	0%	NA	NA
319	Preinstallation Meeting, Aluminum Frames and Storefronts	1 day	Tue 4/7/26	Tue 4/7/26	1 day	0%	NA	NA
320	Preinstallation Meeting, Metal Canopies	1 day	Tue 3/31/26	Tue 3/31/26	1 day	0%	NA	NA
321	Preinstallation Meeting, Hydraulic Passenger Elevator	1 day	Tue 3/3/26	Tue 3/3/26	1 day	0%	NA	NA
322	Preinstallation Meeting, Fencing	1 day	Tue 4/28/26	Tue 4/28/26	1 day	0%	NA	NA
323	Preinstallation Meeting, Security Wire Mesh Fence and Gates	1 day	Tue 4/28/26	Tue 4/28/26	1 day	0%	NA	NA
324	Preinstallation Meeting, Decorative Metal Fences and Gates	1 day	Tue 3/24/26	Tue 3/24/26	1 day	0%	NA	NA
325	Preinstallation Meeting, TPO Roofing/Sheet Metal Flashing & Trim	1 day	Tue 4/28/26	Tue 4/28/26	1 day	0%	NA	NA
326	Preinstallation Meeting, Stucco System	1 day	Wed 4/29/26	Wed 4/29/26	1 day	0%	NA	NA
327	Preinstallation Meeting, Architectural Concrete Sealing & Polishing	1 day	Wed 3/25/26	Wed 3/25/26	1 day	0%	NA	NA
328	**Sitework**	**164 days**	**Thu 7/24/25**	**Tue 3/10/26**	**49.2 days**	**0%**	**Thu 7/24/25**	**NA**
329	Complete Erosion Control Install	4 days	Thu 7/24/25	Mon 9/8/25	0 days	100%	Thu 7/24/25	Mon 9/8/25
330	Silt Fence Inspection	1 day	Tue 9/9/25	Tue 9/9/25	0 days	100%	Tue 9/9/25	Tue 9/9/25
331	Clear and Grub	0 days	Wed 9/3/25	Thu 9/18/25	0 days	100%	Wed 9/3/25	Thu 9/18/25
332	Install Temporary Fencing	1 day	Fri 10/3/25	Fri 10/3/25	0 days	100%	Fri 10/3/25	Fri 10/3/25
333	Mass Grade Site	14 days	Tue 9/16/25	Wed 10/8/25	0 days	100%	Tue 9/16/25	Wed 10/8/25
334	Construct Retention Pond	3 days	Fri 10/10/25	Thu 3/5/26	3 days	50%	Fri 10/10/25	NA
335	Storm Sewer	0 days	Fri 11/14/25	Fri 2/27/26	0 days	100%	Fri 11/14/25	Fri 2/27/26
336	Sanitary Sewer, Fire Line and domestic water	6 days	Fri 11/14/25	Tue 3/10/26	6 days	50%	Fri 11/14/25	NA
337	Grade for building pad	1 day	Wed 10/1/25	Wed 10/8/25	0 days	100%	Wed 10/1/25	Wed 10/8/25
338	**Building Pad Construction**	**43 days**	**Thu 10/9/25**	**Mon 12/8/25**	**0 days**	**0%**	**Thu 10/9/25**	**Mon 12/8/25**
339	Survey and Form Perimeter Walls of Building	10 days	Thu 10/9/25	Wed 10/22/25	0 days	100%	Thu 10/9/25	Wed 10/22/25
340	Concrete Footings for Columns	10 days	Tue 10/28/25	Fri 12/5/25	0 days	100%	Tue 10/28/25	Fri 12/5/25
341	Excavation for Elevator Pits	0 days	Tue 10/28/25	Fri 11/7/25	0 days	100%	Tue 10/28/25	Fri 11/7/25
342	Waterproofing of Below Elevator Pit Floors	3 days	Thu 11/6/25	Mon 11/10/25	0 days	100%	Thu 11/6/25	Mon 11/10/25
343	Construct Concrete Elevator Pit Floors and Sump Pits	0 days	Thu 11/6/25	Fri 11/7/25	0 days	100%	Thu 11/6/25	Fri 11/7/25
344	Form and Pour Elevator Pit Walls	2 days	Thu 11/6/25	Fri 11/7/25	0 days	100%	Thu 11/6/25	Fri 11/7/25
345	Underslab Plumbing Rough	0 days	Tue 11/11/25	Fri 11/21/25	0 days	100%	Tue 11/11/25	Fri 11/21/25
346	Fine Grade SOG-Place Stone	0 days	Thu 11/20/25	Mon 11/24/25	0 days	100%	Thu 11/20/25	Mon 11/24/25
347	Underslab Electrical Rough	0 days	Thu 10/30/25	Fri 12/5/25	0 days	100%	Thu 10/30/25	Fri 12/5/25
348	Vapor Barrier/Rebar for Slab on Grade	9 days	Tue 11/11/25	Fri 12/5/25	0 days	100%	Tue 11/11/25	Fri 12/5/25
349	Pour First Half of Slab on Grade	0 days	Sat 11/22/25	Sat 11/22/25	0 days	100%	Sat 11/22/25	Sat 11/22/25
350	Pour Second Half of Slab on Grade	0 days	Sat 12/6/25	Sat 12/6/25	0 days	100%	Sat 12/6/25	Sat 12/6/25
351	Backfill Around Slab on Grade	1 day	Mon 12/8/25	Mon 12/8/25	0 days	100%	Mon 12/8/25	Mon 12/8/25
352	**Building Construction**	**179 days**	**Wed 12/10/25**	**Mon 8/17/26**	**166.92 days**	**0%**	**Wed 12/10/25**	**NA**
353	Hollow metal frames to job site for CMU	0 days	Wed 12/10/25	Wed 12/10/25	0 days	100%	Wed 12/10/25	Wed 12/10/25
354	Construct First Lift of Elevators/Stair Tower CMU	0 days	Thu 12/11/25	Wed 12/31/25	0 days	100%	Thu 12/11/25	Wed 12/31/25
355	Construct Exterior CMU Walls - SOG to 2nd Floor	0 days	Thu 12/11/25	Thu 1/15/26	0 days	100%	Thu 12/11/25	Thu 1/15/26
356	Install Hollow Metal Frames in CMU - 1st Floor	1 day	Wed 12/10/25	Wed 12/10/25	0 days	100%	Wed 12/10/25	Wed 12/10/25
357	Grout First Lift of CMU at Elevators/Stair Towers	1 day	Wed 12/31/25	Wed 12/31/25	0 days	100%	Wed 12/31/25	Wed 12/31/25

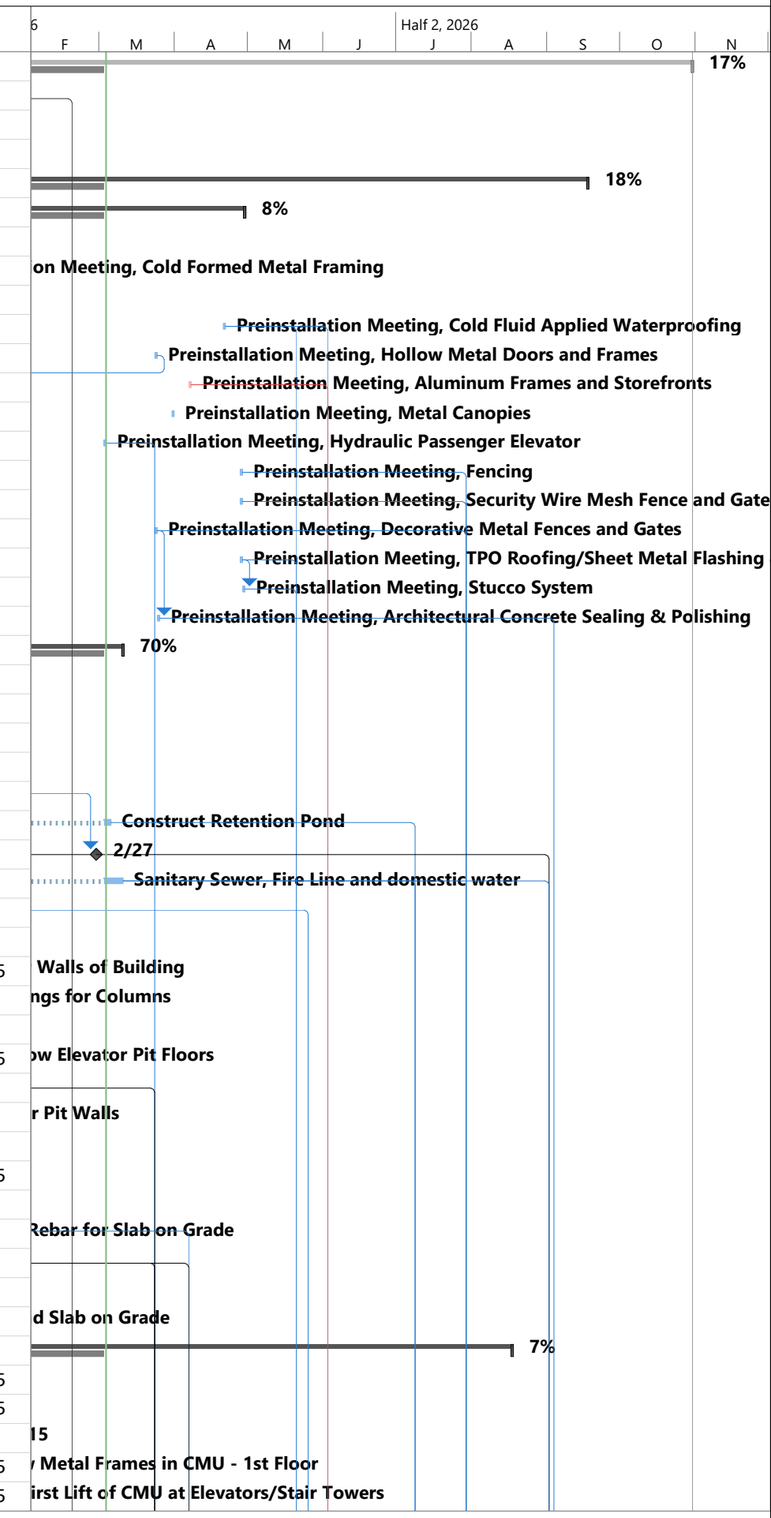

Public Storage
Davenport

ID	Task Name	Duration	Start	Finish	Remaining Duration	Physical % Complete	Actual Start	Actual Finish
358	Construct Second Lift of Elevators/Stair Tower CMU	8 days	Thu 1/15/26	Thu 3/12/26	8 days	75%	Thu 1/15/26	NA
359	Install Hollow Metal Frames in Stair Towers - 2nd Floor	1 day	Wed 2/25/26	Wed 2/25/26	0 days	100%	Wed 2/25/26	Wed 2/25/26
360	Grout Second Lift of CMU at Elevators/Stair Towers	1 day	Thu 2/19/26	Thu 2/26/26	0 days	100%	Thu 2/19/26	Thu 2/26/26
361	Construct Final Lift of Elevators/Stair Tower CMU	8 days	Tue 3/3/26	Thu 3/12/26	8 days	0%	NA	NA
362	Install Hollow Metal Frame in Stair Towers - 3rd Floor	1 day	Tue 3/3/26	Tue 3/3/26	1 day	0%	NA	NA
363	Grout Final Lift of CMU at Elevators/Stair Towers	2 days	Tue 3/24/26	Wed 3/25/26	2 days	0%	NA	NA
364	1st floor structure erection/decking	5 days	Wed 1/7/26	Thu 2/12/26	0 days	100%	Wed 1/7/26	Thu 2/12/26
365	2nd floor SOD-Prep/wire install/Pour	8 days	Wed 1/21/26	Sat 2/21/26	0 days	100%	Wed 1/21/26	Sat 2/21/26
366	2nd floor SOD-Pour Completed	0 days	Sat 2/21/26	Sat 2/21/26	0 days	100%	Sat 2/21/26	Sat 2/21/26
367	Construct Exterior CMU Walls - 2nd to 3rd floor	10 days	Thu 1/15/26	Mon 3/16/26	10 days	75%	Thu 1/15/26	NA
368	2nd floor-structure erection	12 days	Mon 2/16/26	Wed 3/18/26	12 days	50%	Mon 2/16/26	NA
369	3rd floor-SOD prep/wire install/Pour	7 days	Thu 3/19/26	Fri 3/27/26	7 days	0%	NA	NA
370	3rd floor-SOD Pour Completed	0 days	Fri 3/27/26	Fri 3/27/26	0 days	0%	NA	NA
371	Install stairs in stair towers	7 days	Tue 4/7/26	Wed 4/15/26	7 days	0%	NA	NA
372	Install Railings	8 days	Thu 4/16/26	Mon 4/27/26	8 days	0%	NA	NA
373	3rd Floor - Construct CMU walls from 3rd Floor to Roof	15 days	Mon 4/6/26	Fri 4/24/26	15 days	0%	NA	NA
374	3rd floor structure erection & Roof	25 days	Thu 4/16/26	Wed 5/20/26	25 days	0%	NA	NA
375	Install TPO Roofing	7 days	Thu 5/21/26	Fri 5/29/26	7 days	0%	NA	NA
376	Roofing Complete - Building Dry-In	0 days	Mon 6/1/26	Mon 6/1/26	0 days	0%	NA	NA
377	EIFS/Stucco	35 days	Thu 5/21/26	Wed 7/8/26	35 days	0%	NA	NA
378	Storefront Frames Install	10 days	Wed 6/3/26	Tue 6/16/26	10 days	0%	NA	NA
379	Storefront Glass Installed	10 days	Wed 7/1/26	Tue 7/14/26	10 days	0%	NA	NA
380	Stanley Sliding Door Install	1 day	Mon 6/1/26	Mon 6/1/26	1 day	0%	NA	NA
381	Canopies	8 days	Thu 6/18/26	Mon 6/29/26	8 days	0%	NA	NA
382	Install Metal Coping/Downspouts/Trim	6 days	Wed 7/15/26	Wed 7/22/26	6 days	0%	NA	NA
383	Exterior Building Caulking	5 days	Thu 7/23/26	Wed 7/29/26	5 days	0%	NA	NA
384	Exterior Building Punchlist	5 days	Thu 7/30/26	Wed 8/5/26	5 days	0%	NA	NA
385	Light gauge office framing	5 days	Thu 5/21/26	Wed 5/27/26	5 days	0%	NA	NA
386	Elevator #1 Install	20 days	Tue 6/23/26	Mon 7/20/26	20 days	0%	NA	NA
387	Elevator #2 install	20 days	Tue 7/21/26	Mon 8/17/26	20 days	0%	NA	NA
388	Building Façade Complete	0 days	Wed 7/22/26	Wed 7/22/26	0 days	0%	NA	NA
389	**Site Utlities/As-Builts**	**216 days**	**Thu 11/20/25**	**Thu 9/17/26**	**180.69 days**	**0%**	**Thu 11/20/25**	**NA**
390	Electrical Gear Procurement	0 days	Thu 11/20/25	Fri 1/30/26	0 days	100%	Thu 11/20/25	Fri 1/30/26
391	Procure Transformer	60 days	Wed 2/18/26	Mon 5/25/26	60 days	10%	Wed 2/18/26	NA
392	Install Primary Power Conduits to Transformer	17 days	Fri 1/23/26	Mon 2/16/26	0 days	100%	Fri 1/23/26	Mon 2/16/26
393	Install Secondary Power Conduits from Building to Transfomer	0 days	Mon 1/5/26	Mon 2/2/26	0 days	100%	Mon 1/5/26	Mon 2/2/26
394	Set Transformer	5 days	Tue 5/26/26	Mon 6/1/26	5 days	0%	NA	NA
395	Permanent Power to Building	10 days	Tue 6/2/26	Mon 6/15/26	10 days	0%	NA	NA
396	As-Built Drawings for Sanitary and Storm Water	12 days	Wed 9/2/26	Thu 9/17/26	12 days	0%	NA	NA
397	**Rough-ins and Finishes**	**161 days**	**Thu 2/19/26**	**Thu 10/1/26**	**161 days**	**0%**	**Thu 2/19/26**	**NA**
398	1st Floor Electrical/Fire Alarm Rough In	15 days	Thu 2/19/26	Mon 5/25/26	15 days	0%	Thu 2/19/26	NA
399	1st Floor HVAC Rough In	15 days	Tue 2/24/26	Mon 5/4/26	15 days	0%	Tue 2/24/26	NA
400	1st Floor Sprinkler Rough-in/riser room-1st floor	12 days	Tue 3/3/26	Wed 4/22/26	12 days	0%	Tue 3/3/26	NA
401	1st Floor HVAC Trim/Line Set	10 days	Tue 5/26/26	Mon 6/8/26	10 days	0%	NA	NA
402	1st Floor Plumbing rough walls	5 days	Tue 6/9/26	Mon 6/15/26	5 days	0%	NA	NA
403	1st Floor Hallway System- by Janus	20 days	Tue 6/16/26	Mon 7/13/26	20 days	0%	NA	NA
404	1st Floor Electrical Trim/FA/Hang Lights	7 days	Tue 7/14/26	Wed 7/22/26	7 days	0%	NA	NA
405	2nd Floor HVAC Rough In	15 days	Thu 5/21/26	Wed 6/10/26	15 days	0%	NA	NA
406	2nd Floor Electrical/Fire Alarm Rough In	15 days	Thu 6/11/26	Wed 7/1/26	15 days	0%	NA	NA
407	2nd Floor Sprinkler Rough-in	7 days	Thu 6/4/26	Fri 6/12/26	7 days	0%	NA	NA

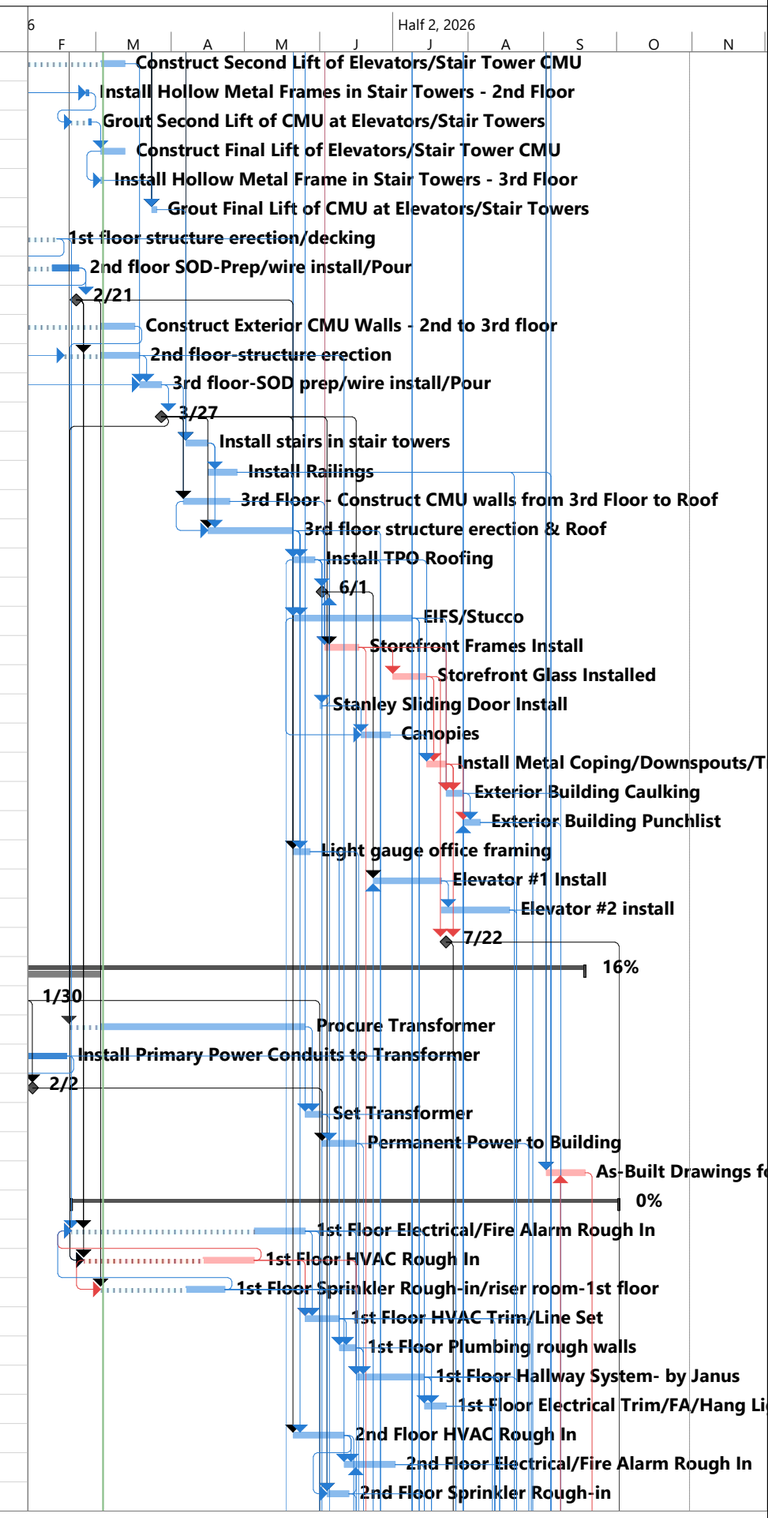

Public Storage
Davenport

ID	Task Name	Duration	Start	Finish	Remaining Duration	Physical % Complete	Actual Start	Actual Finish
408	2nd Floor HVAC Trim/Line Sets	10 days	Mon 6/15/26	Fri 6/26/26	10 days	0%	NA	NA
409	2nd Floor Hallway System - by Janus	20 days	Tue 7/14/26	Mon 8/10/26	20 days	0%	NA	NA
410	2nd Floor Electrical Trim/FA/Hang Light-2nd Floor	7 days	Tue 8/11/26	Wed 8/19/26	7 days	0%	NA	NA
411	Install Gear in Electrical Room	10 days	Mon 6/1/26	Fri 6/12/26	10 days	0%	NA	NA
412	Power to elevator machine rooms	2 days	Tue 6/16/26	Wed 6/17/26	2 days	0%	NA	NA
413	3rd Floor HVAC Rough In	15 days	Tue 5/26/26	Mon 6/15/26	15 days	0%	NA	NA
414	3rd Floor Electrical/Fire Alarm Rough In	15 days	Fri 6/5/26	Thu 6/25/26	15 days	0%	NA	NA
415	3rd Floor Sprinkler Rough-in	5 days	Fri 6/26/26	Thu 7/2/26	5 days	0%	NA	NA
416	3rd Floor HVAC Trim/Line Sets	10 days	Fri 7/3/26	Thu 7/16/26	10 days	0%	NA	NA
417	3rd Floor Hallway System-by Janus	20 days	Fri 7/17/26	Thu 8/13/26	20 days	0%	NA	NA
418	3rd Floor Electrical Trim/FA/Hang Lights	7 days	Fri 8/14/26	Mon 8/24/26	7 days	0%	NA	NA
419	Install Aluminum Wainscot at Elevator Lobbies	5 days	Fri 8/14/26	Thu 8/20/26	5 days	0%	NA	NA
420	Office Buildout	40 days	Wed 6/17/26	Tue 8/11/26	40 days	0%	NA	NA
421	Initial BDA System Requirement Testing	1 day	Fri 8/14/26	Fri 8/14/26	1 day	0%	NA	NA
422	Install BDA System	10 days	Mon 8/31/26	Fri 9/11/26	10 days	0%	NA	NA
423	1st Floor Punchlist Repairs	5 days	Wed 8/12/26	Tue 8/18/26	5 days	0%	NA	NA
424	2nd Floor Punchlist Repairs	5 days	Fri 8/21/26	Thu 8/27/26	5 days	0%	NA	NA
425	3rd Floor Punchlist Repairs	5 days	Tue 8/25/26	Mon 8/31/26	5 days	0%	NA	NA
426	Complete Interior Punchlist Work - All Floors	2 days	Tue 9/1/26	Wed 9/2/26	2 days	0%	NA	NA
427	Final Clean/Floor Sealer	20 days	Fri 9/4/26	Thu 10/1/26	20 days	0%	NA	NA
428	HVAC Startup	6 days	Thu 8/27/26	Thu 9/3/26	6 days	0%	NA	NA
429	Install Plumbing Fixtures and Water Heaters	4 days	Fri 7/17/26	Wed 7/22/26	4 days	0%	NA	NA
430	Install Interior Signage	1 day	Thu 8/27/26	Thu 8/27/26	1 day	0%	NA	NA
431	Install Fire Extinguishers and Cabinets	1 day	Fri 8/14/26	Fri 8/14/26	1 day	0%	NA	NA
432	Final Painting, Stairs/Railings/Doors	5 days	Thu 8/20/26	Wed 8/26/26	5 days	0%	NA	NA
433	Wall Packs	3 days	Thu 7/9/26	Mon 7/13/26	3 days	0%	NA	NA
434	Elevator Trim out by Subs	3 days	Fri 8/21/26	Tue 8/25/26	3 days	0%	NA	NA
435	**Finsh Sitework - Dumpster/Sidewalks/Paving/Landscaping**	**76 days**	**Thu 7/9/26**	**Thu 10/22/26**	**76 days**	**0%**	**NA**	**NA**
436	Rough grade for landscaping	2 days	Thu 7/9/26	Fri 7/10/26	2 days	0%	NA	NA
437	Install Exterior Lighting in Parking Area	5 days	Mon 7/13/26	Fri 7/17/26	5 days	0%	NA	NA
438	Form and Pour Sidewalks	5 days	Thu 7/23/26	Wed 7/29/26	5 days	0%	NA	NA
439	Landscaping and Irrigation Installation	20 days	Mon 7/27/26	Fri 8/21/26	20 days	0%	NA	NA
440	Curb/Asphalt Paving	10 days	Mon 8/24/26	Fri 9/4/26	10 days	0%	NA	NA
441	Install Fencing	5 days	Thu 7/30/26	Wed 8/5/26	5 days	0%	NA	NA
442	Striping	1 day	Mon 9/7/26	Mon 9/7/26	1 day	0%	NA	NA
443	Landscaping As-Built Drawings	10 days	Mon 8/24/26	Fri 9/4/26	10 days	0%	NA	NA
444	Developer's Letter of Dedication	10 days	Mon 9/7/26	Fri 9/18/26	10 days	0%	NA	NA
445	Engineer's Certificate of Completion	5 days	Mon 9/7/26	Fri 9/11/26	5 days	0%	NA	NA
446	Contractor's Letter of Completion	2 days	Tue 9/8/26	Wed 9/9/26	2 days	0%	NA	NA
447	Satisfaction Letter/Email from FDOT and City for Infrastructure	10 days	Mon 9/7/26	Fri 9/18/26	10 days	0%	NA	NA
448	SOV for Site Utilites, Water, Wastewater, Reclaimed Water	10 days	Fri 9/18/26	Thu 10/1/26	10 days	0%	NA	NA
449	Polk County Final Walkthrough Request	5 days	Fri 10/2/26	Thu 10/8/26	5 days	0%	NA	NA
450	Polk County Approval of Site	10 days	Fri 10/9/26	Thu 10/22/26	10 days	0%	NA	NA
451	**Final Building Sign-Offs**	**37 days**	**Wed 8/26/26**	**Thu 10/15/26**	**37 days**	**0%**	**NA**	**NA**
452	Pre Closeout Meeting with AHJ	1 day	Fri 10/2/26	Fri 10/2/26	1 day	0%	NA	NA
453	Final BDA Test	1 day	Mon 9/14/26	Mon 9/14/26	1 day	0%	NA	NA
454	Elevator Ready for State Inspection	1 day	Wed 8/26/26	Wed 8/26/26	1 day	0%	NA	NA
455	Final Building Inspections	5 days	Fri 10/9/26	Thu 10/15/26	5 days	0%	NA	NA
456	Weather Days per Contract (20 Calendar Days)	15 days	Mon 10/12/26	Fri 10/30/26	15 days	0%	NA	NA
457	Substantial Completion	0 days	Fri 10/30/26	Fri 10/30/26	0 days	0%	NA	NA
