	Name	Duration: Current	Duration: Previous	Duration Diff	Baseline Start: Current	Baseline Start: Previous	Basel Start: Diff	Baseline Finish: Current	Baseline Finish: Previous	Baseline Finish: Diff
1	**Overall Project Duration - Public Storage - Delray Beach**	**414 days**	**414 days**	**0d**	**Fri 24/11/29**	**Fri 24/11/29**	**0d**	**Fri 26/07/03**	**Fri 26/07/03**	**0d**
2	Contract Award	35 days	35 days	0d	Fri 24/11/29	Fri 24/11/29	0d	Thu 25/01/16	Thu 25/01/16	0d
3	Release Subcontractors	10 days	10 days	0d	Fri 25/01/17	Fri 25/01/17	0d	Thu 25/01/30	Thu 25/01/30	0d
4	Obtain Vertical Building Pemit By Owner	1 day	1 day	0d	Mon 25/04/28	Mon 25/04/28	0d	Mon 25/04/28	Mon 25/04/28	0d
5	Obtain Water & Sewer Permit	1 day	1 day	0d	Tue 25/05/06	Tue 25/05/06	0d	Tue 25/05/06	Tue 25/05/06	0d
6	DELAY - Gopher Tortoise Relocation Permit - FWC	16 days	16 days	0d	Fri 25/05/09	Fri 25/05/09	0d	Fri 25/05/30	Fri 25/05/30	0d
7	DELAY - Gopher Tortoise Relocation	1 day	1 day	0d	Thu 25/06/12	Thu 25/06/12	0d	Thu 25/06/12	Thu 25/06/12	0d
8	City Precontruction Meeting	0 days	0 days	0d	Tue 25/07/01	Tue 25/07/01	0d	Tue 25/07/01	Tue 25/07/01	0d
9	**SUBMITTALS**	**345 days**	**352 days**	**-7d**	**Fri 24/12/06**	**Fri 24/12/06**	**0d**	**Thu 25/09/04**	**Thu 25/09/04**	**0d**
10	**Site Submittals**	**125 days**	**125 days**	**0d**	**Fri 25/01/24**	**Fri 25/01/24**	**0d**	**Tue 25/07/01**	**Tue 25/07/01**	**0d**
11	Storm Drainage& Sewer System Submittals	5,4 wks	5,4 wks	0d	Fri 25/01/24	Fri 25/01/24	0d	Mon 25/03/03	Mon 25/03/03	0d
12	Approval / EOR	40 days	40 days	0d	Tue 25/03/04	Tue 25/03/04	0d	Mon 25/04/28	Mon 25/04/28	0d
13	Revised Submittals	5 days	5 days	0d	Tue 25/04/29	Tue 25/04/29	0d	Mon 25/05/05	Mon 25/05/05	0d
14	Approval / EOR	8 days	8 days	0d	Tue 25/05/06	Tue 25/05/06	0d	Thu 25/05/15	Thu 25/05/15	0d
15	Fabricate and Deliver Structures	7,5 wks	7,5 wks	0d	Tue 25/05/27	Tue 25/05/27	0d	Tue 25/07/01	Tue 25/07/01	0d
16	**Fire Sprinkler Shop Drawings**	**84 days**	**84 days**	**0d**	**Fri 25/01/31**	**Fri 25/01/31**	**0d**	**Wed 25/07/09**	**Wed 25/07/09**	**0d**
17	Request& Receive CAD Files	55 days	55 days	0d	Fri 25/01/31	Fri 25/01/31	0d	Tue 25/02/04	Tue 25/02/04	0d
18	Shop Drawing Submittal	12 days	12 days	0d	Wed 25/02/05	Wed 25/02/05	0d	Tue 25/02/25	Tue 25/02/25	0d
19	Approval / AOR	17 days	17 days	0d	Wed 25/02/26	Wed 25/02/26	0d	Tue 25/03/11	Tue 25/03/11	0d
20	City Submission& Approval Estimated	0 days	0 days	0d	Tue 25/05/06	Tue 25/05/06	0d	Mon 25/06/23	Mon 25/06/23	0d
21	Fire Sprinkler Permit	10 days	10 days	0d	Thu 25/06/26	Thu 25/06/26	0d	Wed 25/07/09	Wed 25/07/09	0d
22	**Structural Steel Shop Drawings**	**150 days**	**150 days**	**0d**	**Fri 24/12/06**	**Fri 24/12/06**	**0d**	**Thu 25/07/03**	**Thu 25/07/03**	**0d**
23	Release Structural Steel Pkg	88 days	88 days	0d	Fri 24/12/06	Fri 24/12/06	0d	Tue 25/04/08	Tue 25/04/08	0d
24	Structural Steel Shop Drawings Submittal	0 days	0 days	0d	Fri 25/03/07	Fri 25/03/07	0d	Fri 25/03/07	Fri 25/03/07	0d
25	Approval / AOR	49 days	49 days	0d	Mon 25/03/10	Mon 25/03/10	0d	Thu 25/05/15	Thu 25/05/15	0d
26	Fabricate Steel Pkg	6 wks	6 wks	0d	Fri 25/05/23	Fri 25/05/23	0d	Thu 25/07/03	Thu 25/07/03	0d
27	**Cold Formed Framing**	**140 days**	**140 days**	**0d**	**Fri 25/01/31**	**Fri 25/01/31**	**0d**	**Thu 25/07/03**	**Thu 25/07/03**	**0d**
28	Release CFS Package	48 days	48 days	0d	Fri 25/01/31	Fri 25/01/31	0d	Tue 25/04/08	Tue 25/04/08	0d
29	Shop Drawings	0 days	0 days	0d	Mon 25/04/07	Mon 25/04/07	0d	Mon 25/04/07	Mon 25/04/07	0d
30	Approval / AOR	28 days	28 days	0d	Tue 25/04/08	Tue 25/04/08	0d	Thu 25/05/15	Thu 25/05/15	0d
31	Revised Submittals	4 days	4 days	0d	Fri 25/05/16	Fri 25/05/16	0d	Wed 25/05/21	Wed 25/05/21	0d
32	Approval / AOR	16 days	16 days	0d	Mon 25/05/19	Mon 25/05/19	0d	Mon 25/06/09	Mon 25/06/09	0d
33	Material Delivery	7 wks	7 wks	0d	Fri 25/05/16	Fri 25/05/16	0d	Thu 25/07/03	Thu 25/07/03	0d
34	**Concrete / Masonry Submittals**	**138 days**	**138 days**	**0d**	**Fri 25/01/31**	**Fri 25/01/31**	**0d**	**Fri 25/06/27**	**Fri 25/06/27**	**0d**
35	Footing Rebar Submittal	23 days	23 days	0d	Fri 25/01/31	Fri 25/01/31	0d	Tue 25/03/04	Tue 25/03/04	0d
36	Approval AOR	53 days	53 days	0d	Wed 25/03/05	Wed 25/03/05	0d	Fri 25/05/16	Fri 25/05/16	0d
37	Concrete mix Submittals	68 days	68 days	0d	Fri 25/01/31	Fri 25/01/31	0d	Thu 25/02/13	Thu 25/02/13	0d
38	Approval AOR	10 days	10 days	0d	Fri 25/02/14	Fri 25/02/14	0d	Thu 25/02/27	Thu 25/02/27	0d
39	CMU Submittals	81 days	81 days	0d	Fri 25/01/31	Fri 25/01/31	0d	Fri 25/05/23	Fri 25/05/23	0d
40	Approval AOR	11 days	11 days	0d	Mon 25/05/26	Mon 25/05/26	0d	Mon 25/06/09	Mon 25/06/09	0d
41	Release Rebar	15 days	15 days	0d	Mon 25/06/09	Mon 25/06/09	0d	Fri 25/06/27	Fri 25/06/27	0d
42	**Roofing**	**286 days**	**85 days**	**201d**	**Fri 25/01/17**	**Fri 25/01/17**	**0d**	**Mon 25/05/12**	**Mon 25/05/12**	**0d**
43	Roofing Submittal	30 days	30 days	0d	Fri 25/01/17	Fri 25/01/17	0d	Mon 25/03/03	Mon 25/03/03	0d
44	Approval / AOR	34 days	35 days	-1d	Tue 25/03/04	Tue 25/03/04	0d	Mon 25/03/17	Mon 25/03/17	0d
45	Release Roofing Material Production	5 days	5 days	0d	Fri 25/01/17	Fri 25/01/17	0d	Fri 25/01/17	Fri 25/01/17	0d
46	Fabricate & Deliver Roofing Material	5 wks	4 wks	5d	Tue 25/03/18	Tue 25/03/18	0d	Mon 25/05/12	Mon 25/05/12	0d
47	**Storefront & Window Shop drawings**	**145 days**	**156 days**	**-11d**	**Fri 25/01/31**	**Fri 25/01/31**	**0d**	**Tue 25/05/27**	**Tue 25/05/27**	**0d**
48	Storefront& Window Submittal	18 days	18 days	0d	Fri 25/01/31	Fri 25/01/31	0d	Tue 25/02/11	Tue 25/02/11	0d
49	Approval / AOR	32 days	32 days	0d	Wed 25/02/12	Wed 25/02/12	0d	Tue 25/02/25	Tue 25/02/25	0d

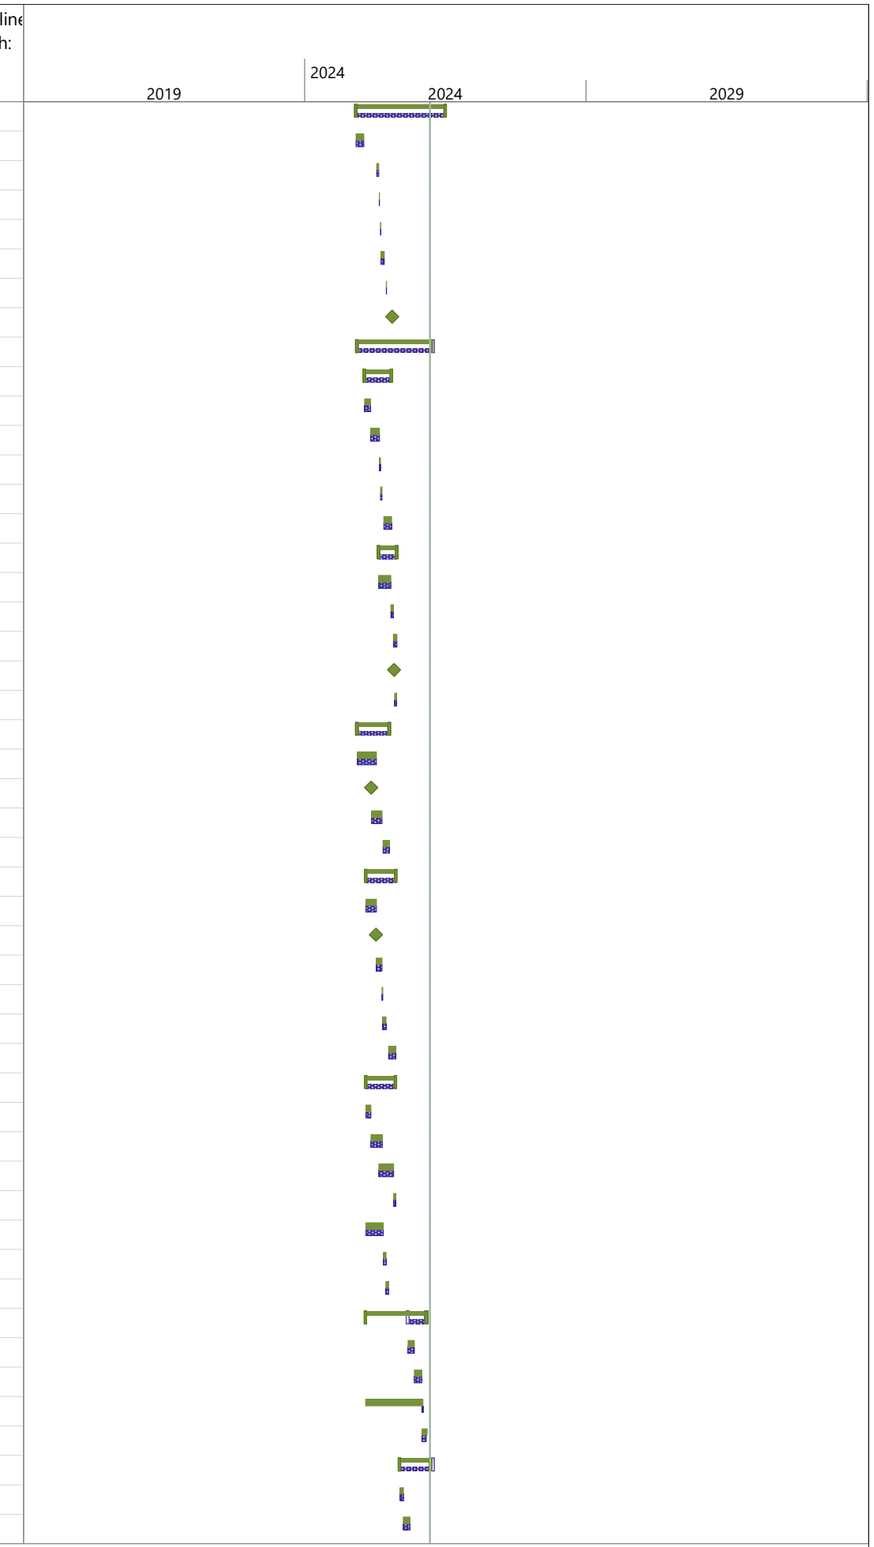

	Name	Duration: Current	Duration: Previous	Duration Diff	Baseline Start: Current	Baseline Start: Previous	Basel Start: Diff	Baseline Finish: Current	Baseline Finish: Previous	Baseline Finish: Diff
50	Glazing Samples	9 days	9 days	0d	NA	NA	0d	NA	NA	0d
51	Approval / AOR	14 days	15 days	-1d	NA	NA	0d	NA	NA	0d
52	City Submission& Approval	11 days	15 days	-4d	Wed 25/02/26	Wed 25/02/26	0d	Tue 25/03/25	Tue 25/03/25	0d
53	Fabrication	35 days	40 days	-5d	Wed 25/03/26	Wed 25/03/26	0d	Tue 25/05/27	Tue 25/05/27	0d
54	**HVAC Submittals**	**158 days**	**163 days**	**-5d**	**Fri 25/01/31**	**Fri 25/01/31**	**0d**	**Thu 25/08/28**	**Thu 25/08/28**	**0d**
55	Equipment, Air Distribution Submittals	10 days	10 days	0d	Fri 25/01/31	Fri 25/01/31	0d	Thu 25/02/20	Thu 25/02/20	0d
56	Approval / AOR & EOR	14 days	14 days	0d	Fri 25/02/21	Fri 25/02/21	0d	Thu 25/03/06	Thu 25/03/06	0d
57	Revised VRV Package - Rev 5	8 days	8 days	0d	NA	NA	0d	NA	NA	0d
58	Approval / AOR & EOR	10 days	10 days	0d	NA	NA	0d	NA	NA	0d
59	Additional Submittals Equipment Requested by EOR	55 days	55 days	0d	NA	NA	0d	NA	NA	0d
60	Approval / AOR & EOR	26 days	26 days	0d	NA	NA	0d	NA	NA	0d
61	3rd Revised Package Submitted - (Daikin Response)	1 day	1 day	0d	NA	NA	0d	NA	NA	0d
62	Approval AOR / EOR	10 days	10 days	0d	NA	NA	0d	NA	NA	0d
63	Fabricate and Delivery	5 wks	6 wks	-5d	Fri 25/03/07	Fri 25/03/07	0d	Thu 25/08/28	Thu 25/08/28	0d
64	**Electrical Submittals**	**197 days**	**197 days**	**0d**	**Fri 25/01/31**	**Fri 25/01/31**	**0d**	**Thu 25/09/04**	**Thu 25/09/04**	**0d**
65	Gear and Lighting Submittals	20 days	20 days	0d	Fri 25/01/31	Fri 25/01/31	0d	Thu 25/02/27	Thu 25/02/27	0d
66	Approval / EOR	10 days	10 days	0d	Fri 25/02/28	Fri 25/02/28	0d	Thu 25/03/13	Thu 25/03/13	0d
67	Fabricate and Delivery	21 wks	21 wks	0d	Fri 25/03/14	Fri 25/03/14	0d	Thu 25/09/04	Thu 25/09/04	0d
68	**Elevator Submittals**	**305 days**	**300 days**	**5d**	**Fri 25/01/31**	**Fri 25/01/31**	**0d**	**Fri 25/08/08**	**Fri 25/08/08**	**0d**
69	Submittals	13 days	13 days	0d	Fri 25/01/31	Fri 25/01/31	0d	Tue 25/02/18	Tue 25/02/18	0d
70	Approval / EOR	23 days	23 days	0d	Wed 25/02/19	Wed 25/02/19	0d	Fri 25/03/21	Fri 25/03/21	0d
71	Revised Submittals	77 days	77 days	0d	Fri 25/01/31	Fri 25/01/31	0d	Mon 25/05/19	Mon 25/05/19	0d
72	Approval / EOR	38 days	38 days	0d	Tue 25/05/20	Tue 25/05/20	0d	Mon 25/06/02	Mon 25/06/02	0d
73	Release Material form Sent to Schindler	1 day	1 day	0d	NA	NA	0d	NA	NA	0d
74	Fabricate and Delivery (Estimated)	19 wks	18 wks	5d	Mon 25/03/24	Mon 25/03/24	0d	Fri 25/08/08	Fri 25/08/08	0d
75	**Construction**	**268 days**	**268 days**	**0d**	**Tue 25/06/24**	**Tue 25/06/24**	**0d**	**Fri 26/07/03**	**Fri 26/07/03**	**0d**
76	**Overall Site Construction**	**249 days**	**241 days**	**8d**	**Tue 25/06/24**	**Tue 25/06/24**	**0d**	**Mon 26/05/11**	**Mon 26/05/11**	**0d**
77	Site Mobilization	4 days	4 days	0d	Tue 25/06/24	Tue 25/06/24	0d	Mon 25/07/07	Mon 25/07/07	0d
78	**Sitework**	**20 days**	**20 days**	**0d**	**Tue 25/06/24**	**Tue 25/06/24**	**0d**	**Mon 25/08/11**	**Mon 25/08/11**	**0d**
79	Build Construction Entrances	1 day	1 day	0d	Tue 25/06/24	Tue 25/06/24	0d	Wed 25/06/25	Wed 25/06/25	0d
80	Clear & Grub	7 days	7 days	0d	Thu 25/06/26	Thu 25/06/26	0d	Wed 25/07/09	Wed 25/07/09	0d
81	Erosion Control	1,3 days	1,3 days	0d	NA	NA	0d	NA	NA	0d
82	Site Survey& Layout (verify building pad)	3 days	3 days	0d	Thu 25/07/10	Thu 25/07/10	0d	Mon 25/07/14	Mon 25/07/14	0d
83	Construct Building Pad - Obtain Pad Certificate	6 days	6 days	0d	Tue 25/07/15	Tue 25/07/15	0d	Mon 25/07/28	Mon 25/07/28	0d
84	**Storm Drainage**	**141 days**	**148 days**	**-7d**	**Tue 25/10/07**	**Tue 25/10/07**	**0d**	**Tue 25/11/11**	**Tue 25/11/11**	**0d**
85	PENDING RFI #08 - DRAINAGE CONFLICT	10 days	10 days	0d	NA	NA	0d	NA	NA	0d
86	Drainage Revision #01 (Estimated)	16 days	16 days	0d	NA	NA	0d	NA	NA	0d
87	Drainage Revision #02 (Pricing Approval)	32 days	32 days	0d	NA	NA	0d	NA	NA	0d
88	Drainage Revision #02 - County Approval	11 days	15 days	-4d	NA	NA	0d	NA	NA	0d
89	Install Storm Structures	4 wks	4 wks	0d	Tue 25/10/07	Tue 25/10/07	0d	Mon 25/10/27	Mon 25/10/27	0d
90	Install storm pipe and exfiltration trenches	3,75 wks	3 wks	3,75d	Tue 25/10/21	Tue 25/10/21	0d	Mon 25/11/10	Mon 25/11/10	0d
91	Inspection	1 day	1 day	0d	Tue 25/11/11	Tue 25/11/11	0d	Tue 25/11/11	Tue 25/11/11	0d
92	**Sewer System**	**24 days**	**24 days**	**0d**	**Tue 25/11/11**	**Tue 25/11/11**	**0d**	**Mon 25/12/15**	**Mon 25/12/15**	**0d**
93	Tie into Existing Stub as required	1 day	1 day	0d	Tue 25/11/11	Tue 25/11/11	0d	Mon 25/11/17	Mon 25/11/17	0d
94	Install Sanitary Piping	21 days	21 days	0d	Tue 25/11/18	Tue 25/11/18	0d	Mon 25/12/15	Mon 25/12/15	0d
95	**Domestic Water Service**	**154 days**	**143 days**	**11d**	**Tue 25/12/16**	**Tue 25/12/16**	**0d**	**Mon 26/01/26**	**Mon 26/01/26**	**0d**
96	Water Main installation	4 wks	4 wks	0d	Tue 25/12/16	Tue 25/12/16	0d	Mon 25/12/29	Mon 25/12/29	0d
97	Tie-in to Existing Water Main	2 days	2 days	0d	Fri 26/01/23	Fri 26/01/23	0d	Mon 26/01/26	Mon 26/01/26	0d
98	PBCWUD - Preliminary AB Review & Approval	16 days	16 days	0d	NA	NA	0d	NA	NA	0d

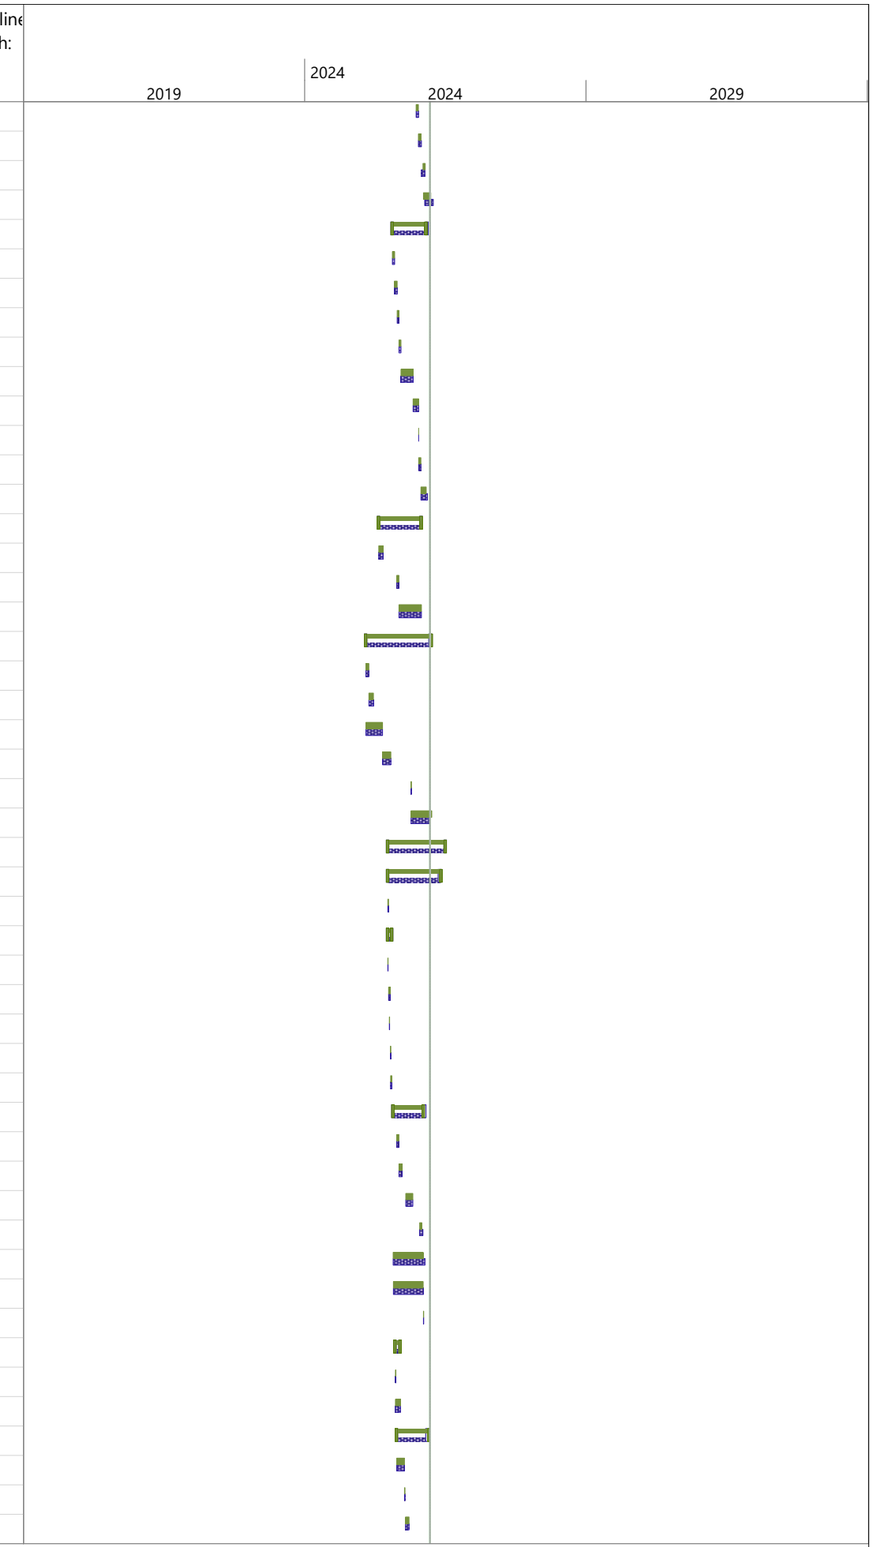

	Name	Duration: Current	Duration: Previous	Duration Diff	Baseline Start: Current	Baseline Start: Previous	Basel Start: Diff	Baseline Finish: Current	Baseline Finish: Previous	Baseline Finish: Diff
99	PBCWUD - S/S AB Hard Copy Submitted Review & Appro	23 days	23 days	0d	NA	NA	0d	NA	NA	0d
100	Building Water Services	5 days	10 days	-5d	Tue 25/12/30	Tue 25/12/30	0d	Mon 26/01/05	Mon 26/01/05	0d
101	PBCWUD - Revised AB (New comments provided)	15 days	20 days	-5d	NA	NA	0d	NA	NA	0d
102	Fire Line Underground w/ DDCV& FDC	3 days	3 days	0d	Tue 26/01/20	Tue 26/01/20	0d	Thu 26/01/22	Thu 26/01/22	0d
103	W&S AB After 1st Lift - Submitted to Civil EOR	1 day			NA			NA		
104	PBCWUD Review - W&S AB After 1st Lift	5 days			NA			NA		
105	**Hardscape& Misc. Site Work**	**54 days**	**60 days**	**-6d**	**Tue 26/02/17**	**Tue 26/02/17**	**0d**	**Mon 26/05/11**	**Mon 26/05/11**	**0d**
106	Primary Electrical Conduit	3 days	5 days	-2d	Tue 26/02/17	Tue 26/02/17	0d	Mon 26/02/23	Mon 26/02/23	0d
107	Site Lighting, brooks boxes,& Fixture Installation	5 days	5 days	0d	Tue 26/02/24	Tue 26/02/24	0d	Mon 26/03/02	Mon 26/03/02	0d
108	Fill balance of Site	3 days	15 days	-12d	Tue 26/02/17	Tue 26/02/17	0d	Mon 26/03/09	Mon 26/03/09	0d
109	Sub-base	4 days	10 days	-6d	Tue 26/02/24	Tue 26/02/24	0d	Mon 26/03/09	Mon 26/03/09	0d
110	Base	5 days	10 days	-5d	Tue 26/03/10	Tue 26/03/10	0d	Mon 26/03/23	Mon 26/03/23	0d
111	Asphalt (first lift)	5 days	8 days	-3d	Thu 26/03/19	Thu 26/03/19	0d	Mon 26/03/30	Mon 26/03/30	0d
112	Irrigation and ancillary conduit sleeves	7 days	5 days	2d	Tue 26/02/24	Tue 26/02/24	0d	Mon 26/03/02	Mon 26/03/02	0d
113	Concrete Curbs	6 days	8 days	-2d	Tue 26/03/24	Tue 26/03/24	0d	Thu 26/04/02	Thu 26/04/02	0d
114	Install Water Meter Boxes	2 days	5 days	-3d	Fri 26/03/27	Fri 26/03/27	0d	Thu 26/04/02	Thu 26/04/02	0d
115	Sidewalks	20 days	20 days	0d	Tue 26/03/31	Tue 26/03/31	0d	Mon 26/04/27	Mon 26/04/27	0d
116	Irrigation Installation	15 days	15 days	0d	Fri 26/04/03	Fri 26/04/03	0d	Thu 26/04/23	Thu 26/04/23	0d
117	Final Lift Asphalt	15 days	15 days	0d	Fri 26/04/17	Fri 26/04/17	0d	Thu 26/05/07	Thu 26/05/07	0d
118	Pavement Marking& Striping	5 days	5 days	0d	Tue 26/05/05	Tue 26/05/05	0d	Mon 26/05/11	Mon 26/05/11	0d
119	Jet Vac System	3 days	3 days	0d	Thu 26/05/07	Thu 26/05/07	0d	Mon 26/05/11	Mon 26/05/11	0d
120	**CONVEYANCE PROCESS**	**54 days**	**54 days**	**0d**	**Mon 25/12/29**	**Mon 25/12/29**	**0d**	**Mon 26/04/27**	**Mon 26/04/27**	**0d**
121	Water (Flush & Pressure Testing)	4 days	4 days	0d	Tue 26/01/27	Tue 26/01/27	0d	Fri 26/01/30	Fri 26/01/30	0d
122	Water Asbuilts (Partitial for HRS)	0 days	0 days	0d	Tue 26/02/03	Tue 26/02/03	0d	Tue 26/02/03	Tue 26/02/03	0d
123	Testing (Bacti Samples / Density Tests)	5 days	5 days	0d	Mon 26/02/09	Mon 26/02/09	0d	Fri 26/02/13	Fri 26/02/13	0d
124	Sewer Asbuilts	0 days	0 days	0d	Mon 25/12/29	Mon 25/12/29	0d	Mon 25/12/29	Mon 25/12/29	0d
125	Release of Lien	0 days	0 days	0d	Fri 26/02/20	Fri 26/02/20	0d	Fri 26/02/20	Fri 26/02/20	0d
126	HRS Certification (Submission)	6 wks	6 wks	0d	Mon 26/02/23	Mon 26/02/23	0d	Fri 26/04/03	Fri 26/04/03	0d
127	Sewer (Leakage & Lamping)	3 days	3 days	0d	Tue 26/03/17	Tue 26/03/17	0d	Thu 26/03/19	Thu 26/03/19	0d
128	DERM Certification (Submission)	6 wks	6 wks	0d	Tue 26/03/17	Tue 26/03/17	0d	Mon 26/04/27	Mon 26/04/27	0d
129	Water Meter Installation	5 days	5 days	0d	Mon 26/04/06	Mon 26/04/06	0d	Fri 26/04/10	Fri 26/04/10	0d
130	Final Asbuilts	1 day	1 day	0d	Fri 26/04/17	Fri 26/04/17	0d	Fri 26/04/17	Fri 26/04/17	0d
131	**Shell Construction**	**227 days**	**227 days**	**0d**	**Tue 25/07/29**	**Tue 25/07/29**	**0d**	**Wed 26/06/03**	**Wed 26/06/03**	**0d**
132	Building Mobilize	3 days	3 days	0d	Tue 25/07/29	Tue 25/07/29	0d	Thu 25/07/31	Thu 25/07/31	0d
133	Prep and Reinforce Perimeter Footings	10 days	10 days	0d	Fri 25/08/01	Fri 25/08/01	0d	Mon 25/08/11	Mon 25/08/11	0d
134	Pour Perimeter Footings	4 days	4 days	0d	NA	NA	0d	NA	NA	0d
135	UG Plumbing	9 days	9 days	0d	NA	NA	0d	NA	NA	0d
136	UG Plumbing Inspection	1 day	1 day	0d	NA	NA	0d	NA	NA	0d
137	UG Electrical	9 days	9 days	0d	NA	NA	Equa	NA	NA	Equal
138	UG Electrical Inspection	1 day	1 day	0d	NA	NA	Equa	NA	NA	Equal
139	Elevator Pit Waterproofing	9 days	9 days	0d	NA	NA	0d	NA	NA	0d
140	WEATHER DELAY	1 day	1 day	0d	NA	NA	0d	NA	NA	0d
141	WEATHER DELAY	1 day	1 day	0d	NA	NA	Equa	NA	NA	Equal
142	Slab on Grade Prep and Pour with 1' of Footers	20 days	20 days	0d	Fri 25/08/15	Fri 25/08/15	0d	Thu 25/09/11	Thu 25/09/11	0d
143	WEATHER DELAY	1 day	1 day	0d	NA	NA	0d	NA	NA	0d
144	CMU	32 days	32 days	0d	Fri 25/09/19	Fri 25/09/19	0d	Thu 25/10/16	Thu 25/10/16	0d
145	CFS Framing & Decking	20 days	20 days	0d	Fri 25/09/26	Fri 25/09/26	0d	Thu 25/10/23	Thu 25/10/23	0d
146	Wall Rough Elec	30 days	30 days	0d	Fri 25/10/24	Fri 25/10/24	0d	Thu 25/11/20	Thu 25/11/20	0d
147	OH Elec	25 days	25 days	0d	Fri 25/11/21	Fri 25/11/21	0d	Thu 25/12/25	Thu 25/12/25	0d

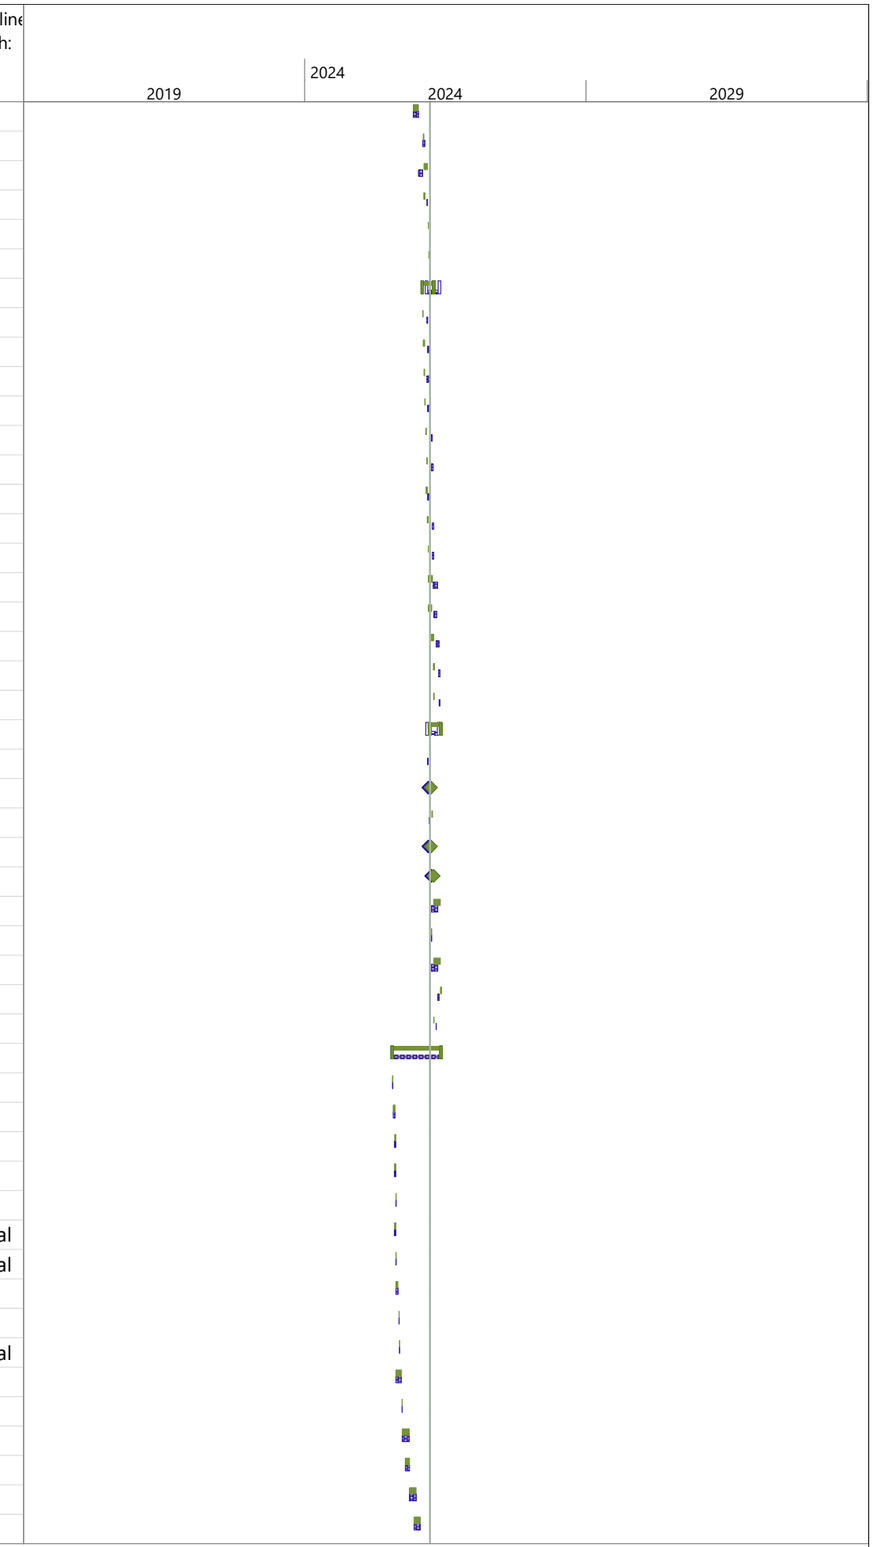
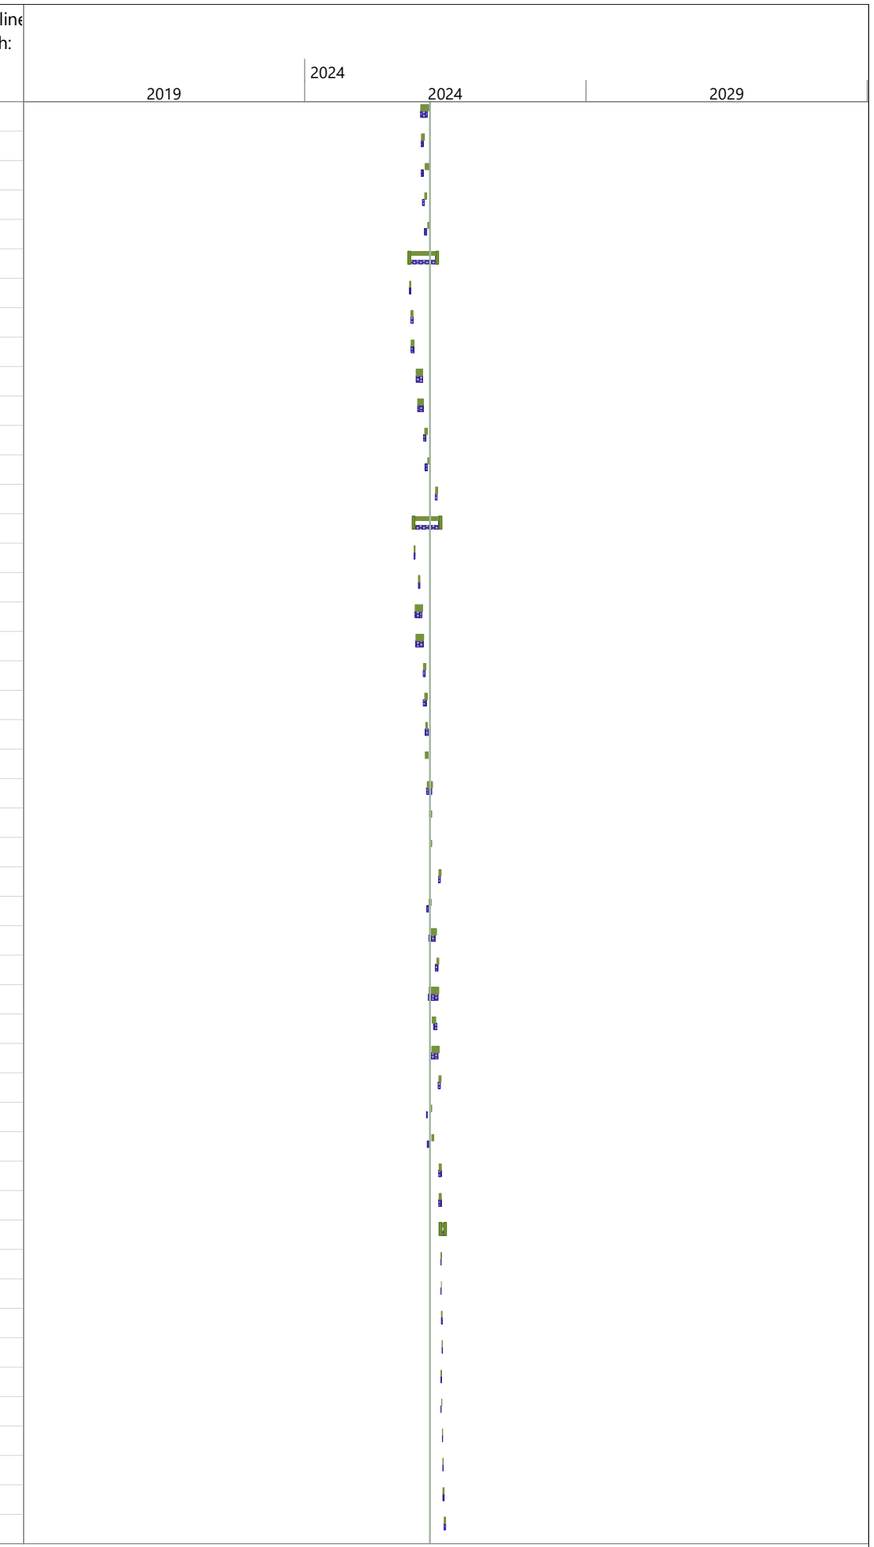
	Name	Duration: Current	Duration: Previous	Duration Diff	Baseline Start: Current	Baseline Start: Previous	Basel Start: Diff	Baseline Finish: Current	Baseline Finish: Previous	Baseline Finish: Diff
148	Interior Build-Out	45 days	30 days	15d	Fri 26/01/30	Fri 26/01/30	0d	Thu 26/03/19	Thu 26/03/19	0d
149	Fire Sprikler OH	15 days	10 days	5d	NA	NA	0d	NA	NA	0d
150	Electrical Room - Finish	20 days	10 days	10d	Tue 26/02/10	Tue 26/02/10	0d	Mon 26/03/02	Mon 26/03/02	0d
151	Duct Work Installation	8 days	10 days	-2d	NA	NA	0d	NA	NA	0d
152	MEP Trim-Out	2 wks	2 wks	0d	Fri 26/01/30	Fri 26/01/30	0d	Thu 26/02/12	Thu 26/02/12	0d
153	**2nd Floor**	**130 days**	**129 days**	**1d**	**Fri 25/10/24**	**Fri 25/10/24**	**0d**	**Thu 26/03/12**	**Thu 26/03/12**	**0d**
154	Prep and Pour Composite Slab	6 days	6 days	0d	Fri 25/10/24	Fri 25/10/24	0d	Fri 25/11/07	Fri 25/11/07	0d
155	CMU	5 days	5 days	0d	Mon 25/11/17	Mon 25/11/17	0d	Fri 25/12/12	Fri 25/12/12	0d
156	CFS Framing & Decking	4 days	4 days	0d	Mon 25/12/01	Mon 25/12/01	0d	Fri 25/12/26	Fri 25/12/26	0d
157	Wall Rough Elec	30 days	30 days	0d	Mon 25/12/29	Mon 25/12/29	0d	Fri 26/01/16	Fri 26/01/16	0d
158	OH Elec	25 days	25 days	0d	Mon 26/01/19	Mon 26/01/19	0d	Fri 26/02/20	Fri 26/02/20	0d
159	Fire Sprikler OH	10 days	10 days	0d	NA	NA	0d	NA	NA	0d
160	Duct Work Installation	10 days	10 days	0d	NA	NA	0d	NA	NA	0d
161	MEP Trim-Out	2 wks	2 wks	0d	Fri 26/02/27	Fri 26/02/27	0d	Thu 26/03/12	Thu 26/03/12	0d
162	**3rd Floor**	**126 days**	**124 days**	**2d**	**Mon 25/12/29**	**Mon 25/12/29**	**0d**	**Tue 26/05/05**	**Tue 26/05/05**	**0d**
163	Prep and Pour Composite Slab	6 days	6 days	0d	Mon 25/12/29	Mon 25/12/29	0d	Fri 26/01/09	Fri 26/01/09	0d
164	PBC Inspections Delay	9 days	9 days	0d	NA	NA	0d	NA	NA	0d
165	CMU	24 days	20 days	4d	Mon 26/01/19	Mon 26/01/19	0d	Fri 26/02/13	Fri 26/02/13	0d
166	CFS Framing & Decking	22 days	20 days	2d	Wed 26/02/04	Wed 26/02/04	0d	Tue 26/03/03	Tue 26/03/03	0d
167	Top-Out	10,25 day	10 days	0,25d	Wed 26/03/04	Wed 26/03/04	0d	Tue 26/03/17	Tue 26/03/17	0d
168	Wall Rough & OH Elec	10,25 day	15 days	-4,75d	Wed 26/03/04	Wed 26/03/04	0d	Tue 26/03/24	Tue 26/03/24	0d
169	Exterior CFD Trusses and Sheathing	8,25 days	15 days	-6,75d	Wed 26/03/18	Wed 26/03/18	0d	Tue 26/04/07	Tue 26/04/07	0d
170	Installation of Additional Framing - South Elevation - Per	15 days			NA			NA		
171	OH Elec	25 days	25 days	0d	Wed 26/03/25	Wed 26/03/25	0d	Tue 26/04/28	Tue 26/04/28	0d
172	Fire Sprikler OH	10 days			NA			NA		
173	Duct Work Install	8 days			NA			NA		
174	MEP Trim-Out	2 wks	2 wks	0d	Wed 26/04/22	Wed 26/04/22	0d	Tue 26/05/05	Tue 26/05/05	0d
175	Roofing	10 days	10 days	0d	Wed 26/03/18	Wed 26/03/18	0d	Tue 26/03/31	Tue 26/03/31	0d
176	Hallway System (By Owner) - 2nd & 3rd Floor	5 wks	6 wks	-5d	Fri 26/01/30	Fri 26/01/30	0d	Thu 26/02/26	Thu 26/02/26	0d
177	Hallway System (By Owner) - 1st Floor	2 wks	3 wks	-5d	Wed 26/03/25	Wed 26/03/25	0d	Tue 26/04/21	Tue 26/04/21	0d
178	Stucco and Architectural Finishes	45 days	45 days	0d	Wed 26/03/04	Wed 26/03/04	0d	Tue 26/05/05	Tue 26/05/05	0d
179	Exterior Storefront& Windows, & Louvers	15 days	15 days	0d	Wed 26/03/18	Wed 26/03/18	0d	Tue 26/04/14	Tue 26/04/14	0d
180	Elevator Installation	35 days	35 days	0d	Wed 26/04/01	Wed 26/04/01	0d	Tue 26/05/19	Tue 26/05/19	0d
181	Install Gutters and downspouts	10 days	10 days	0d	Wed 26/05/06	Wed 26/05/06	0d	Tue 26/05/19	Tue 26/05/19	0d
182	Temp For Test	3 days	3 days	0d	Tue 26/03/03	Tue 26/03/03	0d	Thu 26/03/05	Thu 26/03/05	0d
183	Install Electric Meter	10 days	10 days	0d	Fri 26/03/06	Fri 26/03/06	0d	Thu 26/03/19	Thu 26/03/19	0d
184	Fire Alarm	10 days	12 days	-2d	Wed 26/05/20	Wed 26/05/20	0d	Tue 26/06/09	Tue 26/06/09	0d
185	BDA & Low Voltage	10 days	12 days	-2d	Wed 26/05/20	Wed 26/05/20	0d	Tue 26/06/09	Tue 26/06/09	0d
186	**Final Inspections & Cert. of Completion**	**21 days**	**23 days**	**-2d**	**Wed 26/05/06**	**Wed 26/05/06**	**0d**	**Tue 26/07/07**	**Tue 26/07/07**	**0d**
187	Final Mechanical	1 day	1 day	0d	Tue 26/05/05	Tue 26/05/05	0d	Wed 26/05/06	Wed 26/05/06	0d
188	Final Sprinkler	1 day	1 day	0d	Wed 26/05/06	Wed 26/05/06	0d	Thu 26/05/07	Thu 26/05/07	0d
189	Final Electrical& Fire Alarm	3 days	3 days	0d	Fri 26/06/05	Fri 26/06/05	0d	Wed 26/06/10	Wed 26/06/10	0d
190	Final Fire	2 days	2 days	0d	Wed 26/06/10	Wed 26/06/10	0d	Fri 26/06/12	Fri 26/06/12	0d
191	Photometric Inspection / Certification	3 days	3 days	0d	Tue 26/05/05	Tue 26/05/05	0d	Fri 26/05/08	Fri 26/05/08	0d
192	Final Plumbing	1 day	1 day	0d	Tue 26/05/05	Tue 26/05/05	0d	Wed 26/05/06	Wed 26/05/06	0d
193	Final Building	1 day	1 day	0d	Fri 26/06/12	Fri 26/06/12	0d	Mon 26/06/15	Mon 26/06/15	0d
194	Final Zoning	1 day	1 day	0d	Mon 26/06/15	Mon 26/06/15	0d	Tue 26/06/16	Tue 26/06/16	0d
195	Estimated Certificate Of Completion	5 days	5 days	0d	Tue 26/06/16	Tue 26/06/16	0d	Tue 26/06/23	Tue 26/06/23	0d
196	Weather Allowance	7 days	7 days	0d	Tue 26/06/23	Tue 26/06/23	0d	Wed 26/07/01	Wed 26/07/01	0d
