Activity ID	Activity Name	OD	RD	% Complete	Start	Finish	TF
Public Storage Fairfax VA - JAN 2026		350	155		05-May-25 A	04-Sep-26	-12
Public Storage Fairfax VA		350	155		05-May-25 A	04-Sep-26	-12
Milestones		350	90		05-May-25 A	04-Sep-26	-12
MIL-1000	Notice to Proceed (05.05.25)	0	0	100%	05-May-25 A		
MIL-1010	Weathertight - Main Building	0	0	0%		01-May-26	22
MIL-1020	Permanent Power	0	0	0%	20-May-26		46
MIL-1030	Substantial Completion (08.19.26)	0	0	0%		12-Aug-26*	7
MIL-1040	Final Completion - Main Building	0	0	0%		04-Sep-26*	-16
Impacts/Delays		12	10		26-Jan-26 A	13-Feb-26	-12
Fragnet 001 - Weather Delays		12	10		26-Jan-26 A	13-Feb-26	-12
FRAG01-1000	Site Shutdown Due to Ice and Road Conditions	2	0	100%	26-Jan-26 A	27-Jan-26 A	
FRAG01-1010	Labor Crew Clear Snow and Start Tenting	5	2	60%	28-Jan-26 A	03-Feb-26	-9
FRAG01-1020	Temporary Heat Permit Obtained	7	5	28.57%	29-Jan-26 A	06-Feb-26	-12
FRAG01-1030	Propane Heaters Installed, Melt Snow/Ice	5	5	0%	09-Feb-26	13-Feb-26	-12
Preconstruction		245	25		05-May-25 A	06-Mar-26	103
Procurement		245	25		05-May-25 A	06-Mar-26	103
PROC-1000	Precon Construction	1	0	100%	05-May-25 A	05-May-25 A	
PROC-1010	Contractor Procurement	60	0	100%	06-May-25 A	07-Nov-25 A	
Long Lead Items		217	25		12-Jun-25 A	06-Mar-26	103
PROC-1020	Elevator Submittal	23	0	100%	12-Jun-25 A	14-Jul-25 A	
PROC-1040	Switchgear Submittal	15	0	100%	31-Jul-25 A	20-Aug-25 A	
PROC-1050	Light Fixtures Submittal	20	0	100%	04-Aug-25 A	29-Aug-25 A	
PROC-1030	Brick Submittal and Fabrication	60	0	100%	01-Jul-25 A	19-Sep-25 A	
PROC-1070	Light Fixtures Fabrication	20	0	100%	01-Sep-25 A	25-Sep-25 A	
PROC-1060	Switchgear Fabrication	30	0	100%	21-Aug-25 A	30-Sep-25 A	
PROC-1110	HVAC Equipment Submittal	20	0	100%	15-Sep-25 A	30-Sep-25 A	
PROC-1120	Ferguson Tank Submittal	20	0	100%	29-Jul-25 A	15-Oct-25 A	
PROC-1140	Ferguson Tank Fabrication	15	0	100%	27-Oct-25 A	21-Nov-25 A	
PROC-1080	Glass Field Measurement and Fabrication - Office	45	0	100%	15-Sep-25 A	22-Dec-25 A	
PROC-1130	HVAC Equipment Fabrication	70	0	100%	20-Oct-25 A	16-Jan-26 A	
PROC-1090	Fire Pump Submittal	40	1	97.5%	27-Oct-25 A	02-Feb-26	107
PROC-1150	Fire Pump Fabrication	20	20	0%	03-Feb-26	02-Mar-26	107
PROC-1100	Elevator Fabrication	50	25	50%	02-Dec-25 A	06-Mar-26	43
Construction		333	138		05-May-25 A	12-Aug-26	-5
Site Work		333	138		05-May-25 A	12-Aug-26	-12
SITE-1020	Mobilization	1	0	100%	05-May-25 A	05-May-25 A	
SITE-1000	Erosion Control Phase I	4	0	100%	06-May-25 A	09-May-25 A	
SITE-1010	Stormwater Management Ponds Phase I	10	0	100%	03-Nov-25 A	21-Nov-25 A	
SITE-1030	Stormwater Management Ponds Phase II	10	10	0%	27-Mar-26	10-Apr-26	77
Site Work - Main Building		328	138		12-May-25 A	12-Aug-26	-12
SITE-MB-1010	Demo/Clear Site - Main Building	10	0	100%	12-May-25 A	23-May-25 A	
SITE-MB-1020	Rough Grading - Main Building	10	0	100%	26-May-25 A	06-Jun-25 A	
SITE-MB-1030	Building Pad Delivery - Main Building	35	0	100%	09-Jun-25 A	25-Jul-25 A	
SITE-MB-1040	Domestic & Fire Water Online - Main Building	27	0	100%	28-Jul-25 A	02-Sep-25 A	
SITE-MB-1050	Storm Structures and Pipe - Main Building	30	8	75%	03-Nov-25 A	11-Feb-26	78
SITE-MB-1070	Fine Grading - Main Building	15	8	50%	16-Dec-25 A	11-Feb-26	16
SITE-MB-1060	Sanitary Sewer - Main Building	10	10	0%	11-Feb-26	25-Feb-26	78
SITE-MB-1100	Curb and Gutter - Main Building	7	7	0%	12-May-26	20-May-26	17
SITE-MB-1120	Stone Base Parking Lot - Main Building	10	10	0%	21-May-26	03-Jun-26	17
SITE-MB-1080	Sidewalk - Main Building	10	10	0%	01-Jul-26	14-Jul-26	-12

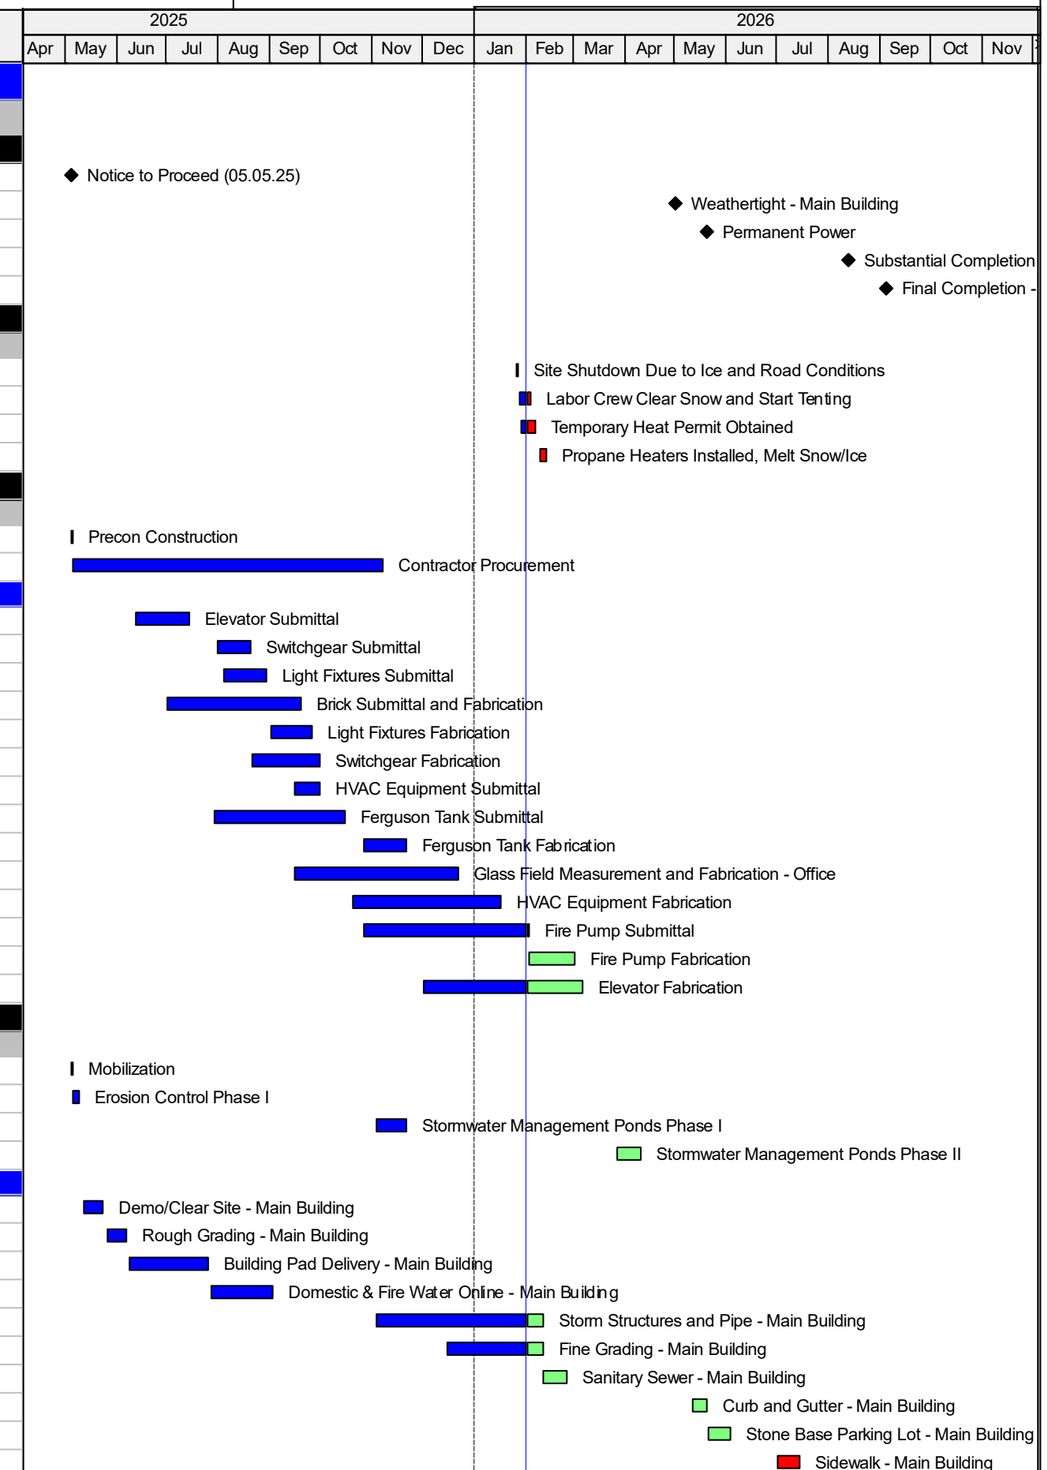

Activity ID	Activity Name	OD	RD	% Complete	Start	Finish	TF
SITE-MB-1130	Paving (Includes SHA Work) - Main Building	11	11	0%	15-Jul-26	29-Jul-26	-12
SITE-MB-1140	Line Striping - Main Building	2	2	0%	30-Jul-26	31-Jul-26	-4
SITE-MB-1090	Landscape - Main Building	10	10	0%	30-Jul-26	12-Aug-26	-12
Site Work - Office		270	80		12-May-25 A	25-May-26	46
SITE-OFF-100	Demo/Clear Site - Office Building	10	0	100%	12-May-25 A	23-May-25 A	
SITE-OFF-101	Rough Grading - Office Building	10	0	100%	26-May-25 A	06-Jun-25 A	
SITE-OFF-102	Building Pad Delivery - Office Building	35	0	100%	09-Jun-25 A	25-Jul-25 A	
SITE-OFF-111	Stone Base Parking Lot - Office Building	1	0	100%	17-Dec-25 A	17-Dec-25 A	
SITE-OFF-106	Fine Grading - Office Building	6	0	100%	16-Dec-25 A	16-Jan-26 A	
SITE-OFF-108	Landscape - Office Building	1	1	0%	02-Feb-26	02-Feb-26	125
SITE-OFF-112	Paving - Office Building	2	2	0%	18-Dec-25 A	03-Feb-26	121
SITE-OFF-113	Line Striping - Office Building	1	1	0%	04-Feb-26	04-Feb-26	123
SITE-OFF-107	Sidewalk - Office Building	2	2	0%	04-Feb-26	05-Feb-26	121
SITE-OFF-103	Domestic & Fire Water Online - Office Building	10	10	0%	02-Feb-26	13-Feb-26	114
SITE-OFF-109	Curb and Gutter - Office Building	1	1	0%	16-Feb-26	16-Feb-26	114
SITE-OFF-110	Misc Exterior Items (Vehicle Gate Operator) - Office Building	3	3	0%	20-May-26	25-May-26	46
Main Building		248	118		04-Aug-25 A	15-Jul-26	15
Substructure		136	5		04-Aug-25 A	10-Feb-26	-3
CON-MB-1000	UG Electric Rough In	10	0	100%	04-Aug-25 A	27-Aug-25 A	
CON-MB-1010	UG Plumbing Roughin	8	0	100%	18-Aug-25 A	27-Aug-25 A	
CON-MB-1020	Prep/Pour SOG 1/2	12	0	100%	27-Aug-25 A	10-Sep-25 A	
CON-MB-1030	Prep/Pour SOG 2/2	18	0	100%	29-Aug-25 A	22-Sep-25 A	
CON-MB-1040	Foundation Waterproofing	5	5	0%	03-Feb-26	10-Feb-26	-3
Superstructure		131	66		29-Sep-25 A	04-May-26	-12
First Floor Superstructure		30	0		29-Sep-25 A	30-Jan-26 A	
CON-MB-L1-	Structural Steel Columns & Beams - 1st Floor	18	0	100%	29-Sep-25 A	28-Oct-25 A	
CON-MB-L1-	Metal Decking - 2nd floor	4	0	100%	23-Oct-25 A	28-Oct-25 A	
CON-MB-L1-	Prep/Pour SOD - 2nd Floor	8	0	100%	29-Oct-25 A	01-Nov-25 A	
CON-MB-L1-	Exterior & Interior Framing - 1st Floor	10	0	100%	28-Oct-25 A	30-Jan-26 A	
Second Floor Superstructure		48	2		04-Nov-25 A	03-Feb-26	-3
CON-MB-L2-	Structural Steel Columns & Beams - 2nd Floor	14	0	100%	04-Nov-25 A	21-Nov-25 A	
CON-MB-L2-	Metal Decking 3rd Floor	4	0	100%	24-Nov-25 A	27-Nov-25 A	
CON-MB-L2-	Prep/Pour SOD - 3rd floor	8	0	100%	28-Nov-25 A	04-Dec-25 A	
CON-MB-L2-	Exterior & Interior Framing - 2nd Floor	10	2	80%	13-Jan-26 A	03-Feb-26	-3
Third Floor Superstructure		40	10		01-Dec-25 A	25-Feb-26	34
CON-MB-L3-	Structural Steel Columns & Beams - 3rd Floor	14	0	100%	01-Dec-25 A	19-Dec-25 A	
CON-MB-L3-	Metal Decking - 4th Floor	4	0	100%	19-Dec-25 A	23-Dec-25 A	
CON-MB-L3-	Prep & Pour SOD - 4th Floor	8	0	100%	22-Dec-25 A	05-Jan-26 A	
CON-MB-L3-	Exterior & Interior Framing - 3rd Floor	10	10	0%	12-Feb-26	25-Feb-26	34
Fourth Floor Superstructure		51	22		06-Jan-26 A	17-Mar-26	-12
CON-MB-L4-	Structural Steel Columns & Beams - 4th Floor	14	0	100%	06-Jan-26 A	23-Jan-26 A	
CON-MB-L4-	Metal Decking - 5th Floor	4	0	100%	16-Jan-26 A	23-Jan-26 A	
CON-MB-L4-	Prep & Pour SOD - 5th Floor	4	4	0%	16-Feb-26	19-Feb-26	-12
CON-MB-L4-	Exterior & Interior Framing - 4th Floor	10	10	0%	04-Mar-26	17-Mar-26	-12
Fifth Floor Superstructure		52	52		20-Feb-26	04-May-26	-12
CON-MB-L5-	Structural Steel Columns & Beams - 5th Floor	14	14	0%	20-Feb-26	11-Mar-26	-12
CON-MB-L5-	Framing & Metal Decking - Roof	10	10	0%	12-Mar-26	25-Mar-26	-12
CON-MB-L5-	Exterior & Interior Framing - 5th Floor	10	10	0%	21-Apr-26	04-May-26	-12
Interior Finishes		218	118		15-Sep-25 A	15-Jul-26	15
CON-MB-2020	Winterization	5	0	100%	22-Dec-25 A	29-Dec-25 A	
CON-MB-2000	Grind/Seal Floors (Full Building)	10	10	0%	19-Jun-26	02-Jul-26	10

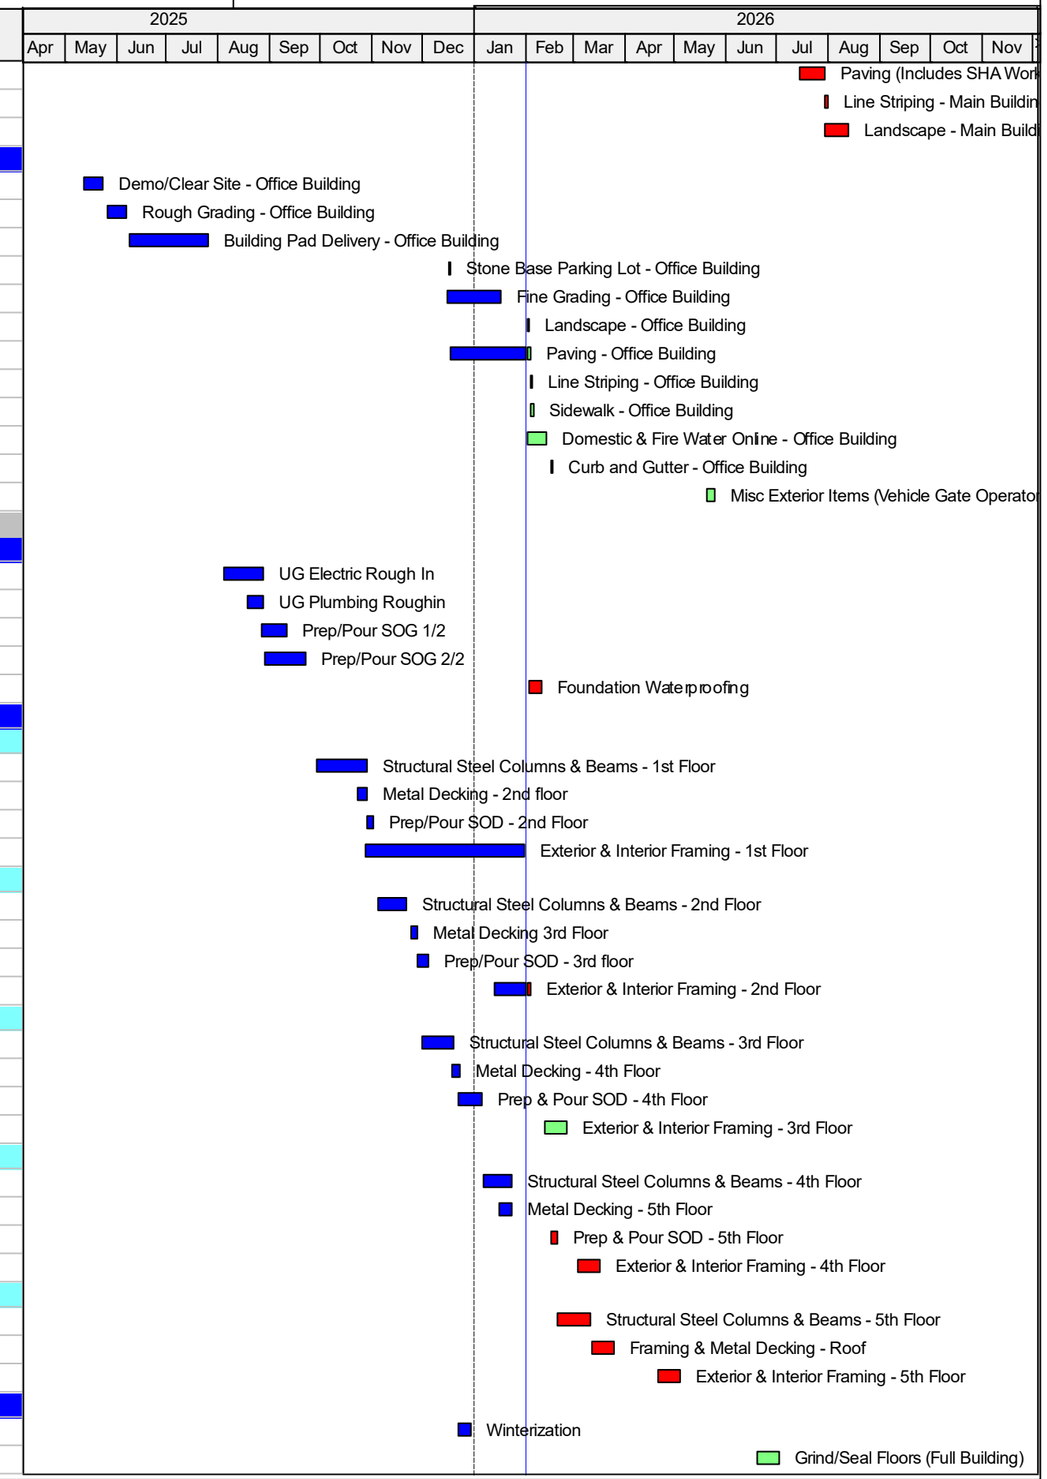

Activity ID	Activity Name	OD	RD	% Complete	Start	Finish	TF
CON-MB-2010	Final Cleaning (Full Building)	15	15	0%	23-Jun-26	13-Jul-26	10
Elevator		218	65		15-Sep-25 A	15-Jul-26	15
CON-ELEV-1	Elevator 3 CMU Shaft	12	0	100%	15-Sep-25 A	30-Sep-25 A	
CON-ELEV-1	Elevator 1/2 CMU Shaft	14	0	100%	01-Oct-25 A	17-Oct-25 A	
CON-ELEV-1	Elevator Install	65	65	0%	16-Apr-26	15-Jul-26	15
Stair Shafts		104	4		15-Sep-25 A	05-Feb-26	122
CON-STAIR-	Stair Tower A CMU	10	0	100%	03-Oct-25 A	17-Oct-25 A	
CON-STAIR-	Stair Tower B CMU	25	0	100%	15-Sep-25 A	24-Oct-25 A	
CON-STAIR-	Stair Stringers and Pans	10	0	100%	29-Dec-25 A	07-Jan-26 A	
CON-STAIR-	Doors & HW - Stairs	2	2	0%	02-Feb-26	03-Feb-26	122
CON-STAIR-	Prep/Paint - Stairs	2	2	0%	04-Feb-26	05-Feb-26	122
First Floor Interior Finishes		103	81		12-Dec-25 A	25-May-26	45
CON-MB-L1-	Fireproofing Structural Steel - 1st Floor	8	0	100%	12-Dec-25 A	09-Jan-26 A	
CON-MB-L1-	OH & Wall Plumbing Rough In - 1st Floor	3	1	60%	07-Jan-26 A	03-Feb-26	46
CON-MB-L1-	HVAC Rough In - 1st Floor	3	2	50%	06-Jan-26 A	03-Feb-26	46
CON-MB-L1-	Electric & Low Voltage OH & Wall Rough In - 1st Floor	10	6	40%	07-Jan-26 A	09-Feb-26	41
CON-MB-L1-	Sprinkler Rough In - 1st Floor	10	8	20%	12-Jan-26 A	11-Feb-26	118
CON-MB-L1-	OH & Wall MEP Inspections - 1st Floor	2	2	0%	10-Feb-26	11-Feb-26	41
CON-MB-L1-	Janus Wall Panels - 1st Floor	15	15	0%	12-Mar-26	01-Apr-26	21
CON-MB-L1-	Hang & Finish Drywall - 1st Floor	7	7	0%	04-May-26	12-May-26	45
CON-MB-L1-	Doors & HW - 1st Floor	2	2	0%	13-May-26	14-May-26	45
CON-MB-L1-	Prep/Paint Walls & Ceilings - 1st Floor	2	2	0%	15-May-26	18-May-26	45
CON-MB-L1-	Plumbing Fixtures - 1st Floor	2	2	0%	19-May-26	20-May-26	48
CON-MB-L1-	Diffusers - 1st Floor	5	5	0%	19-May-26	25-May-26	45
CON-MB-L1-	Light Fixtures - 1st Floor	5	5	0%	19-May-26	25-May-26	45
Second Floor Interior Finishes		26	28		12-Jan-26 A	11-Mar-26	98
CON-MB-L2-	Fireproofing Structural Steel - 2nd Floor	8	0	100%	12-Jan-26 A	23-Jan-26 A	
CON-MB-L2-	HVAC Rough In - 2nd Floor	5	4	20%	19-Jan-26 A	05-Feb-26	29
CON-MB-L2-	Doors & HW - 2nd Floor	2	2	0%	04-Feb-26	05-Feb-26	120
CON-MB-L2-	Prep/Paint Walls - 2nd Floor	2	2	0%	06-Feb-26	09-Feb-26	120
CON-MB-L2-	Electric OH & Wall Rough In - 2nd Floor	10	10	0%	04-Feb-26	17-Feb-26	21
CON-MB-L2-	Sprinkler Rough In - 2nd Floor	10	10	0%	04-Feb-26	17-Feb-26	114
CON-MB-L2-	OH & Wall MEP Inspections - 2nd Floor	1	1	0%	18-Feb-26	18-Feb-26	21
CON-MB-L2-	Diffusers - 2nd Floor	5	5	0%	19-Feb-26	25-Feb-26	108
CON-MB-L2-	Light Fixtures - 2nd Floor	5	5	0%	19-Feb-26	25-Feb-26	108
CON-MB-L2-	Janus Wall Panels - 2nd Floor	15	15	0%	19-Feb-26	11-Mar-26	21
Third Floor Interior Finishes		80	80		02-Feb-26	22-May-26	46
CON-MB-L3-	Fire Proofing Structural Steel - 3rd Floor	8	8	0%	02-Feb-26	11-Feb-26	-6
CON-MB-L3-	OH & Wall Plumbing Rough In - 3rd Floor	3	3	0%	26-Feb-26	02-Mar-26	41
CON-MB-L3-	HVAC Rough In - 3rd Floor	5	5	0%	26-Feb-26	04-Mar-26	39
CON-MB-L3-	Electric & Low Voltage OH & Wall Rough In - 3rd Floor	10	10	0%	26-Feb-26	11-Mar-26	34
CON-MB-L3-	Sprinkler Rough In - 3rd Floor	10	10	0%	26-Feb-26	11-Mar-26	98
CON-MB-L3-	OH & Wall MEP Inspections - 3rd Floor	2	2	0%	12-Mar-26	13-Mar-26	34
CON-MB-L3-	Janus Wall Panels - 3rd Floor	15	15	0%	02-Apr-26	22-Apr-26	21
CON-MB-L3-	Hang/Finish Drywall - 3rd Floor	7	7	0%	04-May-26	12-May-26	46
CON-MB-L3-	Prep/Paint Walls & Ceilings - 3rd Floor	3	3	0%	13-May-26	15-May-26	46
CON-MB-L3-	Plumbing Fixtures - 3rd Floor	4	4	0%	18-May-26	21-May-26	47
CON-MB-L3-	Diffusers - 3rd Floor	5	5	0%	18-May-26	22-May-26	46
CON-MB-L3-	Light Fixtures - 3rd Floor	5	5	0%	18-May-26	22-May-26	46
Fourth Floor Interior Finishes		59	59		20-Feb-26	13-May-26	53

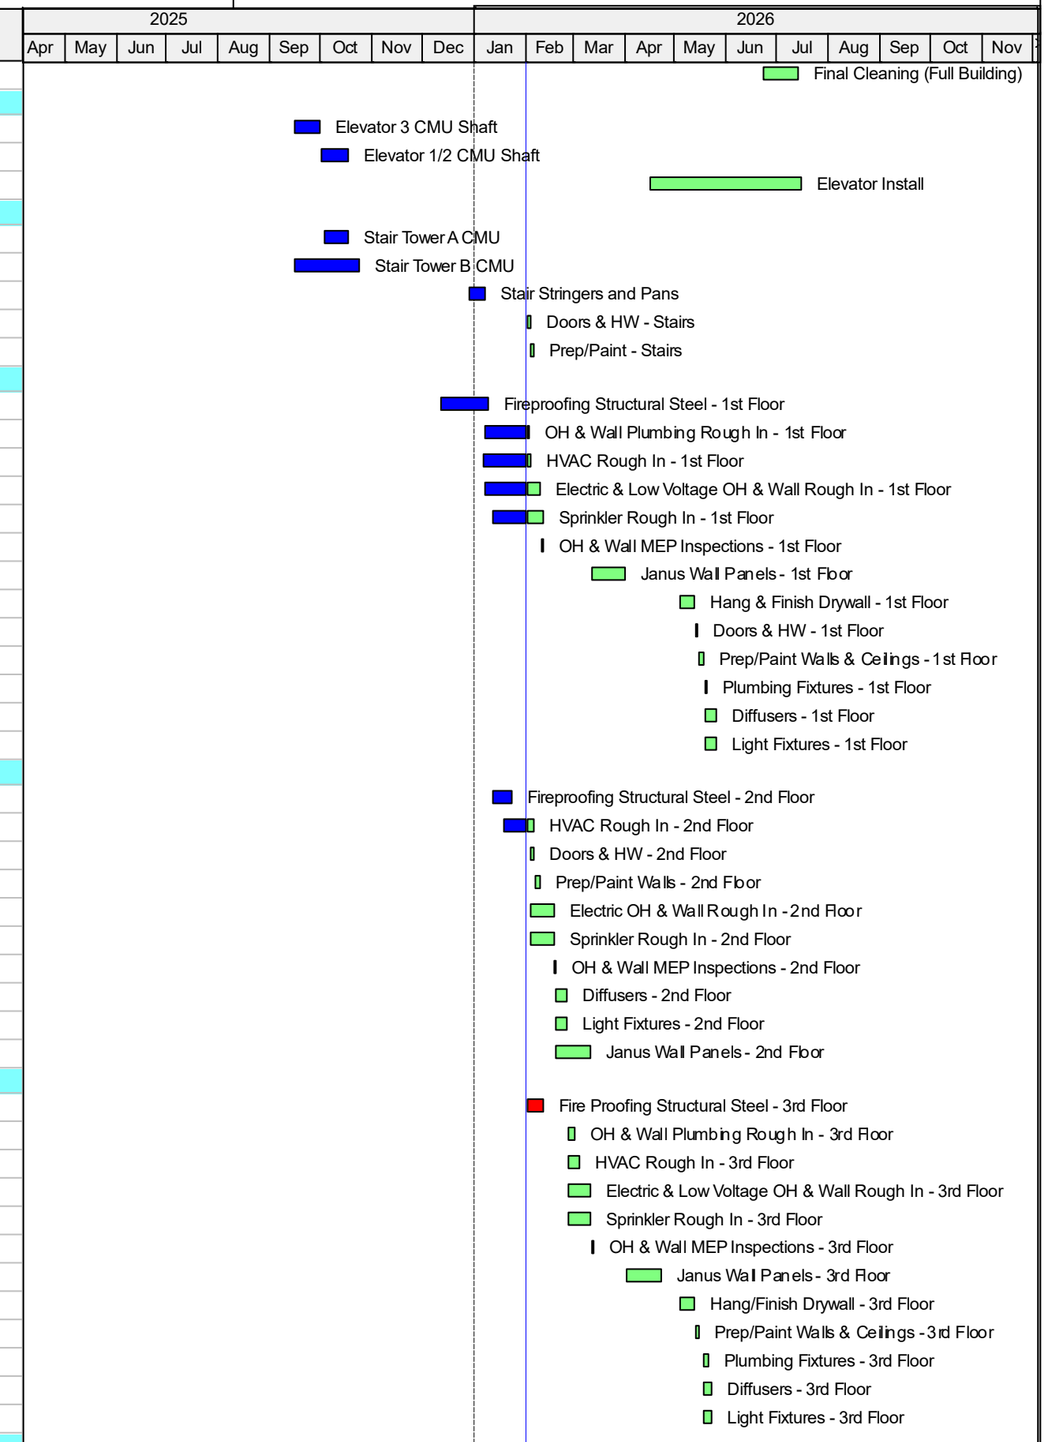

Activity ID	Activity Name	OD	RD	% Complete	Start	Finish	TF
CON-MB-L4-	Fire Proofing Structural Steel - 4th Floor	8	8	0%	20-Feb-26	03-Mar-26	-12
CON-MB-L4-	HVAC Rough In - 4th Floor	5	5	0%	18-Mar-26	24-Mar-26	41
CON-MB-L4-	Electric OH & Wall Rough In - 4th Floor	10	10	0%	18-Mar-26	31-Mar-26	36
CON-MB-L4-	Sprinkler Rough In - 4th Floor	10	10	0%	18-Mar-26	31-Mar-26	84
CON-MB-L4-	OH & Wall MEP Inspections - 4th Floor	1	1	0%	01-Apr-26	01-Apr-26	36
CON-MB-L4-	Prep/Paint Walls - 4th Floor	2	2	0%	02-Apr-26	03-Apr-26	81
CON-MB-L4-	Diffusers - 4th Floor	5	5	0%	02-Apr-26	08-Apr-26	78
CON-MB-L4-	Light Fixtures - 4th Floor	5	5	0%	02-Apr-26	08-Apr-26	78
CON-MB-L4-	Janus Wall Panels - 4th Floor	15	15	0%	23-Apr-26	13-May-26	21
Fifth Floor Interior Finishes		46	46		16-Apr-26	18-Jun-26	27
CON-MB-L5-	Fire Proofing Structural Steel - 5th Floor	8	8	0%	16-Apr-26	27-Apr-26	-12
CON-MB-L5-	OH & Wall Plumbing Rough In - 5th Floor	3	3	0%	05-May-26	07-May-26	17
CON-MB-L5-	HVAC Rough In - 5th Floor	5	5	0%	05-May-26	11-May-26	15
CON-MB-L5-	Electric & Low Voltage OH & Wall Rough In - 5th Floor	10	10	0%	05-May-26	18-May-26	10
CON-MB-L5-	Sprinkler Rough In - 5th Floor	10	10	0%	05-May-26	18-May-26	50
CON-MB-L5-	OH & Wall MEP Inspections - 5th Floor	1	1	0%	19-May-26	19-May-26	10
CON-MB-L5-	Hang/Finish Drywall - 5th Floor	7	7	0%	20-May-26	28-May-26	10
CON-MB-L5-	Prep/Paint Walls - 5th Floor	2	2	0%	29-May-26	01-Jun-26	36
CON-MB-L5-	Diffusers - 5th Floor	1	1	0%	02-Jun-26	02-Jun-26	39
CON-MB-L5-	Light Fixtures - 5th Floor	1	1	0%	02-Jun-26	02-Jun-26	39
CON-MB-L5-	Plumbing Fixtures - 5th Floor	4	4	0%	02-Jun-26	05-Jun-26	36
CON-MB-L5-	Janus Wall Panels - 5th Floor	15	15	0%	29-May-26	18-Jun-26	10
Switchgear Room		76	76		03-Feb-26	20-May-26	46
CON-POW-1	Switchgear Room Enclosure	10	10	0%	03-Feb-26	17-Feb-26	46
CON-POW-1	Install Switchgear Equipment	15	15	0%	17-Feb-26	10-Mar-26	46
CON-POW-1	Switchgear Lights and Power	15	15	0%	10-Mar-26	31-Mar-26	46
CON-POW-1	City Inspection	1	1	0%	31-Mar-26	01-Apr-26	46
CON-POW-1	Dominion Primary	20	20	0%	01-Apr-26	29-Apr-26	46
CON-POW-1	Dominion Transformer	5	5	0%	29-Apr-26	06-May-26	46
CON-POW-1	Dominion Secondary	5	5	0%	06-May-26	13-May-26	46
CON-POW-1	Power Activation	5	5	0%	13-May-26	20-May-26	46
Exterior Finishes		111	111		12-Jan-26 A	06-Jul-26	17
CON-MB-L1-1	Exterior Sheathing - 1st Floor	6	1	80%	12-Jan-26 A	03-Feb-26	-3
CON-MB-L2-1	Exterior Sheathing - 2nd Floor	6	6	0%	02-Feb-26	09-Feb-26	-3
CON-MB-L1-1	Perimeter Waterproofing - 1st Floor	3	3	0%	10-Feb-26	13-Feb-26	-3
CON-MB-L3-1	Exterior Sheathing - 3rd Floor	6	6	0%	17-Feb-26	24-Feb-26	38
CON-MB-L4-1	Exterior Sheathing - 4th Floor	6	6	0%	09-Mar-26	16-Mar-26	-12
CON-MB-L1-1	Perimeter Waterproofing West Elevation (Excluding 5th Floor)	4	4	0%	17-Mar-26	20-Mar-26	-12
CON-MB-L2-1	Perimeter Waterproofing North Elevation (Excluding 5th Floor)	4	4	0%	23-Mar-26	26-Mar-26	2
CON-MB-L5-1	Brick Facade - 1st Floor	30	30	0%	13-Feb-26	27-Mar-26	-3
CON-MB-EXT	Brick West Elevation (Excluding 5th Floor)	18	18	0%	23-Mar-26	15-Apr-26	-12
CON-MB-EXT	Storefront	20	20	0%	27-Mar-26	24-Apr-26	62
CON-MB-L5-1	Exterior Sheathing - 5th Floor	6	6	0%	24-Apr-26	01-May-26	-12
CON-MB-EXT	Canopies	7	7	0%	24-Apr-26	05-May-26	62
CON-MB-L2-1	Perimeter Waterproofing West/North Elevations (5th Floor)	2	2	0%	04-May-26	05-May-26	-12
CON-MB-EXT	Stucco West Elevation	15	15	0%	16-Apr-26	06-May-26	-1
CON-MB-EXT	Brick North and West Elevations (5th Floor)	18	18	0%	16-Apr-26	11-May-26	-12
CON-MB-L2-1	Perimeter Waterproofing East Elevation	4	4	0%	06-May-26	11-May-26	-12
CON-MB-EXT	Glass West Elevation	7	7	0%	07-May-26	15-May-26	32
CON-MB-L2-1	Perimeter Waterproofing South Elevation	4	4	0%	12-May-26	15-May-26	2

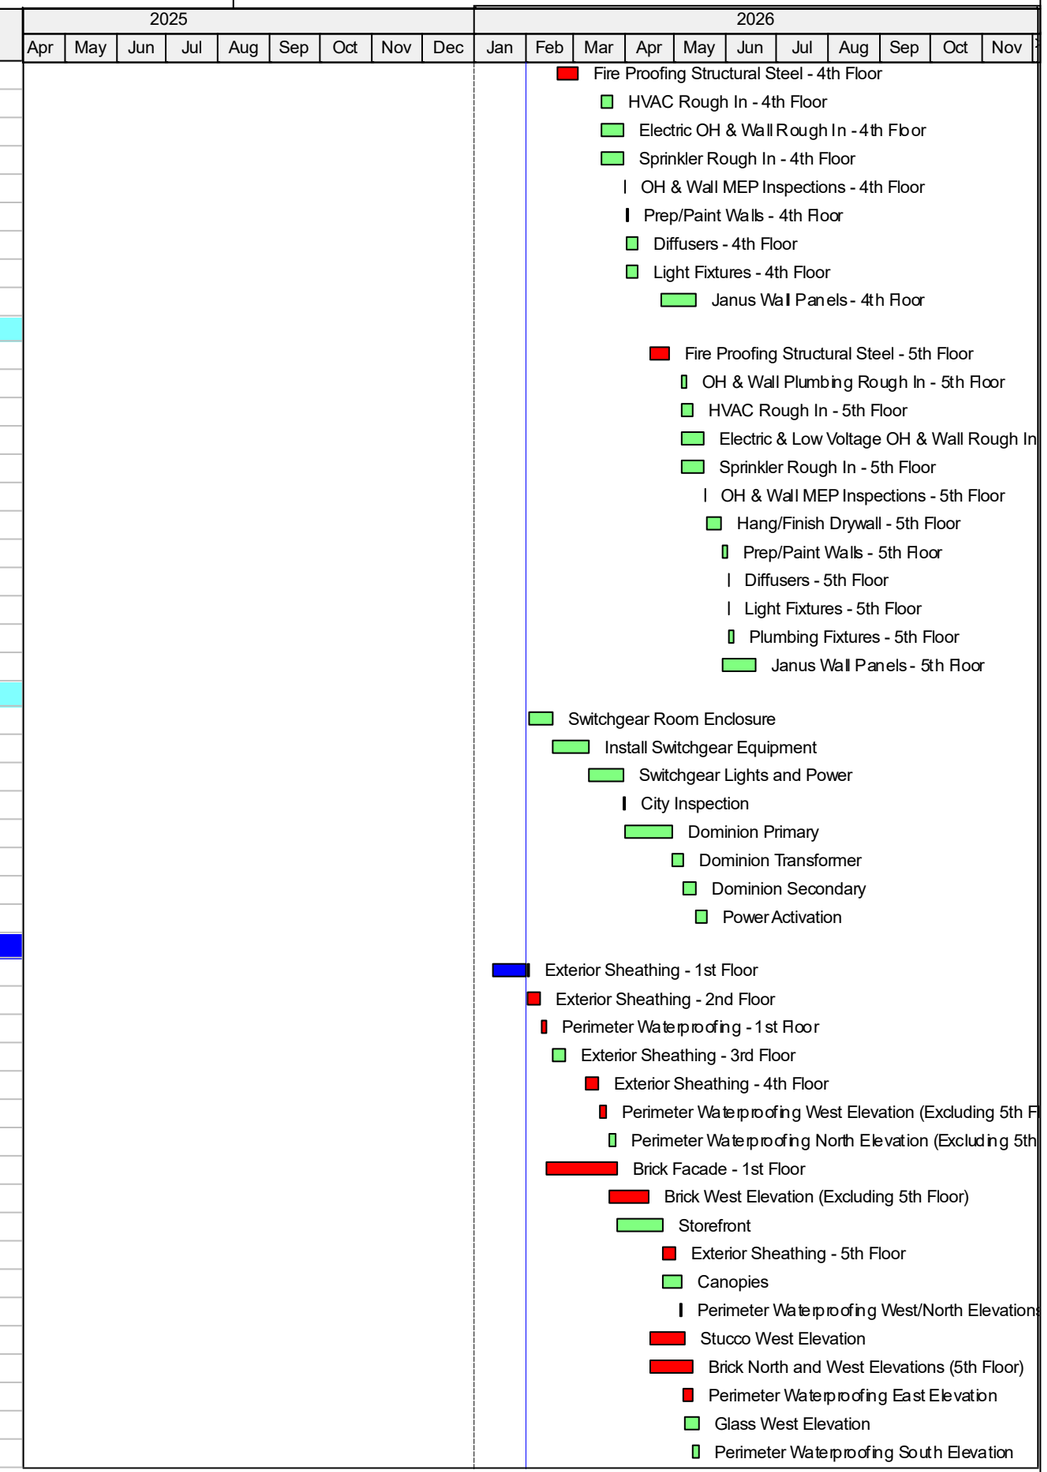
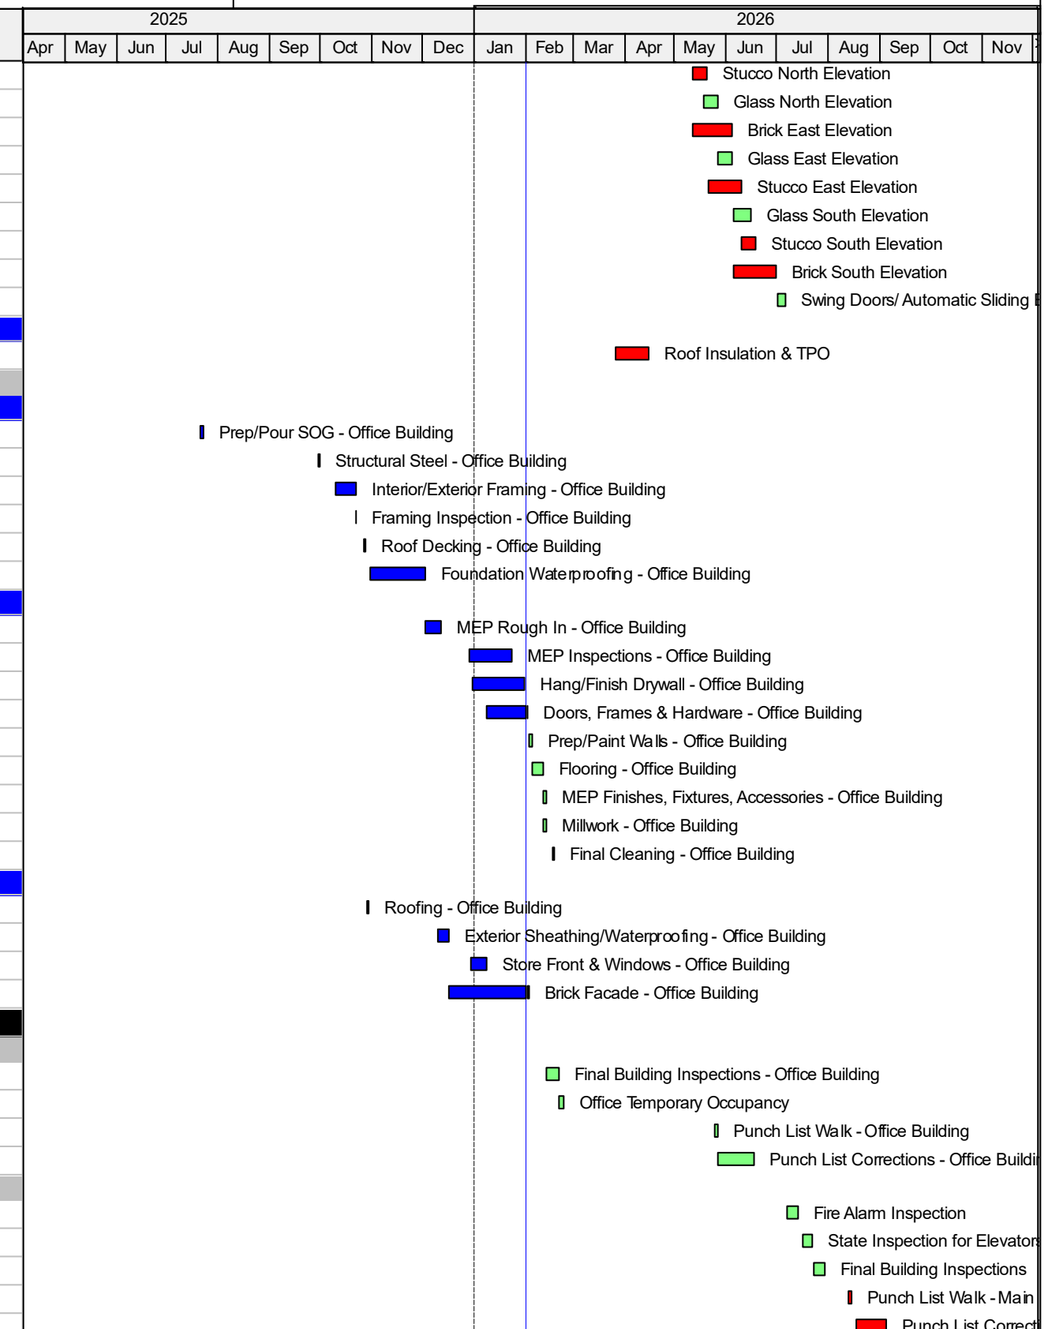
Activity ID	Activity Name	OD	RD	% Complete	Start	Finish	TF
CON-MB-EXT	Stucco North Elevation	7	7	0%	12-May-26	20-May-26	-4
CON-MB-EXT	Glass North Elevation	7	7	0%	18-May-26	26-May-26	32
CON-MB-EXT	Brick East Elevation	18	18	0%	12-May-26	04-Jun-26	-12
CON-MB-EXT	Glass East Elevation	7	7	0%	27-May-26	04-Jun-26	32
CON-MB-EXT	Stucco East Elevation	14	14	0%	21-May-26	09-Jun-26	-4
CON-MB-EXT	Glass South Elevation	7	7	0%	05-Jun-26	15-Jun-26	32
CON-MB-EXT	Stucco South Elevation	7	7	0%	10-Jun-26	18-Jun-26	-4
CON-MB-EXT	Brick South Elevation	18	18	0%	05-Jun-26	30-Jun-26	-12
CON-MB-EXT	Swing Doors/ Automatic Sliding Entrance	4	4	0%	01-Jul-26	06-Jul-26	17
Roofing		15	15		26-Mar-26	15-Apr-26	-12
CON-MB-L5-1	Roof Insulation & TPO	15	15	0%	26-Mar-26	15-Apr-26	-12
Office Building		101	12		21-Jul-25 A	17-Feb-26	114
Structure - Office		32	0		21-Jul-25 A	02-Dec-25 A	
CON-OFF-100	Prep/Pour SOG - Office Building	5	0	100%	21-Jul-25 A	22-Jul-25 A	
CON-OFF-101	Structural Steel - Office Building	2	0	100%	30-Sep-25 A	30-Sep-25 A	
CON-OFF-103	Interior/Exterior Framing - Office Building	8	0	100%	10-Oct-25 A	22-Oct-25 A	
CON-OFF-107	Framing Inspection - Office Building	1	0	100%	22-Oct-25 A	22-Oct-25 A	
CON-OFF-105	Roof Decking - Office Building	1	0	100%	27-Oct-25 A	27-Oct-25 A	
CON-OFF-102	Foundation Waterproofing - Office Building	2	0	100%	31-Oct-25 A	02-Dec-25 A	
Interior Finishes - Office		32	12		03-Dec-25 A	17-Feb-26	114
CON-OFF-108	MEP Rough In - Office Building	3	0	100%	03-Dec-25 A	12-Dec-25 A	
CON-OFF-109	MEP Inspections - Office Building	1	0	100%	29-Dec-25 A	23-Jan-26 A	
CON-OFF-110	Hang/Finish Drywall - Office Building	3	0	100%	31-Dec-25 A	30-Jan-26 A	
CON-OFF-111	Doors, Frames & Hardware - Office Building	2	1	75%	08-Jan-26 A	02-Feb-26	112
CON-OFF-112	Prep/Paint Walls - Office Building	2	2	0%	02-Feb-26	04-Feb-26	112
CON-OFF-113	Flooring - Office Building	5	5	0%	04-Feb-26	11-Feb-26	112
CON-OFF-114	MEP Finishes, Fixtures, Accessories - Office Building	2	2	0%	11-Feb-26	13-Feb-26	112
CON-OFF-115	Millwork - Office Building	2	2	0%	11-Feb-26	13-Feb-26	116
CON-OFF-122	Final Cleaning - Office Building	1	1	0%	17-Feb-26	17-Feb-26	114
Exterior Finishes - Office		71	1		29-Oct-25 A	02-Feb-26	120
CON-OFF-104	Roofing - Office Building	2	0	100%	29-Oct-25 A	29-Oct-25 A	
CON-OFF-106	Exterior Sheathing/Waterproofing - Office Building	3	0	100%	10-Dec-25 A	16-Dec-25 A	
CON-OFF-116	Store Front & Windows - Office Building	3	0	100%	30-Dec-25 A	08-Jan-26 A	
CON-OFF-117	Brick Facade - Office Building	5	1	85%	17-Dec-25 A	02-Feb-26	120
Final Inspections & Close Out		146	146		13-Feb-26	04-Sep-26	-12
Office Building		88	88		13-Feb-26	17-Jun-26	46
CLO-OFF-1030	Final Building Inspections - Office Building	5	5	0%	13-Feb-26	20-Feb-26	112
CLO-OFF-1000	Office Temporary Occupancy	1	1	0%	20-Feb-26	23-Feb-26*	128
CLO-OFF-1040	Punch List Walk - Office Building	2	2	0%	25-May-26	27-May-26	46
CLO-OFF-1050	Punch List Corrections - Office Building	15	15	0%	27-May-26	17-Jun-26	46
Main Building		44	44		07-Jul-26	04-Sep-26	-12
CLO-MB-1000	Fire Alarm Inspection	5	5	0%	07-Jul-26	13-Jul-26	17
CLO-MB-1010	State Inspection for Elevators	5	5	0%	16-Jul-26	22-Jul-26	15
CLO-MB-1020	Final Building Inspections	5	5	0%	23-Jul-26	29-Jul-26	15
CLO-MB-1040	Punch List Walk - Main Building	2	2	0%	13-Aug-26	14-Aug-26	-12
CLO-MB-1050	Punch List Corrections - Main Building	15	15	0%	17-Aug-26	04-Sep-26	-12
