	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Construction Documents**	**50 days**	**50 days**	**0d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Fri 11/14/25**	**Fri 11/14/25**	**0d**
2	CD Kick off and Start	34 days	34 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Thu 10/23/25	Thu 10/23/25	0d
3	65% progress set	1 day	1 day	0d	Fri 10/24/25	Fri 10/24/25	0d	Fri 10/24/25	Fri 10/24/25	0d
4	Owner Drawing review Of 65% set	5 days	5 days	0d	Mon 10/27/25	Mon 10/27/25	0d	Fri 10/31/25	Fri 10/31/25	0d
5	Completon of Bid, Demo and Permit Submital set	10 days	10 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Fri 11/14/25	Fri 11/14/25	0d
6	**Plan Check**	**36 days**	**36 days**	**0d**	**Mon 11/17/25**	**Mon 11/17/25**	**0d**	**Fri 1/9/26**	**Fri 1/9/26**	**0d**
7	**Issue for Interiors Permit (Plan Check)**	**36 days**	**36 days**	**0d**	**Mon 11/17/25**	**Mon 11/17/25**	**0d**	**Fri 1/9/26**	**Fri 1/9/26**	**0d**
8	City Permit Review	15 days	15 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Fri 12/5/25	Fri 12/5/25	0d
9	Drawing Coordination/City Comments	20 days	20 days	0d	Mon 12/8/25	Mon 12/8/25	0d	Thu 1/8/26	Thu 1/8/26	0d
10	Receive interior Tl Building Permit	1 day	1 day	0d	Fri 1/9/26	Fri 1/9/26	0d	Fri 1/9/26	Fri 1/9/26	0d
11	**Issue for Demo Permit**	**16 days**	**16 days**	**0d**	**Mon 11/17/25**	**Mon 11/17/25**	**0d**	**Mon 12/8/25**	**Mon 12/8/25**	**0d**
12	Demo Permit Review	15 days	15 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Fri 12/5/25	Fri 12/5/25	0d
13	Receive Demo Permit	1 day	1 day	0d	Mon 12/8/25	Mon 12/8/25	0d	Mon 12/8/25	Mon 12/8/25	0d
14	**Bidding**	**19 days**	**19 days**	**0d**	**Mon 11/17/25**	**Mon 11/17/25**	**0d**	**Thu 12/11/25**	**Thu 12/11/25**	**0d**
15	Bidding for Tl GCs	15 days	15 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Fri 12/5/25	Fri 12/5/25	0d
16	Award GC Contract	4 days	4 days	0d	Mon 12/8/25	Mon 12/8/25	0d	Thu 12/11/25	Thu 12/11/25	0d
17	**Contracting**	**16 days**	**16 days**	**0d**	**Fri 12/12/25**	**Fri 12/12/25**	**0d**	**Thu 1/8/26**	**Thu 1/8/26**	**0d**
18	Execute Demo LOA	1 day	1 day	0d	Fri 12/12/25	Fri 12/12/25	0d	Fri 12/12/25	Fri 12/12/25	0d
19	Contract Preparation	5 days	5 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Fri 12/19/25	Fri 12/19/25	0d
20	Contract Negotiation	5 days	5 days	0d	Mon 12/22/25	Mon 12/22/25	0d	Tue 12/30/25	Tue 12/30/25	0d
21	Contract Execution	5 days	5 days	0d	Fri 1/2/26	Fri 1/2/26	0d	Thu 1/8/26	Thu 1/8/26	0d
22	**ARCO Procurement**	**84 days**	**79 days**	**5d**	**Fri 1/9/26**	**Fri 1/9/26**	**0d**	**Wed 5/6/26**	**Wed 4/29/26**	**5d**
23	Submittal Approval - MEPs	2.2 wks	2 wks	1d	Fri 1/9/26	Fri 1/9/26	0d	Fri 1/23/26	Thu 1/22/26	1d
24	Regular Light Fixture Submittal Approval (Architect)	9 days			Wed 1/28/26			Mon 2/9/26		
25	Specialty Light Fixture Submittal Approval (Architect)	7 days			Mon 2/9/26			Tue 2/17/26		
26	Light Fixtures - Regular Fixtures	8 wks	9 wks	-5d	Tue 2/10/26	Fri 1/23/26	12d	Mon 4/6/26	Thu 3/26/26	7d
27	Light Fixtures - Specialty Fixtures	9.5 wks			Wed 2/18/26			Fri 4/24/26		
28	Millwork Shop Drawings	2 wks	2 wks	0d	Fri 1/23/26	Fri 1/23/26	0d	Thu 2/5/26	Thu 2/5/26	0d
29	Millwork Drawing Review Approval	3 days			Fri 2/6/26			Tue 2/10/26		
30	Millwork Field Measure and Fab - Level 1 South	5 wks	6 wks	-5d	Thu 3/5/26	Mon 2/16/26	13d	Wed 4/8/26	Fri 3/27/26	8d
31	Millwork Field Measure and Fab - Level 1 North	5 wks	6 wks	-5d	Tue 3/17/26	Thu 3/19/26	-2d	Mon 4/20/26	Wed 4/29/26	-7d
32	Millwork Field Measure and Fab - Level 2 South	5 wks	6 wks	-5d	Wed 3/11/26	Mon 3/9/26	2d	Tue 4/14/26	Fri 4/17/26	-3d
33	Millwork Field Measure and Fab - Level 2 North	5 wks	6 wks	-5d	Fri 3/13/26	Fri 3/13/26	0d	Thu 4/16/26	Thu 4/23/26	-5d
34	Flooring - FC1 Submittal Approval	1.4 wks	3 wks	-8d	Wed 2/4/26	Fri 1/9/26	18d	Thu 2/12/26	Thu 1/29/26	10d
35	Flooring - FC2 - Submittal Approval	1.4 wks	3 wks	-8d	Wed 2/4/26	Fri 1/9/26	18d	Thu 2/12/26	Thu 1/29/26	10d
36	Flooring - FC3 - Submittal Approval	1.4 wks	3 wks	-8d	Wed 2/4/26	Fri 1/9/26	18d	Thu 2/12/26	Thu 1/29/26	10d
37	Flooring - FC4 -Submittal Approval	1.4 wks	3 wks	-8d	Wed 2/4/26	Fri 1/9/26	18d	Thu 2/12/26	Thu 1/29/26	10d
38	Flooring - FC5 - Submittal Approval		3 wks			Fri 1/9/26			Thu 1/29/26	
39	Flooring - FC7 - Submittal Approval		3 wks			Fri 1/9/26			Thu 1/29/26	
40	Flooring - LVT1 - Submittal Approval	1.4 wks	3 wks	-8d	Wed 2/4/26	Fri 1/9/26	18d	Thu 2/12/26	Thu 1/29/26	10d

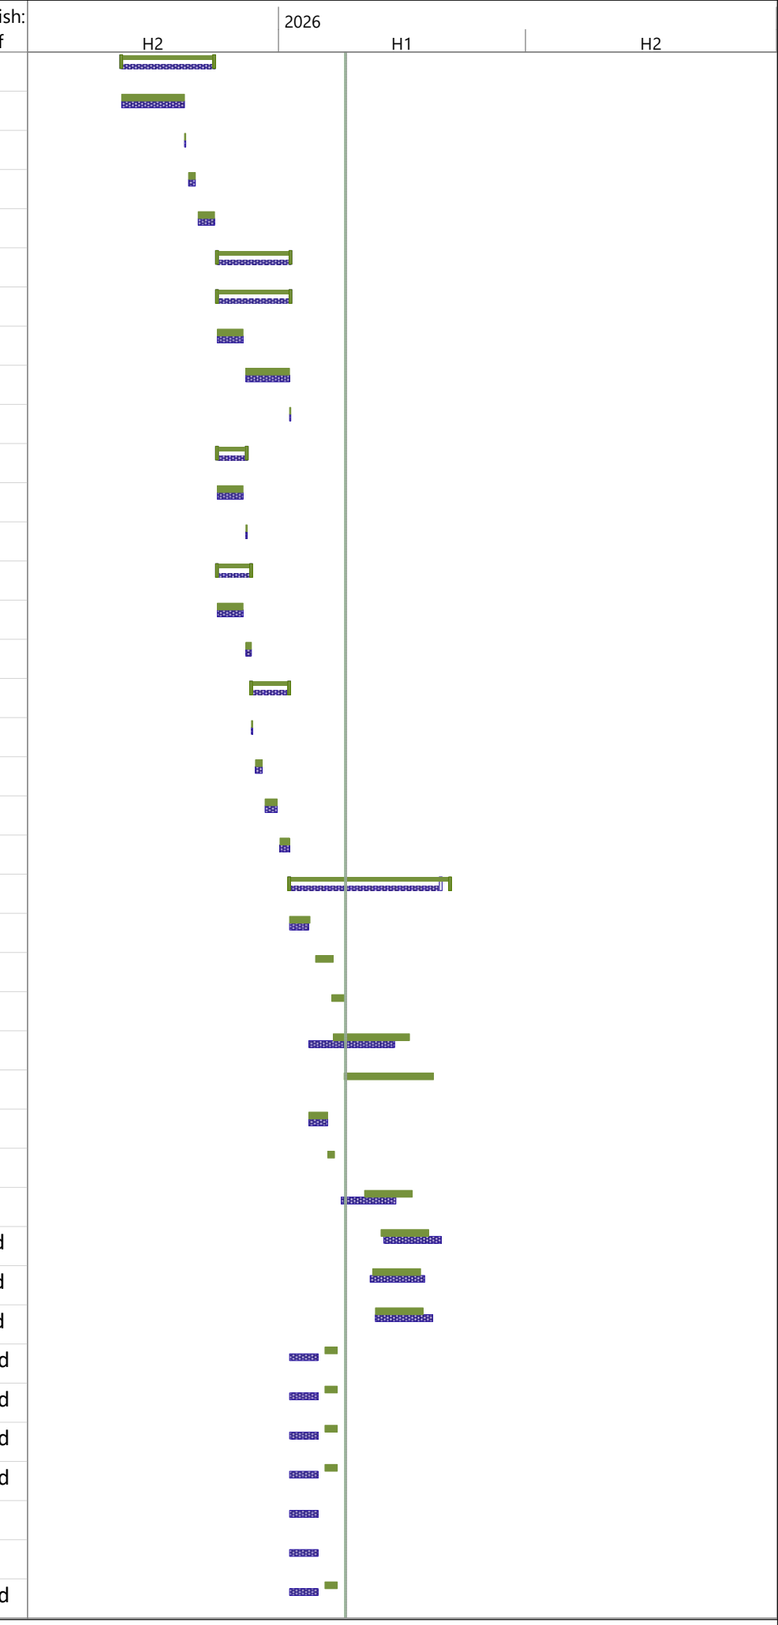

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
41	Flooring - VCT1 - Submittal Approval	1.4 wks	3 wks	-8d	Wed 2/4/26	Fri 1/9/26	18d	Thu 2/12/26	Thu 1/29/26	10d
42	Flooring - FT1 - Submittal Approval	1 wk	3 wks	-10d	Wed 2/4/26	Fri 1/9/26	18d	Tue 2/10/26	Thu 1/29/26	8d
43	Flooring - FT2 - Submittal Approval	1 wk	3 wks	-10d	Wed 2/4/26	Fri 1/9/26	18d	Tue 2/10/26	Thu 1/29/26	8d
44	Wall Tile - WT1 - Submittal Approval	1 wk	3 wks	-10d	Wed 2/4/26	Fri 1/9/26	18d	Tue 2/10/26	Thu 1/29/26	8d
45	Wall Tile - WT2 - Submittal Approval	1 wk	3 wks	-10d	Wed 2/4/26	Fri 1/9/26	18d	Tue 2/10/26	Thu 1/29/26	8d
46	Wall Tile - WT3 - Submittal Approval	1 wk	3 wks	-10d	Wed 2/4/26	Fri 1/9/26	18d	Tue 2/10/26	Thu 1/29/26	8d
47	Wall Tile - WT4 - Submittal Approval	1 wk	3 wks	-10d	Wed 2/4/26	Fri 1/9/26	18d	Tue 2/10/26	Thu 1/29/26	8d
48	Flooring - FC1	6 wks	6 wks	0d	Fri 2/13/26	Fri 1/30/26	10d	Thu 3/26/26	Thu 3/12/26	10d
49	Flooring - FC2	6 wks	6 wks	0d	Fri 2/13/26	Fri 1/30/26	10d	Thu 3/26/26	Thu 3/12/26	10d
50	Flooring - FC3	6 wks	6 wks	0d	Fri 2/13/26	Fri 1/30/26	10d	Thu 3/26/26	Thu 3/12/26	10d
51	Flooring - FC4	6 wks	6 wks	0d	Fri 2/13/26	Fri 1/30/26	10d	Thu 3/26/26	Thu 3/12/26	10d
52	Flooring - FC5		6 wks			Fri 1/30/26			Thu 3/12/26	
53	Flooring - FC7		6 wks			Fri 1/30/26			Thu 3/12/26	
54	Flooring - LVT1	6 wks	6 wks	0d	Fri 2/13/26	Fri 1/30/26	10d	Thu 3/26/26	Thu 3/12/26	10d
55	Flooring - VCT1	6 wks	6 wks	0d	Fri 2/13/26	Fri 1/30/26	10d	Thu 3/26/26	Thu 3/12/26	10d
56	Flooring - FT1	3 wks	3 wks	0d	Wed 2/11/26	Fri 1/30/26	8d	Tue 3/3/26	Thu 2/19/26	8d
57	Flooring - FT2	6 wks	6 wks	0d	Wed 2/11/26	Fri 1/30/26	8d	Tue 3/24/26	Thu 3/12/26	8d
58	Wall Tile - WT1	2 wks	2 wks	0d	Wed 2/11/26	Fri 1/30/26	8d	Tue 2/24/26	Thu 2/12/26	8d
59	Wall Tile - WT2	2 wks	2 wks	0d	Wed 2/11/26	Fri 1/30/26	8d	Tue 2/24/26	Thu 2/12/26	8d
60	Wall Tile - WT3	4 wks	4 wks	0d	Wed 2/11/26	Fri 1/30/26	8d	Tue 3/10/26	Thu 2/26/26	8d
61	Wall Tile - WT4	2 wks	2 wks	0d	Wed 2/11/26	Fri 1/30/26	8d	Tue 2/24/26	Thu 2/12/26	8d
62	Doors, Frames, and Hardware Submittal Review	5 days			Mon 2/16/26			Fri 2/20/26		
63	Door Frames	5 wks	6 wks	-5d	Wed 2/25/26	Fri 1/23/26	23d	Tue 3/31/26	Thu 3/5/26	18d
64	Doors, Hardware	8 wks	8 wks	0d	Mon 2/23/26	Fri 1/23/26	21d	Fri 4/17/26	Thu 3/19/26	21d
65	Appliances	8 wks	8 wks	0d	Mon 1/26/26	Fri 1/23/26	1d	Fri 3/20/26	Thu 3/19/26	1d
66	Breakroom Ceiling Baffle Product Selection (by others)	6 days			Thu 2/19/26			Thu 2/26/26		
67	Ceiling Baffles - Breakroom	10 wks	10 wks	0d	Thu 2/26/26	Fri 1/23/26	24d	Wed 5/6/26	Thu 4/2/26	24d
68	**Procurement Of Direct FBO items**	**116 days**	**103 days**	**13d**	**Mon 11/3/25**	**Fri 10/31/25**	**1d**	**Fri 4/17/26**	**Mon 3/30/26**	**14d**
69	**Furniture**	**116 days**	**97 days**	**19d**	**Mon 11/3/25**	**Fri 10/31/25**	**1d**	**Fri 4/17/26**	**Fri 3/20/26**	**20d**
70	Select Furniture Vendor	1 day	1 day	0d	Thu 2/19/26	Fri 10/31/25	79d	Thu 2/19/26	Fri 10/31/25	79d
71	Review and finalize details for furniture	15 days	15 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Fri 11/21/25	Fri 11/21/25	0d
72	Furniture Order Due	1 day	1 day	0d	Mon 11/24/25	Mon 11/24/25	0d	Mon 11/24/25	Mon 11/24/25	0d
73	Furniture Lead Time	80 days	80 days	0d	Tue 12/23/25	Tue 11/25/25	20d	Fri 4/17/26	Fri 3/20/26	20d
74	**HVAC Equipment**	**80 days**	**58 days**	**22d**	**Tue 12/9/25**	**Mon 12/8/25**	**1d**	**Fri 4/3/26**	**Tue 3/3/26**	**23d**
75	Order Roof Top HVAC equipment	1 day	1 day	0d	Tue 12/9/25	Mon 12/8/25	1d	Tue 12/9/25	Mon 12/8/25	1d
76	HVAC Equipment Lead Time - RTUs	58 days	50 days	8d	Tue 12/9/25	Wed 12/17/25	-6d	Wed 3/4/26	Mon 3/2/26	2d
77	HVAC Equipment Lead Time - VAVs (Round 1)	58 days	57 days	1d	Tue 12/9/25	Tue 12/9/25	0d	Wed 3/4/26	Tue 3/3/26	1d
78	HVAC Equipment Lead Time - VAVs (Round 2)	32 days			Thu 2/19/26			Fri 4/3/26		
79	**Elevator Modernization**	**60 days**	**56 days**	**4d**	**Tue 1/13/26**	**Mon 1/12/26**	**1d**	**Mon 4/6/26**	**Mon 3/30/26**	**5d**
80	Contract for Elevator Modernization	1 day	1 day	0d	Thu 2/19/26	Mon 1/12/26	28d	Thu 2/19/26	Mon 1/12/26	28d

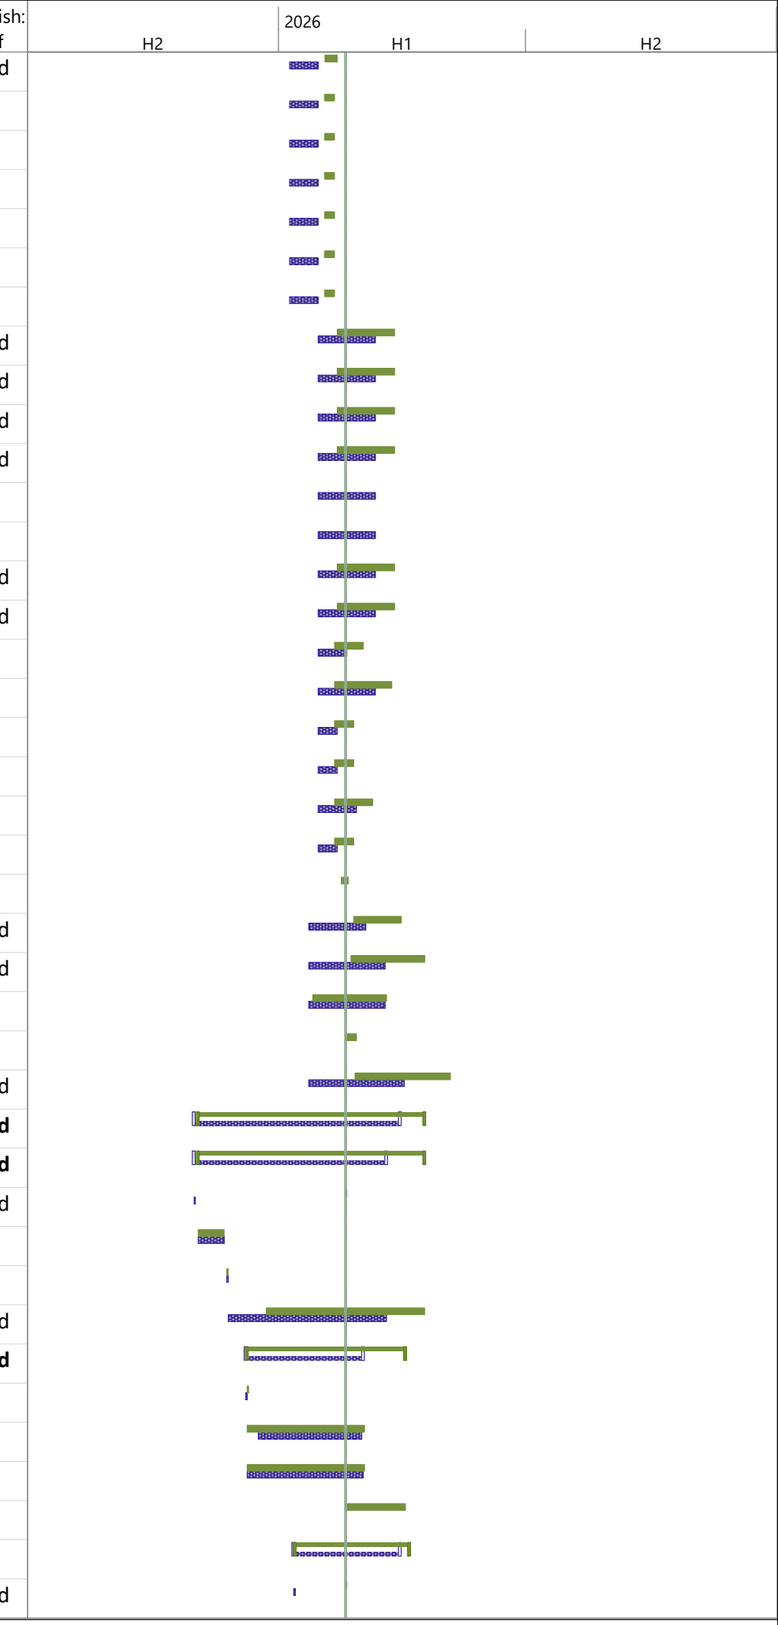

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
81	Elevator Equipment Lead Time	35 days	30 days	5d	Tue 1/13/26	Tue 1/13/26	0d	Mon 3/2/26	Mon 2/23/26	5d
82	Elevator Modernization	25 days	25 days	0d	Tue 3/3/26	Tue 2/24/26	5d	Mon 4/6/26	Mon 3/30/26	5d
83	**Demolition**	**34 days**	**29 days**	**5d**	**Mon 12/15/25**	**Mon 12/15/25**	**0d**	**Wed 2/4/26**	**Wed 1/28/26**	**5d**
84	MEP/F Make Safe	3 wks	3 wks	0d	Mon 12/15/25	Mon 12/15/25	0d	Thu 1/8/26	Thu 1/8/26	0d
85	Demolition	3 wks	5 wks	-10d	Thu 1/15/26	Fri 12/19/25	19d	Wed 2/4/26	Wed 1/28/26	5d
86	**Construction**	**103 days**	**101 days**	**2d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Thu 6/4/26**	**Mon 6/1/26**	**3d**
87	**Level 1 South**	**82.5 days**	**70 days**	**12.5d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Wed 5/6/26**	**Fri 4/17/26**	**12.5d**
88	Overhead MEP Rough In	20 days	30 days	-10d	Mon 1/12/26	Mon 1/12/26	0d	Fri 2/6/26	Fri 2/20/26	-10d
89	Low Voltage Bulk Cabling	10 days	20 days	-10d	Thu 2/19/26	Mon 2/2/26	13d	Wed 3/4/26	Fri 2/27/26	3d
90	Slab Demo and Coring	4 days	4 days	0d	Tue 1/20/26	Tue 1/20/26	0d	Fri 1/23/26	Fri 1/23/26	0d
91	Walls - Studs and Track	4 days	4 days	0d	Thu 1/22/26	Thu 1/22/26	0d	Tue 1/27/26	Tue 1/27/26	0d
92	Underslab MEP	6 days	6 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Mon 2/2/26	Mon 2/2/26	0d
93	Underslab MEP Inspection	1 day	1 day	0d	Thu 2/19/26	Tue 2/3/26	12d	Thu 2/19/26	Tue 2/3/26	12d
94	Concrete Slab Pourback	2 days	2 days	0d	Fri 2/20/26	Wed 2/4/26	12d	Mon 2/23/26	Thu 2/5/26	12d
95	Fire Alarm Rough-in	2 days	2 days	0d	Thu 2/19/26	Wed 1/28/26	16d	Fri 2/20/26	Thu 1/29/26	16d
96	MEP Rough-in Walls	10 days	10 days	0d	Fri 1/23/26	Fri 1/23/26	0d	Thu 2/5/26	Thu 2/5/26	0d
97	MEP Rough-in Inspection	5 days	1 day	4d	Fri 2/6/26	Fri 2/6/26	0d	Thu 2/12/26	Fri 2/6/26	4d
98	Single Side Drywall	5 days	5 days	0d	Thu 2/19/26	Wed 1/28/26	16d	Wed 2/25/26	Tue 2/3/26	16d
99	Second Side Drywall	5 days	5 days	0d	Thu 2/26/26	Mon 2/9/26	13d	Wed 3/4/26	Fri 2/13/26	13d
100	Wall Tape and Bed	13 days	6 days	7d	Tue 2/17/26	Wed 2/11/26	4d	Thu 3/5/26	Wed 2/18/26	11d
101	Grid Install Rework	5 days	6 days	-1d	Thu 3/12/26	Wed 3/11/26	1d	Wed 3/18/26	Wed 3/18/26	0d
102	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	8 days	0d	Tue 4/7/26	Fri 3/27/26	7d	Thu 4/16/26	Tue 4/7/26	7d
103	Light Fixture Install (Specialty)	8 days			Fri 4/24/26			Wed 5/6/26		
104	Ceiling Cover Inspection	1 day	1 day	0d	Fri 4/17/26	Wed 4/8/26	7d	Fri 4/17/26	Wed 4/8/26	7d
105	Ceiling Tile Installation	3 days	3 days	0d	Fri 4/24/26	Wed 4/15/26	7d	Tue 4/28/26	Fri 4/17/26	7d
106	Restroom Renovations	10 days	10 days	0d	Fri 3/13/26	Fri 2/27/26	10d	Fri 3/27/26	Fri 3/13/26	10d
107	Carpet and Tile Prep and Install	8 days	8 days	0d	Fri 3/27/26	Fri 3/13/26	10d	Tue 4/7/26	Tue 3/24/26	10d
108	Painting	10 days	10 days	0d	Fri 3/6/26	Thu 2/19/26	11d	Thu 3/19/26	Wed 3/4/26	11d
109	MEP Trimout	8 days	10 days	-2d	Fri 3/27/26	Fri 3/13/26	10d	Tue 4/7/26	Thu 3/26/26	8d
110	Millwork Install	5 days	5 days	0d	Thu 4/9/26	Mon 3/30/26	8d	Wed 4/15/26	Fri 4/3/26	8d
111	**Level 1 North**	**81 days**	**83 days**	**-2d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Mon 5/4/26**	**Wed 5/6/26**	**-2d**
112	Overhead MEP Rough In	20 days	30 days	-10d	Mon 1/12/26	Mon 1/12/26	0d	Fri 2/6/26	Fri 2/20/26	-10d
113	Low Voltage Bulk Cabling	10 days	20 days	-10d	Thu 2/19/26	Mon 2/2/26	13d	Wed 3/4/26	Fri 2/27/26	3d
114	Slab Demo and Coring	3 days	3 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Wed 1/28/26	Wed 1/28/26	0d
115	Walls - Studs and Track	3 days	3 days	0d	Mon 2/9/26	Mon 2/9/26	0d	Wed 2/11/26	Wed 2/11/26	0d
116	Underslab MEP	3 days	3 days	0d	Thu 1/29/26	Thu 1/29/26	0d	Mon 2/2/26	Mon 2/2/26	0d
117	Underslab MEP Inspection	1 day	1 day	0d	Thu 2/19/26	Tue 2/3/26	12d	Thu 2/19/26	Tue 2/3/26	12d
118	Concrete Slab Pourback	4 days	4 days	0d	Fri 2/20/26	Wed 2/4/26	12d	Wed 2/25/26	Mon 2/9/26	12d
119	Fire Alarm Rough-in	2 days	2 days	0d	Thu 2/19/26	Thu 2/12/26	5d	Fri 2/20/26	Fri 2/13/26	5d
120	MEP Rough-in Walls	10 days	10 days	0d	Mon 2/23/26	Mon 2/23/26	0d	Fri 3/6/26	Fri 3/6/26	0d

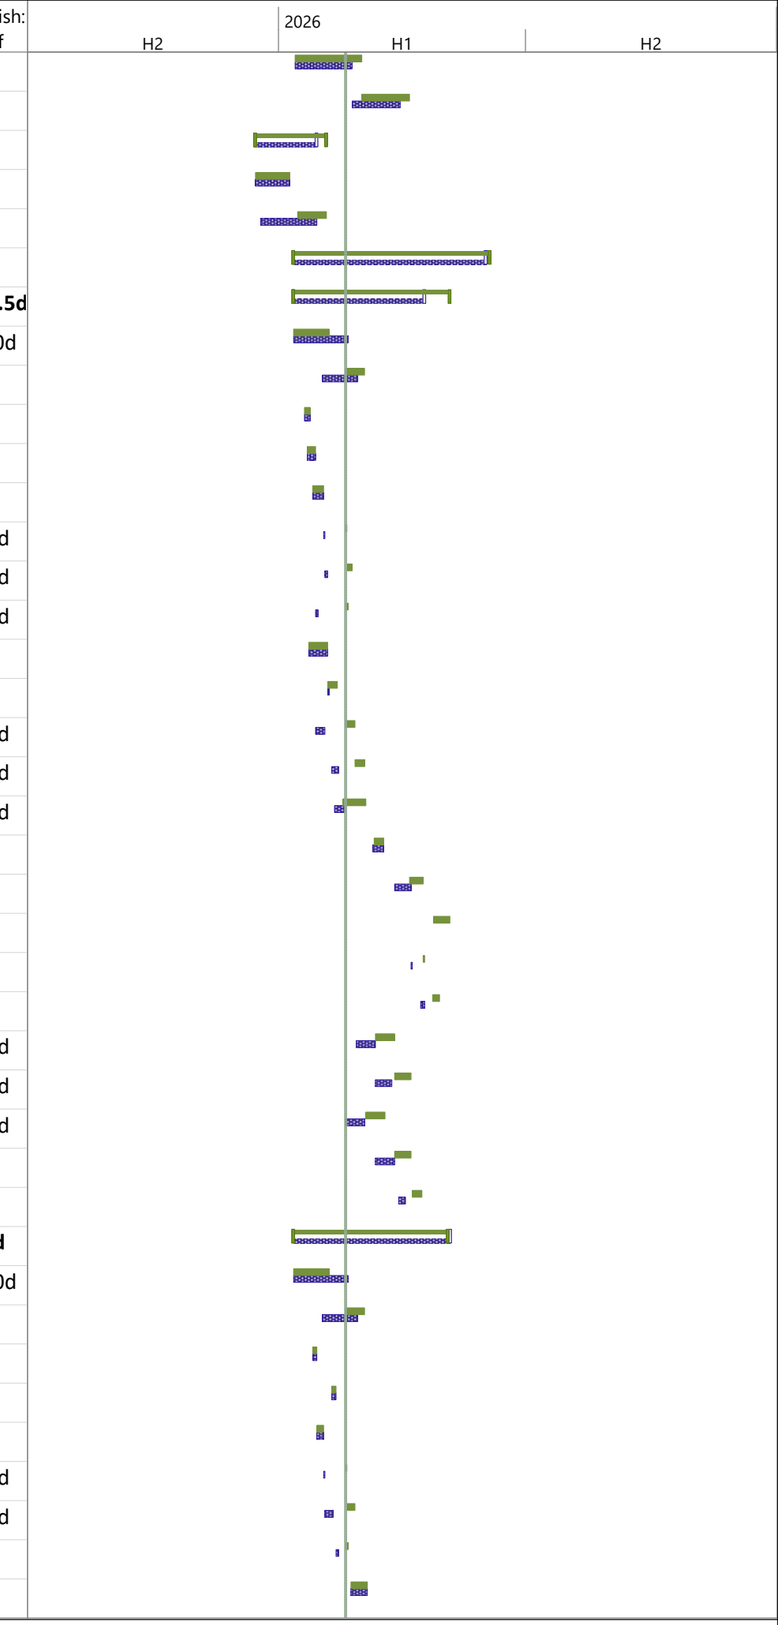

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
121	MEP Rough-in Inspection	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
122	Single Side Drywall	5 days	7 days	-2d	Thu 2/19/26	Thu 2/12/26	5d	Wed 2/25/26	Fri 2/20/26	3d
123	Second Side Drywall	5 days	7 days	-2d	Tue 3/10/26	Tue 3/10/26	0d	Mon 3/16/26	Wed 3/18/26	-2d
124	Wall Tape and Bed	6 days	6 days	0d	Wed 4/1/26	Thu 3/19/26	9d	Wed 4/8/26	Thu 3/26/26	9d
125	Grid Install Rework	4 days	4 days	0d	Thu 4/2/26	Fri 3/20/26	9d	Tue 4/7/26	Wed 3/25/26	9d
126	Light Fixture Install (Regular) and Ceiling MEP Finishes	12 days	12 days	0d	Tue 4/7/26	Fri 3/27/26	7d	Wed 4/22/26	Mon 4/13/26	7d
127	Ceiling Cover Inspection	1 day	1 day	0d	Thu 4/23/26	Tue 4/14/26	7d	Thu 4/23/26	Tue 4/14/26	7d
128	Ceiling Tile Installation	5 days	10 days	-5d	Fri 4/24/26	Wed 4/15/26	7d	Thu 4/30/26	Tue 4/28/26	2d
129	Restroom Renovations	10 days	10 days	0d	Thu 3/26/26	Fri 3/13/26	9d	Thu 4/9/26	Fri 3/27/26	9d
130	Carpet and Tile Prep and Install	8 days	8 days	0d	Thu 4/9/26	Fri 3/27/26	9d	Mon 4/20/26	Tue 4/7/26	9d
131	Painting	10 days	10 days	0d	Thu 4/9/26	Fri 3/27/26	9d	Wed 4/22/26	Thu 4/9/26	9d
132	MEP Trimout	8 days	10 days	-2d	Thu 4/23/26	Fri 4/10/26	9d	Mon 5/4/26	Thu 4/23/26	7d
133	Millwork Install	5 days	5 days	0d	Tue 4/21/26	Thu 4/30/26	-7d	Mon 4/27/26	Wed 5/6/26	-7d
134	**Level 2 South**	**80 days**	**83 days**	**-3d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Fri 5/1/26**	**Wed 5/6/26**	**-3d**
135	Overhead MEP Rough In	20 days	30 days	-10d	Mon 1/12/26	Mon 1/12/26	0d	Fri 2/6/26	Fri 2/20/26	-10d
136	Low Voltage Bulk Cabling	10 days	20 days	-10d	Thu 2/19/26	Mon 2/2/26	13d	Wed 3/4/26	Fri 2/27/26	3d
137	Slab Demo and Coring	2 days	2 days	0d	Thu 1/29/26	Thu 1/29/26	0d	Fri 1/30/26	Fri 1/30/26	0d
138	Walls - Studs and Track	4 days	4 days	0d	Wed 1/28/26	Wed 1/28/26	0d	Mon 2/2/26	Mon 2/2/26	0d
139	Underslab MEP	3 days	3 days	0d	Mon 2/2/26	Mon 2/2/26	0d	Wed 2/4/26	Wed 2/4/26	0d
140	Underslab MEP Inspection		1 day			Thu 2/5/26			Thu 2/5/26	
141	Fire Alarm Rough-in	2 days	2 days	0d	Thu 2/19/26	Tue 2/3/26	12d	Fri 2/20/26	Wed 2/4/26	12d
142	MEP Rough-in Walls	10 days	10 days	0d	Wed 2/11/26	Wed 2/11/26	0d	Tue 2/24/26	Tue 2/24/26	0d
143	MEP Rough-in Inspection	1 day	1 day	0d	Wed 2/25/26	Wed 2/25/26	0d	Wed 2/25/26	Wed 2/25/26	0d
144	Single Side Drywall	7 days	7 days	0d	Thu 2/19/26	Tue 2/3/26	12d	Fri 2/27/26	Wed 2/11/26	12d
145	Second Side Drywall	7 days	7 days	0d	Mon 3/2/26	Thu 2/26/26	2d	Tue 3/10/26	Fri 3/6/26	2d
146	Wall Tape and Bed	5 days	5 days	0d	Wed 4/1/26	Mon 3/9/26	17d	Tue 4/7/26	Fri 3/13/26	17d
147	Grid Install Rework	5 days	5 days	0d	Wed 4/1/26	Wed 3/11/26	15d	Tue 4/7/26	Tue 3/17/26	15d
148	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	12 days	-4d	Tue 4/7/26	Fri 3/27/26	7d	Thu 4/16/26	Mon 4/13/26	3d
149	Ceiling Cover Inspection	1 day	1 day	0d	Fri 4/17/26	Tue 4/14/26	3d	Fri 4/17/26	Tue 4/14/26	3d
150	Ceiling Tile Installation	5 days	10 days	-5d	Mon 4/20/26	Wed 4/15/26	3d	Fri 4/24/26	Tue 4/28/26	-2d
151	Restroom Renovations	10 days	10 days	0d	Wed 3/25/26	Mon 3/2/26	17d	Wed 4/8/26	Mon 3/16/26	17d
152	Carpet and Tile Prep and Install	10 days	10 days	0d	Wed 4/8/26	Mon 3/16/26	17d	Tue 4/21/26	Fri 3/27/26	17d
153	Painting	10 days	10 days	0d	Wed 4/8/26	Mon 3/16/26	17d	Tue 4/21/26	Fri 3/27/26	17d
154	MEP Trimout	8 days	10 days	-2d	Wed 4/22/26	Mon 3/30/26	17d	Fri 5/1/26	Fri 4/10/26	15d
155	Millwork Install	5 days	5 days	0d	Tue 4/21/26	Thu 4/30/26	-7d	Mon 4/27/26	Wed 5/6/26	-7d
156	**Level 2 North**	**81 days**	**83 days**	**-2d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Mon 5/4/26**	**Wed 5/6/26**	**-2d**
157	Overhead MEP Rough In	20 days	30 days	-10d	Mon 1/12/26	Mon 1/12/26	0d	Fri 2/6/26	Fri 2/20/26	-10d
158	Low Voltage Bulk Cabling	10 days	20 days	-10d	Thu 2/19/26	Mon 2/2/26	13d	Wed 3/4/26	Fri 2/27/26	3d
159	Slab Demo and Coring - Level 2 North	3 days	3 days	0d	Mon 2/2/26	Mon 2/2/26	0d	Wed 2/4/26	Wed 2/4/26	0d
160	Walls - Studs and Track	4 days	4 days	0d	Tue 2/3/26	Tue 2/3/26	0d	Fri 2/6/26	Fri 2/6/26	0d

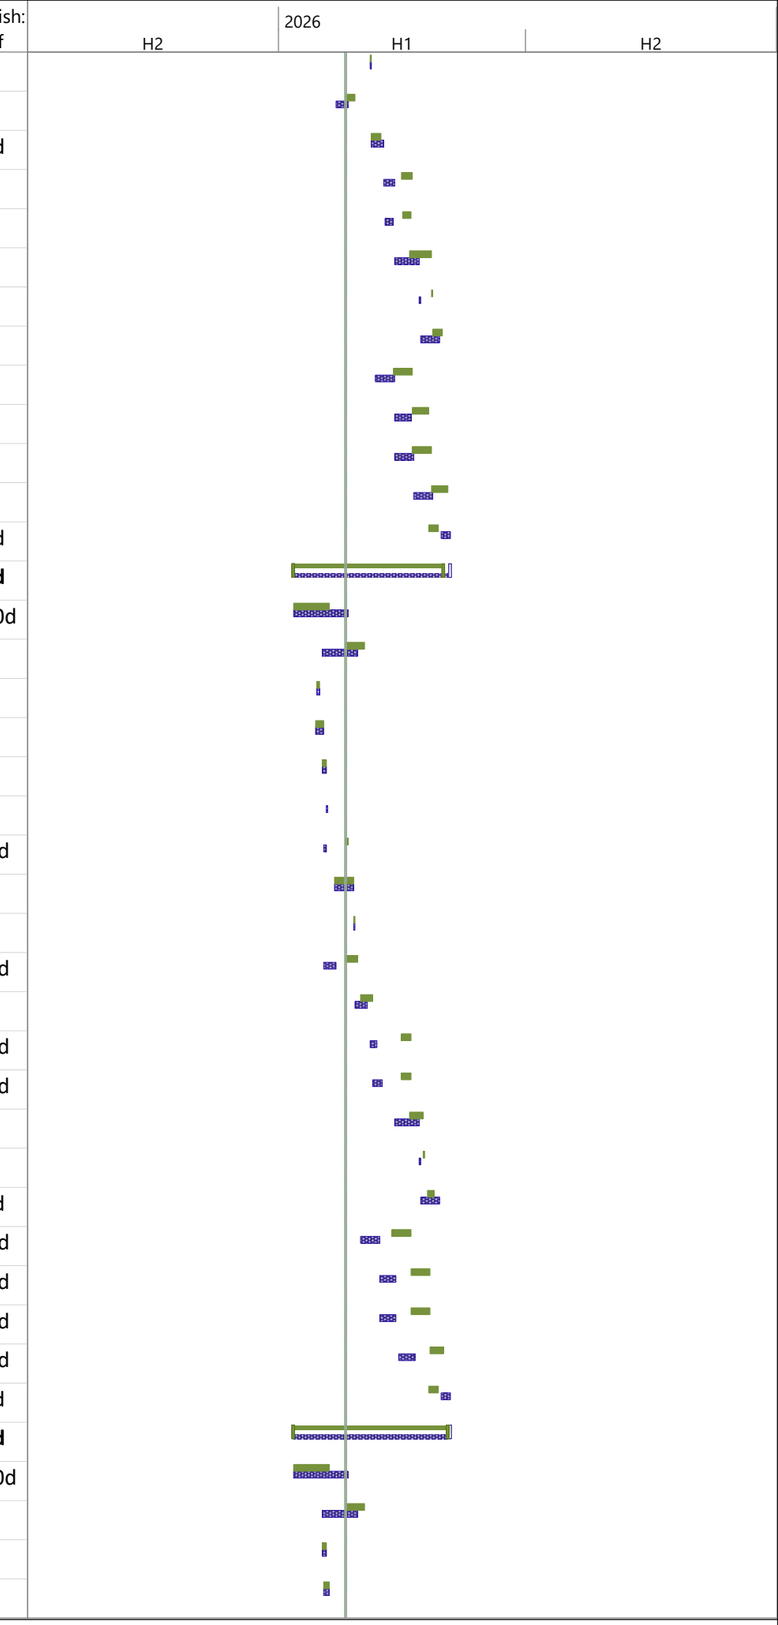
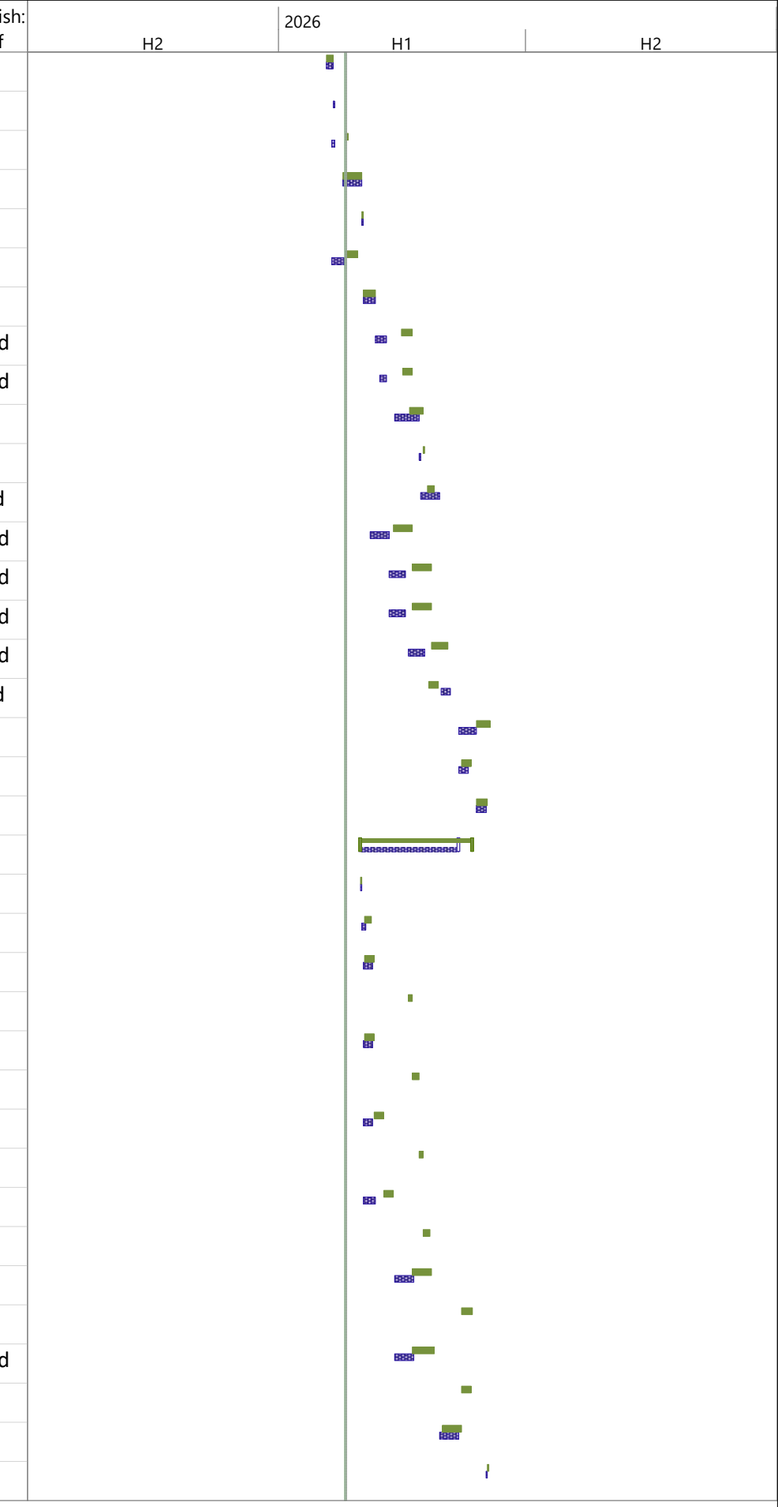
	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
161	Underslab MEP	3 days	3 days	0d	Thu 2/5/26	Thu 2/5/26	0d	Mon 2/9/26	Mon 2/9/26	0d
162	Underslab MEP Inspection		1 day			Tue 2/10/26			Tue 2/10/26	
163	Fire Alarm Rough-in	2 days	2 days	0d	Thu 2/19/26	Mon 2/9/26	8d	Fri 2/20/26	Tue 2/10/26	8d
164	MEP Rough-in Walls	10 days	10 days	0d	Tue 2/17/26	Tue 2/17/26	0d	Mon 3/2/26	Mon 3/2/26	0d
165	MEP Rough-in Inspection	1 day	1 day	0d	Tue 3/3/26	Tue 3/3/26	0d	Tue 3/3/26	Tue 3/3/26	0d
166	Single Side Drywall	7 days	7 days	0d	Thu 2/19/26	Mon 2/9/26	8d	Fri 2/27/26	Tue 2/17/26	8d
167	Second Side Drywall - Level 2 North	7 days	7 days	0d	Wed 3/4/26	Wed 3/4/26	0d	Thu 3/12/26	Thu 3/12/26	0d
168	Wall Tape and Bed	6 days	6 days	0d	Wed 4/1/26	Fri 3/13/26	13d	Wed 4/8/26	Fri 3/20/26	13d
169	Grid Install Rework	5 days	5 days	0d	Thu 4/2/26	Mon 3/16/26	13d	Wed 4/8/26	Fri 3/20/26	13d
170	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	12 days	-4d	Tue 4/7/26	Fri 3/27/26	7d	Thu 4/16/26	Mon 4/13/26	3d
171	Ceiling Cover Inspection	1 day	1 day	0d	Fri 4/17/26	Tue 4/14/26	3d	Fri 4/17/26	Tue 4/14/26	3d
172	Ceiling Tile Installation - Level 2 North	5 days	10 days	-5d	Mon 4/20/26	Wed 4/15/26	3d	Fri 4/24/26	Tue 4/28/26	-2d
173	Restroom Renovations	10 days	10 days	0d	Thu 3/26/26	Mon 3/9/26	13d	Thu 4/9/26	Mon 3/23/26	13d
174	Carpet and Tile Prep and Install	10 days	10 days	0d	Thu 4/9/26	Mon 3/23/26	13d	Wed 4/22/26	Fri 4/3/26	13d
175	Painting	10 days	10 days	0d	Thu 4/9/26	Mon 3/23/26	13d	Wed 4/22/26	Fri 4/3/26	13d
176	MEP Trimout - Level 2 North	8 days	10 days	-2d	Thu 4/23/26	Mon 4/6/26	13d	Mon 5/4/26	Fri 4/17/26	11d
177	Millwork Install	5 days	5 days	0d	Tue 4/21/26	Thu 4/30/26	-7d	Mon 4/27/26	Wed 5/6/26	-7d
178	Inspections and Commissioning	8 days	9 days	-1d	Tue 5/26/26	Wed 5/13/26	9d	Thu 6/4/26	Mon 5/25/26	8d
179	Punch Walk and Corrections	5 days	5 days	0d	Fri 5/15/26	Wed 5/13/26	2d	Thu 5/21/26	Tue 5/19/26	2d
180	Final Clean	6 days	5 days	1d	Tue 5/26/26	Tue 5/26/26	0d	Tue 6/2/26	Mon 6/1/26	1d
181	**Install of Owner Provided Equipment/Vendors**	**60 days**	**52 days**	**8d**	**Mon 3/2/26**	**Mon 3/2/26**	**0d**	**Fri 5/22/26**	**Tue 5/12/26**	**8d**
182	Confirm Weather For RTU Replacements	1 day	1 day	0d	Mon 3/2/26	Mon 3/2/26	0d	Mon 3/2/26	Mon 3/2/26	0d
183	RTU Replacement	3 days	3 days	0d	Thu 3/5/26	Tue 3/3/26	2d	Mon 3/9/26	Thu 3/5/26	2d
184	VAV Replacements - Level 1 South (Round 1)	5 days	5 days	0d	Thu 3/5/26	Wed 3/4/26	1d	Wed 3/11/26	Tue 3/10/26	1d
185	VAV Replacements - Level 1 South (Round 2)	3 days			Mon 4/6/26			Wed 4/8/26		
186	VAV Replacements - Level 1 North (Round 1)	5 days	5 days	0d	Thu 3/5/26	Wed 3/4/26	1d	Wed 3/11/26	Tue 3/10/26	1d
187	VAV Replacements - Level 1 North (Round 2)	3 days			Thu 4/9/26			Mon 4/13/26		
188	VAV Replacements - Level 2 South (Round 1)	5 days	5 days	0d	Thu 3/12/26	Wed 3/4/26	6d	Wed 3/18/26	Tue 3/10/26	6d
189	VAV Replacements - Level 2 South (Round 2)	3 days			Tue 4/14/26			Thu 4/16/26		
190	VAV Replacements - Level 2 North (Round 1)	5 days	7 days	-2d	Thu 3/19/26	Wed 3/4/26	11d	Wed 3/25/26	Thu 3/12/26	9d
191	VAV Replacements - Level 2 North	3 days			Fri 4/17/26			Tue 4/21/26		
192	AV Equipment Rough-in (By Others)	10 days	10 days	0d	Thu 4/9/26	Fri 3/27/26	9d	Wed 4/22/26	Thu 4/9/26	9d
193	AV Equipment Installation and Trim (By Others)	6 days			Fri 5/15/26			Fri 5/22/26		
194	Security Systems Equipment Rough-in (By Others)	12 days	10 days	2d	Thu 4/9/26	Fri 3/27/26	9d	Fri 4/24/26	Thu 4/9/26	11d
195	Security Systems Equipment Installation and Trim (By Others)	5 days			Fri 5/15/26			Thu 5/21/26		
196	Furniture Systems Installation (By Others)	10 days	10 days	0d	Fri 5/1/26	Wed 4/29/26	2d	Thu 5/14/26	Tue 5/12/26	2d
197	Move in	1 day	1 day	0d	Wed 6/3/26	Tue 6/2/26	1d	Wed 6/3/26	Tue 6/2/26	1d
