Public Storage HQ - Project Orange
Preliminary Project Schedule
2811 Internet Blvd
Frisco, TX 75034

ID	Task Name	Duration	% Complete	Start	Finish
0	**Public Storage HQ**	**235 days**	**75%**	**Mon 9/8/25**	**Fri 8/7/26**
22	**ARCO Procurement**	**91 days**	**88%**	**Fri 1/9/26**	**Fri 5/15/26**
26	Light Fixtures - Regular Fixtures	8 wks	95%	Tue 2/10/26	Mon 4/6/26
27	Light Fixtures - Specialty Fixtures	9.5 wks	67%	Wed 2/18/26	Fri 4/24/26
30	Millwork Field Measure and Fab - Level 1 South	5 wks	84%	Thu 3/5/26	Wed 4/8/26
31	Millwork Field Measure and Fab - Level 1 North	5 wks	52%	Tue 3/17/26	Mon 4/20/26
32	Millwork Field Measure and Fab - Level 2 South	5 wks	96%	Mon 3/2/26	Fri 4/3/26
33	Millwork Field Measure and Fab - Level 2 North	5 wks	60%	Fri 3/13/26	Thu 4/16/26
46	Flooring - FC1	7.8 wks	90%	Fri 2/13/26	Wed 4/8/26
47	Flooring - FC2	7.8 wks	90%	Fri 2/13/26	Wed 4/8/26
50	Flooring - LVT1	8.8 wks	80%	Fri 2/13/26	Wed 4/15/26
56	Wall Tile - WT3	7.8 wks	95%	Wed 2/11/26	Mon 4/6/26
59	Door Frames	6.2 wks	87%	Wed 2/25/26	Wed 4/8/26
60	Doors, Hardware	8 wks	73%	Mon 2/23/26	Fri 4/17/26
61	Appliances	6 wks	93%	Mon 4/6/26	Fri 5/15/26
63	Ceiling Baffles - Breakroom	7.6 wks	68%	Thu 2/26/26	Mon 4/20/26
64	**Procurement Of Direct FBO items**	**116 days**	**96%**	**Mon 11/3/25**	**Fri 4/17/26**
65	**Furniture**	**116 days**	**89%**	**Mon 11/3/25**	**Fri 4/17/26**
69	Furniture Lead Time	80 days	86%	Tue 12/23/25	Fri 4/17/26
70	**HVAC Equipment**	**80 days**	**99%**	**Tue 12/9/25**	**Fri 4/3/26**
74	HVAC Equipment Lead Time - VAVs (Round 2)	32 days	97%	Thu 2/19/26	Fri 4/3/26
75	**Elevator Modernization**	**60 days**	**97%**	**Tue 1/13/26**	**Mon 4/6/26**
78	Elevator Modernization	25 days	92%	Tue 3/3/26	Mon 4/6/26
82	**Construction**	**149 days**	**47%**	**Mon 1/12/26**	**Fri 8/7/26**
83	**Level 1 South**	**82.5 days**	**69%**	**Mon 1/12/26**	**Wed 5/6/26**
98	Light Fixture Install (Regular) and Ceiling MEP Finishes	12.4 days	13%	Mon 3/30/26	Wed 4/15/26

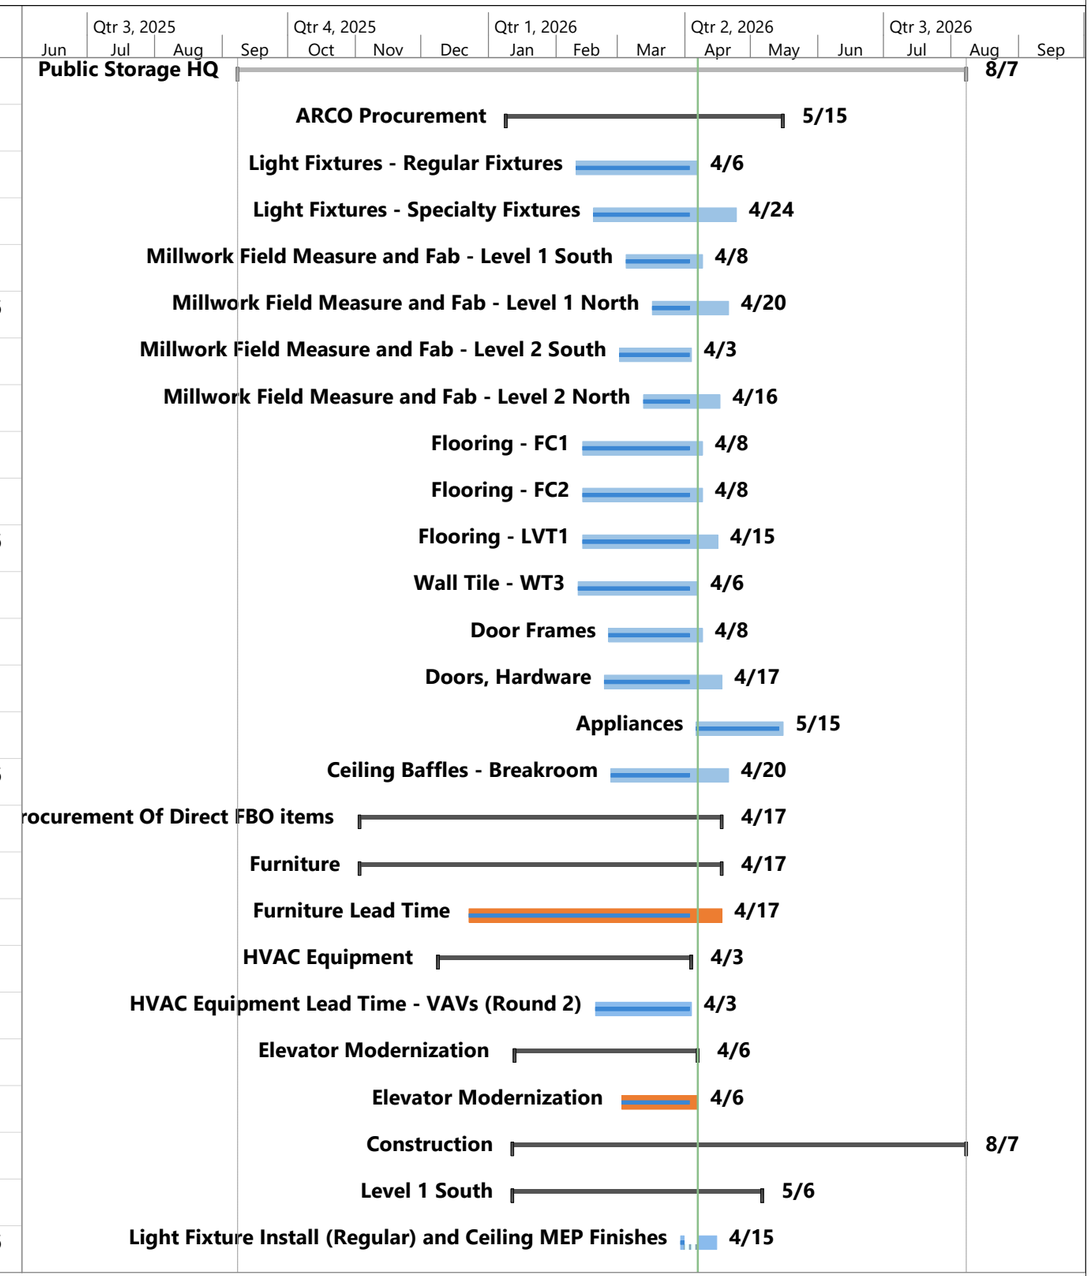

Public Storage HQ - Project Orange
Preliminary Project Schedule
2811 Internet Blvd
Frisco, TX 75034

ID	Task Name	Duration	% Complete	Start	Finish
99	Light Fixture Install (Specialty)	8 days	0%	Fri 4/24/26	Wed 5/6/26
100	Ceiling Cover Inspection	1 day	0%	Wed 4/15/26	Thu 4/16/26
101	Ceiling Tile Installation	3 days	0%	Tue 4/28/26	Thu 4/30/26
102	Restroom Renovations	10 days	50%	Fri 3/27/26	Thu 4/9/26
103	Carpet and Tile Prep and Install	9 days	0%	Mon 4/6/26	Thu 4/16/26
105	MEP Trimout	8 days	0%	Fri 4/10/26	Tue 4/21/26
106	Millwork Install	5 days	0%	Thu 4/16/26	Wed 4/22/26
107	**Level 1 North**	**149 days**	**33%**	**Mon 1/12/26**	**Fri 8/7/26**
120	Wall Tape and Bed	6 days	0%	Thu 4/9/26	Thu 4/16/26
121	Grid Install Rework	4 days	0%	Fri 4/10/26	Wed 4/15/26
122	Light Fixture Install (Regular) and Ceiling MEP Finishes	12 days	0%	Thu 4/9/26	Fri 4/24/26
123	Ceiling Cover Inspection	1 day	0%	Mon 4/27/26	Mon 4/27/26
124	Ceiling Tile Installation	73 days	0%	Tue 4/28/26	Fri 8/7/26
125	Restroom Renovations	10 days	0%	Fri 4/3/26	Fri 4/17/26
126	Carpet and Tile Prep and Install	7 days	0%	Fri 4/17/26	Mon 4/27/26
127	Painting	10 days	0%	Fri 4/17/26	Thu 4/30/26
128	MEP Trimout	8 days	0%	Fri 5/1/26	Tue 5/12/26
129	Millwork Install	5 days	0%	Tue 5/5/26	Mon 5/11/26
130	**Level 2 South**	**80 days**	**61%**	**Mon 1/12/26**	**Fri 5/1/26**
143	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	0%	Mon 3/30/26	Wed 4/8/26
144	Ceiling Cover Inspection	1 day	0%	Thu 4/9/26	Thu 4/9/26
145	Ceiling Tile Installation	5 days	0%	Fri 4/10/26	Thu 4/16/26
146	Restroom Renovations	10 days	30%	Tue 3/31/26	Tue 4/14/26
147	Carpet and Tile Prep and Install	6 days	0%	Tue 4/14/26	Tue 4/21/26
148	Painting	10 days	0%	Wed 4/8/26	Tue 4/21/26
149	MEP Trimout	8 days	0%	Wed 4/22/26	Fri 5/1/26

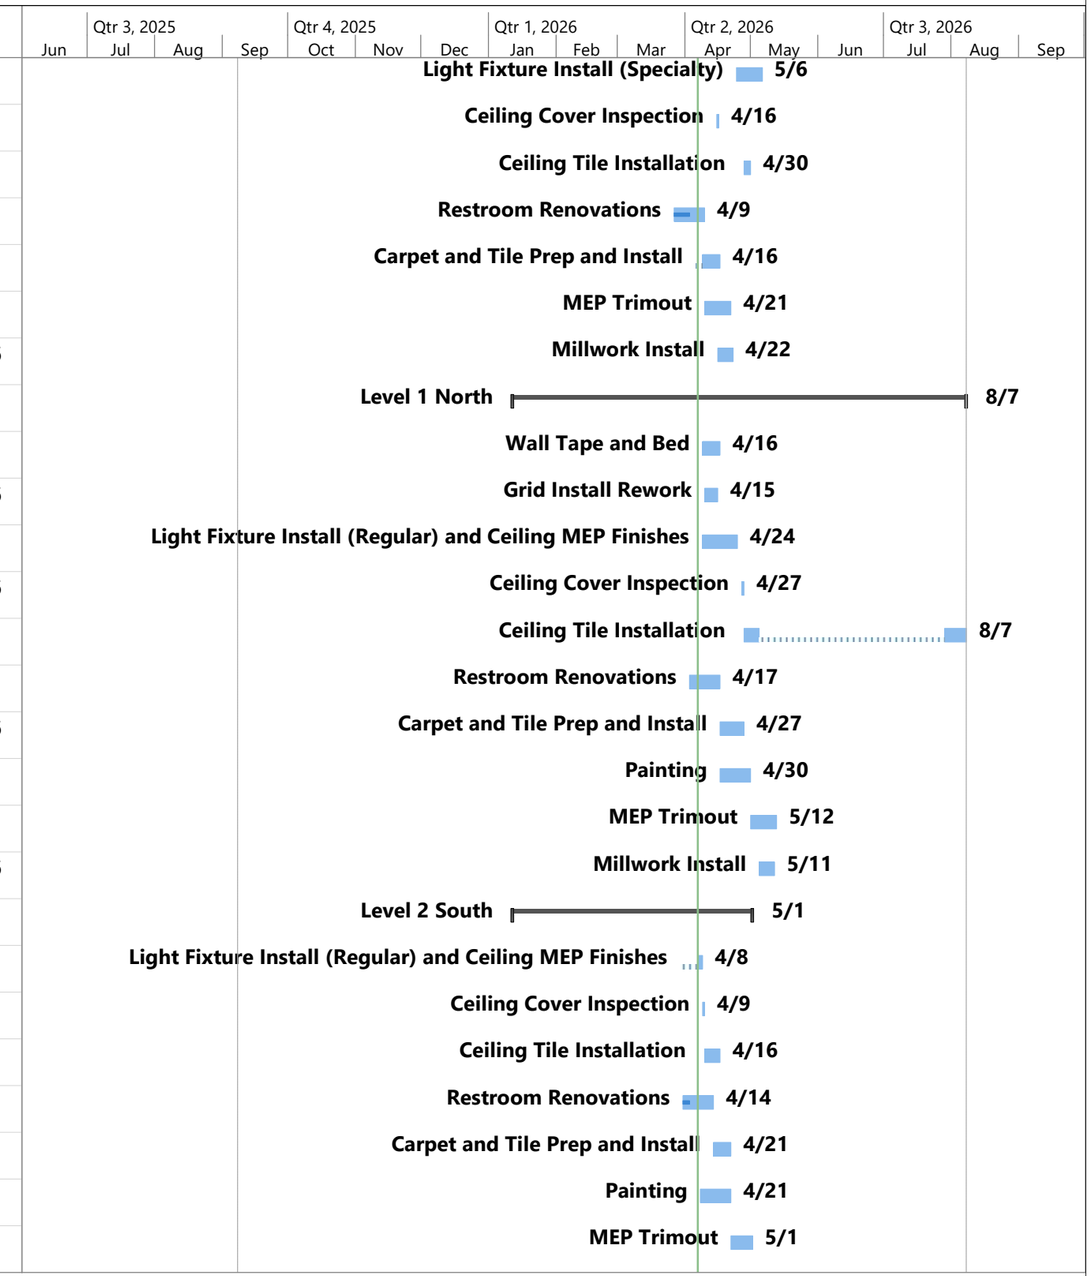

Public Storage HQ - Project Orange
Preliminary Project Schedule
2811 Internet Blvd
Frisco, TX 75034
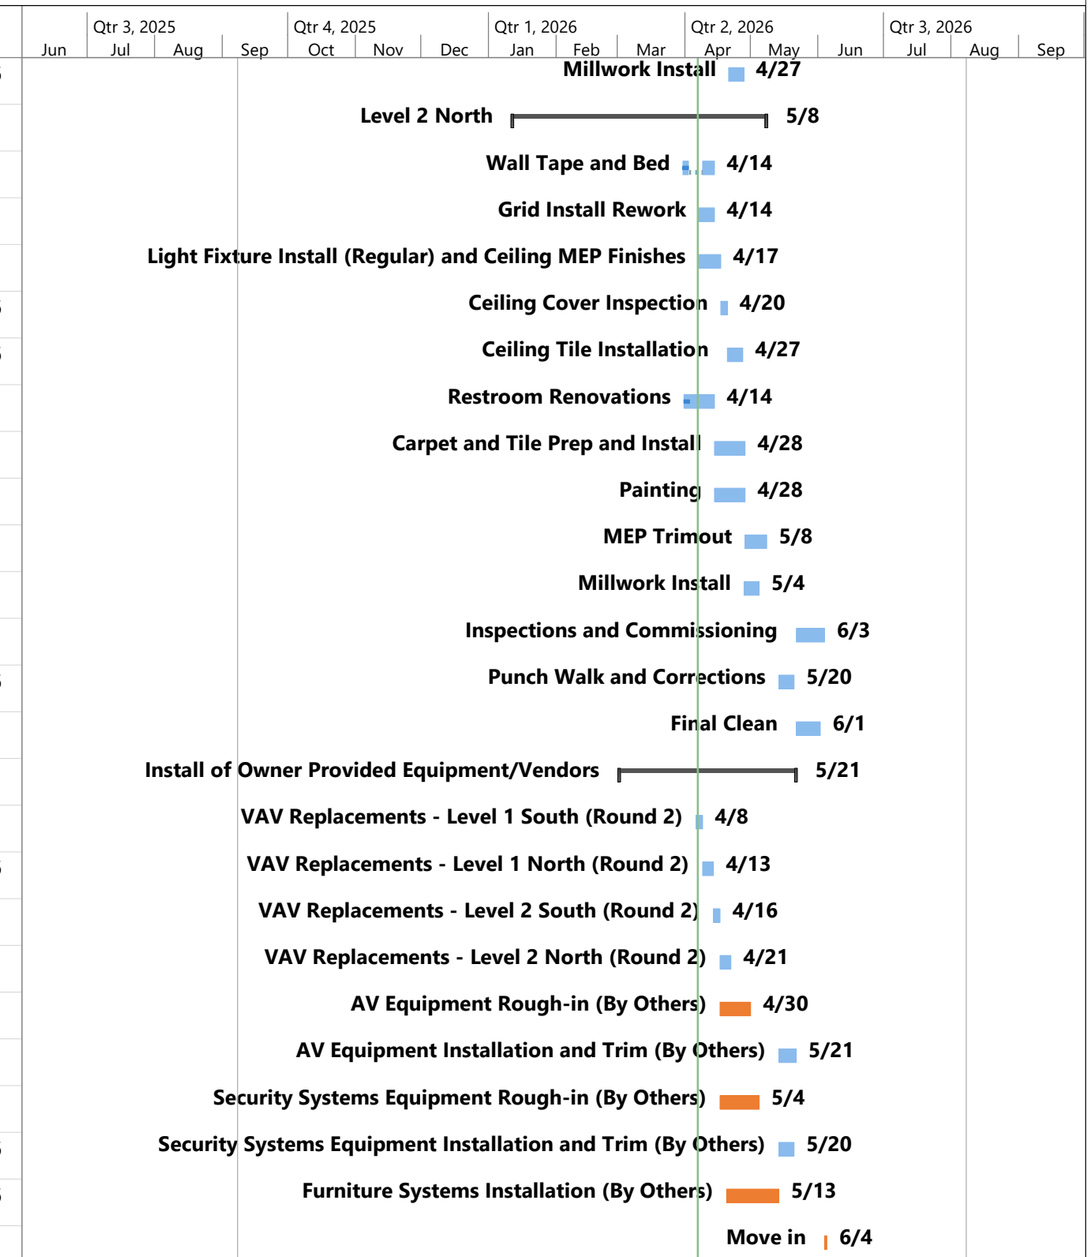
ID	Task Name	Duration	% Complete	Start	Finish
150	Millwork Install	5 days	0%	Tue 4/21/26	Mon 4/27/26
151	**Level 2 North**	**84.3 days**	**52%**	**Mon 1/12/26**	**Fri 5/8/26**
162	Wall Tape and Bed	10.3 days	26%	Tue 3/31/26	Tue 4/14/26
163	Grid Install Rework	5 days	0%	Tue 4/7/26	Tue 4/14/26
164	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	0%	Tue 4/7/26	Fri 4/17/26
165	Ceiling Cover Inspection	1 day	0%	Fri 4/17/26	Mon 4/20/26
166	Ceiling Tile Installation	5 days	0%	Mon 4/20/26	Mon 4/27/26
167	Restroom Renovations	10 days	27%	Tue 3/31/26	Tue 4/14/26
168	Carpet and Tile Prep and Install	10 days	0%	Tue 4/14/26	Tue 4/28/26
169	Painting	10 days	0%	Tue 4/14/26	Tue 4/28/26
170	MEP Trimout	8 days	0%	Tue 4/28/26	Fri 5/8/26
171	Millwork Install	5 days	0%	Tue 4/28/26	Mon 5/4/26
172	Inspections and Commissioning	8 days	0%	Fri 5/22/26	Wed 6/3/26
173	Punch Walk and Corrections	5 days	0%	Thu 5/14/26	Wed 5/20/26
174	Final Clean	6 days	0%	Fri 5/22/26	Mon 6/1/26
175	**Install of Owner Provided Equipment/Vendors**	**59 days**	**26%**	**Mon 3/2/26**	**Thu 5/21/26**
179	VAV Replacements - Level 1 South (Round 2)	3 days	0%	Mon 4/6/26	Wed 4/8/26
181	VAV Replacements - Level 1 North (Round 2)	3 days	0%	Thu 4/9/26	Mon 4/13/26
183	VAV Replacements - Level 2 South (Round 2)	3 days	0%	Tue 4/14/26	Thu 4/16/26
185	VAV Replacements - Level 2 North (Round 2)	3 days	0%	Fri 4/17/26	Tue 4/21/26
186	AV Equipment Rough-in (By Others)	10 days	0%	Fri 4/17/26	Thu 4/30/26
187	AV Equipment Installation and Trim (By Others)	6 days	0%	Thu 5/14/26	Thu 5/21/26
188	Security Systems Equipment Rough-in (By Others)	12 days	0%	Fri 4/17/26	Mon 5/4/26
189	Security Systems Equipment Installation and Trim (By Others)	5 days	0%	Thu 5/14/26	Wed 5/20/26
190	Furniture Systems Installation (By Others)	18 days	0%	Mon 4/20/26	Wed 5/13/26
191	Move in	1 day	0%	Thu 6/4/26	Thu 6/4/26
