	Name	Duration Current	Duration Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finis Diff
1	**GENERAL REQUIREMENTS AND CONDITIONS**	**241 day**	**241 day**	**0d**	**Mon 25/09/08**	**Mon 25/09/08**	**0d**	**Tue 26/08/18**	**Tue 26/08/18**	**0d**
2	Notice to Proceed	1 day	1 day	0d	Mon 25/09/08	Mon 25/09/08	0d	Mon 25/09/08	Mon 25/09/08	0d
3	DELAY - PERMIT DELAY	32 days	32 days	0d	Tue 25/09/09	Tue 25/09/09	0d	Wed 25/10/22	Wed 25/10/22	0d
4	Obtain Building Permit	0 days	0 days	0d	Wed 25/10/22	Wed 25/10/22	0d	Wed 25/10/22	Wed 25/10/22	0d
5	ACHD ROW Permit	0 days	0 days	0d	Wed 25/10/29	Wed 25/10/29	0d	Wed 25/10/29	Wed 25/10/29	0d
6	Obtain LDIR Approval to Proceed	0 days	0 days	0d	Mon 25/10/27	Mon 25/10/27	0d	Mon 25/10/27	Mon 25/10/27	0d
7	Receive CAD Base Files from Public Storage	10 days	10 days	0d	Tue 25/09/09	Tue 25/09/09	0d	Mon 25/09/22	Mon 25/09/22	0d
8	Procure Early Work Subcontractors	5 days	5 days	0d	Tue 25/09/09	Tue 25/09/09	0d	Mon 25/09/15	Mon 25/09/15	0d
9	Procure Remaining Subcontractors	20 days	20 days	0d	Tue 25/09/16	Tue 25/09/16	0d	Mon 25/10/13	Mon 25/10/13	0d
10	Submittals (SWPPP/NOI)	10 days	10 days	0d	Tue 25/09/16	Tue 25/09/16	0d	Mon 25/09/29	Mon 25/09/29	0d
11	Submittals (SES /Switchgear)	34 days	10 days	24d	Tue 25/09/16	Tue 25/09/16	0d	Fri 25/10/31	Mon 25/09/29	24c
12	Submittals (numerous)	90 days	70 days	20d	Tue 25/10/14	Tue 25/10/14	0d	Fri 26/02/20	Fri 26/01/23	20c
13	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG B	40 days	40 days	0d	Thu 25/10/23	Tue 25/09/09	32d	Fri 25/12/19	Mon 25/11/03	34c
14	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG A	40 days	40 days	0d	Thu 25/11/06	Tue 25/09/23	32d	Tue 26/01/06	Mon 25/11/17	36c
15	Procure SES's/Switchgears (6 mos ~ 130 WD)	70 days	130 day	-60d	Mon 25/11/03	Tue 25/09/30	24d	Thu 26/02/12	Fri 26/04/03	-36
16	Light Fixture Submittal Review and Approval	10 days			Mon 26/01/26			Fri 26/02/06		
17	Light Fixture Package Alternate - Fab and Deliver	10 days			Mon 26/02/09			Fri 26/02/20		
18	Light Fixture Package Spec'd - Fab and Deliver	8 wks			Mon 26/02/09			Fri 26/04/03		
19	Fire Sprinkler Design and Approval	65 days	55 days	10d	Tue 25/10/14	Tue 25/10/14	0d	Fri 26/01/16	Fri 26/01/02	10c
20	Fire Alarm System Design and Approval	40 days	40 days	0d	Tue 25/10/14	Tue 25/10/14	0d	Wed 25/12/10	Wed 25/12/10	0d
21	ASPHALT BATCH PLANT SHUTDOWN	70 days	70 days	0d	Mon 25/11/17	Mon 25/11/17	0d	Thu 26/02/26	Thu 26/02/26	0d
22	TWENTY WORKING DAYS OF WEATHER DELAY	14 days	17 days	-3d	Thu 26/07/30	Mon 26/07/27	3d	Tue 26/08/18	Tue 26/08/18	0d
23	WEATHER DELAY - Rain and High Winds - Imapct SOG B	2 days	2 days	0d	Wed 25/12/17	Wed 25/12/17	0d	Thu 25/12/18	Thu 25/12/18	0d
24	WEATHER DELAY - Rain - Impact SOG B	1 day	1 day	0d	Mon 25/12/22	Mon 25/12/22	0d	Mon 25/12/22	Mon 25/12/22	0d
25	WEATHER DELAY - Rain - Impact SOG B	3 days			Thu 26/01/08			Mon 26/01/12		
26	Substantial Completion	0 days	0 days	0d	Tue 26/08/18	Tue 26/08/18	0d	Tue 26/08/18	Tue 26/08/18	0d
27	Clean Up and Project Close Out	5 days	5 days	0d	Mon 26/07/20	Wed 26/07/15	3d	Fri 26/07/24	Tue 26/07/21	3d
28	Demobilize	3 days	3 days	0d	Mon 26/07/27	Wed 26/07/22	3d	Wed 26/07/29	Fri 26/07/24	3d
29	**SITEWORK**	**197 day**	**196 day**	**1d**	**Mon 25/09/08**	**Mon 25/09/08**	**0d**	**Tue 26/06/16**	**Mon 26/06/15**	**1d**
30	Mobilization	5 days	5 days	0d	Mon 25/09/08	Mon 25/09/08	0d	Mon 25/09/15	Mon 25/09/15	0d
31	Construction Staking & Surveying	90 days	70 days	20d	Mon 25/09/08	Mon 25/09/08	0d	Fri 26/01/16	Wed 25/12/17	22c
32	Inspections and Testing	100 day	100 day	0d	Fri 25/09/12	Fri 25/09/12	0d	Fri 26/02/13	Fri 26/02/13	0d
33	Erosion Control & SWPP	5 days	5 days	0d	Tue 25/09/16	Tue 25/09/16	0d	Mon 25/09/22	Mon 25/09/22	0d
34	Maintain Erosion Control	120 day	100 day	20d	Tue 25/09/23	Tue 25/09/23	0d	Fri 26/03/13	Fri 26/02/13	20c
35	Structure Demo (Partial Building & RV Storage)	5 days	5 days	0d	Mon 25/11/03	Mon 25/11/03	0d	Fri 25/11/07	Fri 25/11/07	0d
36	Site Demolition (Trees,Sawcut, Asphalt, Base)	0 days	0 days	0d	Mon 25/09/08	Mon 25/09/08	0d	Fri 25/09/12	Fri 25/09/12	0d
37	Re-Mobilization	4 days	4 days	0d	Thu 25/10/23	Thu 25/10/23	0d	Tue 25/10/28	Tue 25/10/28	0d
38	Clear/Grub & Overlot Grading	12 days	12 days	0d	Mon 25/09/08	Mon 25/09/08	0d	Tue 25/09/23	Tue 25/09/23	0d
39	FRAGNET - CITY PRE-CON & 7 DAY NOTICE	7 days	7 days	0d	Wed 25/10/29	Wed 25/10/29	0d	Thu 25/11/06	Thu 25/11/06	0d
40	Site - Sewer Lines and Devices/Ten Mile Tie-In	13 days	13 days	0d	Fri 25/11/14	Fri 25/11/14	0d	Thu 25/12/04	Thu 25/12/04	0d
41	Storm Drain Lines and Devices - North & South of Buildings	15 days	15 days	0d	Tue 26/03/24	Thu 26/03/26	-2d	Mon 26/04/13	Wed 26/04/15	-2d
42	Storm Drain Lines South	6 days	6 days	0d	Mon 25/12/22	Mon 25/12/22	0d	Tue 25/12/30	Tue 25/12/30	0d
43	DELAY - GIRR License Agreement Approval to Proceed	6 days	6 days	0d	Fri 25/12/05	Fri 25/12/05	0d	Fri 25/12/12	Fri 25/12/12	0d
44	DELAY - RFI #14 - GIRR Separation	4 days	4 days	0d	Mon 25/12/15	Mon 25/12/15	0d	Thu 25/12/18	Thu 25/12/18	0d

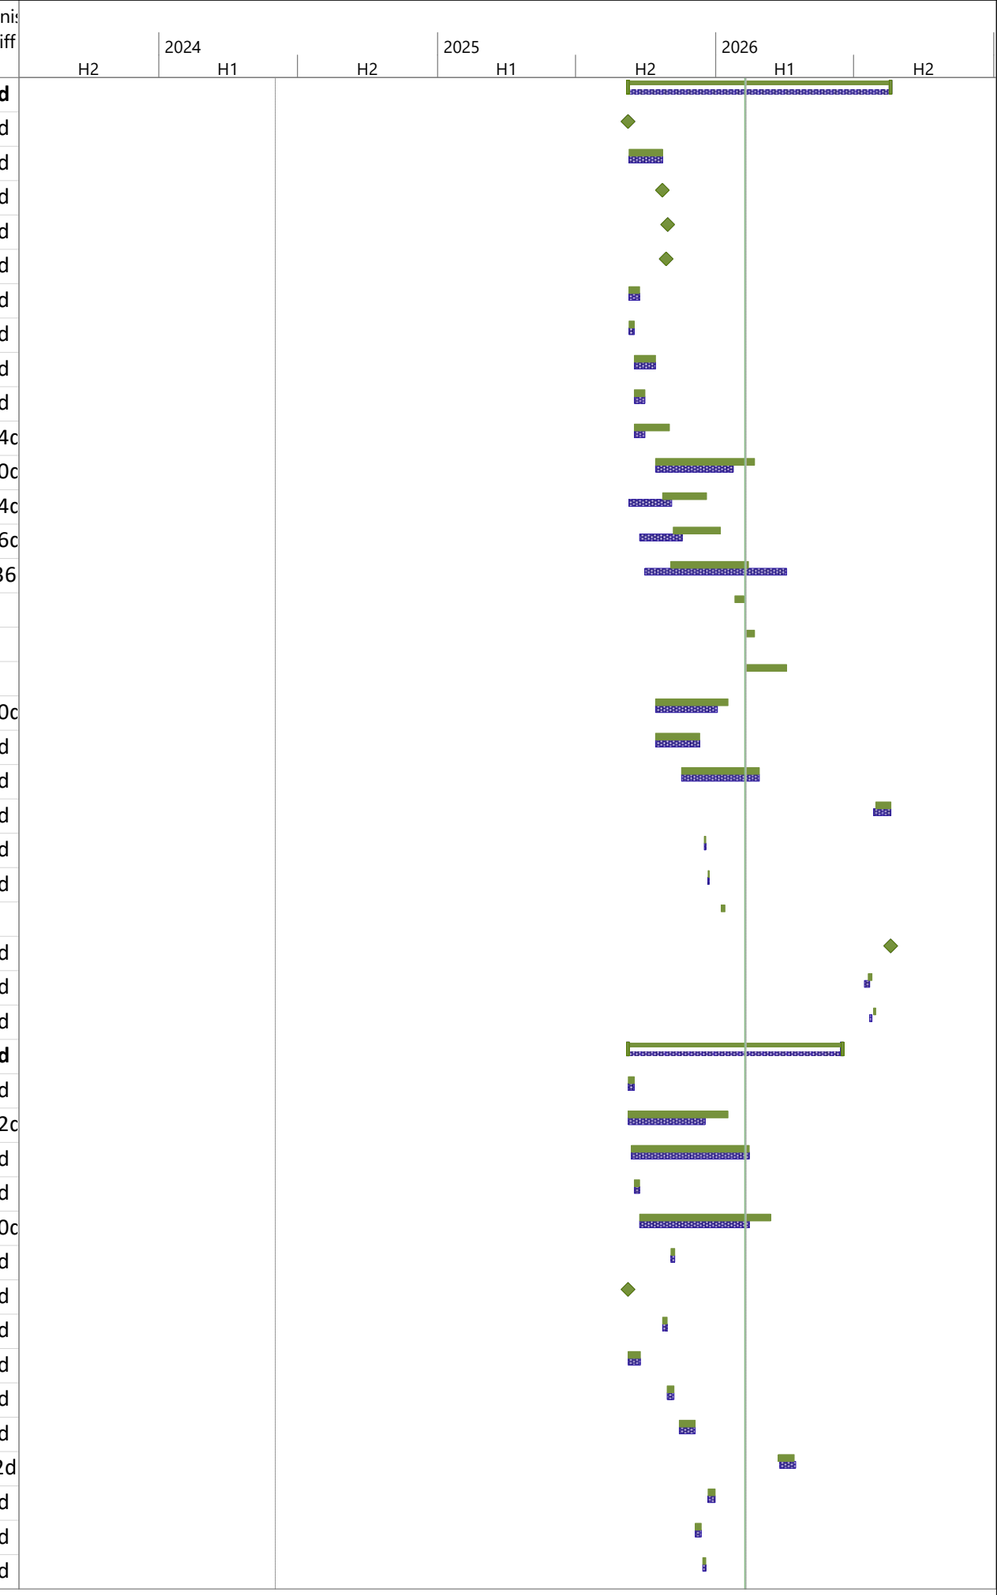

	Name	Duration Current	Duration Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finis Diff
45	Site - GIRR Piping & Devices	16 days	10 days	6d	Mon 26/01/12	Wed 25/12/31	8d	Mon 26/02/02	Wed 26/01/14	13c
46	TP DELAY - Site - GIRR Box Delivery and Placement	6 days			Mon 26/01/26			Mon 26/02/02		
47	Site - Water Line Ten Mile Tie-In	2 days	2 days	0d	Sat 25/11/08	Sat 25/11/08	0d	Tue 25/11/11	Tue 25/11/11	0d
48	Site - Water Line & Fire Lines/Hydrants and Devices Remain	18 days	12 days	6d	Mon 26/01/05	Thu 26/01/08	-3d	Wed 26/01/28	Fri 26/01/23	3d
49	Complete Utility Lines Tie-ins to Building A	5 days	5 days	0d	Tue 26/04/14	Thu 26/04/16	-2d	Mon 26/04/20	Wed 26/04/22	-2d
50	Gravel Road Finish Grade Prep	5 days	5 days	0d	Tue 26/04/14	Mon 26/01/26	56d	Mon 26/04/20	Fri 26/01/30	56c
51	Gravel Road Rough Grade Prep	8 days			Mon 25/12/08			Wed 25/12/17		
52	BLDG B Foundation Excavation	6 days	6 days	0d	Wed 25/10/29	Wed 25/10/29	0d	Wed 25/11/05	Wed 25/11/05	0d
53	DELAY - BLDG B FOOTING OVER-EX	4 days	4 days	0d	Fri 25/10/31	Fri 25/10/31	0d	Wed 25/11/05	Wed 25/11/05	0d
54	BLDG B SOG Prep	5 days	0 days	5d	Wed 25/11/26	Mon 25/12/01	-3d	Thu 25/12/04	Mon 25/12/01	4d
55	FRAGNET - Bldg B Soft Spot Repair	8 days	8 days	0d	Thu 25/12/04	Thu 25/12/04	0d	Mon 25/12/15	Mon 25/12/15	0d
56	BLDG B Backfill Foundations	18 days	18 days	0d	Mon 25/12/15	Mon 25/12/15	0d	Fri 26/01/09	Fri 26/01/09	0d
57	BLDG A Foundation Excavation	5 days	5 days	0d	Mon 26/01/26	Mon 26/01/26	0d	Fri 26/01/30	Fri 26/01/30	0d
58	FRAGNET - BLDG A Footing Seepage Bed Over Ex.	1 day			Mon 26/02/02			Mon 26/02/02		
59	BLDG A - Interoir Backfill Foundations	5 days	3 days	2d	Tue 26/02/17	Mon 26/02/16	1d	Mon 26/02/23	Wed 26/02/18	3d
60	FRAGNET - BLDG A Seepage Bed Pad Over Ex.	3 days			Tue 26/02/24			Thu 26/02/26		
61	BLDG A - Exterior Backfill Foundations	2 days	3 days	-1d	Tue 26/02/24	Mon 26/02/23	1d	Wed 26/02/25	Wed 26/02/25	0d
62	BLDG A SOG Prep	5 days	5 days	0d	Tue 26/03/03	Thu 26/02/26	3d	Mon 26/03/09	Wed 26/03/04	3d
63	Site - Base Course Asphalt Prep & Flatwork Prep	8 days			Tue 26/03/24			Thu 26/04/02		
64	Site Flatwork and Curb and Gutter	15 days	15 days	0d	Tue 26/04/21	Thu 26/04/23	-2d	Mon 26/05/11	Wed 26/05/13	-2d
65	Site - Fine Grade Asphalt Prep	3 days			Tue 26/05/12			Thu 26/05/14		
66	Asphalt Paving	2 days	2 days	0d	Fri 26/05/15	Thu 26/05/14	1d	Mon 26/05/18	Fri 26/05/15	1d
67	Pavement Markings, Signage & Bumpers	2 days	2 days	0d	Tue 26/05/19	Mon 26/05/18	1d	Wed 26/05/20	Tue 26/05/19	1d
68	Landscaping and Irrigation	15 days	15 days	0d	Tue 26/05/19	Mon 26/05/18	1d	Tue 26/06/09	Mon 26/06/08	1d
69	Site Fencing Chainlink	5 days	5 days	0d	Tue 26/05/19	Mon 26/05/18	1d	Tue 26/05/26	Fri 26/05/22	2d
70	Site Fencing Vinyl	10 days	10 days	0d	Wed 26/05/27	Tue 26/05/26	1d	Tue 26/06/09	Mon 26/06/08	1d
71	Site Fencing Rod Iron and Gates	5 days	5 days	0d	Wed 26/06/10	Tue 26/06/09	1d	Tue 26/06/16	Mon 26/06/15	1d
72	**BUILDING B**	**163 day**	**157 day**	**6d**	**Thu 25/11/06**	**Thu 25/11/06**	**0d**	**Mon 26/06/29**	**Fri 26/06/19**	**6d**
73	**CONCRETE WORK**	**44 days**	**42 days**	**2d**	**Thu 25/11/06**	**Thu 25/11/06**	**0d**	**Mon 26/01/12**	**Thu 26/01/08**	**2d**
74	BLDG B Foundation	14 days	14 days	0d	Thu 25/11/06	Thu 25/11/06	0d	Tue 25/11/25	Tue 25/11/25	0d
75	BLDG B Dampproofing	1 day	1 day	0d	Tue 25/11/18	Tue 25/11/18	0d	Wed 25/11/26	Wed 25/11/26	0d
76	BLDG B Slab On Grade	19 days	17 days	2d	Mon 25/12/15	Mon 25/12/15	0d	Mon 26/01/12	Thu 26/01/08	2d
77	BLDG B Slab On Grade Complete	0 days	0 days	0d	Mon 26/01/12	Thu 26/01/08	2d	Mon 26/01/12	Thu 26/01/08	2d
78	**STEEL AND METALS**	**81 days**	**80 days**	**1d**	**Mon 26/01/12**	**Fri 26/01/09**	**1d**	**Mon 26/05/04**	**Thu 26/04/30**	**2d**
79	Frame & Panel Load Bearing & Shear Walls (JANUS)	25 days	25 days	0d	Mon 26/01/12	Fri 26/01/09	1d	Mon 26/02/16	Thu 26/02/12	2d
80	Frame & Panel Partition & Corridor Walls (JANUS)	20 days	20 days	0d	Tue 26/04/07	Fri 26/04/03	2d	Mon 26/05/04	Thu 26/04/30	2d
81	**WOOD & FRP**	**5 days**	**5 days**	**0d**	**Tue 26/03/17**	**Fri 26/03/13**	**2d**	**Mon 26/03/23**	**Thu 26/03/19**	**2d**
82	Misc Finish Carpentry	5 days	5 days	0d	Tue 26/03/17	Fri 26/03/13	2d	Mon 26/03/23	Thu 26/03/19	2d
83	**ROOF & SIDING**	**35 days**	**30 days**	**5d**	**Fri 26/01/30**	**Fri 26/02/13**	**-10d**	**Thu 26/03/19**	**Thu 26/03/26**	**-5d**
84	Exterior Sheathing	10 days	10 days	0d	Fri 26/01/30	Fri 26/02/27	-20d	Thu 26/02/12	Thu 26/03/12	-20
85	Weather Barrier	10 days			Fri 26/02/06			Thu 26/02/19		
86	Rigid Insulation Behind CMU	5 days			Fri 26/02/20			Thu 26/02/26		
87	Rigid Insulation Behind Metal Panels	3 days			Fri 26/02/27			Tue 26/03/03		
88	CMU Veneer	15 days	15 days	0d	Fri 26/02/27	Fri 26/02/27	0d	Thu 26/03/19	Thu 26/03/19	0d

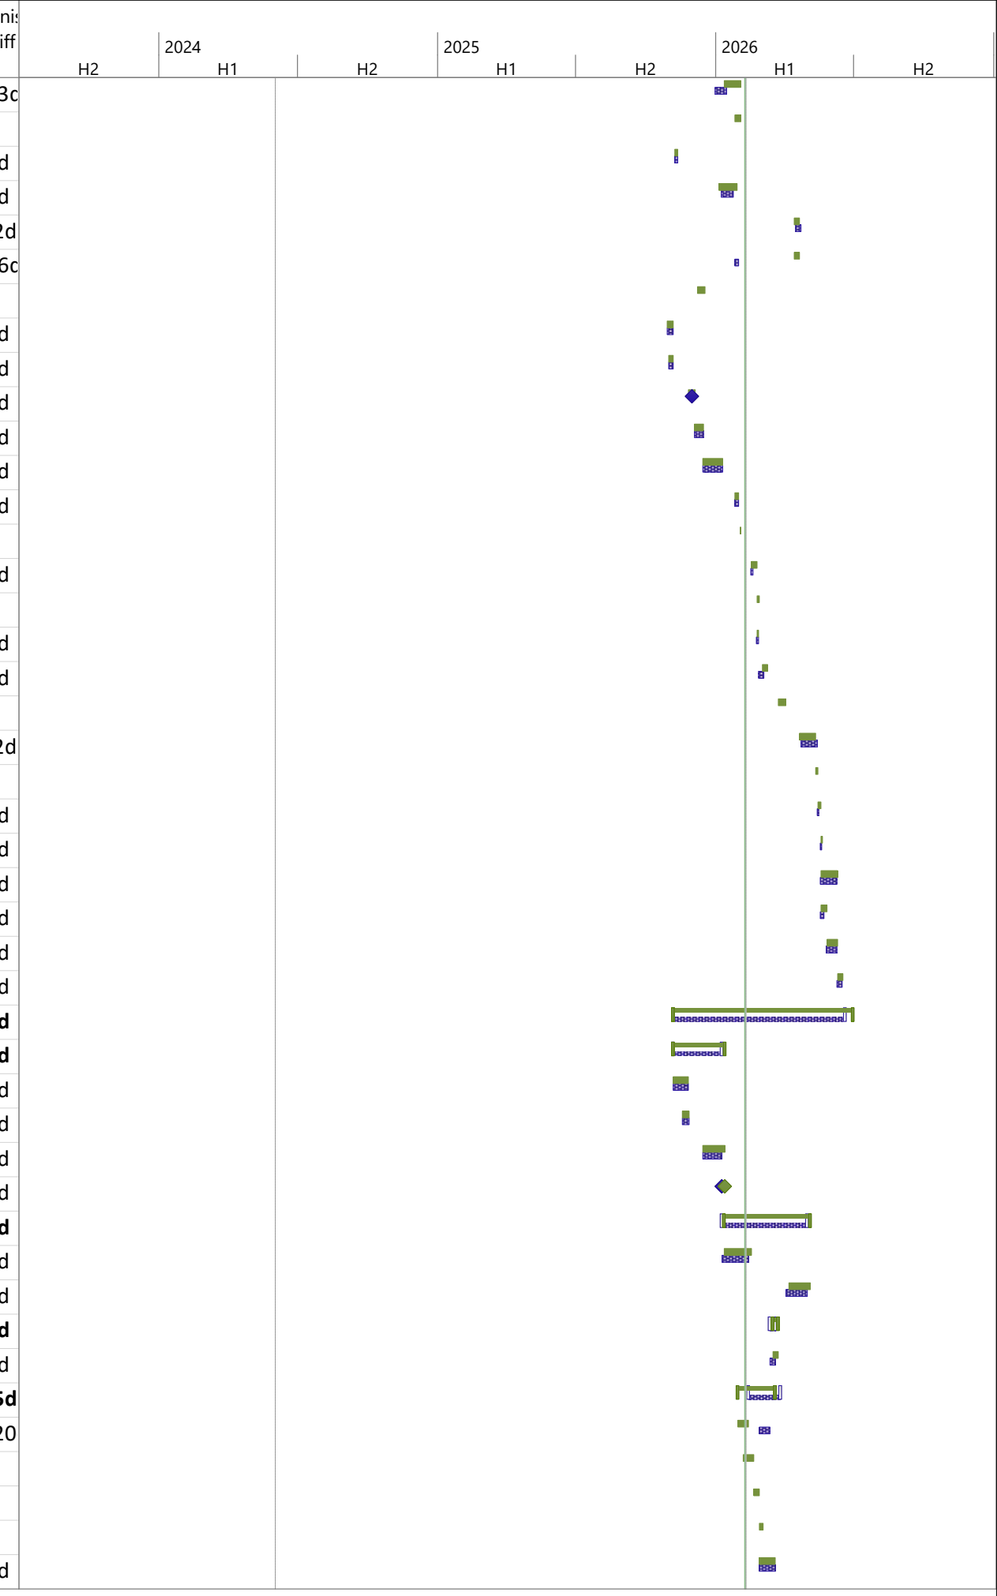

	Name	Duration Current	Duration Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finis Diff
89	Exterior Metal Panels (JANUS)	10 days	10 days	0d	Wed 26/03/04	Fri 26/03/13	-7d	Tue 26/03/17	Thu 26/03/26	-7d
90	Install Roof & Roof Insulation (JANUS)	10 days	10 days	0d	Tue 26/02/17	Fri 26/02/13	2d	Mon 26/03/02	Thu 26/02/26	2d
91	BLDG B Roofing Complete	0 days	0 days	0d	Mon 26/03/02	Thu 26/02/26	2d	Mon 26/03/02	Thu 26/02/26	2d
92	**DOORS & WINDOWS**	**20 days**	**20 days**	**0d**	**Wed 26/05/27**	**Fri 26/05/22**	**3d**	**Tue 26/06/23**	**Fri 26/06/19**	**2d**
93	F&I Storage Unit Doors (JANUS)	20 days	20 days	0d	Wed 26/05/27	Fri 26/05/22	3d	Tue 26/06/23	Fri 26/06/19	2d
94	F&I HM Doors and Hardware (JANUS)	15 days	15 days	0d	Wed 26/05/27	Fri 26/05/22	3d	Tue 26/06/16	Fri 26/06/12	2d
95	**FINISHES**	**30 days**	**30 days**	**0d**	**Tue 26/03/03**	**Fri 26/02/27**	**2d**	**Mon 26/04/13**	**Thu 26/04/09**	**2d**
96	Install Gypsum Board	10 days	10 days	0d	Tue 26/03/03	Fri 26/02/27	2d	Mon 26/03/16	Thu 26/03/12	2d
97	Flooring Polished Concrete	5 days	5 days	0d	Tue 26/03/17	Fri 26/03/13	2d	Mon 26/03/23	Thu 26/03/19	2d
98	FRP / Vinyl Base	5 days	5 days	0d	Tue 26/03/24	Fri 26/03/20	2d	Mon 26/03/30	Thu 26/03/26	2d
99	Painting	10 days	10 days	0d	Tue 26/03/31	Fri 26/03/27	2d	Mon 26/04/13	Thu 26/04/09	2d
100	**SPECIALTIES**	**23 days**	**23 days**	**0d**	**Tue 26/03/17**	**Fri 26/03/13**	**2d**	**Thu 26/04/16**	**Tue 26/04/14**	**2d**
101	Install Misc Equipment & Lockers	20 days	20 days	0d	Tue 26/03/17	Fri 26/03/13	2d	Mon 26/04/13	Thu 26/04/09	2d
102	Bathroom Accessories	2 days	2 days	0d	Tue 26/03/24	Fri 26/03/20	2d	Wed 26/03/25	Mon 26/03/23	2d
103	Building Interior Signage	3 days	3 days	0d	Tue 26/04/14	Fri 26/04/10	2d	Thu 26/04/16	Tue 26/04/14	2d
104	**FIRE SPRINKLERS**	**30 days**	**30 days**	**0d**	**Tue 26/03/03**	**Fri 26/02/27**	**2d**	**Mon 26/04/13**	**Thu 26/04/09**	**2d**
105	Fire Sprinkler System Rough In	15 days	15 days	0d	Tue 26/03/03	Fri 26/02/27	2d	Mon 26/03/23	Thu 26/03/19	2d
106	Fire Sprinkler System Trim Out	15 days	15 days	0d	Tue 26/03/24	Fri 26/03/20	2d	Mon 26/04/13	Thu 26/04/09	2d
107	**PLUMBING**	**87 days**	**107 day**	**-20d**	**Thu 25/11/20**	**Thu 25/11/13**	**5d**	**Thu 26/03/26**	**Thu 26/04/16**	**-15**
108	Plumbing Rough-in Underground	4 days	5 days	-1d	Thu 25/11/20	Thu 25/11/13	5d	Tue 25/11/25	Wed 25/11/19	4d
109	Drains, Water, Sewer Lines	15 days	15 days	0d	Tue 26/03/03	Fri 26/02/27	2d	Mon 26/03/23	Thu 26/03/19	2d
110	Bathroom Fixtures	3 days	10 days	-7d	Tue 26/03/24	Fri 26/03/20	2d	Thu 26/03/26	Thu 26/04/02	-5d
111	Other Plumbing Fixtures	3 days	10 days	-7d	Tue 26/03/24	Fri 26/04/03	-8d	Thu 26/03/26	Thu 26/04/16	-15
112	**HVAC**	**30 days**	**30 days**	**0d**	**Tue 26/03/03**	**Fri 26/02/27**	**2d**	**Mon 26/04/13**	**Thu 26/04/09**	**2d**
113	HVAC Installation	25 days	25 days	0d	Tue 26/03/03	Fri 26/02/27	2d	Mon 26/04/06	Thu 26/04/02	2d
114	HVAC Commisioning & T&B	5 days	5 days	0d	Tue 26/04/07	Fri 26/04/03	2d	Mon 26/04/13	Thu 26/04/09	2d
115	**ELECTRICAL**	**153 day**	**137 day**	**16d**	**Thu 25/11/20**	**Thu 25/11/20**	**0d**	**Mon 26/06/29**	**Fri 26/06/05**	**16c**
116	Building Rough-in Underground	0 days	0 days	0d	Thu 25/11/20	Thu 25/11/20	0d	Tue 25/11/25	Tue 25/11/25	0d
117	Elect Rough-In	25 days	25 days	0d	Tue 26/03/03	Fri 26/02/27	2d	Mon 26/04/06	Thu 26/04/02	2d
118	New Service Equipment Install, Wire & Inspect	10 days	10 days	0d	Tue 26/02/24	Mon 26/04/06	-29d	Mon 26/03/09	Fri 26/04/17	-29
119	Install and Wire Panels	15 days	15 days	0d	Tue 26/03/17	Fri 26/03/13	2d	Mon 26/04/06	Thu 26/04/02	2d
120	Permanent Power On	0 days	0 days	0d	Mon 26/04/06	Fri 26/04/17	-9d	Mon 26/04/06	Fri 26/04/17	-9d
121	Electric Lights, Devices and Trim	55 days	55 days	0d	Mon 26/04/06	Fri 26/03/13	16d	Mon 26/06/22	Fri 26/05/29	16c
122	Fire Alarm System	3 days	5 days	-2d	Tue 26/04/07	Fri 26/04/03	2d	Thu 26/04/09	Thu 26/04/09	0d
123	Electrical Commissioning	5 days	5 days	0d	Tue 26/06/23	Mon 26/06/01	16d	Mon 26/06/29	Fri 26/06/05	16c
124	**BUILDING A**	**117 day**	**115 day**	**2d**	**Tue 26/02/03**	**Mon 26/02/02**	**1d**	**Fri 26/07/17**	**Tue 26/07/14**	**3d**
125	**CONCRETE WORK**	**35 days**	**38 days**	**-3d**	**Tue 26/02/03**	**Mon 26/02/02**	**1d**	**Mon 26/03/23**	**Wed 26/03/25**	**-2d**
126	BLDG A Foundation	10 days	10 days	0d	Tue 26/02/03	Mon 26/02/02	1d	Mon 26/02/16	Fri 26/02/13	1d
127	BLDG A Dampproofing	2 days	2 days	0d	Tue 26/02/17	Mon 26/02/16	1d	Wed 26/02/18	Tue 26/02/17	1d
128	BLDG A Exterior Footing Insulation	3 days	3 days	0d	Thu 26/02/19	Wed 26/02/18	1d	Mon 26/02/23	Fri 26/02/20	1d
129	BLDG A Slab On Grade	10 days	15 days	-5d	Tue 26/03/10	Thu 26/03/05	3d	Mon 26/03/23	Wed 26/03/25	-2d
130	BLDG A Slab On Grade Complete	0 days	0 days	0d	Mon 26/03/23	Wed 26/03/25	-2d	Mon 26/03/23	Wed 26/03/25	-2d
131	**STEEL AND METALS**	**67 days**	**44 days**	**23d**	**Fri 26/03/20**	**Tue 26/03/17**	**3d**	**Tue 26/06/23**	**Fri 26/05/15**	**27c**
132	Frame & Panel Load Bearing & Shear Walls (JANUS)	25 days	25 days	0d	Fri 26/03/20	Tue 26/03/17	3d	Thu 26/04/23	Mon 26/04/20	3d

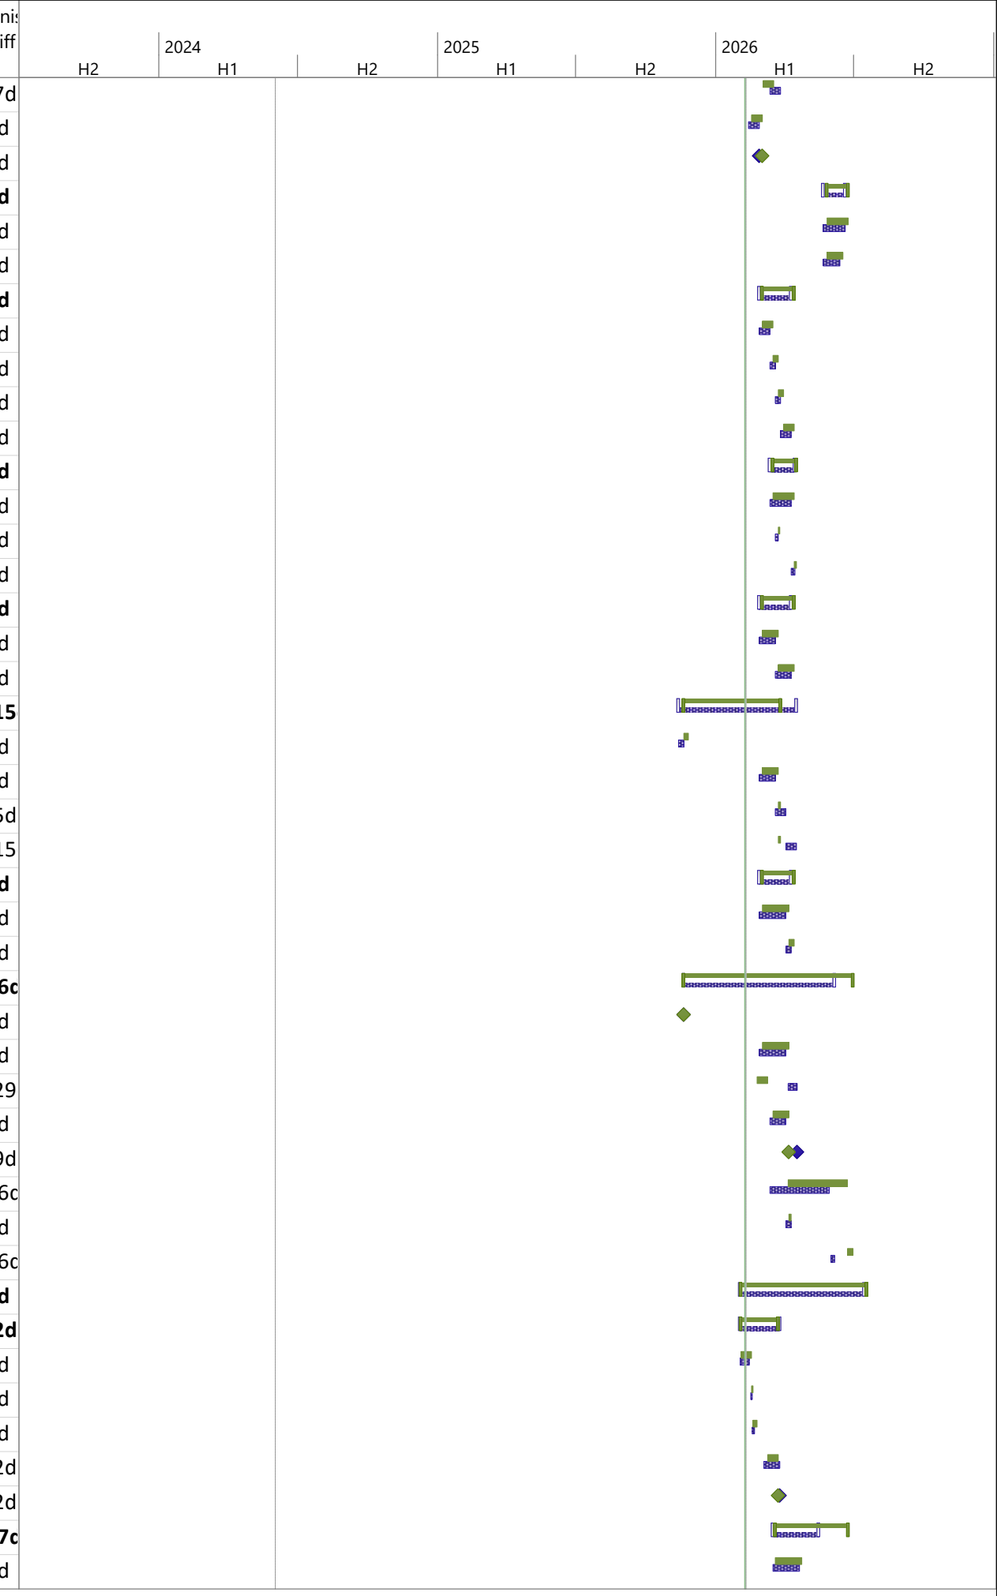

	Name	Duration Current	Duration Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finis Diff
133	Frame & Panel Partition & Corridor Walls (JANUS)	15 days	15 days	0d	Wed 26/06/03	Tue 26/04/21	31d	Tue 26/06/23	Mon 26/05/11	31c
134	Canopy Install	8 days	8 days	0d	Fri 26/04/24	Wed 26/05/06	-8d	Tue 26/05/05	Fri 26/05/15	-8d
135	**WOOD & FRP**	**5 days**	**5 days**	**0d**	**Fri 26/05/15**	**Wed 26/05/20**	**-3d**	**Thu 26/05/21**	**Wed 26/05/27**	**-4d**
136	Misc Finish Carpentry	5 days	5 days	0d	Fri 26/05/15	Wed 26/05/20	-3d	Thu 26/05/21	Wed 26/05/27	-4d
137	**ROOF & SIDING**	**35 days**	**26 days**	**9d**	**Fri 26/04/10**	**Tue 26/04/21**	**-7d**	**Fri 26/05/29**	**Wed 26/05/27**	**2d**
138	Exterior Sheathing	10 days	10 days	0d	Fri 26/04/10	Wed 26/04/22	-8d	Thu 26/04/23	Tue 26/05/05	-8d
139	Weather Barrier	10 days			Fri 26/04/17			Thu 26/04/30		
140	Rigid Insulation Behind CMU	5 days			Fri 26/05/01			Thu 26/05/07		
141	CMU Veneer	15 days	15 days	0d	Fri 26/05/08	Wed 26/05/06	2d	Fri 26/05/29	Wed 26/05/27	2d
142	Rigid Insulation Behind Metal Panels	3 days			Fri 26/05/01			Tue 26/05/05		
143	Exterior Metal Panels (JANUS)	10 days	10 days	0d	Tue 26/05/12	Fri 26/05/08	2d	Tue 26/05/26	Thu 26/05/21	3d
144	Install Roof & Roof Insulation (JANUS)	5 days	5 days	0d	Fri 26/04/24	Tue 26/04/21	3d	Thu 26/04/30	Mon 26/04/27	3d
145	BLDG A Roofing Complete	0 days	0 days	0d	Thu 26/04/30	Mon 26/04/27	3d	Thu 26/04/30	Mon 26/04/27	3d
146	**DOORS & WINDOWS**	**5 days**	**11 days**	**-6d**	**Wed 26/06/24**	**Tue 26/05/12**	**31d**	**Tue 26/06/30**	**Wed 26/05/27**	**24c**
147	F&I Storage Unit Doors (JANUS)	5 days	5 days	0d	Wed 26/06/24	Tue 26/05/12	31d	Tue 26/06/30	Mon 26/05/18	31c
148	F&I HM Doors and Hardware (JANUS)	5 days	5 days	0d	Wed 26/06/24	Wed 26/05/20	25d	Tue 26/06/30	Wed 26/05/27	24c
149	**FINISHES**	**30 days**	**30 days**	**0d**	**Fri 26/05/01**	**Wed 26/05/06**	**-3d**	**Fri 26/06/12**	**Wed 26/06/17**	**-3d**
150	Install Gypsum Board	10 days	10 days	0d	Fri 26/05/01	Wed 26/05/06	-3d	Thu 26/05/14	Tue 26/05/19	-3d
151	Painting	10 days	10 days	0d	Fri 26/05/15	Wed 26/05/20	-3d	Fri 26/05/29	Wed 26/06/03	-3d
152	Flooring Polished Conc.	5 days	5 days	0d	Mon 26/06/01	Thu 26/06/04	-3d	Fri 26/06/05	Wed 26/06/10	-3d
153	FRP & Vinyl Base	5 days	5 days	0d	Mon 26/06/08	Thu 26/06/11	-3d	Fri 26/06/12	Wed 26/06/17	-3d
154	**SPECIALTIES**	**22 days**	**22 days**	**0d**	**Fri 26/05/15**	**Wed 26/05/20**	**-3d**	**Tue 26/06/16**	**Fri 26/06/19**	**-3d**
155	Install Misc Equipment & Lockers	20 days	20 days	0d	Fri 26/05/15	Wed 26/05/20	-3d	Fri 26/06/12	Wed 26/06/17	-3d
156	Bathroom Accessories	2 days	2 days	0d	Mon 26/06/15	Thu 26/06/18	-3d	Tue 26/06/16	Fri 26/06/19	-3d
157	Building Interior Signage	3 days	3 days	0d	Mon 26/06/01	Thu 26/06/04	-3d	Wed 26/06/03	Mon 26/06/08	-3d
158	**FIRE SPRINKLERS**	**30 days**	**30 days**	**0d**	**Fri 26/05/01**	**Tue 26/04/28**	**3d**	**Fri 26/06/12**	**Tue 26/06/09**	**3d**
159	Fire Sprinkler System Rough In	15 days	15 days	0d	Fri 26/05/01	Tue 26/04/28	3d	Thu 26/05/21	Mon 26/05/18	3d
160	Fire Sprinkler System Trim Out	15 days	15 days	0d	Fri 26/05/22	Tue 26/05/19	3d	Fri 26/06/12	Tue 26/06/09	3d
161	**PLUMBING**	**83 days**	**84 days**	**-1d**	**Tue 26/02/24**	**Thu 26/02/19**	**3d**	**Fri 26/06/19**	**Wed 26/06/17**	**2d**
162	Plumbing Rough-in Underground	5 days	5 days	0d	Tue 26/02/24	Thu 26/02/19	3d	Mon 26/03/02	Wed 26/02/25	3d
163	Drains, Water, Sewer Lines	15 days	15 days	0d	Fri 26/05/01	Tue 26/04/28	3d	Thu 26/05/21	Mon 26/05/18	3d
164	Bathroom Fixtures	10 days	10 days	0d	Fri 26/05/22	Wed 26/05/20	2d	Fri 26/06/05	Wed 26/06/03	2d
165	Other Plumbing Fixtures	10 days	10 days	0d	Mon 26/06/08	Thu 26/06/04	2d	Fri 26/06/19	Wed 26/06/17	2d
166	**HVAC**	**30 days**	**30 days**	**0d**	**Fri 26/05/01**	**Tue 26/04/28**	**3d**	**Fri 26/06/12**	**Tue 26/06/09**	**3d**
167	HVAC Installation	20 days	20 days	0d	Fri 26/05/01	Tue 26/04/28	3d	Fri 26/05/29	Tue 26/05/26	3d
168	HVAC Commisioning & T& B	10 days	10 days	0d	Mon 26/06/01	Wed 26/05/27	3d	Fri 26/06/12	Tue 26/06/09	3d
169	**ELECTRICAL**	**102 day**	**102 day**	**0d**	**Tue 26/02/24**	**Thu 26/02/19**	**3d**	**Fri 26/07/17**	**Tue 26/07/14**	**3d**
170	Building Rough-in Underground	5 days	5 days	0d	Tue 26/02/24	Thu 26/02/19	3d	Mon 26/03/02	Wed 26/02/25	3d
171	Electrical Rough-In	25 days	25 days	0d	Tue 26/04/28	Thu 26/04/23	3d	Tue 26/06/02	Thu 26/05/28	3d
172	New Service Equipment Install, Wire & Inspect	10 days	10 days	0d	Tue 26/04/28	Thu 26/04/23	3d	Mon 26/05/11	Wed 26/05/06	3d
173	Install and Wire Panels	15 days	15 days	0d	Fri 26/05/15	Wed 26/05/20	-3d	Fri 26/06/05	Wed 26/06/10	-3d
174	Permanent Power On	0 days	0 days	0d	Fri 26/06/05	Wed 26/06/10	-3d	Fri 26/06/05	Wed 26/06/10	-3d
175	Electric Lights, Devices and Trim	42 days	42 days	0d	Tue 26/05/12	Thu 26/05/07	3d	Fri 26/07/10	Tue 26/07/07	3d
176	Fire Alarm System	5 days	5 days	0d	Mon 26/06/01	Wed 26/05/27	3d	Fri 26/06/05	Tue 26/06/02	3d

	Name	Duration Current	Duration Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finis Diff
177	Electrical Commissioning	5 days	5 days	0d	Mon 26/07/13	Wed 26/07/08	3d	Fri 26/07/17	Tue 26/07/14	3d
