	Name	Duration: Current	Duration: Previous	Duration: Diff
1	**GENERAL REQUIREMENTS AND CONDITIONS**	**265 days**	**241 days**	**24d**
2	Notice to Proceed	1 day	1 day	0d
3	DELAY - PERMIT DELAY	32 days	32 days	0d
4	Obtain Building Permit	0 days	0 days	0d
5	ACHD ROW Permit	0 days	0 days	0d
6	Obtain LDIR Approval to Proceed	0 days	0 days	0d
7	Receive CAD Base Files from Public Storage	10 days	10 days	0d
8	Procure Early Work Subcontractors	5 days	5 days	0d
9	Procure Remaining Subcontractors	20 days	20 days	0d
10	Submittals (SWPPP/NOI)	10 days	10 days	0d
11	Submittals (SES /Switchgear)	125 days	34 days	91d
12	Submittals (numerous)	90 days	90 days	0d
13	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG B	40 days	40 days	0d
14	PUBLIC STORAGE Fab/Delv Framing & Panels BLDG A	40 days	40 days	0d
15	Procure SES's/Switchgears (6 mos ~ 130 WD)	56 days	70 days	-14d
16	Light Fixture Submittal Review and Approval	10 days	10 days	0d
17	Light Fixture Package Alternate - Fab and Deliver	10 days	10 days	0d
18	Light Fixture Package Spec'd - Fab and Deliver		8 wks	
19	Fire Sprinkler Design and Approval	78 days	65 days	13d
20	Fire Alarm System Design and Approval	40 days	40 days	0d
21	ASPHALT BATCH PLANT SHUTDOWN	70 days	70 days	0d
22	TWENTY WORKING DAYS OF WEATHER DELAY	10 days	14 days	-4d
23	WEATHER DELAY - Rain and High Winds - Imapct SOG B	2 days	2 days	0d
24	WEATHER DELAY - Rain - Impact SOG B	1 day	1 day	0d
25	WEATHER DELAY - Rain - Impact SOG B	3 days	3 days	0d
26	WEATHER DELAY - Rain - Impact Footing Bldg A	2 days		
27	WEATHER DELAY - Rain - Impact Footing Bldg A	2 days		
28	Substantial Completion	0 days	0 days	0d
29	Clean Up and Project Close Out	5 days	5 days	0d
30	Demobilize	3 days	3 days	0d
31	**SITEWORK**	**219 days**	**197 days**	**22d**
32	**Level of Effort**	**131 days**	**131 days**	**0d**
33	Construction Staking & Surveying	90 days	90 days	0d
34	Inspections and Testing	100 days	100 days	0d
35	Maintain Erosion Control	120 days	120 days	0d
36	Erosion Control & SWPP	5 days	5 days	0d
37	Mobilization	5 days	5 days	0d
38	Site Demolition (Trees,Sawcut, Asphalt, Base)	0 days	0 days	0d
39	Clear/Grub & Overlot Grading	12 days	12 days	0d
40	Structure Demo (Partial Building & RV Storage)	5 days	5 days	0d
41	Re-Mobilization	4 days	4 days	0d
42	FRAGNET - CITY PRE-CON & 7 DAY NOTICE	7 days	7 days	0d
43	Site - Water Line Ten Mile Tie-In	2 days	2 days	0d
44	Work Week Restriction	5 days	5 days	0d
45	Site - Sewer Lines and Devices/Ten Mile Tie-In	13 days	13 days	0d
46	DELAY - GIRR License Agreement Approval to Proceed	6 days	6 days	0d
47	DELAY - RFI #14 - GIRR Separation	4 days	4 days	0d
48	Storm Drain Lines South	6 days	6 days	0d
49	Site - Water Line & Fire Lines/Hydrants and Devices Remaining	18 days	18 days	0d
50	Site - GIRR Piping & Devices	16 days	16 days	0d
51	TP DELAY - Site - GIRR Box Delivery and Placement	6 days	6 days	0d
52	Complete Utility Lines Tie-ins to Building A	5 days	5 days	0d
53	Gravel Road Rough Grade Prep	8 days	8 days	0d
54	**FRAGNET - Site - Drive Aisle Unsuitable Soils**	**53 days**		
55	FRAGNET - Site - Drive Aisle Over Ex Unsuitable Soil Identified	1 day		

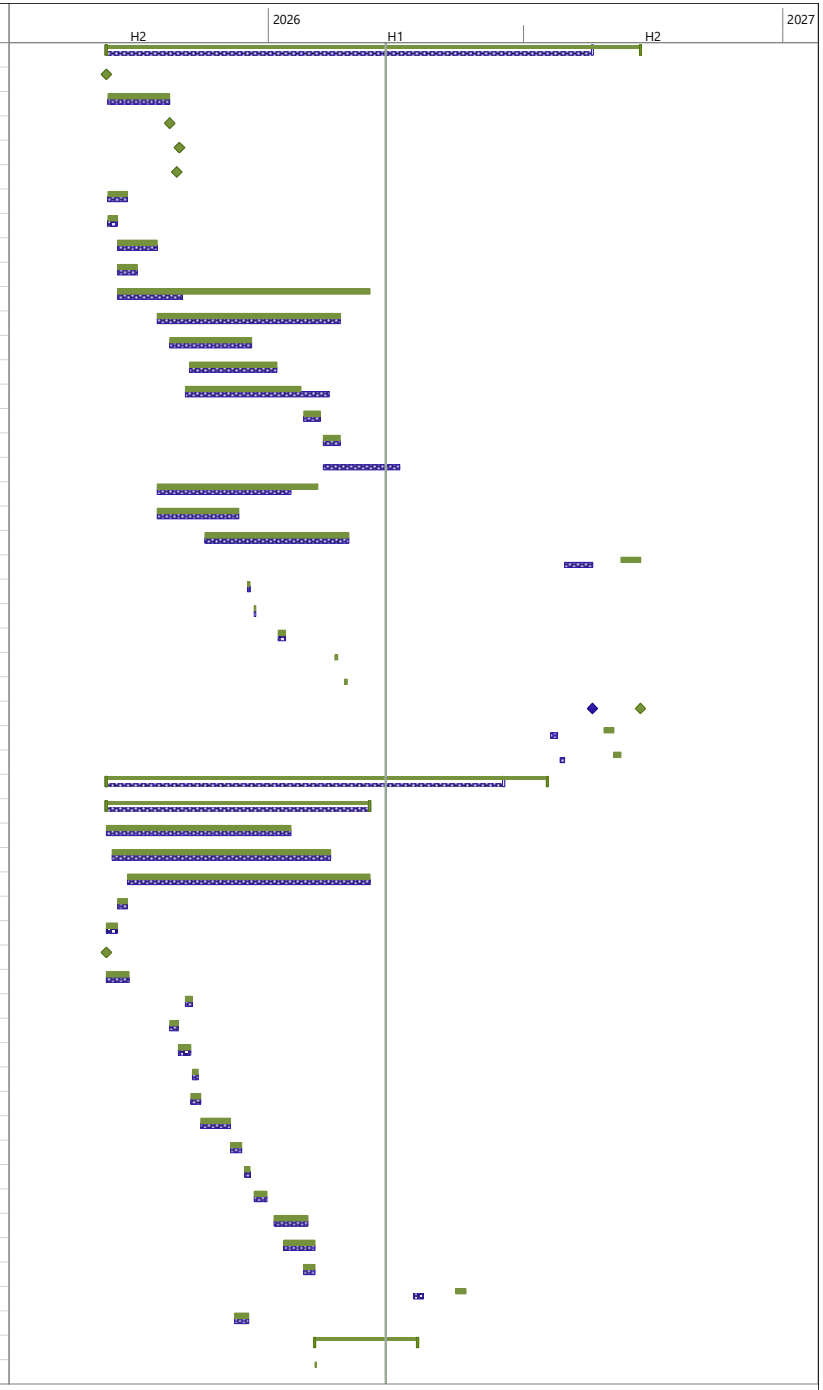

	Name	Duration: Current	Duration: Previous	Duration: Diff
56	FRAGNET - Site - Drive Aisle Over Ex Discussion and Confirmation on Solution	2 days		
57	FRAGNET - Site - Idaho Power - Pivot to Moblize and Peform the UG JT in Drive Aisle	15 days		
58	FRAGNET - Site - Owner Review of Impact and Discussion with Geo Tech to Identify Alternative Solutions M	5 days		
59	FRAGNET - Prepare and Submit Pricing for Approval	13 days		
60	FRAGNET - Owner Issued CCD 07 Directive for Driveisle and Soft Spots	1 day		
61	FRAGNET - Mobilize Crew, Rough Grade Prep, Scarify and Air Dry	1 day		
62	FRAGNET - Re-Prep, Proof Roll, Confirm Soft Spot Magnitude	1 day		
63	FRAGNET - Site - Partial Soft Spot Repair Examination of Pit Run to Proceed. If failed, provide geo grid per F	3 days		
64	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Start	1 day		
65	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld A	5 days		
66	(TOTAL MAGNITUDE, TBD) FRAGNET - Site - Drive Aisle Over Ex Finish South Bld B	5 days		
67	Site - Idaho Power Boring	2 days		
68	Site - Idaho Power Trench, Conduit and Backfill	5 days		
69	Site - Idaho Power Transformer Set and Make Live	0 days		
70	Site - Base Course Asphalt Prep & Flatwork Prep	8 days	8 days	0d
71	Storm Drain Lines and Devices - North & South of Buildings	15 days	15 days	0d
72	Gravel Road Finish Grade Prep	5 days	5 days	0d
73	Site Flatwork and Curb and Gutter	15 days	15 days	0d
74	Site - Fine Grade Asphalt Prep	3 days	3 days	0d
75	Asphalt Paving	2 days	2 days	0d
76	Pavement Markings, Signage & Bumpers	2 days	2 days	0d
77	Landscaping and Irrigation	15 days	15 days	0d
78	Site Fencing Chainlink	5 days	5 days	0d
79	Site Fencing Vinyl	10 days	10 days	0d
80	Site Fencing Rod Iron and Gates	5 days	5 days	0d
81	**BUILDING B**	**193 days**	**169 days**	**24d**
82	BLDG B Foundation Excavation	6 days	6 days	0d
83	DELAY - BLDG B FOOTING OVER-EX	4 days	4 days	0d
84	BLDG B SOG Prep	5 days	5 days	0d
85	FRAGNET - Bldg B Soft Spot Repair	8 days	8 days	0d
86	BLDG B Backfill Foundations	18 days	18 days	0d
87	**CONCRETE WORK**	**44 days**	**44 days**	**0d**
88	BLDG B Foundation	14 days	14 days	0d
89	BLDG B Dampproofing	1 day	1 day	0d
90	BLDG B Slab On Grade	19 days	19 days	0d
91	BLDG B Slab On Grade Complete	0 days	0 days	0d
92	**STEEL AND METALS**	**108.5 day**	**81 days**	**27.5d**
93	Frame & Panel Load Bearing & Shear Walls (JANUS)	20 days	25 days	-5d
94	FRAGNET - Extended Shear Wall Durations (JANUS)	30 days		
95	Frame & Panel Partition & Corridor Walls (JANUS)	20 days	20 days	0d
96	**WOOD & FRP**	**5 days**	**5 days**	**0d**
97	Misc Finish Carpentry	5 days	5 days	0d
98	**ROOF & SIDING**	**78 days**	**35 days**	**43d**
99	Exterior Sheathing	0 days	10 days	-10d
100	Weather Barrier Fluid Applied	8 days		
101	Weather Barrier Tyvek	10 days	10 days	0d
102	CMU Veneer Base Course & Grout	15 days	15 days	0d
103	Rigid Insulation Behind CMU	5 days	5 days	0d
104	Rigid Insulation Behind Metal Panels	3 days	3 days	0d
105	CMU Veneer Remaining	15 days		
106	Exterior Metal Panels (JANUS)	10 days	10 days	0d
107	Install Roof & Roof Insulation (JANUS)	15 days	10 days	5d
108	BLDG B Roofing Complete	0 days	0 days	0d
109	**DOORS & WINDOWS**	**20 days**	**20 days**	**0d**
110	F&I Storage Unit Doors (JANUS)	20 days	20 days	0d

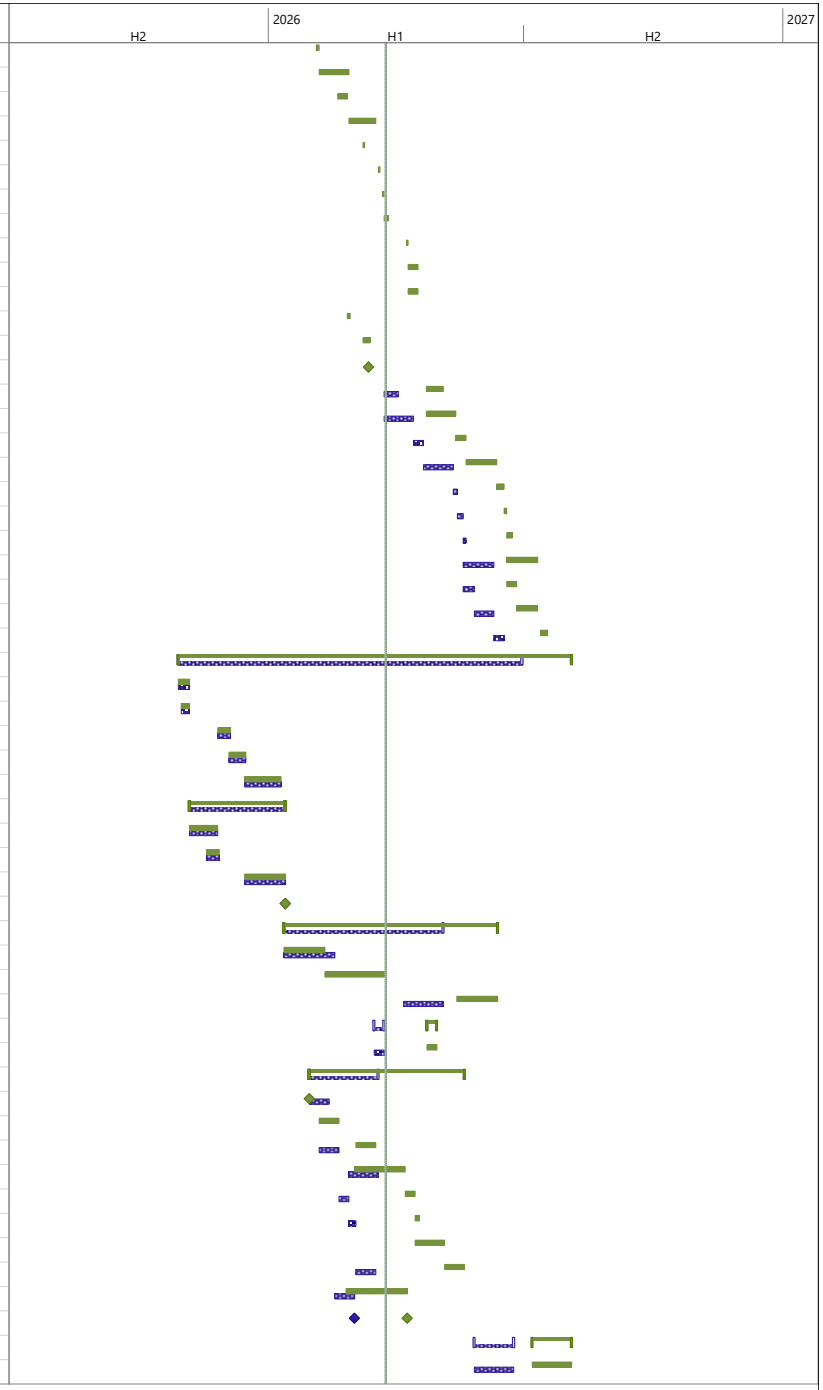

	Name	Duration: Current	Duration: Previous	Duration: Diff
111	F&I HM Doors and Hardware (JANUS)	15 days	15 days	0d
112	**FINISHES**	**30 days**	**30 days**	**0d**
113	Install Gypsum Board	10 days	10 days	0d
114	Flooring Polished Concrete	5 days	5 days	0d
115	FRP / Vinyl Base	5 days	5 days	0d
116	Painting	10 days	10 days	0d
117	**SPECIALTIES**	**23 days**	**23 days**	**0d**
118	Install Misc Equipment & Lockers	20 days	20 days	0d
119	Bathroom Accessories	2 days	2 days	0d
120	Building Interior Signage	3 days	3 days	0d
121	**FIRE SPRINKLERS**	**50 days**	**30 days**	**20d**
122	Fire Sprinkler System Rough In	28 days	15 days	13d
123	Fire Sprinkler System Trim Out	15 days	15 days	0d
124	**PLUMBING**	**114.5 day**	**87 days**	**27.5d**
125	Plumbing Rough-in Underground	4 days	4 days	0d
126	Drains, Water, Sewer Lines	15 days	15 days	0d
127	Bathroom Fixtures	3 days	3 days	0d
128	Other Plumbing Fixtures	3 days	3 days	0d
129	**HVAC**	**30 days**	**30 days**	**0d**
130	HVAC Installation	25 days	25 days	0d
131	HVAC Commisioning & T&B	5 days	5 days	0d
132	**ELECTRICAL**	**156.5 day**	**153 days**	**3.5d**
133	Building Rough-in Underground	0 days	0 days	0d
134	Elect Rough-In	25 days	25 days	0d
135	New Service Equipment Install, Wire & Inspect	10 days	10 days	0d
136	Install and Wire Panels	15 days	15 days	0d
137	Permanent Power On	0 days	0 days	0d
138	FRAGNET - RFI 35 - Light Fixture Mounting Height Clarification Submitted/Closed,	3 days		
139	Electric Lights, Devices and Trim	55 days	55 days	0d
140	Fire Alarm System	3 days	3 days	0d
141	Electrical Commissioning	5 days	5 days	0d
142	**BUILDING A**	**151 days**	**123 days**	**28d**
143	BLDG A Foundation Excavation	24 days	5 days	19d
144	FRAGNET - BLDG A Footing Seepage Bed Over Ex.	1 day	1 day	0d
145	BLDG A - Interoir Backfill Foundations	2 days	5 days	-3d
146	**FRAGNET - BLDG A Seepage Bed Pad Over Ex.**	**11 days**	**3 days**	**8d**
147	FRAGNET -Proposed direction received from Owner to perform BLDG A Seepage Bed Pad Over Ex.	1 day		
148	FRAGNET - Prepare and Submit Pricing for Approval	8 days		
149	FRAGNET - Owner Issued CCD 06 on Seepage Bed Cost Impact	1 day		
150	FRAGNET - Mobilize Crew for BLDG A Seepage Bed Pad Over Ex.	1 day		
151	FRAGNET - Start BLDG A Seepage Bed Pad Over Ex.	1 day		
152	FRAGNET - Finish BLDG A Seepage Bed Pad Over Ex.	1 day		
153	BLDG A - Exterior Backfill Foundations	2 days	2 days	0d
154	BLDG A SOG Rough Grade Prep	2 days		
155	**FRAGNET - BLDG A Soft Spot Over Ex**	**30 days**		
156	FRAGNET - Proposed direction received from Owner to perform BLDG A Soft Spot Repairs Using Only Pit R	1 day		
157	FRAGNET - Prepare and Submit Pricing for Approval	13 days		
158	FRAGNET - Owner Issued CCD 07 Directive for Driveisle and Soft Spots	1 day		
159	FRAGNET - Mobilize Crew, SOG Rough Grade Prep, Scarify, Air Dry Pad A	5 days		
160	FRAGNET - Air Dry Pad A, Re-Prep, Proof Roll to Idendify Soft Spots	7 days		
161	(IF REQUIRED, TBD) FRAGNET - Start Soft Spot Repairs	1 day		
162	(IF REQUIRED, TBD) FRAGNET - Test and Review Compaction Results for Soft Spot - If Approved, Proceed w	1 day		
163	(IF REQUIRED, TBD) FRAGNET - Soft Spot Repairs East Area	5 days		
164	(IF REQUIRED, TBD) FRAGNET - Soft Spot Repairs West Area	5 days		
165	**CONCRETE WORK**	**56 days**	**35 days**	**21d**

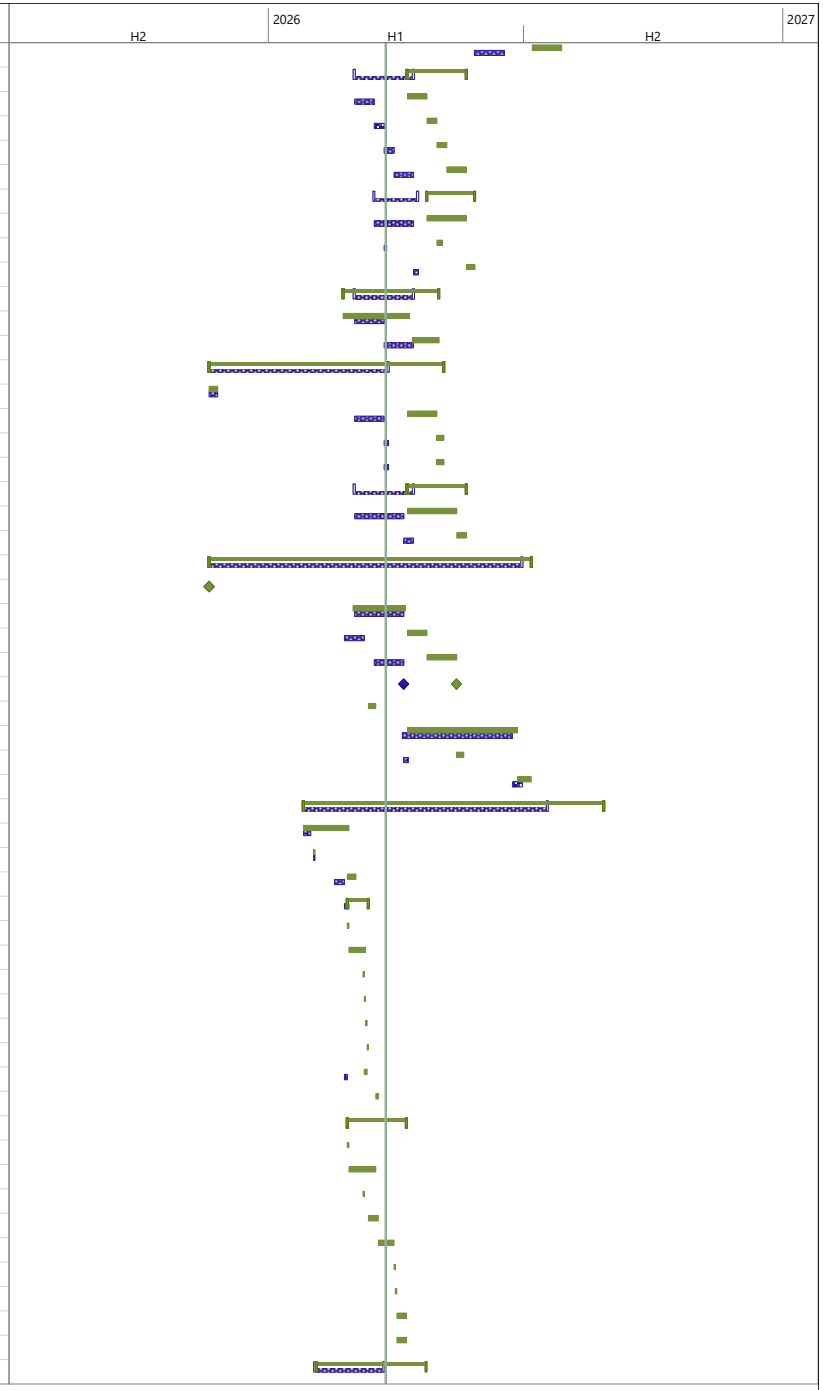
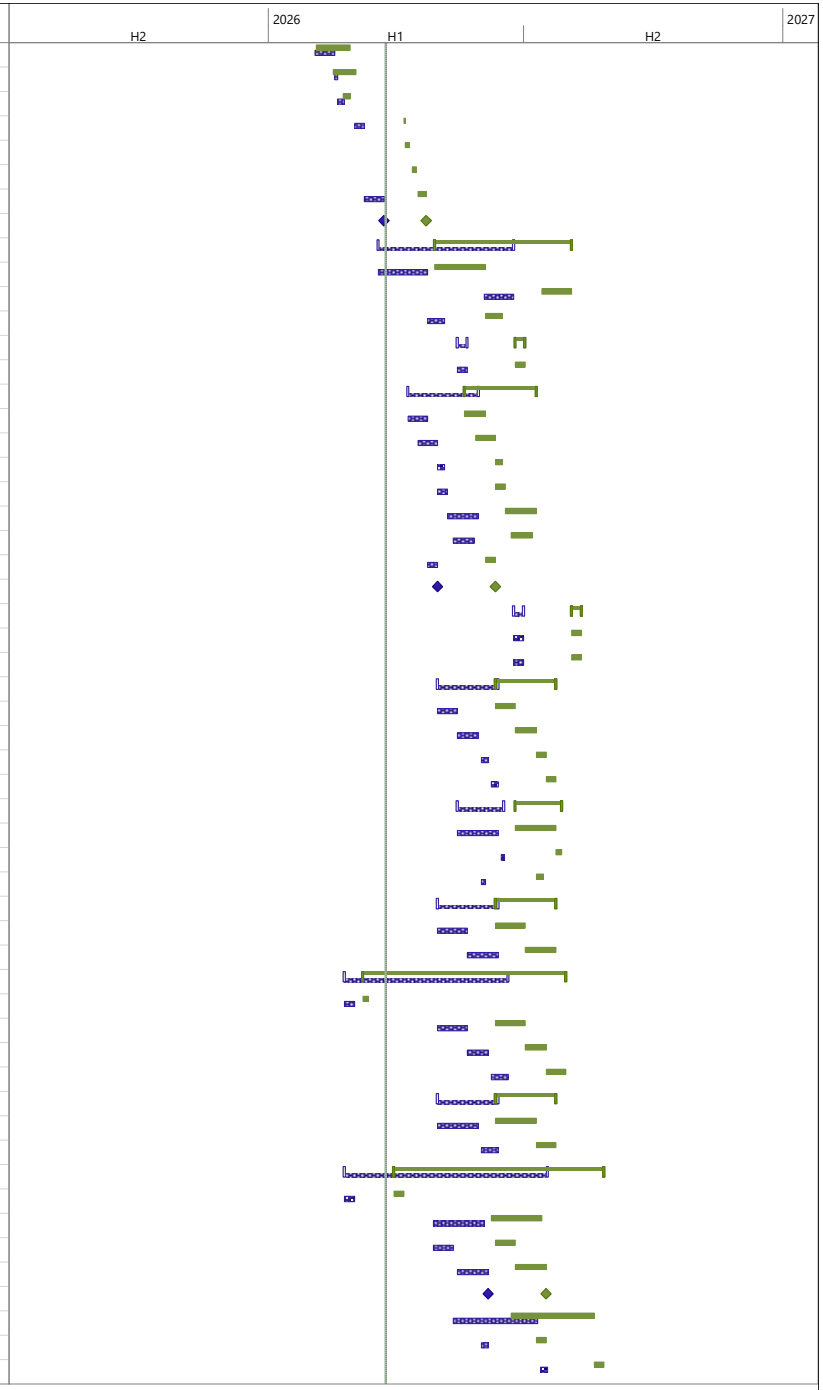
	Name	Duration: Current	Duration: Previous	Duration: Diff
166	BLDG A Foundation	18 days	10 days	8d
167	BLDG A Dampproofing	4 days	2 days	2d
168	BLDG A Exterior Footing Insulation	5 days	3 days	2d
169	BLDG A SOG Fine Prep	1 day	5 days	-4d
170	BLDG A Slab On Grade (East)	3 days		
171	BLDG A Slab On Grade (Center)	3 days		
172	BLDG A Slab On Grade (West)	4 days	10 days	-6d
173	BLDG A Slab On Grade Complete	0 days	0 days	0d
174	**STEEL AND METALS**	**67 days**	**67 days**	**0d**
175	Frame & Panel Load Bearing & Shear Walls (JANUS)	25 days	25 days	0d
176	Frame & Panel Partition & Corridor Walls (JANUS)	15 days	15 days	0d
177	Canopy Install	8 days	8 days	0d
178	**WOOD & FRP**	**5 days**	**5 days**	**0d**
179	Misc Finish Carpentry	5 days	5 days	0d
180	**ROOF & SIDING**	**35 days**	**35 days**	**0d**
181	Exterior Sheathing	10 days	10 days	0d
182	Exterior Sheathing, Weather Barrier & Rigid Insulation - Building A	10 days	10 days	0d
183	Rigid Insulation Behind Metal Panels	3 days	3 days	0d
184	Rigid Insulation Behind CMU	5 days	5 days	0d
185	CMU Veneer	15 days	15 days	0d
186	Exterior Metal Panels (JANUS)	10 days	10 days	0d
187	Install Roof & Roof Insulation (JANUS)	5 days	5 days	0d
188	BLDG A Roofing Complete	0 days	0 days	0d
189	**DOORS & WINDOWS**	**5 days**	**5 days**	**0d**
190	F&I Storage Unit Doors (JANUS)	5 days	5 days	0d
191	F&I HM Doors and Hardware (JANUS)	5 days	5 days	0d
192	**FINISHES**	**30 days**	**30 days**	**0d**
193	Install Gypsum Board	10 days	10 days	0d
194	Painting	10 days	10 days	0d
195	Flooring Polished Conc.	5 days	5 days	0d
196	FRP & Vinyl Base	5 days	5 days	0d
197	**SPECIALTIES**	**22 days**	**22 days**	**0d**
198	Install Misc Equipment & Lockers	20 days	20 days	0d
199	Bathroom Accessories- Building A	2 days	2 days	0d
200	Building Interior Signage	3 days	3 days	0d
201	**FIRE SPRINKLERS**	**30 days**	**30 days**	**0d**
202	Fire Sprinkler System Rough In	15 days	15 days	0d
203	Fire Sprinkler System Trim Out	15 days	15 days	0d
204	**PLUMBING**	**102 days**	**83 days**	**19d**
205	Plumbing Rough-in Underground	4 days	5 days	-1d
206	Drains, Water, Sewer Lines	15 days	15 days	0d
207	Bathroom Fixtures- Building A	10 days	10 days	0d
208	Other Plumbing Fixtures	10 days	10 days	0d
209	**HVAC**	**30 days**	**30 days**	**0d**
210	HVAC Installation	20 days	20 days	0d
211	HVAC Commisioning - Building A	10 days	10 days	0d
212	**ELECTRICAL**	**105 days**	**102 days**	**3d**
213	Building Rough-in Underground	5 days	5 days	0d
214	Electrical Rough-In	25 days	25 days	0d
215	New Service Equipment Install, Wire & Inspect	10 days	10 days	0d
216	Install and Wire Panels	15 days	15 days	0d
217	Permanent Power On- Building A	0 days	0 days	0d
218	Electric Lights, Devices and Trim	42 days	42 days	0d
219	Fire Alarm System	5 days	5 days	0d
220	Electrical Commissioning	5 days	5 days	0d
