PETRA General Contractors

Meridian, MS - 2026.01.30 - UP01

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Mod	Task Name	Duration	Start	Finish	Total Slack	Actual Start	Actual Finish
1		**GENERAL REQUIREMENTS AND CONDITIONS**	**241 days**	**Mon 9/8/25**	**Tue 8/18/26**	**-14 days**	**Mon 9/8/25**	**NA**
2		**Notice to Proceed**	**1 day**	**Mon 9/8/25**	**Mon 9/8/25**	**0 days**	**Mon 9/8/25**	**Mon 9/8/25**
3		DELAY - PERMIT DELAY	32 days	Tue 9/9/25	Wed 10/22/25	0 days	Tue 9/9/25	Wed 10/22/25
4		**Obtain Building Permit**	**0 days**	**Wed 10/22/25**	**Wed 10/22/25**	**0 days**	**Wed 10/22/25**	**Wed 10/22/25**
5		**ACHD ROW Permit**	**0 days**	**Wed 10/29/25**	**Wed 10/29/25**	**0 days**	**Wed 10/29/25**	**Wed 10/29/25**
6		**Obtain LDIR Approval to Proceed**	**0 days**	**Mon 10/27/25**	**Mon 10/27/25**	**0 days**	**Mon 10/27/25**	**Mon 10/27/25**
7		Receive CAD Base Files from Public Storage	10 days	Tue 9/9/25	Mon 9/22/25	0 days	Tue 9/9/25	Mon 9/22/25
8		Procure Early Work Subcontractors	5 days	Tue 9/9/25	Mon 9/15/25	0 days	Tue 9/9/25	Mon 9/15/25
9		Procure Remaining Subcontractors	20 days	Tue 9/16/25	Mon 10/13/25	0 days	Tue 9/16/25	Mon 10/13/25
10		Submittals (SWPPP/NOI)	10 days	Tue 9/16/25	Mon 9/29/25	0 days	Tue 9/16/25	Mon 9/29/25
11		Submittals (SES /Switchgear)	34 days	Tue 9/16/25	Fri 10/31/25	0 days	Tue 9/16/25	Fri 10/31/25
12		Submittals (numerous)	90 days	Tue 10/14/25	Fri 2/20/26	80 days	Tue 10/14/25	NA
13		PUBLIC STORAGE Fab/Delv Framing & Panels BLDG B	40 days	Thu 10/23/25	Fri 12/19/25	14 days	Thu 10/23/25	NA
14		PUBLIC STORAGE Fab/Delv Framing & Panels BLDG A	40 days	Thu 11/6/25	Tue 1/6/26	38 days	Thu 11/6/25	NA
15		Procure SES's/Switchgears (6 mos ~ 130 WD)	70 days	Mon 11/3/25	Thu 2/12/26	75 days	Mon 11/3/25	NA
16		Light Fixture Submittal Review and Approval	10 days	Mon 1/26/26	Fri 2/6/26	7 days	Mon 1/26/26	NA
17		Light Fixture Package Alternate - Fab and Deliver	10 days	Mon 2/9/26	Fri 2/20/26	37 days	NA	NA
18		Light Fixture Package Spec'd - Fab and Deliver	8 wks	Mon 2/9/26	Fri 4/3/26	1.4 wks	NA	NA
19		Fire Sprinkler Design and Approval	65 days	Tue 10/14/25	Fri 1/16/26	67 days	Tue 10/14/25	NA
20		Fire Alarm System Design and Approval	40 days	Tue 10/14/25	Wed 12/10/25	0 days	Tue 10/14/25	Wed 12/10/25
21		**ASPHALT BATCH PLANT SHUTDOWN**	70 days	Mon 11/17/25	Thu 2/26/26	0 days	Mon 11/17/25	NA
22		**TWENTY WORKING DAYS OF WEATHER DELAY**	14 days	Thu 7/30/26	Tue 8/18/26	-14 days	NA	NA
23		WEATHER DELAY - Rain and High Winds - Imapct SOG B	2 days	Wed 12/17/25	Thu 12/18/25	0 days	Wed 12/17/25	Thu 12/18/25
24		WEATHER DELAY - Rain - Impact SOG B	1 day	Mon 12/22/25	Mon 12/22/25	0 days	Mon 12/22/25	Mon 12/22/25
25		WEATHER DELAY - Rain - Impact SOG B	3 days	Thu 1/8/26	Mon 1/12/26	0 days	NA	NA
26		**Substantial Completion**	**0 days**	**Tue 8/18/26**	**Tue 8/18/26**	**-14 days**	**NA**	**NA**
27		Clean Up and Project Close Out	5 days	Mon 7/20/26	Fri 7/24/26	-14 days	NA	NA
28		Demobilize	3 days	Mon 7/27/26	Wed 7/29/26	-14 days	NA	NA
29		**SITEWORK**	**197 days**	**Mon 9/8/25**	**Tue 6/16/26**	**30 days**	**Mon 9/8/25**	**NA**
30		Mobilization	5 days	Mon 9/8/25	Mon 9/15/25	0 days	Mon 9/8/25	Mon 9/15/25
31		Construction Staking & Surveying	90 days	Mon 9/8/25	Fri 1/16/26	87 days	Mon 9/8/25	NA
32		Inspections and Testing	100 days	Fri 9/12/25	Fri 2/13/26	85 days	Fri 9/12/25	NA
33		Erosion Control & SWPP	5 days	Tue 9/16/25	Mon 9/22/25	0 days	Tue 9/16/25	Mon 9/22/25
34		Maintain Erosion Control	120 days	Tue 9/23/25	Fri 3/13/26	82 days	Tue 9/23/25	NA
35		Structure Demo (Partial Building & RV Storage)	5 days	Mon 11/3/25	Fri 11/7/25	0 days	Mon 11/3/25	Fri 11/7/25
36		**Site Demolition (Trees,Sawcut, Asphalt, Base)**	**0 days**	**Mon 9/8/25**	**Fri 9/12/25**	**0 days**	**Mon 9/8/25**	**Fri 9/12/25**

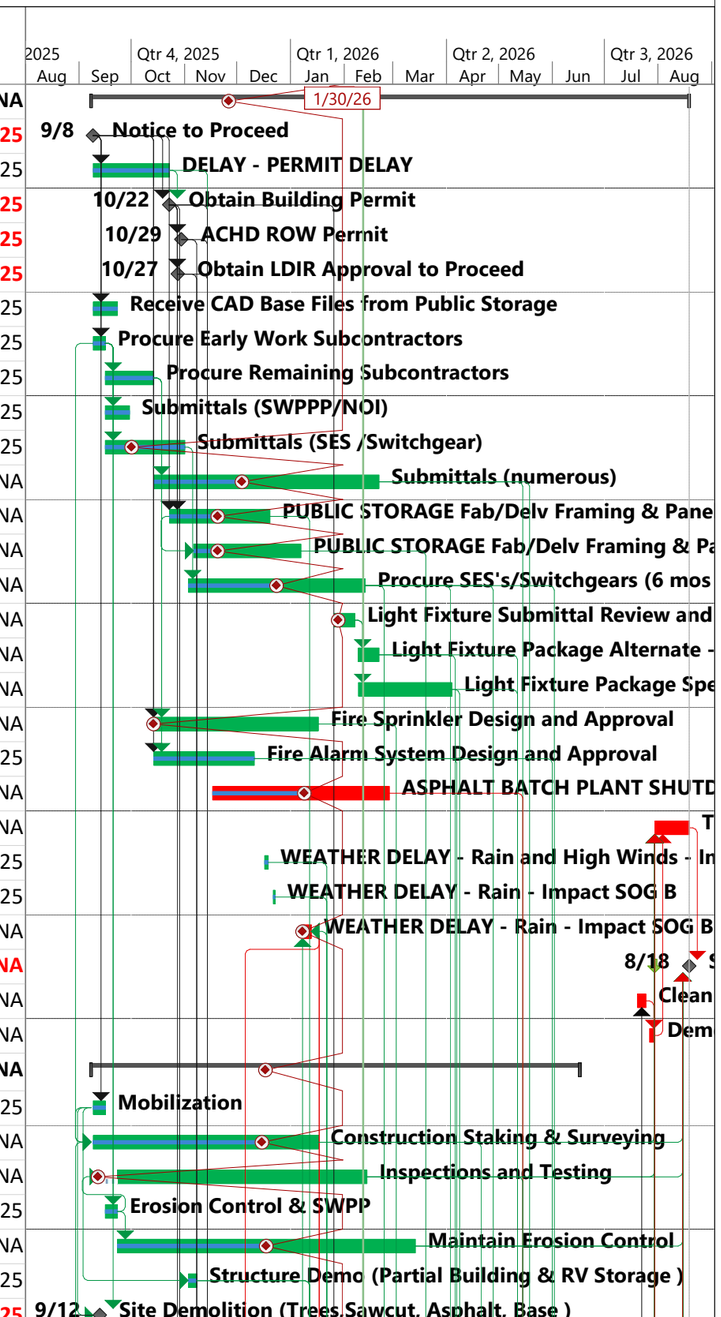

Printed: Thu 2/12/26 6:25 PM

PETRA General Contractors

Meridian, MS - 2026.01.30 - UP01

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Mod	Task Name	Duration	Start	Finish	Total Slack	Actual Start	Actual Finish
37		Re-Mobilization	4 days	Thu 10/23/25	Tue 10/28/25	0 days	Thu 10/23/25	Tue 10/28/25
38		Clear/Grub & Overlot Grading	12 days	Mon 9/8/25	Tue 9/23/25	0 days	Mon 9/8/25	Tue 9/23/25
39		FRAGNET - CITY PRE-CON & 7 DAY NOTICE	7 days	Wed 10/29/25	Thu 11/6/25	0 days	Wed 10/29/25	Thu 11/6/25
40		Site - Sewer Lines and Devices/Ten Mile Tie-In	13 days	Fri 11/14/25	Thu 12/4/25	0 days	Fri 11/14/25	Thu 12/4/25
41		Storm Drain Lines and Devices - North & South of Buildings	15 days	Tue 3/24/26	Mon 4/13/26	21 days	NA	NA
42		Storm Drain Lines South	6 days	Mon 12/22/25	Tue 12/30/25	0 days	Mon 12/22/25	Tue 12/30/25
43		DELAY - GIRR License Agreement Approval to Proceed	6 days	Fri 12/5/25	Fri 12/12/25	0 days	Fri 12/5/25	Fri 12/12/25
44		DELAY - RFI #14 - GIRR Separation	4 days	Mon 12/15/25	Thu 12/18/25	0 days	Mon 12/15/25	Thu 12/18/25
45		Site - GIRR Piping & Devices	16 days	Mon 1/12/26	Mon 2/2/26	0 days	Mon 1/12/26	Mon 2/2/26
46		TP DELAY - Site - GIRR Box Delivery and Placement	6 days	Mon 1/26/26	Mon 2/2/26	0 days	Mon 1/26/26	Mon 2/2/26
47		Site - Water Line Ten Mile Tie-In	2 days	Sat 11/8/25	Tue 11/11/25	0 days	Sat 11/8/25	Tue 11/11/25
48		Site - Water Line & Fire Lines/Hydrants and Devices Remaining	18 days	Mon 1/5/26	Wed 1/28/26	0 days	Mon 1/5/26	Wed 1/28/26
49		Complete Utility Lines Tie-ins to Building A	5 days	Tue 4/14/26	Mon 4/20/26	21 days	NA	NA
50		Gravel Road Finish Grade Prep	5 days	Tue 4/14/26	Mon 4/20/26	39 days	NA	NA
51		Gravel Road Rough Grade Prep	8 days	Mon 12/8/25	Wed 12/17/25	0 days	Mon 12/8/25	Wed 12/17/25
52		BLDG B Foundation Excavation	6 days	Wed 10/29/25	Wed 11/5/25	0 days	Wed 10/29/25	Wed 11/5/25
53		DELAY - BLDG B FOOTING OVER-EX	4 days	Fri 10/31/25	Wed 11/5/25	0 days	Fri 10/31/25	Wed 11/5/25
54		BLDG B SOG Prep	5 days	Wed 11/26/25	Thu 12/4/25	0 days	Wed 11/26/25	Thu 12/4/25
55		FRAGNET - Bldg B Soft Spot Repair	8 days	Thu 12/4/25	Mon 12/15/25	0 days	Thu 12/4/25	Mon 12/15/25
56		BLDG B Backfill Foundations	18 days	Mon 12/15/25	Fri 1/9/26	0 days	Mon 12/15/25	Fri 1/9/26
57		BLDG A Foundation Excavation	5 days	Mon 1/26/26	Fri 1/30/26	-14 days	Mon 1/26/26	NA
58		FRAGNET - BLDG A Footing Seepage Bed Over Ex.	1 day	Mon 2/2/26	Mon 2/2/26	-14 days	NA	NA
59		BLDG A - Interoir Backfill Foundations	5 days	Tue 2/17/26	Mon 2/23/26	-14 days	NA	NA
60		FRAGNET - BLDG A Seepage Bed Pad Over Ex.	3 days	Tue 2/24/26	Thu 2/26/26	-12 days	NA	NA
61		BLDG A - Exterior Backfill Foundations	2 days	Tue 2/24/26	Wed 2/25/26	59 days	NA	NA
62		BLDG A SOG Prep	5 days	Tue 3/3/26	Mon 3/9/26	-14 days	NA	NA
63		Site - Base Course Asphalt Prep & Flatwork Prep	8 days	Tue 3/24/26	Thu 4/2/26	33 days	NA	NA
64		Site Flatwork and Curb and Gutter	15 days	Tue 4/21/26	Mon 5/11/26	21 days	NA	NA
65		Site - Fine Grade Asphalt Prep	3 days	Tue 5/12/26	Thu 5/14/26	21 days	NA	NA
66		Asphalt Paving	2 days	Fri 5/15/26	Mon 5/18/26	21 days	NA	NA
67		Pavement Markings, Signage & Bumpers	2 days	Tue 5/19/26	Wed 5/20/26	34 days	NA	NA
68		Landscaping and Irrigation	15 days	Tue 5/19/26	Tue 6/9/26	21 days	NA	NA
69		Site Fencing Chainlink	5 days	Tue 5/19/26	Tue 5/26/26	30 days	NA	NA
70		Site Fencing Vinyl	10 days	Wed 5/27/26	Tue 6/9/26	30 days	NA	NA
71		Site Fencing Rod Iron and Gates	5 days	Wed 6/10/26	Tue 6/16/26	30 days	NA	NA
72		**BUILDING B**	**163 days**	**Thu 11/6/25**	**Mon 6/29/26**	**7 days**	**Thu 11/6/25**	**NA**

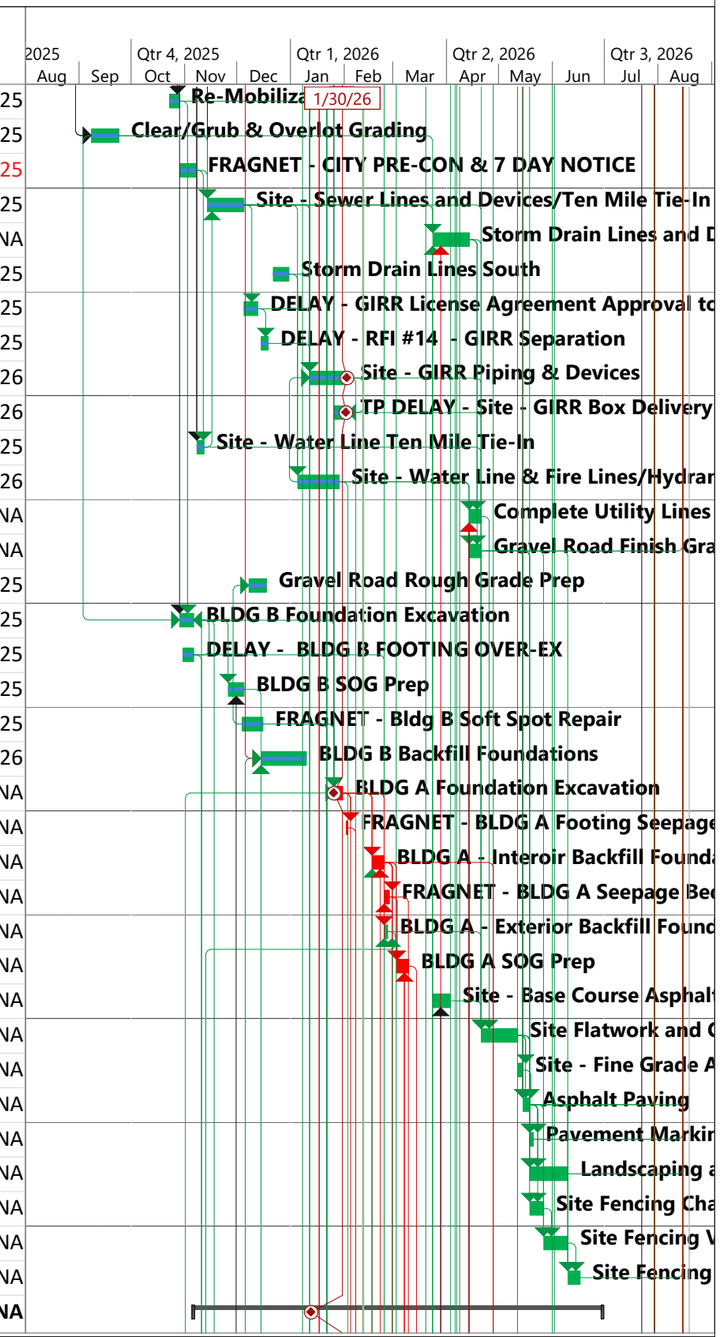

Printed: Thu 2/12/26 6:25 PM

PETRA General Contractors

Meridian, MS - 2026.01.30 - UP01

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Mod	Task Name	Duration	Start	Finish	Total Slack	Actual Start	Actual Finish
73		**CONCRETE WORK**	**44 days**	**Thu 11/6/25**	**Mon 1/12/26**	**0 days**	**Thu 11/6/25**	**Mon 1/12/26**
74		BLDG B Foundation	14 days	Thu 11/6/25	Tue 11/25/25	0 days	Thu 11/6/25	Tue 11/25/25
75		BLDG B Dampproofing	1 day	Tue 11/18/25	Wed 11/26/25	0 days	Tue 11/18/25	Wed 11/26/25
76		BLDG B Slab On Grade	19 days	Mon 12/15/25	Mon 1/12/26	0 days	Mon 12/15/25	Mon 1/12/26
77		**BLDG B Slab On Grade Complete**	**0 days**	**Mon 1/12/26**	**Mon 1/12/26**	**0 days**	**Mon 1/12/26**	**Mon 1/12/26**
78		**STEEL AND METALS**	**81 days**	**Mon 1/12/26**	**Mon 5/4/26**	**26 days**	**Mon 1/12/26**	**NA**
79		Frame & Panel Load Bearing & Shear Walls (JANUS)	25 days	Mon 1/12/26	Mon 2/16/26	21 days	Mon 1/12/26	NA
80		Frame & Panel Partition & Corridor Walls (JANUS)	20 days	Tue 4/7/26	Mon 5/4/26	26 days	NA	NA
81		**WOOD & FRP**	**5 days**	**Tue 3/17/26**	**Mon 3/23/26**	**63 days**	**NA**	**NA**
82		Misc Finish Carpentry	5 days	Tue 3/17/26	Mon 3/23/26	63 days	NA	NA
83		**ROOF & SIDING**	**35 days**	**Fri 1/30/26**	**Thu 3/19/26**	**33 days**	**NA**	**NA**
84		Exterior Sheathing	10 days	Fri 1/30/26	Thu 2/12/26	60 days	NA	NA
85		Weather Barrier	10 days	Fri 2/6/26	Thu 2/19/26	60 days	NA	NA
86		Rigid Insulation Behind CMU	5 days	Fri 2/20/26	Thu 2/26/26	60 days	NA	NA
87		Rigid Insulation Behind Metal Panels	3 days	Fri 2/27/26	Tue 3/3/26	60 days	NA	NA
88		CMU Veneer	15 days	Fri 2/27/26	Thu 3/19/26	63 days	NA	NA
89		Exterior Metal Panels (JANUS)	10 days	Wed 3/4/26	Tue 3/17/26	60 days	NA	NA
90		Install Roof & Roof Insulation (JANUS)	10 days	Tue 2/17/26	Mon 3/2/26	21 days	NA	NA
91		**BLDG B Roofing Complete**	**0 days**	**Mon 3/2/26**	**Mon 3/2/26**	**21 days**	**NA**	**NA**
92		**DOORS & WINDOWS**	**20 days**	**Wed 5/27/26**	**Tue 6/23/26**	**11 days**	**NA**	**NA**
93		F&I Storage Unit Doors (JANUS)	20 days	Wed 5/27/26	Tue 6/23/26	11 days	NA	NA
94		F&I HM Doors and Hardware (JANUS)	15 days	Wed 5/27/26	Tue 6/16/26	16 days	NA	NA
95		**FINISHES**	**30 days**	**Tue 3/3/26**	**Mon 4/13/26**	**48 days**	**NA**	**NA**
96		Install Gypsum Board	10 days	Tue 3/3/26	Mon 3/16/26	48 days	NA	NA
97		Flooring Polished Concrete	5 days	Tue 3/17/26	Mon 3/23/26	58 days	NA	NA
98		FRP / Vinyl Base	5 days	Tue 3/24/26	Mon 3/30/26	58 days	NA	NA
99		Painting	10 days	Tue 3/31/26	Mon 4/13/26	58 days	NA	NA
100		**SPECIALTIES**	**23 days**	**Tue 3/17/26**	**Thu 4/16/26**	**58 days**	**NA**	**NA**
101		Install Misc Equipment & Lockers	20 days	Tue 3/17/26	Mon 4/13/26	61 days	NA	NA
102		Bathroom Accessories	2 days	Tue 3/24/26	Wed 3/25/26	74 days	NA	NA
103		Building Interior Signage	3 days	Tue 4/14/26	Thu 4/16/26	58 days	NA	NA
104		**FIRE SPRINKLERS**	**30 days**	**Tue 3/3/26**	**Mon 4/13/26**	**36 days**	**NA**	**NA**
105		Fire Sprinkler System Rough In	15 days	Tue 3/3/26	Mon 3/23/26	36 days	NA	NA
106		Fire Sprinkler System Trim Out	15 days	Tue 3/24/26	Mon 4/13/26	61 days	NA	NA
107		**PLUMBING**	**87 days**	**Thu 11/20/25**	**Thu 3/26/26**	**73 days**	**Thu 11/20/25**	**NA**
108		Plumbing Rough-in Underground	4 days	Thu 11/20/25	Tue 11/25/25	0 days	Thu 11/20/25	Tue 11/25/25

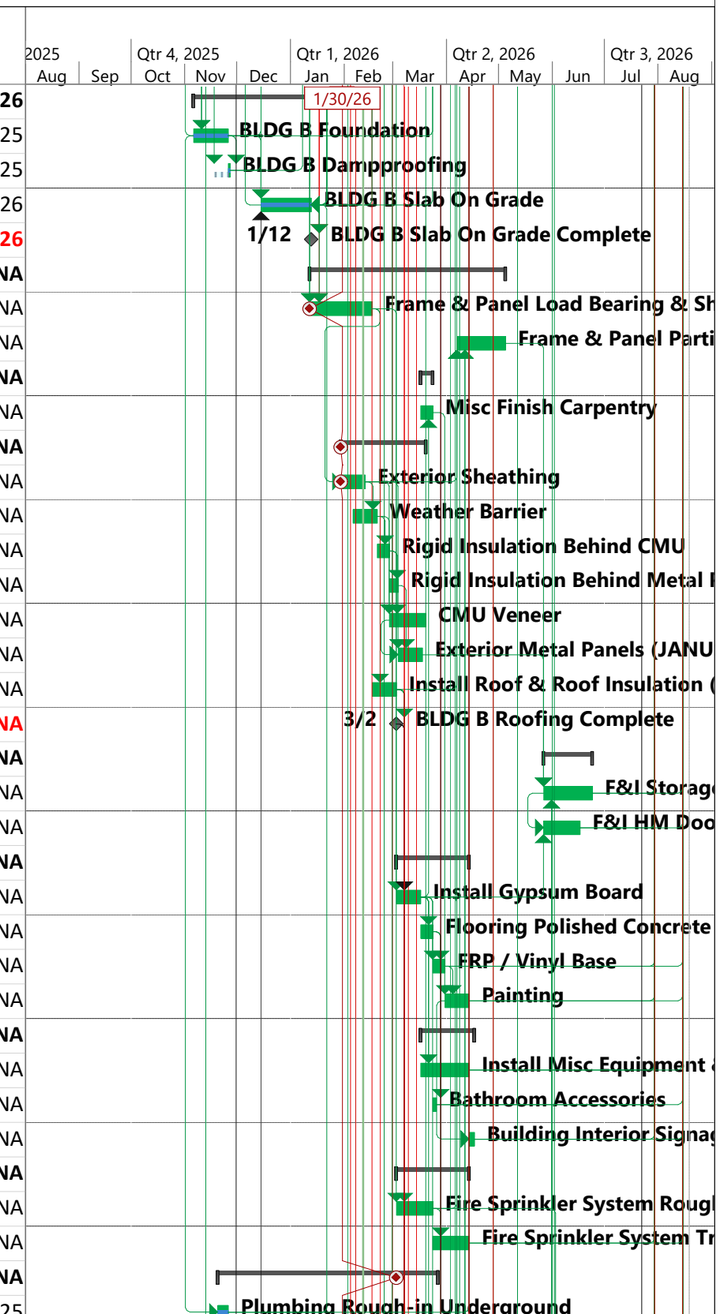

Printed: Thu 2/12/26 6:25 PM

PETRA General Contractors

Meridian, MS - 2026.01.30 - UP01

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Mod	Task Name	Duration	Start	Finish	Total Slack	Actual Start	Actual Finish
109		Drains, Water, Sewer Lines	15 days	Tue 3/3/26	Mon 3/23/26	73 days	NA	NA
110		Bathroom Fixtures	3 days	Tue 3/24/26	Thu 3/26/26	73 days	NA	NA
111		Other Plumbing Fixtures	3 days	Tue 3/24/26	Thu 3/26/26	73 days	NA	NA
112		**HVAC**	**30 days**	**Tue 3/3/26**	**Mon 4/13/26**	**26 days**	**NA**	**NA**
113		HVAC Installation	25 days	Tue 3/3/26	Mon 4/6/26	26 days	NA	NA
114		HVAC Commisioning & T&B	5 days	Tue 4/7/26	Mon 4/13/26	61 days	NA	NA
115		**ELECTRICAL**	**153 days**	**Thu 11/20/25**	**Mon 6/29/26**	**7 days**	**Thu 11/20/25**	**NA**
116		**Building Rough-in Underground**	**0 days**	**Thu 11/20/25**	**Tue 11/25/25**	**0 days**	**Thu 11/20/25**	**Tue 11/25/25**
117		Elect Rough-In	25 days	Tue 3/3/26	Mon 4/6/26	21 days	NA	NA
118		New Service Equipment Install, Wire & Inspect	10 days	Tue 2/24/26	Mon 3/9/26	68 days	NA	NA
119		Install and Wire Panels	15 days	Tue 3/17/26	Mon 4/6/26	48 days	NA	NA
120		**Permanent Power On**	**0 days**	**Mon 4/6/26**	**Mon 4/6/26**	**48 days**	**NA**	**NA**
121		Electric Lights, Devices and Trim	55 days	Mon 4/6/26	Mon 6/22/26	7 days	NA	NA
122		Fire Alarm System	3 days	Tue 4/7/26	Thu 4/9/26	58 days	NA	NA
123		Electrical Commissioning	5 days	Tue 6/23/26	Mon 6/29/26	7 days	NA	NA
124		**BUILDING A**	**117 days**	**Tue 2/3/26**	**Fri 7/17/26**	**-14 days**	**NA**	**NA**
125		**CONCRETE WORK**	**35 days**	**Tue 2/3/26**	**Mon 3/23/26**	**-14 days**	**NA**	**NA**
126		BLDG A Foundation	10 days	Tue 2/3/26	Mon 2/16/26	-14 days	NA	NA
127		BLDG A Dampproofing	2 days	Tue 2/17/26	Wed 2/18/26	59 days	NA	NA
128		BLDG A Exterior Footing Insulation	3 days	Thu 2/19/26	Mon 2/23/26	59 days	NA	NA
129		BLDG A Slab On Grade	10 days	Tue 3/10/26	Mon 3/23/26	-14 days	NA	NA
130		**BLDG A Slab On Grade Complete**	**0 days**	**Mon 3/23/26**	**Mon 3/23/26**	**33 days**	**NA**	**NA**
131		**STEEL AND METALS**	**67 days**	**Fri 3/20/26**	**Tue 6/23/26**	**-14 days**	**NA**	**NA**
132		Frame & Panel Load Bearing & Shear Walls (JANUS)	25 days	Fri 3/20/26	Thu 4/23/26	-14 days	NA	NA
133		Frame & Panel Partition & Corridor Walls (JANUS)	15 days	Wed 6/3/26	Tue 6/23/26	-2 days	NA	NA
134		Canopy Install	8 days	Fri 4/24/26	Tue 5/5/26	37 days	NA	NA
135		**WOOD & FRP**	**5 days**	**Fri 5/15/26**	**Thu 5/21/26**	**25 days**	**NA**	**NA**
136		Misc Finish Carpentry	5 days	Fri 5/15/26	Thu 5/21/26	25 days	NA	NA
137		**ROOF & SIDING**	**35 days**	**Fri 4/10/26**	**Fri 5/29/26**	**-4 days**	**NA**	**NA**
138		Exterior Sheathing	10 days	Fri 4/10/26	Thu 4/23/26	11 days	NA	NA
139		Weather Barrier	10 days	Fri 4/17/26	Thu 4/30/26	11 days	NA	NA
140		Rigid Insulation Behind CMU	5 days	Fri 5/1/26	Thu 5/7/26	11 days	NA	NA
141		CMU Veneer	15 days	Fri 5/8/26	Fri 5/29/26	11 days	NA	NA
142		Rigid Insulation Behind Metal Panels	3 days	Fri 5/1/26	Tue 5/5/26	15 days	NA	NA
143		Exterior Metal Panels (JANUS)	10 days	Tue 5/12/26	Tue 5/26/26	11 days	NA	NA
144		Install Roof & Roof Insulation (JANUS)	5 days	Fri 4/24/26	Thu 4/30/26	-14 days	NA	NA

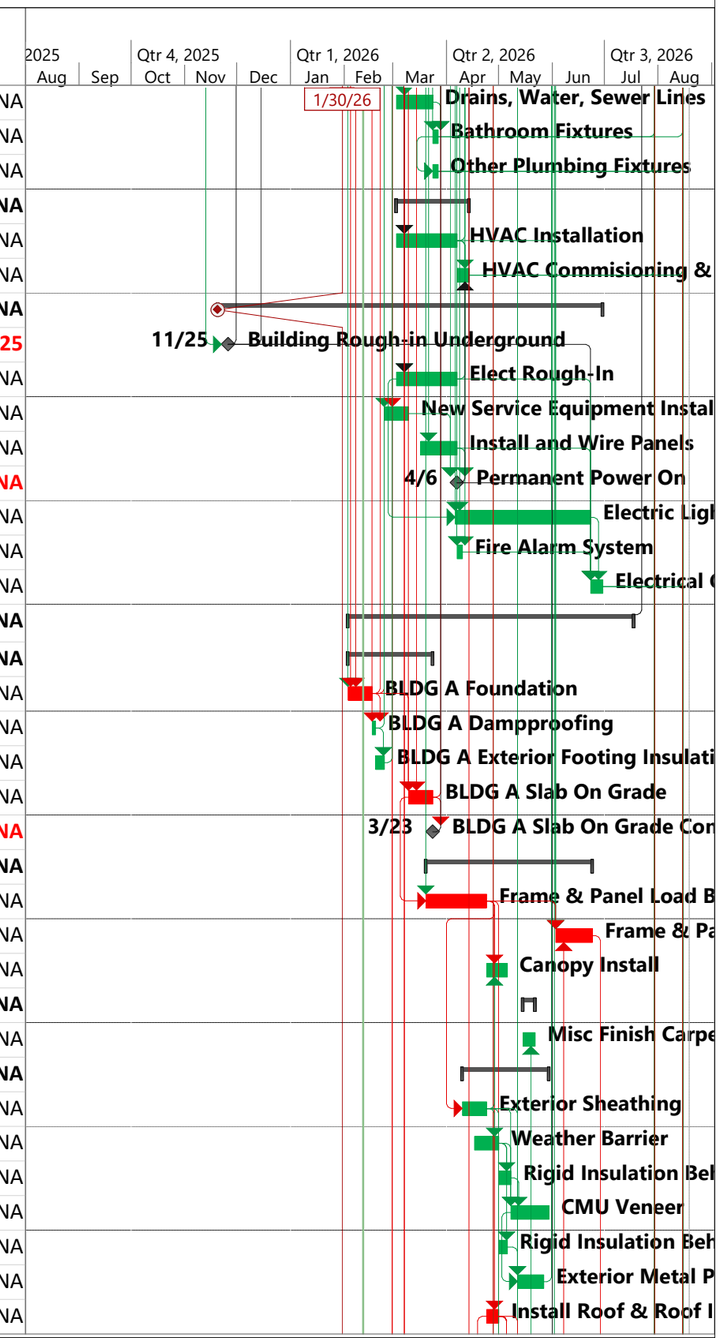

Printed: Thu 2/12/26 6:25 PM

PETRA General Contractors

Meridian, MS - 2026.01.30 - UP01

Public Storage Ten Mile Rd

Contract Schedule

Public Storage

ID	Task Mod	Task Name	Duration	Start	Finish	Total Slack	Actual Start	Actual Finish
145		**BLDG A Roofing Complete**	**0 days**	**Thu 4/30/26**	**Thu 4/30/26**	**-7 days**	**NA**	**NA**
146		**DOORS & WINDOWS**	**5 days**	**Wed 6/24/26**	**Tue 6/30/26**	**-2 days**	**NA**	**NA**
147		F&I Storage Unit Doors (JANUS)	5 days	Wed 6/24/26	Tue 6/30/26	-2 days	NA	NA
148		F&I HM Doors and Hardware (JANUS)	5 days	Wed 6/24/26	Tue 6/30/26	-2 days	NA	NA
149		**FINISHES**	**30 days**	**Fri 5/1/26**	**Fri 6/12/26**	**8 days**	**NA**	**NA**
150		Install Gypsum Board	10 days	Fri 5/1/26	Thu 5/14/26	8 days	NA	NA
151		Painting	10 days	Fri 5/15/26	Fri 5/29/26	8 days	NA	NA
152		Flooring Polished Conc.	5 days	Mon 6/1/26	Fri 6/5/26	8 days	NA	NA
153		FRP & Vinyl Base	5 days	Mon 6/8/26	Fri 6/12/26	8 days	NA	NA
154		**SPECIALTIES**	**22 days**	**Fri 5/15/26**	**Tue 6/16/26**	**8 days**	**NA**	**NA**
155		Install Misc Equipment & Lockers	20 days	Fri 5/15/26	Fri 6/12/26	10 days	NA	NA
156		Bathroom Accessories	2 days	Mon 6/15/26	Tue 6/16/26	8 days	NA	NA
157		Building Interior Signage	3 days	Mon 6/1/26	Wed 6/3/26	17 days	NA	NA
158		**FIRE SPRINKLERS**	**30 days**	**Fri 5/1/26**	**Fri 6/12/26**	**10 days**	**NA**	**NA**
159		Fire Sprinkler System Rough In	15 days	Fri 5/1/26	Thu 5/21/26	10 days	NA	NA
160		Fire Sprinkler System Trim Out	15 days	Fri 5/22/26	Fri 6/12/26	10 days	NA	NA
161		**PLUMBING**	**83 days**	**Tue 2/24/26**	**Fri 6/19/26**	**-14 days**	**NA**	**NA**
162		Plumbing Rough-in Underground	5 days	Tue 2/24/26	Mon 3/2/26	-14 days	NA	NA
163		Drains, Water, Sewer Lines	15 days	Fri 5/1/26	Thu 5/21/26	5 days	NA	NA
164		Bathroom Fixtures- Building A	10 days	Fri 5/22/26	Fri 6/5/26	5 days	NA	NA
165		Other Plumbing Fixtures	10 days	Mon 6/8/26	Fri 6/19/26	5 days	NA	NA
166		**HVAC**	**30 days**	**Fri 5/1/26**	**Fri 6/12/26**	**10 days**	**NA**	**NA**
167		HVAC Installation	20 days	Fri 5/1/26	Fri 5/29/26	10 days	NA	NA
168		HVAC Commisioning & T& B	10 days	Mon 6/1/26	Fri 6/12/26	10 days	NA	NA
169		**ELECTRICAL**	**102 days**	**Tue 2/24/26**	**Fri 7/17/26**	**-14 days**	**NA**	**NA**
170		Building Rough-in Underground	5 days	Tue 2/24/26	Mon 3/2/26	-14 days	NA	NA
171		Electrical Rough-In	25 days	Tue 4/28/26	Tue 6/2/26	-14 days	NA	NA
172		New Service Equipment Install, Wire & Inspect	10 days	Tue 4/28/26	Mon 5/11/26	33 days	NA	NA
173		Install and Wire Panels	15 days	Fri 5/15/26	Fri 6/5/26	10 days	NA	NA
174		**Permanent Power On- Building A**	**0 days**	**Fri 6/5/26**	**Fri 6/5/26**	**15 days**	**NA**	**NA**
175		Electric Lights, Devices and Trim	42 days	Tue 5/12/26	Fri 7/10/26	-14 days	NA	NA
176		Fire Alarm System	5 days	Mon 6/1/26	Fri 6/5/26	10 days	NA	NA
177		Electrical Commissioning	5 days	Mon 7/13/26	Fri 7/17/26	-14 days	NA	NA

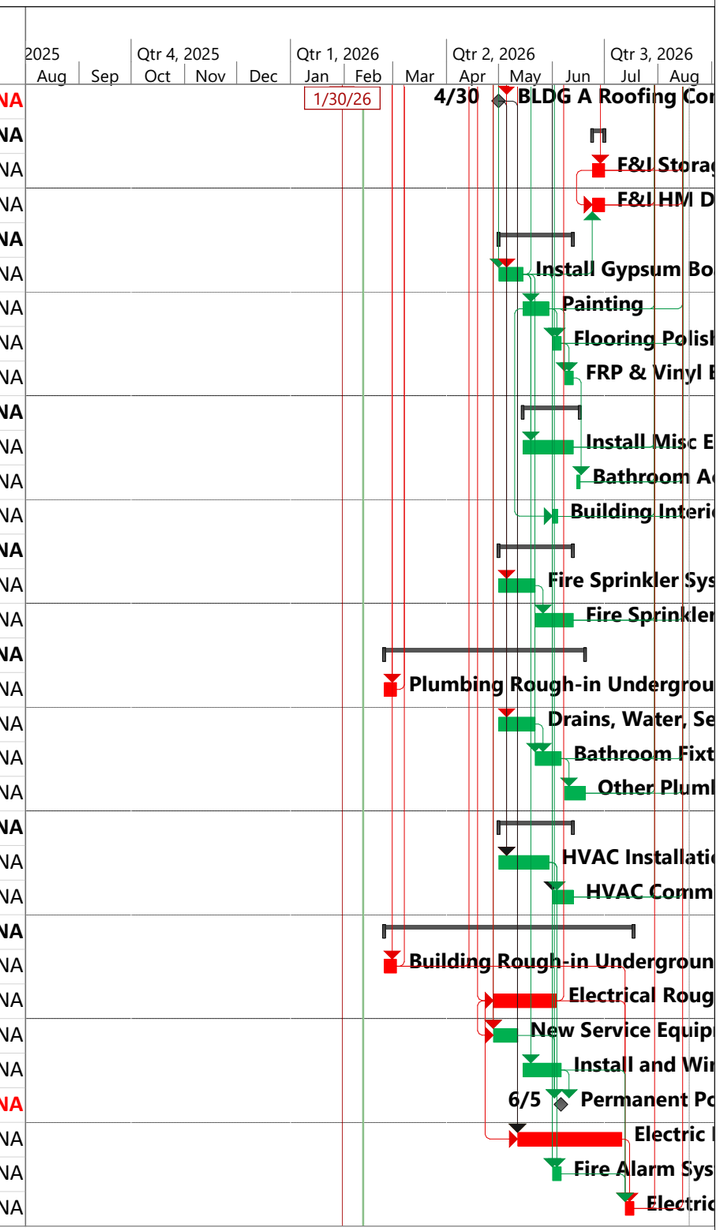

Printed: Thu 2/12/26 6:25 PM
