	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Public Storage - Mesa AZ**	**323 days**	**347 days**	**-24d**	**Fri 24/12/27**	**Fri 24/12/27**	**0d**	**Wed 26/04/08**	**Tue 26/05/12**	**-24d**
2	**PreConstruction**	**18 days**	**18 days**	**0d**	**Fri 24/12/27**	**Fri 24/12/27**	**0d**	**Tue 25/01/21**	**Tue 25/01/21**	**0d**
3	Notice To Proceed	0 days	0 days	0d	Fri 24/12/27	Fri 24/12/27	0d	Fri 24/12/27	Fri 24/12/27	0d
4	Mobilzation	5 days	5 days	0d	Mon 24/12/30	Mon 24/12/30	0d	Fri 25/01/03	Fri 25/01/03	0d
5	Erosion Control	3 days	3 days	0d	Mon 25/01/06	Mon 25/01/06	0d	Wed 25/01/08	Wed 25/01/08	0d
6	Hydrant Meter	0 days	0 days	0d	Fri 25/01/03	Fri 25/01/03	0d	Fri 25/01/03	Fri 25/01/03	0d
7	Hydrant Meter Delay	12 days	12 days	0d	Mon 25/01/06	Mon 25/01/06	0d	Tue 25/01/21	Tue 25/01/21	0d
8	**Surface Demo & Grading**	**42 days**	**42 days**	**0d**	**Wed 25/01/22**	**Wed 25/01/22**	**0d**	**Fri 25/03/21**	**Fri 25/03/21**	**0d**
9	Surface Demo	15 days	15 days	0d	Wed 25/01/22	Wed 25/01/22	0d	Tue 25/02/11	Tue 25/02/11	0d
10	Site Survey	1 day	1 day	0d	Wed 25/02/12	Wed 25/02/12	0d	Wed 25/02/12	Wed 25/02/12	0d
11	Pregrade Meeting	1 day	1 day	0d	Wed 25/02/12	Wed 25/02/12	0d	Wed 25/02/12	Wed 25/02/12	0d
12	Over-Ex & Recompact Bldg Pad	15 days	15 days	0d	Thu 25/02/13	Thu 25/02/13	0d	Thu 25/03/06	Thu 25/03/06	0d
13	Grading Delay For Spetic System 2/12, 2/13, 2/14	3 days	3 days	0d	Fri 25/03/07	Fri 25/03/07	0d	Tue 25/03/11	Tue 25/03/11	0d
14	Grading Rain Day Delays 3/7, 3/8, 3/9, 3/12, 3/13, 3/14, 3/15	7 days	7 days	0d	Wed 25/03/12	Wed 25/03/12	0d	Thu 25/03/20	Thu 25/03/20	0d
15	Pad Certification	1 day	1 day	0d	Fri 25/03/21	Fri 25/03/21	0d	Fri 25/03/21	Fri 25/03/21	0d
16	**On Site Improvements**	**35 days**	**35 days**	**0d**	**Mon 25/03/24**	**Mon 25/03/24**	**0d**	**Fri 25/05/09**	**Fri 25/05/09**	**0d**
17	Site Wall	35 days	35 days	0d	Mon 25/03/24	Mon 25/03/24	0d	Fri 25/05/09	Fri 25/05/09	0d
18	**On Site Wet Utilites**	**20 days**	**20 days**	**0d**	**Mon 25/05/12**	**Mon 25/05/12**	**0d**	**Mon 25/06/09**	**Mon 25/06/09**	**0d**
19	Install Sewer	5 days	5 days	0d	Mon 25/05/12	Mon 25/05/12	0d	Fri 25/05/16	Fri 25/05/16	0d
20	Install Storm Drain	5 days	5 days	0d	Mon 25/05/19	Mon 25/05/19	0d	Fri 25/05/23	Fri 25/05/23	0d
21	Install Fire Loop & Riser	6 days	6 days	0d	Tue 25/05/27	Tue 25/05/27	0d	Tue 25/06/03	Tue 25/06/03	0d
22	Install Domestic Water	4 days	4 days	0d	Wed 25/06/04	Wed 25/06/04	0d	Mon 25/06/09	Mon 25/06/09	0d
23	**Off Site Wet Utilites**	**92 days**	**92 days**	**0d**	**Mon 25/05/12**	**Mon 25/05/12**	**0d**	**Fri 25/09/19**	**Fri 25/09/19**	**0d**
24	Water: Fire & Domestic Laterals 8th Street	5 days	5 days	0d	Mon 25/05/12	Mon 25/05/12	0d	Fri 25/05/16	Fri 25/05/16	0d
25	Water: Delay (City could not Shut Down)	82 days	82 days	0d	Mon 25/05/19	Mon 25/05/19	0d	Fri 25/09/12	Fri 25/09/12	0d
26	Water: Fire & Domestic 8th Street	5 days	5 days	0d	Mon 25/09/15	Mon 25/09/15	0d	Fri 25/09/19	Fri 25/09/19	0d
27	Water: Fire Line Lateral Country Club Only	5 days	5 days	0d	Mon 25/05/12	Mon 25/05/12	0d	Fri 25/05/16	Fri 25/05/16	0d
28	Water: Delay Country Club (City could not Shut Down)	26 days	26 days	0d	Mon 25/05/19	Mon 25/05/19	0d	Tue 25/06/24	Tue 25/06/24	0d
29	Water: Fire Line lateral Coutnry Club (Weekend Only)	31 days	31 days	0d	Wed 25/06/25	Wed 25/06/25	0d	Thu 25/08/07	Thu 25/08/07	0d
30	**On & Off Site Dry Utilites Power & Comms**	**250 days**	**250 days**	**0d**	**Mon 25/03/24**	**Mon 25/03/24**	**0d**	**Fri 26/03/20**	**Fri 26/03/20**	**0d**
31	Approved Power & Comms Permits & Plans	1 day	1 day	0d	Mon 25/03/24	Mon 25/03/24	0d	Mon 25/03/24	Mon 25/03/24	0d
32	Delay: Approved Power & Comms Permits & Plans	159 days	159 days	0d	Tue 25/03/25	Tue 25/03/25	0d	Wed 25/11/05	Wed 25/11/05	0d
33	ROW Permit	1 day	1 day	0d	Thu 25/11/06	Thu 25/11/06	0d	Thu 25/11/06	Thu 25/11/06	0d
34	Delay: ROW Permit 8th Street (City Moratorium)	13 days	13 days	0d	Fri 25/11/07	Fri 25/11/07	0d	Tue 25/11/25	Tue 25/11/25	0d
35	Delay: ROW Permit Country Club (City Moratorium)	40 days	40 days	0d	Fri 25/11/07	Fri 25/11/07	0d	Fri 26/01/09	Fri 26/01/09	0d
36	**8th Street Dry Utilies Power & Comms**	**54 days**	**46 days**	**8d**	**Wed 25/11/26**	**Wed 25/11/26**	**0d**	**Wed 26/02/18**	**Thu 26/02/05**	**9d**
37	Set Up Message Board (5day Notice Period)	1 day	1 day	0d	Wed 25/11/26	Wed 25/11/26	0d	Wed 25/11/26	Wed 25/11/26	0d
38	Set Up Lane & Sidewalk Closure	1 day	2 days	-1d	Mon 25/12/01	Mon 25/12/01	0d	Mon 25/12/01	Tue 25/12/02	-1d
39	Relocate Temp fence to behind Barricades	2 days	2 days	0d	Wed 25/12/03	Wed 25/12/03	0d	Thu 25/12/04	Thu 25/12/04	0d
40	Demo & Haul off Sidewalks	1 day	2 days	-1d	Fri 25/12/05	Fri 25/12/05	0d	Fri 25/12/05	Mon 25/12/08	-1d
41	Survey For New UG Power & Comms	1 day	1 day	0d	Mon 25/12/08	Tue 25/12/09	-1d	Mon 25/12/08	Tue 25/12/09	-1d
42	OH to UG Power & Comms 8th Ave		2 days			Wed 25/12/10			Thu 25/12/11	
43	Open Up Splits pits		2 days			Fri 25/12/12			Mon 25/12/15	
44	Splits UG Power		2 days			Tue 25/12/16			Wed 25/12/17	
45	Penetrate vaults		1 day			Thu 25/12/18			Thu 25/12/18	
46	BF Splits Pits		1 day			Fri 25/12/19			Fri 25/12/19	
47	UG for Coms & Power from Building to Splice Pit	12 days			Mon 25/12/08			Tue 25/12/23		
48	City of Mesa Working In Vaults	3 days			Mon 25/12/08			Wed 25/12/10		
49	2nd Crew Cox Trench & Conduits	2 days			Thu 25/12/11			Fri 25/12/12		
50	City of Mesa Shut Down Redesign	7 days			Mon 25/12/15			Tue 25/12/23		
51	City Inspection Shut down for PTO	4 days			Mon 25/12/29			Fri 26/01/02		
52	Restart Excavation By Main Vault	2 days			Mon 26/01/05			Tue 26/01/06		
53	Break Into Splice Pit by Main Vault	2 days			Tue 26/01/06			Wed 26/01/07		
54	Rain	1 day			Thu 26/01/08			Thu 26/01/08		
55	Penetrate Vault West Side	1 day			Fri 26/01/09			Fri 26/01/09		
56	Install UG Conduit WestSide Splice pit into Vault	1 day			Mon 26/01/12			Mon 26/01/12		
57	Install UG Conduit SouthSide Main Vault	3 days			Mon 26/01/12			Wed 26/01/14		
58	Slurry Encase Conduits	1 day			Thu 26/01/15			Thu 26/01/15		
59	Backfill Vault Area	1 day			Fri 26/01/16			Fri 26/01/16		
60	Trench For Coms	1 day	1 day	0d	Mon 26/01/19	Mon 25/12/22	20d	Mon 26/01/19	Mon 25/12/22	20d
61	Install UG Comms Conduits	1 day	3 days	-2d	Tue 26/01/20	Tue 25/12/23	20d	Tue 26/01/20	Tue 25/12/30	15d
62	Slurry Encase Conduits		2 days			Wed 25/12/31			Fri 26/01/02	
63	Slurry & Set Boxes	2 days	2 days	0d	Wed 26/01/21	Mon 26/01/05	12d	Thu 26/01/22	Tue 26/01/06	12d
64	Set Vaults/Pads	2 days	2 days	0d	Fri 26/01/23	Wed 26/01/07	12d	Mon 26/01/26	Thu 26/01/08	12d
65	Punch Work	1 day	1 day	0d	Tue 26/01/27	Fri 26/01/09	12d	Tue 26/01/27	Fri 26/01/09	12d
66	Survey For New UG Power & Comms For As-Builts	2 days	2 days	0d	Wed 26/01/28	Mon 26/01/12	12d	Thu 26/01/29	Tue 26/01/13	12d
67	Grade for new Drive Entry	4 days			Mon 25/12/29			Fri 26/01/02		
68	Form New Drive Entry & Curbs	3 days			Mon 26/01/05			Wed 26/01/07		
69	Rain	1 day			Thu 26/01/08			Thu 26/01/08		
70	Pour New Drive Entry & Curbs	3 days			Mon 26/01/12			Wed 26/01/14		
71	Grade for Aspahlt Paving	2 days			Thu 26/01/15			Fri 26/01/16		
72	Asphalt Slot Patch & Pave at New Drive Entry	1 day			Mon 26/01/19			Mon 26/01/19		
73	Grade for new Sidewalks	1 day	3 days	-2d	Fri 26/01/30	Wed 26/01/14	12d	Fri 26/01/30	Fri 26/01/16	10d
74	Form & Pour New Concrete & Sidewalks	2 days	8 days	-6d	Mon 26/02/02	Mon 26/01/19	10d	Tue 26/02/03	Wed 26/01/28	4d
75	Asphalt Slot Patch @ Drive Entry		2 days			Thu 26/01/29			Fri 26/01/30	
76	Relocate Temp Fence	2 days	2 days	0d	Mon 26/02/02	Mon 26/02/02	0d	Tue 26/02/03	Tue 26/02/03	0d
77	Traffic Control Removal	2 days	2 days	0d	Wed 26/02/04	Wed 26/02/04	0d	Thu 26/02/05	Thu 26/02/05	0d
78	Public Sidewalk Open	0 days	0 days	0d	Thu 26/02/05	Thu 26/02/05	0d	Thu 26/02/05	Thu 26/02/05	0d
79	City Of Mesa Work Scope Power to Building	10 days	10 days	0d	Wed 26/01/28	Mon 26/01/12	12d	Tue 26/02/10	Fri 26/01/23	12d
80	City Of Mesa or Cox Poles Removal?	5 days	5 days	0d	Wed 26/02/11	Mon 26/01/26	12d	Wed 26/02/18	Fri 26/01/30	13d
81	**Country Club Dry Utilies Power**	**49 days**	**49 days**	**0d**	**Mon 26/01/12**	**Mon 26/01/12**	**0d**	**Fri 26/03/20**	**Fri 26/03/20**	**0d**

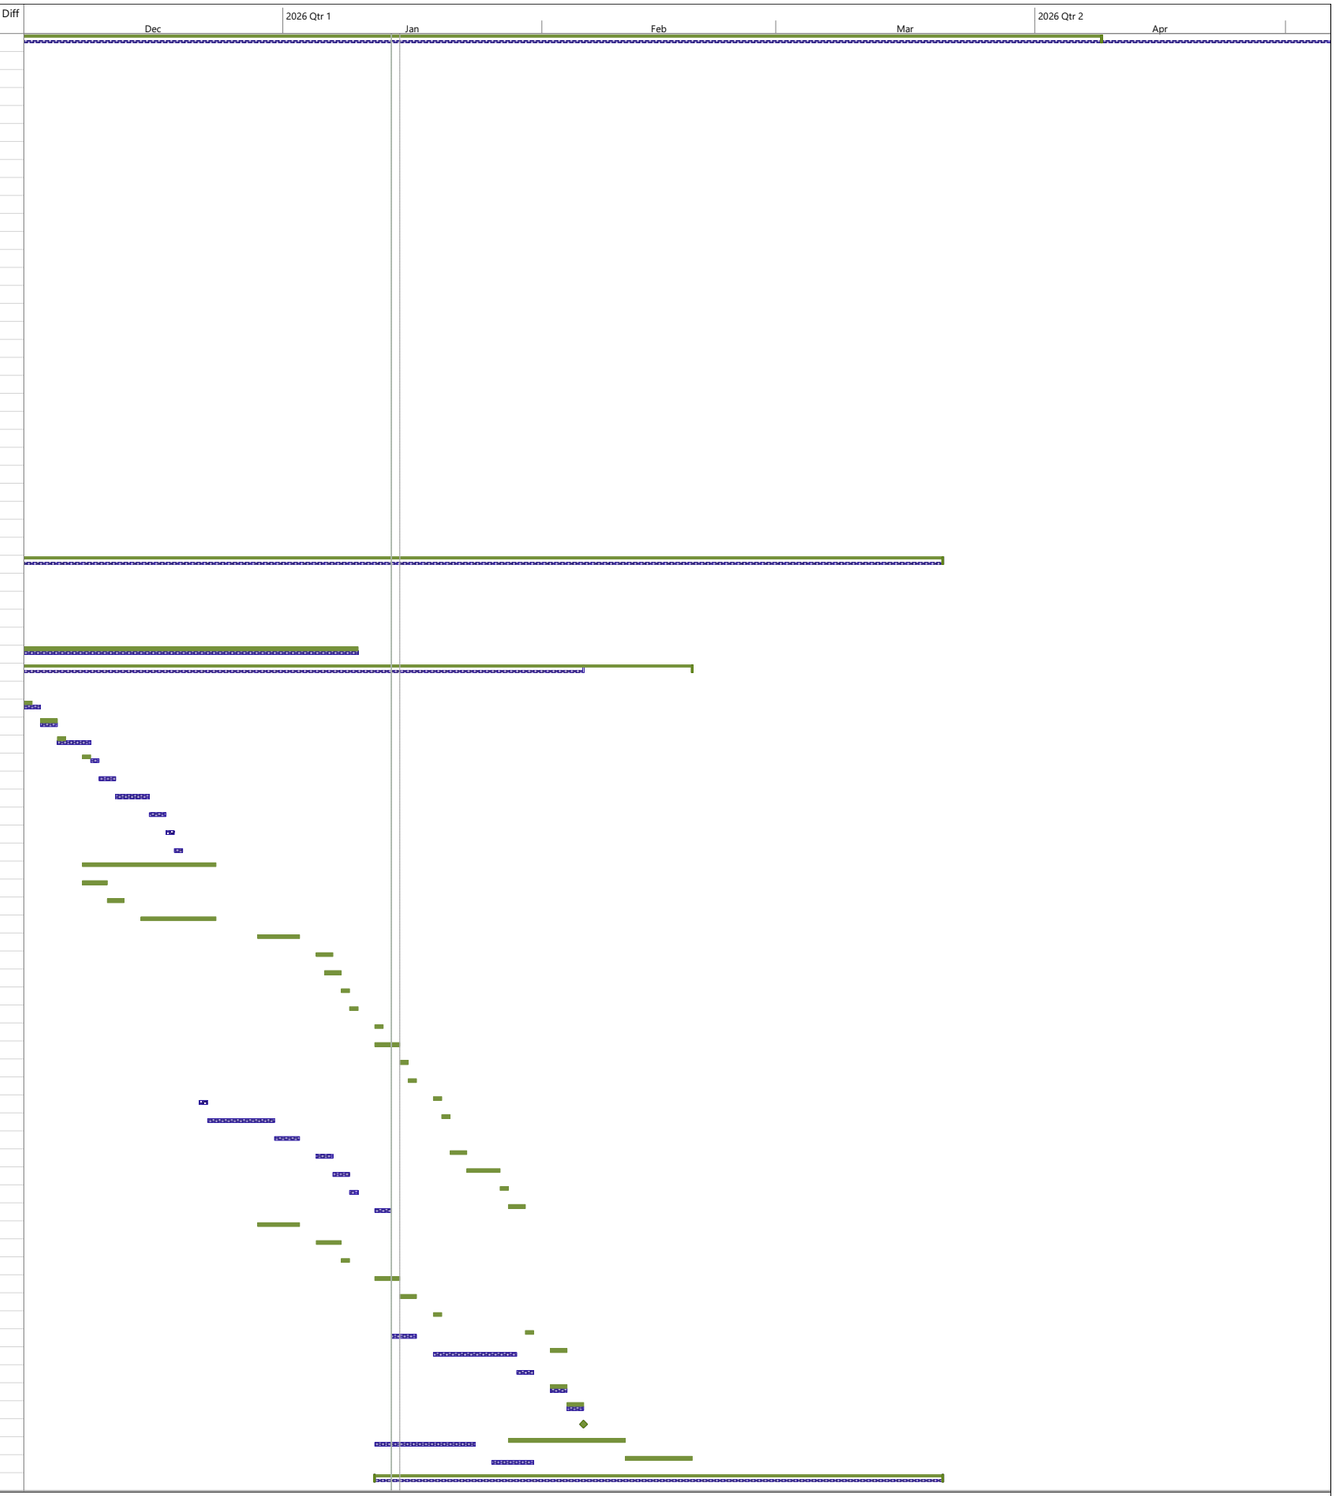

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
82	Set Up Message Board (5day Notice Period)	5 days	5 days	0d	Mon 26/01/12	Mon 26/01/12	0d	Fri 26/01/16	Fri 26/01/16	0d
83	Set Up Lane & Sidewalk Closure	2 days	2 days	0d	Mon 26/01/19	Mon 26/01/19	0d	Tue 26/01/20	Tue 26/01/20	0d
84	Relocate Temp fence to behind Barricades	1 day	1 day	0d	Wed 26/01/21	Wed 26/01/21	0d	Wed 26/01/21	Wed 26/01/21	0d
85	Demo & Haul off Sidewalks	2 days	2 days	0d	Thu 26/01/22	Thu 26/01/22	0d	Fri 26/01/23	Fri 26/01/23	0d
86	Survey For New UG Power & Comms	1 day	1 day	0d	Mon 26/01/26	Mon 26/01/26	0d	Mon 26/01/26	Mon 26/01/26	0d
87	Dig Vaults	2 days	2 days	0d	Tue 26/01/27	Tue 26/01/27	0d	Wed 26/01/28	Wed 26/01/28	0d
88	Build Junction	1 day	1 day	0d	Thu 26/01/29	Thu 26/01/29	0d	Thu 26/01/29	Thu 26/01/29	0d
89	Build Switch	3 days	3 days	0d	Fri 26/01/30	Fri 26/01/30	0d	Tue 26/02/03	Tue 26/02/03	0d
90	Dig Vault	1 day	1 day	0d	Wed 26/02/04	Wed 26/02/04	0d	Wed 26/02/04	Wed 26/02/04	0d
91	Build Vault	2 days	2 days	0d	Thu 26/02/05	Thu 26/02/05	0d	Fri 26/02/06	Fri 26/02/06	0d
92	Set Vault	1 day	1 day	0d	Mon 26/02/09	Mon 26/02/09	0d	Mon 26/02/09	Mon 26/02/09	0d
93	Build TX	1 day	1 day	0d	Tue 26/02/10	Tue 26/02/10	0d	Tue 26/02/10	Tue 26/02/10	0d
94	Trench	2 days	2 days	0d	Wed 26/02/11	Wed 26/02/11	0d	Thu 26/02/12	Thu 26/02/12	0d
95	Pipe/Rack	2 days	2 days	0d	Fri 26/02/13	Fri 26/02/13	0d	Tue 26/02/17	Tue 26/02/17	0d
96	Slurry Encasement	2 days	2 days	0d	Wed 26/02/18	Wed 26/02/18	0d	Thu 26/02/19	Thu 26/02/19	0d
97	Backfill	2 days	2 days	0d	Fri 26/02/20	Fri 26/02/20	0d	Mon 26/02/23	Mon 26/02/23	0d
98	Punch Work	2 days	2 days	0d	Tue 26/02/24	Tue 26/02/24	0d	Wed 26/02/25	Wed 26/02/25	0d
99	Dig For Bore Receiving Pit	1 day	1 day	0d	Tue 26/02/17	Tue 26/02/17	0d	Tue 26/02/17	Tue 26/02/17	0d
100	Mobilize Bore Equipment	1 day	1 day	0d	Wed 26/02/18	Wed 26/02/18	0d	Wed 26/02/18	Wed 26/02/18	0d
101	Bore Trench	2 days	2 days	0d	Thu 26/02/19	Thu 26/02/19	0d	Fri 26/02/20	Fri 26/02/20	0d
102	Back Ream Bore Trench	1 day	1 day	0d	Mon 26/02/23	Mon 26/02/23	0d	Mon 26/02/23	Mon 26/02/23	0d
103	Bore Punch	2 days	2 days	0d	Tue 26/02/24	Tue 26/02/24	0d	Wed 26/02/25	Wed 26/02/25	0d
104	Survey For New UG Power & Comms For As-Builts	1 day	1 day	0d	Thu 26/02/26	Thu 26/02/26	0d	Thu 26/02/26	Thu 26/02/26	0d
105	Grade for new Sidewalks & Drive Entry	3 days	3 days	0d	Fri 26/02/27	Fri 26/02/27	0d	Tue 26/03/03	Tue 26/03/03	0d
106	Form & Pour New Concrete & Sidewalks	8 days	8 days	0d	Wed 26/03/04	Wed 26/03/04	0d	Fri 26/03/13	Fri 26/03/13	0d
107	Asphalt Slot Patch @ Drive Entry	2 days	2 days	0d	Mon 26/03/16	Mon 26/03/16	0d	Tue 26/03/17	Tue 26/03/17	0d
108	Relocate Temp Fence	1 day	1 day	0d	Wed 26/03/18	Wed 26/03/18	0d	Wed 26/03/18	Wed 26/03/18	0d
109	Traffic Control Removal	1 day	1 day	0d	Thu 26/03/19	Thu 26/03/19	0d	Thu 26/03/19	Thu 26/03/19	0d
110	Public Sidewalk Open	0 days	0 days	0d	Fri 26/03/20	Fri 26/03/20	0d	Fri 26/03/20	Fri 26/03/20	0d
111	City Of Mesa Work Scope Power to AAMCO	10 days	10 days	0d	Thu 26/02/26	Thu 26/02/26	0d	Wed 26/03/11	Wed 26/03/11	0d
112	City Of Mesa of Pole Removal?	2 days	2 days	0d	Thu 26/03/12	Thu 26/03/12	0d	Fri 26/03/13	Fri 26/03/13	0d
113	**On-Site Improvements West & South**	**52 days**	**47 days**	**5d**	**Mon 25/12/01**	**Mon 25/12/01**	**0d**	**Tue 26/02/17**	**Mon 26/02/09**	**6d**
114	Grade for Curb & Gutter	5 days	5 days	0d	Mon 25/12/01	Mon 25/12/01	0d	Fri 25/12/05	Fri 25/12/05	0d
115	Concrete Curb & Gutters	4 days	4 days	0d	Mon 25/12/08	Mon 25/12/08	0d	Thu 25/12/11	Thu 25/12/11	0d
116	Grade for Sidewalks, Handicap Ramps, etc	2 days	2 days	0d	Fri 25/12/12	Fri 25/12/12	0d	Mon 25/12/15	Mon 25/12/15	0d
117	Concrete Pour Walks, Ramps, Etc	4 days	4 days	0d	Tue 25/12/16	Tue 25/12/16	0d	Fri 25/12/19	Fri 25/12/19	0d
118	Grade For Paving	2 days	2 days	0d	Mon 25/12/22	Mon 25/12/22	0d	Tue 25/12/23	Tue 25/12/23	0d
119	AC Paving	2 days	2 days	0d	Mon 25/12/29	Mon 25/12/29	0d	Tue 25/12/30	Tue 25/12/30	0d
120	Landscape Sleeving	2 days	2 days	0d	Wed 25/12/31	Wed 25/12/31	0d	Fri 26/01/02	Fri 26/01/02	0d
121	Gate Tracks	5 days	5 days	0d	Mon 26/01/05	Mon 26/01/05	0d	Fri 26/01/09	Fri 26/01/09	0d
122	Gate Fencing	5 days	5 days	0d	Mon 26/01/12	Mon 26/01/12	0d	Fri 26/01/16	Fri 26/01/16	0d
123	Gate Installation	5 days	5 days	0d	Mon 26/01/19	Mon 26/01/19	0d	Fri 26/01/23	Fri 26/01/23	0d
124	Landscape Irrigation and Planting	9 days	9 days	0d	Mon 26/02/02	Mon 26/01/26	5d	Thu 26/02/12	Thu 26/02/05	5d
125	Striping & Signage	2 days	2 days	0d	Fri 26/02/13	Fri 26/02/06	5d	Tue 26/02/17	Mon 26/02/09	6d
126	**Building Shell Construction**	**151 days**	**151 days**	**0d**	**Mon 25/03/24**	**Mon 25/03/24**	**0d**	**Thu 25/10/23**	**Thu 25/10/23**	**0d**
127	Underslab Plumbing & Electrical	8 days	8 days	0d	Mon 25/03/24	Mon 25/03/24	0d	Wed 25/04/02	Wed 25/04/02	0d
128	Elevator Pits form & Pour	10 days	10 days	0d	Mon 25/03/24	Mon 25/03/24	0d	Fri 25/04/04	Fri 25/04/04	0d
129	Drill & Set Jack Casings	5 days	5 days	0d	Mon 25/04/07	Mon 25/04/07	0d	Fri 25/04/11	Fri 25/04/11	0d
130	CMU Wall Footings	10 days	10 days	0d	Thu 25/03/27	Thu 25/03/27	0d	Wed 25/04/09	Wed 25/04/09	0d
131	Fine grade Granular Base & Reinforce Slab on grade -North	5 days	5 days	0d	Thu 25/04/03	Thu 25/04/03	0d	Wed 25/04/09	Wed 25/04/09	0d
132	Fine grade Granular Base & Reinforce Slab on grade -South	5 days	5 days	0d	Thu 25/04/10	Thu 25/04/10	0d	Wed 25/04/16	Wed 25/04/16	0d
133	Pour Slab on grade North 8"	3 days	3 days	0d	Mon 25/04/14	Mon 25/04/14	0d	Wed 25/04/16	Wed 25/04/16	0d
134	Pour Slab on grade South 8"	3 days	3 days	0d	Thu 25/04/17	Thu 25/04/17	0d	Mon 25/04/21	Mon 25/04/21	0d
135	CMU walls/Ledgers to 3rd floor	24 days	24 days	0d	Thu 25/04/17	Thu 25/04/17	0d	Tue 25/05/20	Tue 25/05/20	0d
136	Shearwalls/Beams & Deck for 2nd floor North	16 days	16 days	0d	Wed 25/05/14	Wed 25/05/14	0d	Thu 25/06/05	Thu 25/06/05	0d
137	Reinforce & Pour 2nd floor deck North	4 days	4 days	0d	Fri 25/06/06	Fri 25/06/06	0d	Wed 25/06/11	Wed 25/06/11	0d
138	Deck cure	5 days	5 days	0d	Thu 25/06/12	Thu 25/06/12	0d	Wed 25/06/18	Wed 25/06/18	0d
139	Shearwalls/Beams & Deck for 2nd floor South	16 days	16 days	0d	Fri 25/06/06	Fri 25/06/06	0d	Fri 25/06/27	Fri 25/06/27	0d
140	Reinforce & Pour 2nd floor deck South	4 days	4 days	0d	Mon 25/06/30	Mon 25/06/30	0d	Thu 25/07/03	Thu 25/07/03	0d
141	Deck cure	5 days	5 days	0d	Tue 25/07/08	Tue 25/07/08	0d	Mon 25/07/14	Mon 25/07/14	0d
142	CMU walls 3rd floor to top out North	15 days	15 days	0d	Thu 25/06/19	Thu 25/06/19	0d	Thu 25/07/10	Thu 25/07/10	0d
143	Shearwalls/Beams & Deck for 3rd floor North	16 days	16 days	0d	Mon 25/07/14	Mon 25/07/14	0d	Mon 25/08/04	Mon 25/08/04	0d
144	Reinforce & Pour deck 3 North	4 days	4 days	0d	Tue 25/08/05	Tue 25/08/05	0d	Fri 25/08/08	Fri 25/08/08	0d
145	Deck Cure	5 days	5 days	0d	Mon 25/08/11	Mon 25/08/11	0d	Fri 25/08/15	Fri 25/08/15	0d
146	CMU walls 3rd floor to top out South	18 days	18 days	0d	Tue 25/07/15	Tue 25/07/15	0d	Thu 25/08/07	Thu 25/08/07	0d
147	Shearwalls/Beams & Deck for 3rd floor South	18 days	18 days	0d	Fri 25/08/08	Fri 25/08/08	0d	Wed 25/09/03	Wed 25/09/03	0d
148	Reinforce & Pour Deck 3 South	4 days	4 days	0d	Thu 25/09/04	Thu 25/09/04	0d	Tue 25/09/09	Tue 25/09/09	0d
149	Deck Cure	5 days	5 days	0d	Wed 25/09/10	Wed 25/09/10	0d	Tue 25/09/16	Tue 25/09/16	0d
150	Shearwalls/Beams & Roof Deck North	18 days	18 days	0d	Thu 25/09/04	Thu 25/09/04	0d	Mon 25/09/29	Mon 25/09/29	0d
151	Shearwalls/Beams & Roof Deck South	18 days	18 days	0d	Tue 25/09/30	Tue 25/09/30	0d	Thu 25/10/23	Thu 25/10/23	0d
152	Roof Structural @ platforms & Screens	5 days	5 days	0d	Tue 25/09/30	Tue 25/09/30	0d	Mon 25/10/06	Mon 25/10/06	0d
153	**Building Roof Exterior**	**35 days**	**35 days**	**0d**	**Tue 25/09/30**	**Tue 25/09/30**	**0d**	**Mon 25/11/17**	**Mon 25/11/17**	**0d**
154	Install roof accessories/Curbs, drains etc.	10 days	10 days	0d	Tue 25/09/30	Tue 25/09/30	0d	Mon 25/10/13	Mon 25/10/13	0d
155	Roof Insulation cover board & Membrane	22 days	22 days	0d	Tue 25/10/14	Tue 25/10/14	0d	Wed 25/11/12	Wed 25/11/12	0d
156	Set rooftop Equipment	3 days	3 days	0d	Thu 25/11/13	Thu 25/11/13	0d	Mon 25/11/17	Mon 25/11/17	0d
157	**Building Interior Main Storage**	**145 days**	**145 days**	**0d**	**Tue 25/07/15**	**Tue 25/07/15**	**0d**	**Wed 26/02/11**	**Wed 26/02/11**	**0d**
158	Layout & Install Hangars from 2nd fl deck	5 days	5 days	0d	Tue 25/07/15	Tue 25/07/15	0d	Mon 25/07/21	Mon 25/07/21	0d
159	Overhead M,P,E & Fire 1st fl	20 days	20 days	0d	Tue 25/07/22	Tue 25/07/22	0d	Mon 25/08/18	Mon 25/08/18	0d
160	Hallway System & Doors 1st floor	25 days	25 days	0d	Tue 25/08/19	Tue 25/08/19	0d	Tue 25/09/23	Tue 25/09/23	0d
161	Finish Mech. & Electrical 1st Fl	3 days	3 days	0d	Wed 25/09/24	Wed 25/09/24	0d	Fri 25/09/26	Fri 25/09/26	0d
162	Layout & Install Overhead Hangars from 3rd fl deck	5 days	5 days	0d	Mon 25/08/18	Mon 25/08/18	0d	Fri 25/08/22	Fri 25/08/22	0d

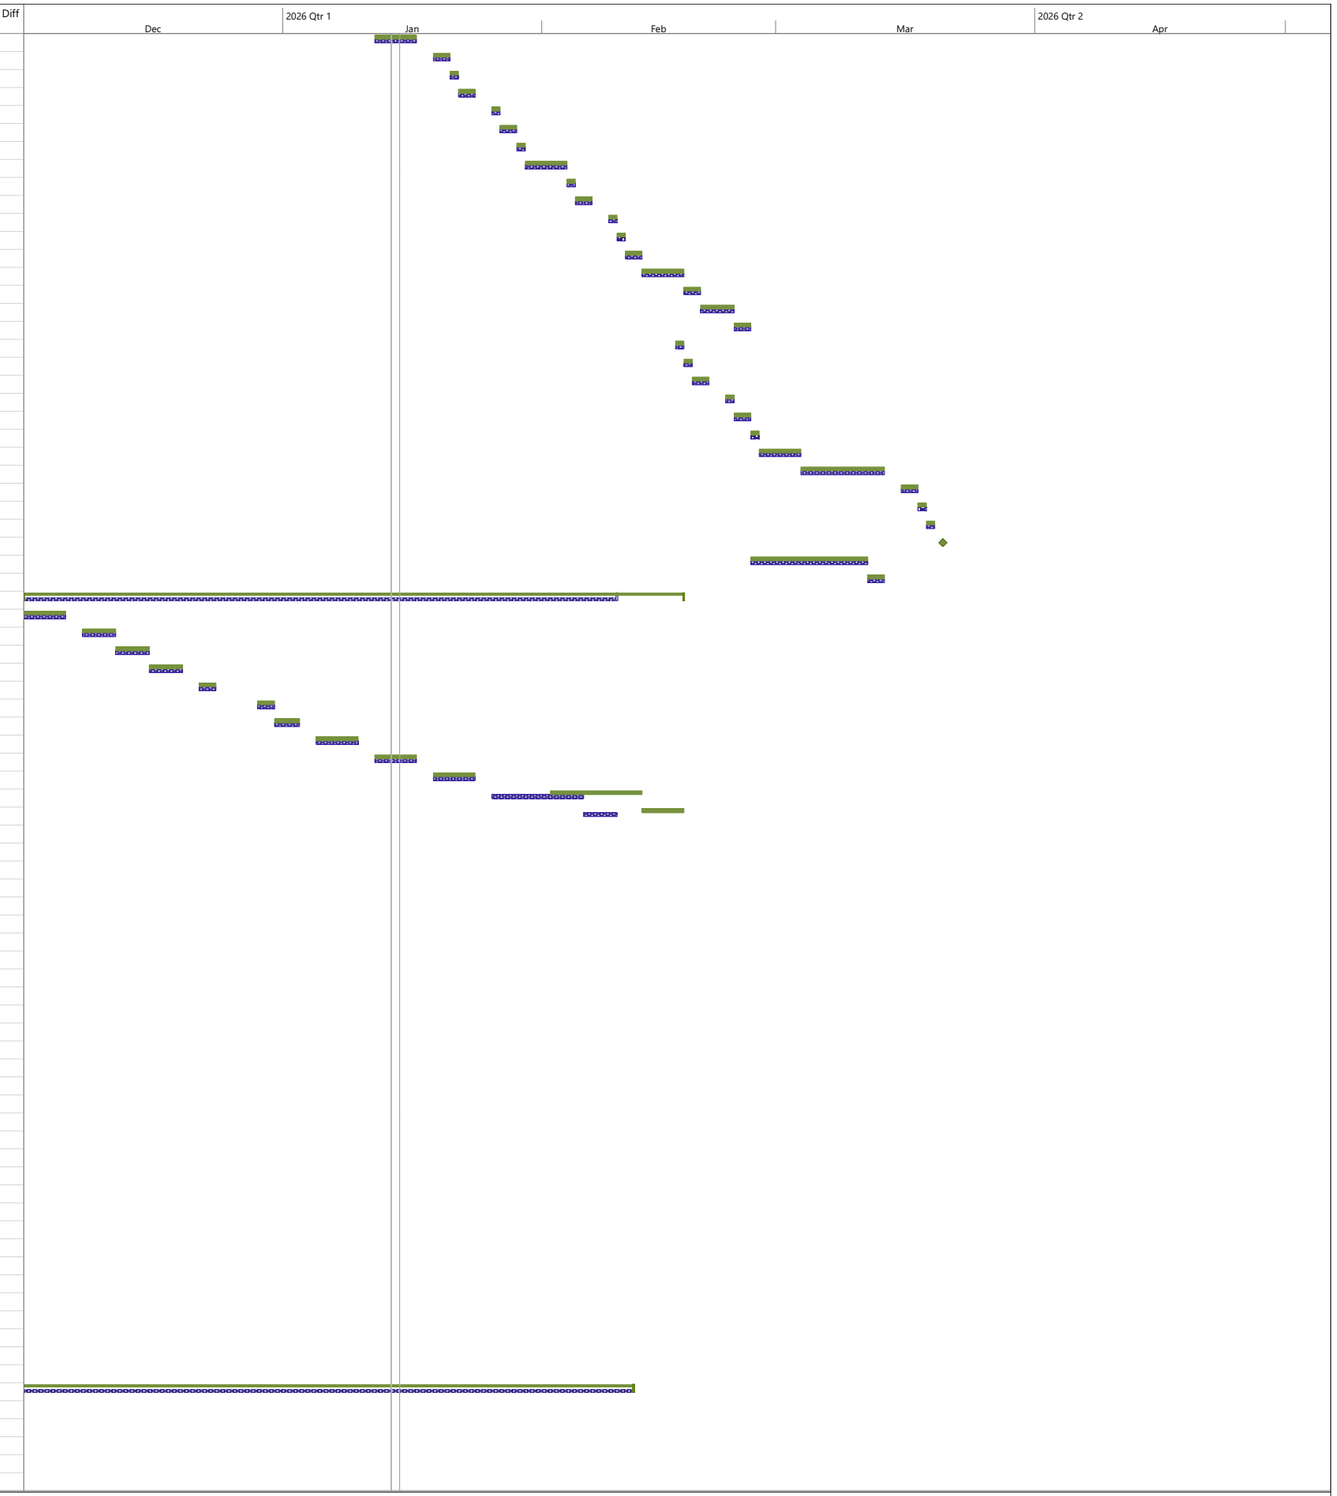
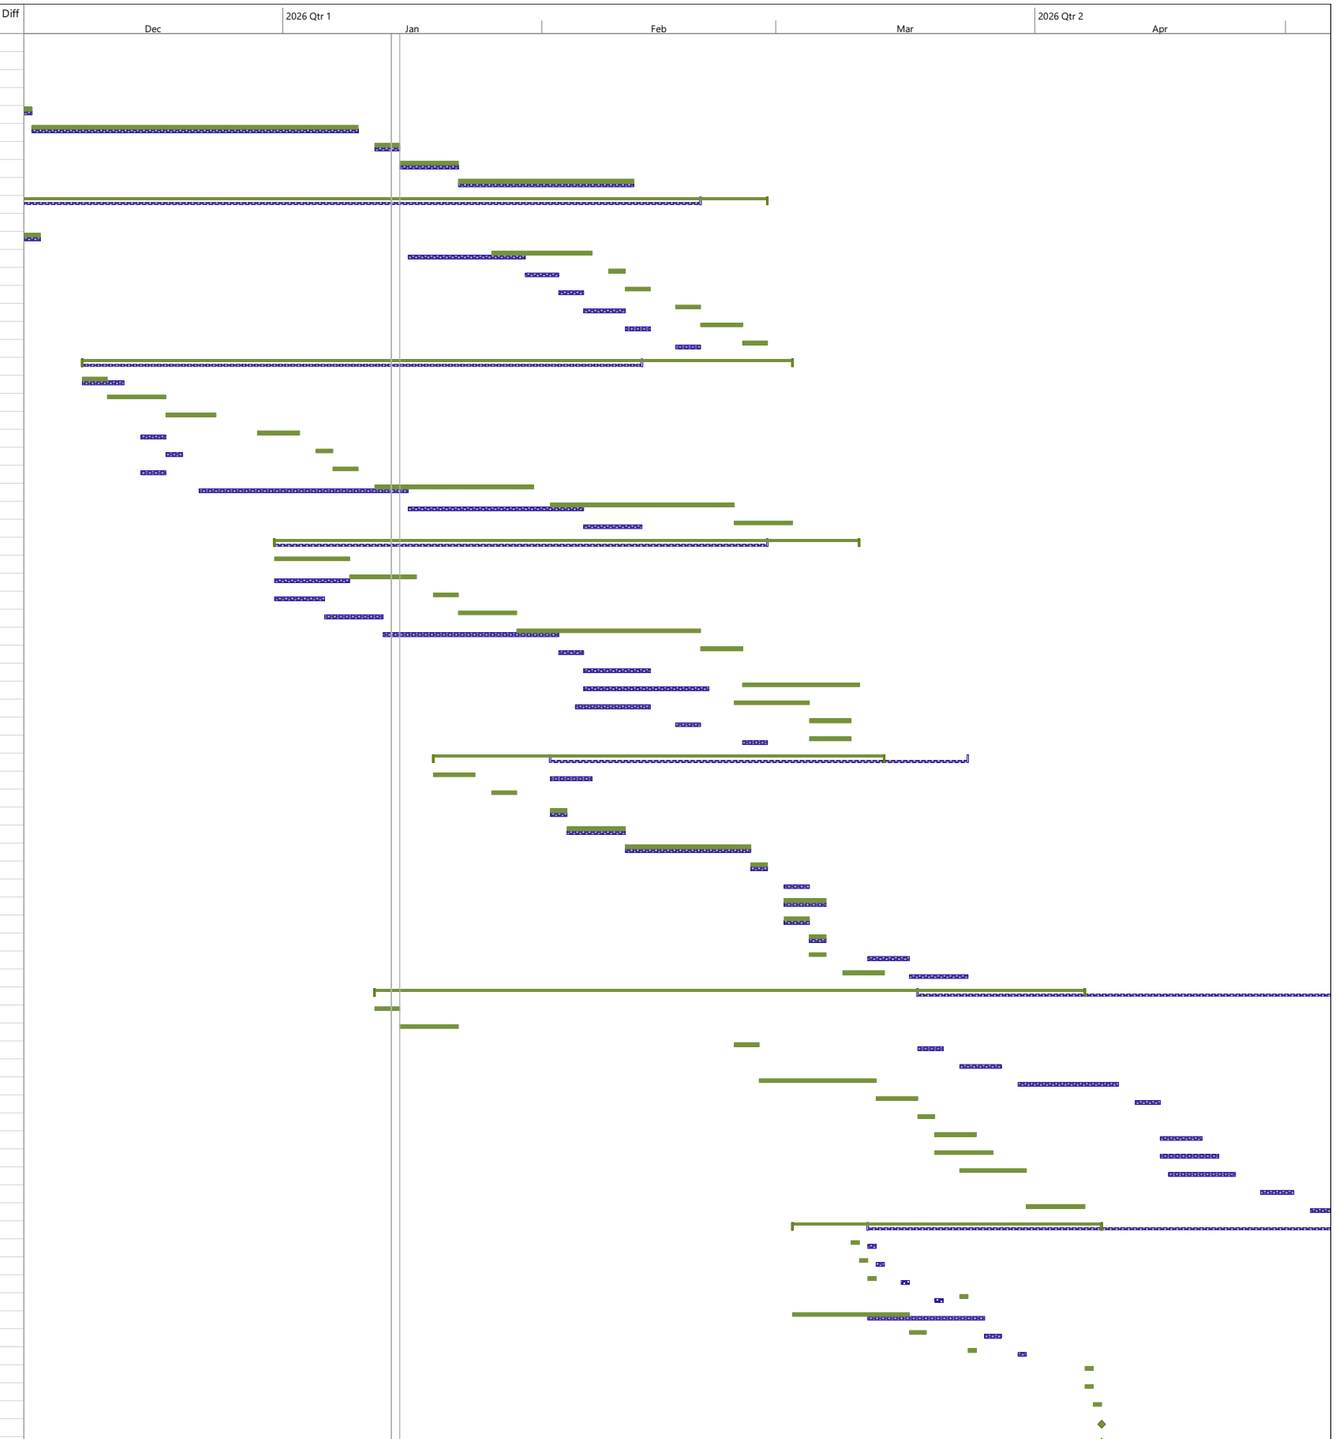
	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
163	Overhead M,P,E & Fire 2nd Fl	20 days	20 days	0d	Mon 25/08/25	Mon 25/08/25	0d	Mon 25/09/22	Mon 25/09/22	0d
164	Hallway System & Doors 2nd Floor	22 days	22 days	0d	Tue 25/09/23	Tue 25/09/23	0d	Wed 25/10/22	Wed 25/10/22	0d
165	Finish Mech. & Electrical 2nd Fl	3 days	3 days	0d	Thu 25/10/23	Thu 25/10/23	0d	Mon 25/10/27	Mon 25/10/27	0d
166	Layout & Install Overhead Hangars from Roof deck	5 days	5 days	0d	Fri 25/10/24	Fri 25/10/24	0d	Thu 25/10/30	Thu 25/10/30	0d
167	Overhead M,P,E & Fire 3rd Fl	20 days	20 days	0d	Fri 25/10/31	Fri 25/10/31	0d	Mon 25/12/01	Mon 25/12/01	0d
168	Hallway System & Doors 3rd Floor	25 days	25 days	0d	Tue 25/12/02	Tue 25/12/02	0d	Fri 26/01/09	Fri 26/01/09	0d
169	Finish Mech. & Electrical 3rd Fl	3 days	3 days	0d	Mon 26/01/12	Mon 26/01/12	0d	Wed 26/01/14	Wed 26/01/14	0d
170	Finish Paint Storage Area	5 days	5 days	0d	Thu 26/01/15	Thu 26/01/15	0d	Wed 26/01/21	Wed 26/01/21	0d
171	Final Clean up & Seal floors	15 days	15 days	0d	Thu 26/01/22	Thu 26/01/22	0d	Wed 26/02/11	Wed 26/02/11	0d
172	**Building Interior Office**	**70 days**	**64 days**	**6d**	**Thu 25/11/13**	**Thu 25/11/13**	**0d**	**Fri 26/02/27**	**Thu 26/02/19**	**6d**
173	Office Framing	6 days	6 days	0d	Thu 25/11/13	Thu 25/11/13	0d	Thu 25/11/20	Thu 25/11/20	0d
174	Office M/E/P Rough in	6 days	6 days	0d	Fri 25/11/21	Fri 25/11/21	0d	Tue 25/12/02	Tue 25/12/02	0d
175	Office Drywall	10 days	10 days	0d	Mon 26/01/26	Fri 26/01/16	6d	Fri 26/02/06	Thu 26/01/29	6d
176	Install HM Doors & Hardware	2 days	2 days	0d	Mon 26/02/09	Fri 26/01/30	6d	Tue 26/02/10	Mon 26/02/02	6d
177	Finish Painting in Storage areas	3 days	3 days	0d	Wed 26/02/11	Tue 26/02/03	6d	Fri 26/02/13	Thu 26/02/05	6d
178	Suspended Ceilings	3 days	3 days	0d	Tue 26/02/17	Fri 26/02/06	7d	Thu 26/02/19	Tue 26/02/10	7d
179	Office Fixtures & Finishes	3 days	3 days	0d	Fri 26/02/20	Wed 26/02/11	7d	Tue 26/02/24	Fri 26/02/13	7d
180	Final Clean up & Seal floors	3 days	3 days	0d	Wed 26/02/25	Tue 26/02/17	6d	Fri 26/02/27	Thu 26/02/19	6d
181	**Elevator**	**56 days**	**45 days**	**11d**	**Mon 25/12/08**	**Mon 25/12/08**	**0d**	**Mon 26/03/02**	**Thu 26/02/12**	**12d**
182	Demo for Sump Pit Relocation	3 days	5 days	-2d	Mon 25/12/08	Mon 25/12/08	0d	Wed 25/12/10	Fri 25/12/12	-2d
183	Sump Pit Delay Filling Up with Ground Water	5 days			Thu 25/12/11			Wed 25/12/17		
184	Construct & Concrete Pour New Pit	4 days			Thu 25/12/18			Tue 25/12/23		
185	Install Pit Lights & Electric	4 days	3 days	1d	Mon 25/12/29	Mon 25/12/15	10d	Fri 26/01/02	Wed 25/12/17	12d
186	Relocate Plumb & Fire Sprinkler	2 days	2 days	0d	Mon 26/01/05	Thu 25/12/18	12d	Tue 26/01/06	Fri 25/12/19	12d
187	Build Temp Cover	3 days	3 days	0d	Wed 26/01/07	Mon 25/12/15	17d	Fri 26/01/09	Wed 25/12/17	17d
188	Elevator Construction Car #1	15 days	15 days	0d	Mon 26/01/12	Mon 25/12/22	15d	Fri 26/01/30	Thu 26/01/15	11d
189	Elevator Construction Car #2	15 days	15 days	0d	Mon 26/02/02	Fri 26/01/16	11d	Mon 26/02/23	Thu 26/02/05	12d
190	Test & Adjust Elevators	5 days	5 days	0d	Tue 26/02/24	Fri 26/02/06	12d	Mon 26/03/02	Thu 26/02/12	12d
191	**Building Exterior West & South**	**48 days**	**41 days**	**7d**	**Wed 25/12/31**	**Wed 25/12/31**	**0d**	**Tue 26/03/10**	**Fri 26/02/27**	**7d**
192	Install Storefront Spandral at EFIS	6 days			Wed 25/12/31			Thu 26/01/08		
193	Install Storefront At Main Openings	6 days	6 days	0d	Fri 26/01/09	Wed 25/12/31	7d	Fri 26/01/16	Thu 26/01/08	6d
194	Install Scaffolding at Building Perimeter	3 days	3 days	0d	Mon 26/01/19	Wed 25/12/31	13d	Wed 26/01/21	Mon 26/01/05	12d
195	Exterior Sheathing	5 days	5 days	0d	Thu 26/01/22	Tue 26/01/06	12d	Wed 26/01/28	Mon 26/01/12	12d
196	EIFS	15 days	15 days	0d	Thu 26/01/29	Tue 26/01/13	12d	Thu 26/02/19	Mon 26/02/02	13d
197	Remove Scaffolding	3 days	3 days	0d	Fri 26/02/20	Tue 26/02/03	13d	Tue 26/02/24	Thu 26/02/05	13d
198	Install Storefront Spandral at EFIS		6 days			Fri 26/02/06			Fri 26/02/13	
199	Install Metal Panel Systems @ Tower Framing	10 days	10 days	0d	Wed 26/02/25	Fri 26/02/06	13d	Tue 26/03/10	Fri 26/02/20	12d
200	Exterior Breakmetal, flashings, Sealants, & Painting	7 days	7 days	0d	Tue 26/02/24	Thu 26/02/05	13d	Wed 26/03/04	Fri 26/02/13	13d
201	Install Steel Canopies	3 days	3 days	0d	Thu 26/03/05	Tue 26/02/17	12d	Mon 26/03/09	Thu 26/02/19	12d
202	Install Glass	3 days	3 days	0d	Thu 26/03/05	Wed 26/02/25	6d	Mon 26/03/09	Fri 26/02/27	6d
203	**Building Exterior North**	**39 days**	**35 days**	**4d**	**Mon 26/01/19**	**Mon 26/02/02**	**-10d**	**Fri 26/03/13**	**Mon 26/03/23**	**-6d**
204	Install Storefront At Main Openings	5 days	5 days	0d	Mon 26/01/19	Mon 26/02/02	-10d	Fri 26/01/23	Fri 26/02/06	-10d
205	Install Storefront Spandral at EFIS	3 days			Mon 26/01/26			Wed 26/01/28		
206	Install Scaffolding at Building Perimeter	2 days	2 days	0d	Mon 26/02/02	Mon 26/02/02	0d	Tue 26/02/03	Tue 26/02/03	0d
207	Exterior Sheathing	5 days	5 days	0d	Wed 26/02/04	Wed 26/02/04	0d	Tue 26/02/10	Tue 26/02/10	0d
208	EIFS	10 days	10 days	0d	Wed 26/02/11	Wed 26/02/11	0d	Wed 26/02/25	Wed 26/02/25	0d
209	Remove Scaffolding	2 days	2 days	0d	Thu 26/02/26	Thu 26/02/26	0d	Fri 26/02/27	Fri 26/02/27	0d
210	Install Storefront Spandral at EFIS		3 days			Mon 26/03/02			Wed 26/03/04	
211	Install Metal Panel Systems @ Tower Framing	5 days	5 days	0d	Mon 26/03/02	Mon 26/03/02	0d	Fri 26/03/06	Fri 26/03/06	0d
212	Exterior Breakmetal, flashings, Sealants, & Painting	3 days	3 days	0d	Mon 26/03/02	Mon 26/03/02	0d	Wed 26/03/04	Wed 26/03/04	0d
213	Install Steel Canopies	2 days	2 days	0d	Thu 26/03/05	Thu 26/03/05	0d	Fri 26/03/06	Fri 26/03/06	0d
214	Install Glass	2 days	3 days	-1d	Thu 26/03/05	Thu 26/03/12	-5d	Fri 26/03/06	Mon 26/03/16	-6d
215	Landscape	5 days	5 days	0d	Mon 26/03/09	Tue 26/03/17	-6d	Fri 26/03/13	Mon 26/03/23	-6d
216	**Building Exterior East**	**60 days**	**38 days**	**22d**	**Mon 26/01/12**	**Wed 26/03/18**	**-47d**	**Mon 26/04/06**	**Fri 26/05/08**	**-24d**
217	Install Storefront Spandral at EFIS	3 days			Mon 26/01/12			Wed 26/01/14		
218	Exterior Sheathing	5 days			Thu 26/01/15			Wed 26/01/21		
219	Install Scaffolding at Building Perimeter	3 days	3 days	0d	Tue 26/02/24	Wed 26/03/18	-16d	Thu 26/02/26	Fri 26/03/20	-16d
220	Exterior Sheathing		5 days			Mon 26/03/23			Fri 26/03/27	
221	EIFS	10 days	10 days	0d	Fri 26/02/27	Mon 26/03/30	-21d	Thu 26/03/12	Fri 26/04/10	-21d
222	Remove Scaffolding	3 days	3 days	0d	Fri 26/03/13	Mon 26/04/13	-21d	Tue 26/03/17	Wed 26/04/15	-21d
223	Final Grade	2 days			Wed 26/03/18			Thu 26/03/19		
224	Install Storefront Glass	3 days	3 days	0d	Fri 26/03/20	Thu 26/04/16	-19d	Tue 26/03/24	Mon 26/04/20	-19d
225	Install Metal Panel Systems @ Tower Framing	5 days	5 days	0d	Fri 26/03/20	Thu 26/04/16	-19d	Thu 26/03/26	Wed 26/04/22	-19d
226	Exterior Breakmetal, flashings, Sealants, & Painting	6 days	6 days	0d	Mon 26/03/23	Fri 26/04/17	-19d	Mon 26/03/30	Fri 26/04/24	-19d
227	Install Glass		4 days			Tue 26/04/28			Fri 26/05/01	
228	Landscape	5 days	5 days	0d	Tue 26/03/31	Mon 26/05/04	-24d	Mon 26/04/06	Fri 26/05/08	-24d
229	**Final Inspections**	**27 days**	**44 days**	**-17d**	**Tue 26/03/03**	**Thu 26/03/12**	**-7d**	**Wed 26/04/08**	**Tue 26/05/12**	**-24d**
230	Electrical	1 day	1 day	0d	Tue 26/03/10	Thu 26/03/12	-2d	Tue 26/03/10	Thu 26/03/12	-2d
231	Mechanical	1 day	1 day	0d	Wed 26/03/11	Fri 26/03/13	-2d	Wed 26/03/11	Fri 26/03/13	-2d
232	Plumbing	1 day	1 day	0d	Thu 26/03/12	Mon 26/03/16	-2d	Thu 26/03/12	Mon 26/03/16	-2d
233	Public Works	1 day	1 day	0d	Mon 26/03/23	Fri 26/03/20	1d	Mon 26/03/23	Fri 26/03/20	1d
234	Elevator inspection scheduling and approval	10 days	10 days	0d	Tue 26/03/03	Thu 26/03/12	-7d	Mon 26/03/16	Wed 26/03/25	-7d
235	Fire Life & Safety	2 days	2 days	0d	Tue 26/03/17	Thu 26/03/26	-7d	Wed 26/03/18	Fri 26/03/27	-7d
236	TCO (If City Will Allow it)	1 day	1 day	0d	Tue 26/03/24	Mon 26/03/30	-4d	Tue 26/03/24	Mon 26/03/30	-4d
237	Grading	1 day	1 day	0d	Tue 26/04/07	Mon 26/05/11	-24d	Tue 26/04/07	Mon 26/05/11	-24d
238	Planning & Zoning	1 day	1 day	0d	Tue 26/04/07	Mon 26/05/11	-24d	Tue 26/04/07	Mon 26/05/11	-24d
239	Building Final	1 day	1 day	0d	Wed 26/04/08	Tue 26/05/12	-24d	Wed 26/04/08	Tue 26/05/12	-24d
240	CofO	0 days	0 days	0d	Wed 26/04/08	Tue 26/05/12	-24d	Wed 26/04/08	Tue 26/05/12	-24d
241	Open Date	0 days	0 days	0d	Wed 26/04/08	Tue 26/05/12	-24d	Wed 26/04/08	Tue 26/05/12	-24d
