Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
TN23676 - Mt. Juliet - Golden Bear (land) - TBA-2026.03.02 UP06		466	0%	12-Dec-25A	15-Nov-27	0	17-Dec-25	04-Nov-27	-7
Project Summary		211	0%	16-Feb-26	07-Dec-26	245	09-Feb-26	16-Dec-26	7
Contract Milestones		16	0%	13-Nov-26	07-Dec-26	245	18-Nov-26	16-Dec-26	7
PS-CMIL-1010	Project Substantial Completion	0	0%		13-Nov-26	0		18-Nov-26	3
PS-CMIL-1160	Remaining Weather Allowance (Originally 20 Days)	11	0%	16-Nov-26	02-Dec-26	0	20-Nov-26	16-Dec-26	10
PS-CMIL-1170	Project Substantial Completion with Weather Projection	0	0%		02-Dec-26	0		16-Dec-26	10
PS-CMIL-1190	Public Storage Final Acceptance	0	0%		02-Dec-26	35			
PS-CMIL-1150	Contractual Substantial Completion Date	0	0%		07-Dec-26	237		19-Nov-26	-10
Construction Milestones		176	0%	16-Feb-26	22-Oct-26	15	09-Feb-26	14-Oct-26	-6
PS-CMIL-1090	Start of Elevated Structure	0	0%	16-Feb-26		191	09-Feb-26		-5
PS-CMIL-1100	Stair & Elevator Cores Complete to Roof	0	0%		27-Feb-26	181		24-Feb-26	-3
PS-CMIL-1120	Structure Complete	0	0%		03-Jun-26	114		27-May-26	-5
PS-CMIL-1130	Building Dry In	0	0%		13-Jul-26	87		02-Jul-26	-6
PS-CMIL-1110	Exterior Work Complete	0	0%		05-Oct-26	28		28-Sep-26	-5
PS-CMIL-1140	Landscape & Hardscape Complete	0	0%		22-Oct-26	15		14-Oct-26	-6
Pre-Construction		100	0%	12-Dec-25A	19-Jun-26	98	09-Jan-26	15-Jan-26	-111
Procurement		100	0%	12-Dec-25A	19-Jun-26	98	09-Jan-26	15-Jan-26	-111
PS-PROC-1070	Submit and Approve HVAC	10	0%	26-Jan-26A	13-Feb-26	73			
PS-PROC-1080	Submit and Approve Plumbing Fixtures	10	0%	12-Dec-25A	13-Feb-26	161			
PS-PROC-1140	Submit and Approve Glazing	10	0%	02-Feb-26A	13-Feb-26	84			
PS-PROC-1250	Procure CFMF	12	0%	16-Jan-26A	17-Feb-26	11			
PS-PROC-1110	Submit and Approve Drywall / Ceilings	15	0%	02-Feb-26A	20-Feb-26	151			
PS-PROC-1180	Submit and Approve Fireproofing	17	0%	16-Jan-26A	24-Feb-26	122			
PS-PROC-1300	Submit and Approve Brick Veneer	20	0%	12-Jan-26A	27-Feb-26	37			
PS-PROC-1150	Submit and Approve D/F/HW	15	0%	10-Feb-26	02-Mar-26	82			
PS-PROC-1130	Submit and Approve Roofing	15	0%	11-Feb-26	03-Mar-26	82			
PS-PROC-1120	Submit and Approve Floor Finishes	15	0%	17-Feb-26	09-Mar-26	141			
PS-PROC-1340	Procure Fireproofing / Intumescent	15	0%	25-Feb-26	17-Mar-26	122			
PS-PROC-1350	Procure Plumbing Fixtures	25	0%	16-Feb-26	20-Mar-26	161			
PS-PROC-1160	Submit and Approve Toilet Accessories	15	0%	03-Mar-26	23-Mar-26	142			
PS-PROC-1170	Submit and Approve Specialties	15	0%	03-Mar-26	23-Mar-26	142			
PS-PROC-1260	Procure Roofing	15	0%	04-Mar-26	24-Mar-26	82			
PS-PROC-1360	Procure Ceilings	25	0%	23-Feb-26	27-Mar-26	151			
PS-PROC-1190	Submit and Approve Appliances	15	0%	17-Mar-26	06-Apr-26	131			
PS-PROC-1220	Procure Light Fixtures	50	0%	30-Jan-26A	10-Apr-26	139			
PS-PROC-1270	Procure Storefront / Glazing	40	0%	16-Feb-26	10-Apr-26	84			
PS-PROC-1280	Procure D/F/HW	30	0%	03-Mar-26	13-Apr-26	82			
PS-PROC-1290	Procure Finishes	25	0%	10-Mar-26	13-Apr-26	141			
PS-PROC-1310	Procure Toilet Accessories	20	0%	24-Mar-26	20-Apr-26	142			
PS-PROC-1320	Procure Specialties	20	0%	24-Mar-26	20-Apr-26	142			
PS-PROC-1020	Procure Electric Room MDP	40	100%	03-Mar-26	27-Apr-26	105	09-Jan-26	15-Jan-26	-71
PS-PROC-1230	Procure HVAC Equipment and Fab Ductwork	55	0%	16-Feb-26	01-May-26	73			
PS-PROC-1330	Procure Appliances	20	0%	07-Apr-26	04-May-26	131			
PS-PROC-1370	Procure Brick Veneer	80	0%	02-Mar-26	19-Jun-26	37			
Construction		211	0%	17-Dec-25A	23-Nov-26	255	17-Dec-25	18-Nov-26	-3
Sitework & Utilities		35	0%	02-Feb-26	20-Mar-26	92	14-Jan-26	26-Feb-26	-16
Sitework		22	0%	19-Feb-26	20-Mar-26	92	03-Feb-26	26-Feb-26	-16
SU-STWK-1050	Install Site Stone Base	6	0%	19-Feb-26	26-Feb-26	92	03-Feb-26	05-Feb-26	-15
SU-STWK-1060	Install Prime Coat, Binder, & Tack Coat	3	0%	27-Feb-26	03-Mar-26	92	06-Feb-26	09-Feb-26	-16
SU-STWK-1070	Install Asphalt (Wearing Course)	1	0%	04-Mar-26	04-Mar-26	92	10-Feb-26	10-Feb-26	-16
SU-STWK-1080	Form & Reinforce Curb & Gutter	5	0%	05-Mar-26	11-Mar-26	92	11-Feb-26	17-Feb-26	-16
SU-STWK-1090	Pour Curb & Gutter	2	0%	12-Mar-26	13-Mar-26	92	18-Feb-26	19-Feb-26	-16
SU-STWK-1100	Rough Grade Site	5	0%	16-Mar-26	20-Mar-26	92	20-Feb-26	26-Feb-26	-16
Site Utilities		13	0%	02-Feb-26	18-Feb-26	92	14-Jan-26	02-Feb-26	-12
SU-SUTL-1050	Install U.G. Fire Water & Domestic	10	100%	02-Feb-26	13-Feb-26	92	14-Jan-26	28-Jan-26	-12
SU-SUTL-1010	Install Irrigation Sleeves	3	66.67%	16-Feb-26	18-Feb-26	92	29-Jan-26	02-Feb-26	-12
Foundation & Structural		87	0%	17-Dec-25A	03-Jun-26	68	17-Dec-25	27-May-26	-5
Level 1		35	0%	17-Dec-25A	20-Mar-26	120	17-Dec-25	25-Feb-26	-17
FS-LVL1-1010	Underground MEPF Install (Pre-Pour)	3	100%	06-Jan-26A	04-Feb-26	0	06-Jan-26	06-Jan-26	-20
FS-LVL1-1030	Slab Prep & Pour (Pour A1)	8	60%	02-Feb-26	11-Feb-26	0	28-Jan-26	03-Feb-26	-6
FS-LVL1-1040	Slab Prep & Pour (Pour A2)	3	0%	12-Feb-26	16-Feb-26	0	04-Feb-26	06-Feb-26	-6
FS-LVL1-1000	Footings & Foundation CIP Walls (includes elevator pit)	12	100%	17-Dec-25A	17-Feb-26	0	17-Dec-25	27-Jan-26	-15
FS-LVL1-1050	Steel Erection (Columns & Beams)	10	0%	16-Feb-26	27-Feb-26	0	09-Feb-26	20-Feb-26	-5
FS-LVL1-1020	Erect Stairs & Elevator Shafts (CMU Cores)	15	0%	09-Feb-26	27-Feb-26	91	04-Feb-26	24-Feb-26	-3
FS-LVL1-1060	Fireproofing	3	0%	18-Mar-26	20-Mar-26	120	23-Feb-26	25-Feb-26	-17
Level 2		25	0%	24-Feb-26	30-Mar-26	0	17-Feb-26	23-Mar-26	-5
FS-LVL2-1000	Install Metal Decking	4	0%	24-Feb-26	27-Feb-26	0	17-Feb-26	20-Feb-26	-5
FS-LVL2-1010	MEPF Rough-In (Pre-Pour)	5	0%	26-Feb-26	04-Mar-26	0	19-Feb-26	25-Feb-26	-5
FS-LVL2-1020	FRP Metal Deck Slab (Pour A1)	5	0%	05-Mar-26	11-Mar-26	0	26-Feb-26	04-Mar-26	-5
FS-LVL2-1030	FRP Metal Deck Slab (Pour A2)	3	0%	12-Mar-26	16-Mar-26	0	05-Mar-26	09-Mar-26	-5

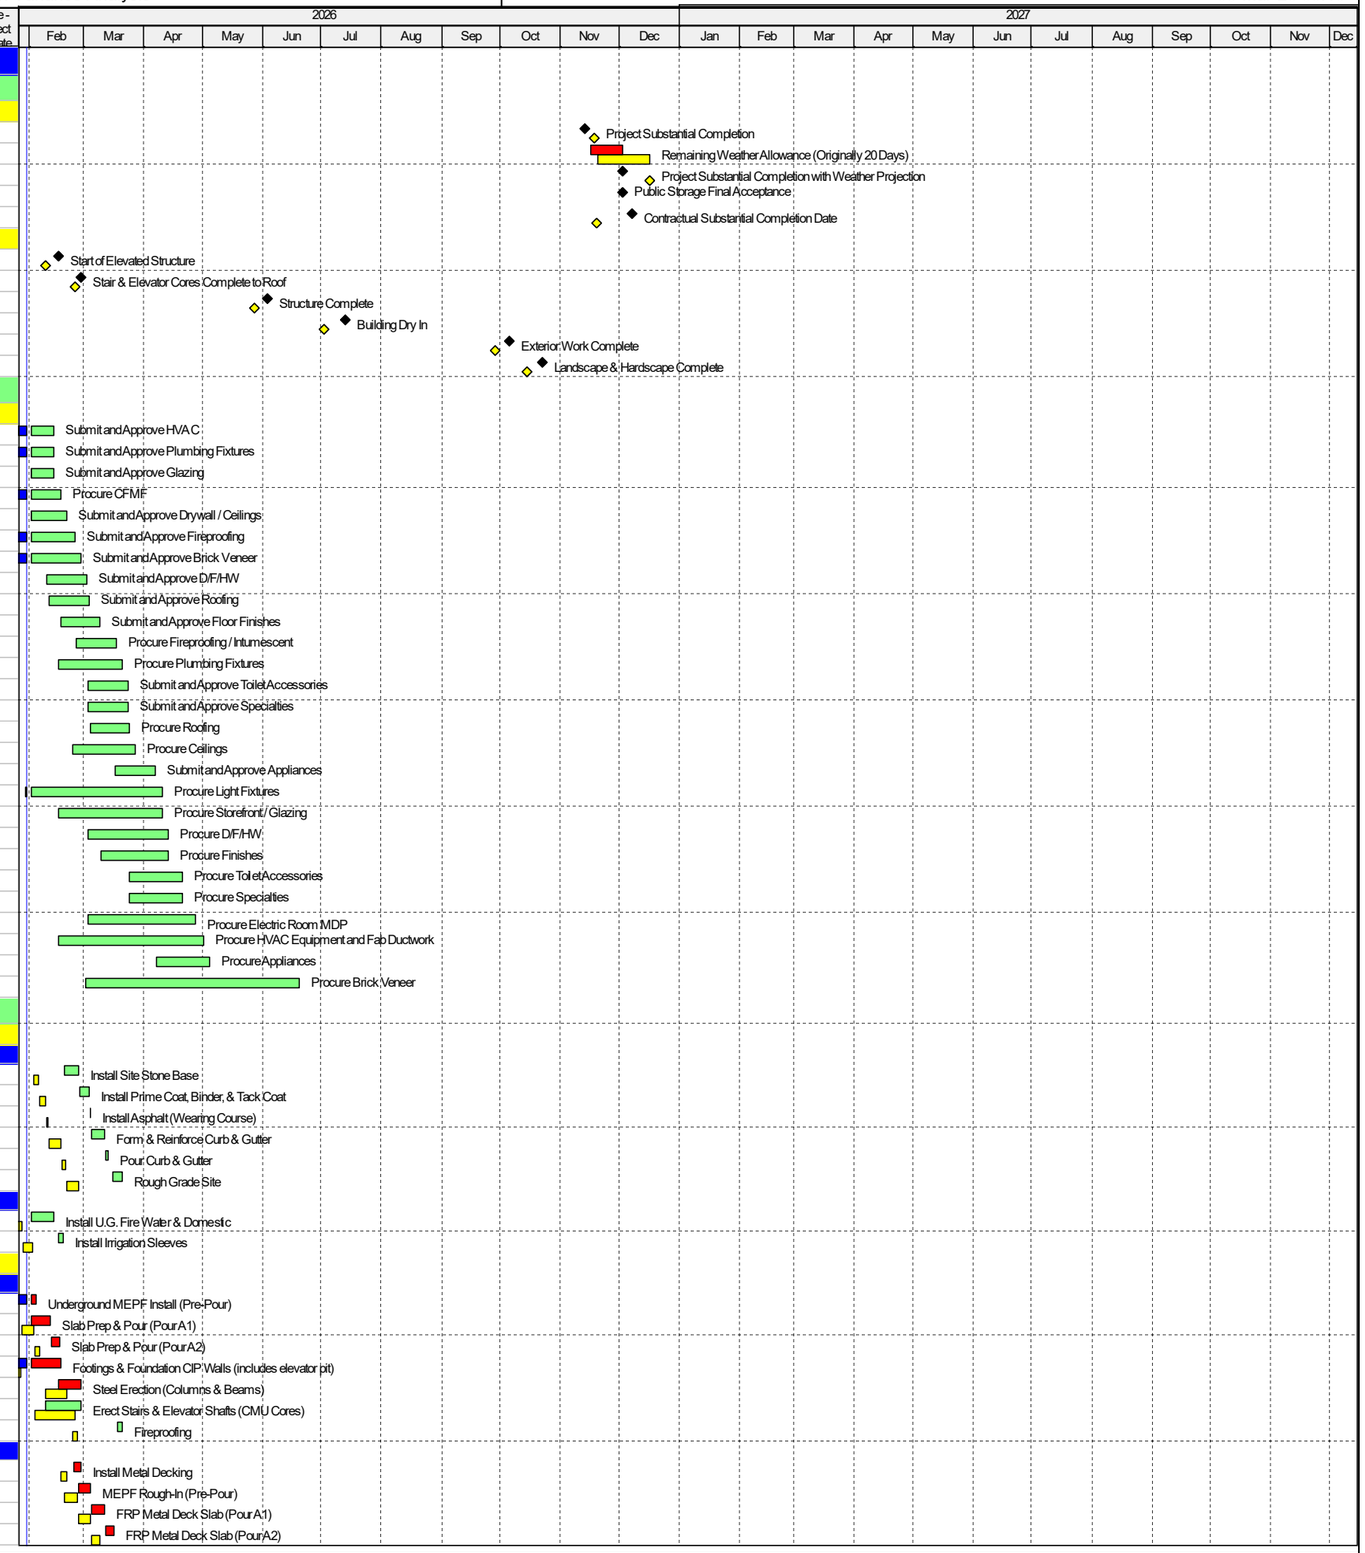

Project Baseline Bar | Remaining Work | ◇ Baseline Milestone
Actual Work | Critical Remaining Work | ◆ Milestone

TASK filter: Remaining .

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
FS-LVL2-1040	Layout & Erect Load Bearing Framing	10	0%	17-Mar-26	30-Mar-26	0	10-Mar-26	23-Mar-26	-5
Level 3		25	0%	25-Mar-26	28-Apr-26	0	18-Mar-26	21-Apr-26	-5
FS-LVL3-1000	Install Metal Decking	4	0%	25-Mar-26	30-Mar-26	0	18-Mar-26	23-Mar-26	-5
FS-LVL3-1010	MEPF Rough-In (Pre-Pour)	5	0%	27-Mar-26	02-Apr-26	0	20-Mar-26	26-Mar-26	-5
FS-LVL3-1020	FRP Metal Deck Slab (Pour A1)	5	0%	03-Apr-26	09-Apr-26	0	27-Mar-26	02-Apr-26	-5
FS-LVL3-1030	FRP Metal Deck Slab (Pour A2)	3	0%	10-Apr-26	14-Apr-26	0	03-Apr-26	07-Apr-26	-5
FS-LVL3-1040	Layout & Erect Load Bearing Framing	10	0%	15-Apr-26	28-Apr-26	0	08-Apr-26	21-Apr-26	-5
Level 4		25	0%	23-Apr-26	28-May-26	0	16-Apr-26	20-May-26	-5
FS-LVL4-1000	Install Metal Decking	4	0%	23-Apr-26	28-Apr-26	0	16-Apr-26	21-Apr-26	-5
FS-LVL4-1010	MEPF Rough-In (Pre-Pour)	5	0%	27-Apr-26	01-May-26	0	20-Apr-26	24-Apr-26	-5
FS-LVL4-1020	FRP Metal Deck Slab (Pour A1)	5	0%	04-May-26	08-May-26	0	27-Apr-26	01-May-26	-5
FS-LVL4-1030	FRP Metal Deck Slab (Pour A2)	3	0%	11-May-26	13-May-26	0	04-May-26	06-May-26	-5
FS-LVL4-1040	Layout & Erect Load Bearing Framing	10	0%	14-May-26	28-May-26	0	07-May-26	20-May-26	-5
Roof		8	0%	22-May-26	03-Jun-26	0	15-May-26	27-May-26	-5
FS-ROOF-1000	Install Metal Decking	4	0%	22-May-26	28-May-26	0	15-May-26	20-May-26	-5
FS-ROOF-1010	MEPF Rough-In (Stubups)	3	0%	27-May-26	29-May-26	0	19-May-26	21-May-26	-5
FS-ROOF-1020	Layout & Frame Parapets	3	0%	01-Jun-26	03-Jun-26	0	22-May-26	27-May-26	-5
Envelope & Exterior		108	0%	14-May-26	15-Oct-26	62	07-May-26	08-Oct-26	-5
North Elevation		77	0%	14-May-26	01-Sep-26	93	07-May-26	25-Aug-26	-5
EE-NRTH-1000	Layout & Exterior Framing (Level 1)	5	0%	14-May-26	20-May-26	8	07-May-26	13-May-26	-5
EE-NRTH-1010	City Inspection (Rough Framing)	1	0%	21-May-26	21-May-26	8	14-May-26	14-May-26	-5
EE-NRTH-1020	Electrical Rough-In	5	0%	04-Jun-26	10-Jun-26	0	28-May-26	03-Jun-26	-5
EE-NRTH-1030	City Inspection (Electrical)	1	0%	11-Jun-26	11-Jun-26	23	04-Jun-26	04-Jun-26	-5
EE-NRTH-1040	Install Exterior Sheathing	5	0%	12-Jun-26	18-Jun-26	23	05-Jun-26	11-Jun-26	-5
EE-NRTH-1050	City Inspection (Screw Inspection)	1	0%	19-Jun-26	19-Jun-26	23	12-Jun-26	12-Jun-26	-5
EE-NRTH-1060	Weather Barrier & Flashing	5	0%	22-Jun-26	26-Jun-26	23	15-Jun-26	19-Jun-26	-5
EE-NRTH-1070	Install Rigid Insulation	5	0%	29-Jun-26	06-Jul-26	23	22-Jun-26	26-Jun-26	-5
EE-NRTH-1080	Storefront, Windows & Metals	3	0%	07-Jul-26	09-Jul-26	23	29-Jun-26	01-Jul-26	-5
EE-NRTH-1090	Install Brick Veneer	15	0%	10-Jul-26	30-Jul-26	23	02-Jul-26	23-Jul-26	-5
EE-NRTH-1100	Install Canopies & Trim	3	0%	31-Jul-26	04-Aug-26	56	24-Jul-26	28-Jul-26	-5
EE-NRTH-1110	Install Lighting Fixtures	3	0%	05-Aug-26	07-Aug-26	56	29-Jul-26	31-Jul-26	-5
EE-NRTH-1120	Install Signage	1	0%	10-Aug-26	10-Aug-26	56	03-Aug-26	03-Aug-26	-5
EE-NRTH-1130	Install Doors & Hardware	2	0%	11-Aug-26	12-Aug-26	56	04-Aug-26	05-Aug-26	-5
EE-NRTH-1140	Install Downspouts	1	0%	13-Aug-26	13-Aug-26	56	06-Aug-26	06-Aug-26	-5
EE-NRTH-1150	Final Paint	3	0%	14-Aug-26	18-Aug-26	56	07-Aug-26	11-Aug-26	-5
EE-NRTH-1160	Punch List & Corrections	5	0%	19-Aug-26	25-Aug-26	56	12-Aug-26	18-Aug-26	-5
EE-NRTH-1170	Final Owner Walk (Punch List & Corrections)	5	0%	26-Aug-26	01-Sep-26	93	19-Aug-26	25-Aug-26	-5
East Elevation		75	0%	21-May-26	04-Sep-26	90	14-May-26	28-Aug-26	-5
EE-EAST-1000	Layout & Exterior Framing (Level 1)	5	0%	21-May-26	28-May-26	8	14-May-26	20-May-26	-5
EE-EAST-1010	City Inspection (Rough Framing)	1	0%	29-May-26	29-May-26	8	21-May-26	21-May-26	-5
EE-EAST-1020	Electrical Rough-In	5	0%	11-Jun-26	17-Jun-26	0	04-Jun-26	10-Jun-26	-5
EE-EAST-1030	City Inspection (Electrical)	1	0%	18-Jun-26	18-Jun-26	33	11-Jun-26	11-Jun-26	-5
EE-EAST-1040	Install Exterior Sheathing	5	0%	19-Jun-26	25-Jun-26	33	12-Jun-26	18-Jun-26	-5
EE-EAST-1050	City Inspection (Screw Inspection)	1	0%	26-Jun-26	26-Jun-26	33	19-Jun-26	19-Jun-26	-5
EE-EAST-1060	Weather Barrier & Flashing	5	0%	29-Jun-26	06-Jul-26	33	22-Jun-26	26-Jun-26	-5
EE-EAST-1070	Install Rigid Insulation	5	0%	07-Jul-26	13-Jul-26	33	29-Jun-26	06-Jul-26	-5
EE-EAST-1080	Install Windows & Metals	3	0%	14-Jul-26	16-Jul-26	33	07-Jul-26	09-Jul-26	-5
EE-EAST-1090	Install Brick Veneer	15	0%	31-Jul-26	20-Aug-26	23	24-Jul-26	13-Aug-26	-5
EE-EAST-1100	Install Signage	1	0%	21-Aug-26	21-Aug-26	53	14-Aug-26	14-Aug-26	-5
EE-EAST-1110	Punch List & Corrections	5	0%	24-Aug-26	28-Aug-26	53	17-Aug-26	21-Aug-26	-5
EE-EAST-1120	Final Owner Walk (Punch List & Corrections)	5	0%	31-Aug-26	04-Sep-26	90	24-Aug-26	28-Aug-26	-5
South Elevation		90	0%	29-May-26	05-Oct-26	70	21-May-26	28-Sep-26	-5
EE-SOTH-1000	Layout & Exterior Framing (Level 1)	5	0%	29-May-26	04-Jun-26	8	21-May-26	28-May-26	-5
EE-SOTH-1010	City Inspection (Rough Framing)	1	0%	05-Jun-26	05-Jun-26	8	29-May-26	29-May-26	-5
EE-SOTH-1020	Electrical Rough-In	5	0%	18-Jun-26	24-Jun-26	0	11-Jun-26	17-Jun-26	-5
EE-SOTH-1030	City Inspection (Electrical)	1	0%	25-Jun-26	25-Jun-26	46	18-Jun-26	18-Jun-26	-5
EE-SOTH-1040	Install Exterior Sheathing	5	0%	26-Jun-26	02-Jul-26	46	19-Jun-26	25-Jun-26	-5
EE-SOTH-1050	City Inspection (Screw Inspection)	1	0%	06-Jul-26	06-Jul-26	46	26-Jun-26	26-Jun-26	-5
EE-SOTH-1060	Weather Barrier & Flashing	5	0%	07-Jul-26	13-Jul-26	46	29-Jun-26	06-Jul-26	-5
EE-SOTH-1070	Install Rigid Insulation	5	0%	14-Jul-26	20-Jul-26	46	07-Jul-26	13-Jul-26	-5
EE-SOTH-1080	Install Brick Veneer	15	0%	21-Aug-26	11-Sep-26	23	14-Aug-26	03-Sep-26	-5
EE-SOTH-1090	Install Signage	1	0%	14-Sep-26	14-Sep-26	33	04-Sep-26	04-Sep-26	-5
EE-SOTH-1100	Install Doors & Hardware	1	0%	15-Sep-26	15-Sep-26	33	08-Sep-26	08-Sep-26	-5
EE-SOTH-1110	Install Downspouts	2	0%	16-Sep-26	17-Sep-26	33	09-Sep-26	10-Sep-26	-5
EE-SOTH-1120	Final Paint	2	0%	18-Sep-26	21-Sep-26	33	11-Sep-26	14-Sep-26	-5
EE-SOTH-1130	Punch List & Corrections	5	0%	22-Sep-26	28-Sep-26	33	15-Sep-26	21-Sep-26	-5
EE-SOTH-1140	Final Owner Walk (Punch List & Corrections)	5	0%	29-Sep-26	05-Oct-26	70	22-Sep-26	28-Sep-26	-5
West Elevation		93	0%	05-Jun-26	15-Oct-26	62	29-May-26	08-Oct-26	-5
EE-WEST-1000	Layout & Exterior Framing (Level 1)	5	0%	05-Jun-26	11-Jun-26	8	29-May-26	04-Jun-26	-5
EE-WEST-1010	City Inspection (Rough Framing)	1	0%	12-Jun-26	12-Jun-26	8	05-Jun-26	05-Jun-26	-5
EE-WEST-1020	Electrical Rough-In	5	0%	25-Jun-26	01-Jul-26	0	18-Jun-26	24-Jun-26	-5

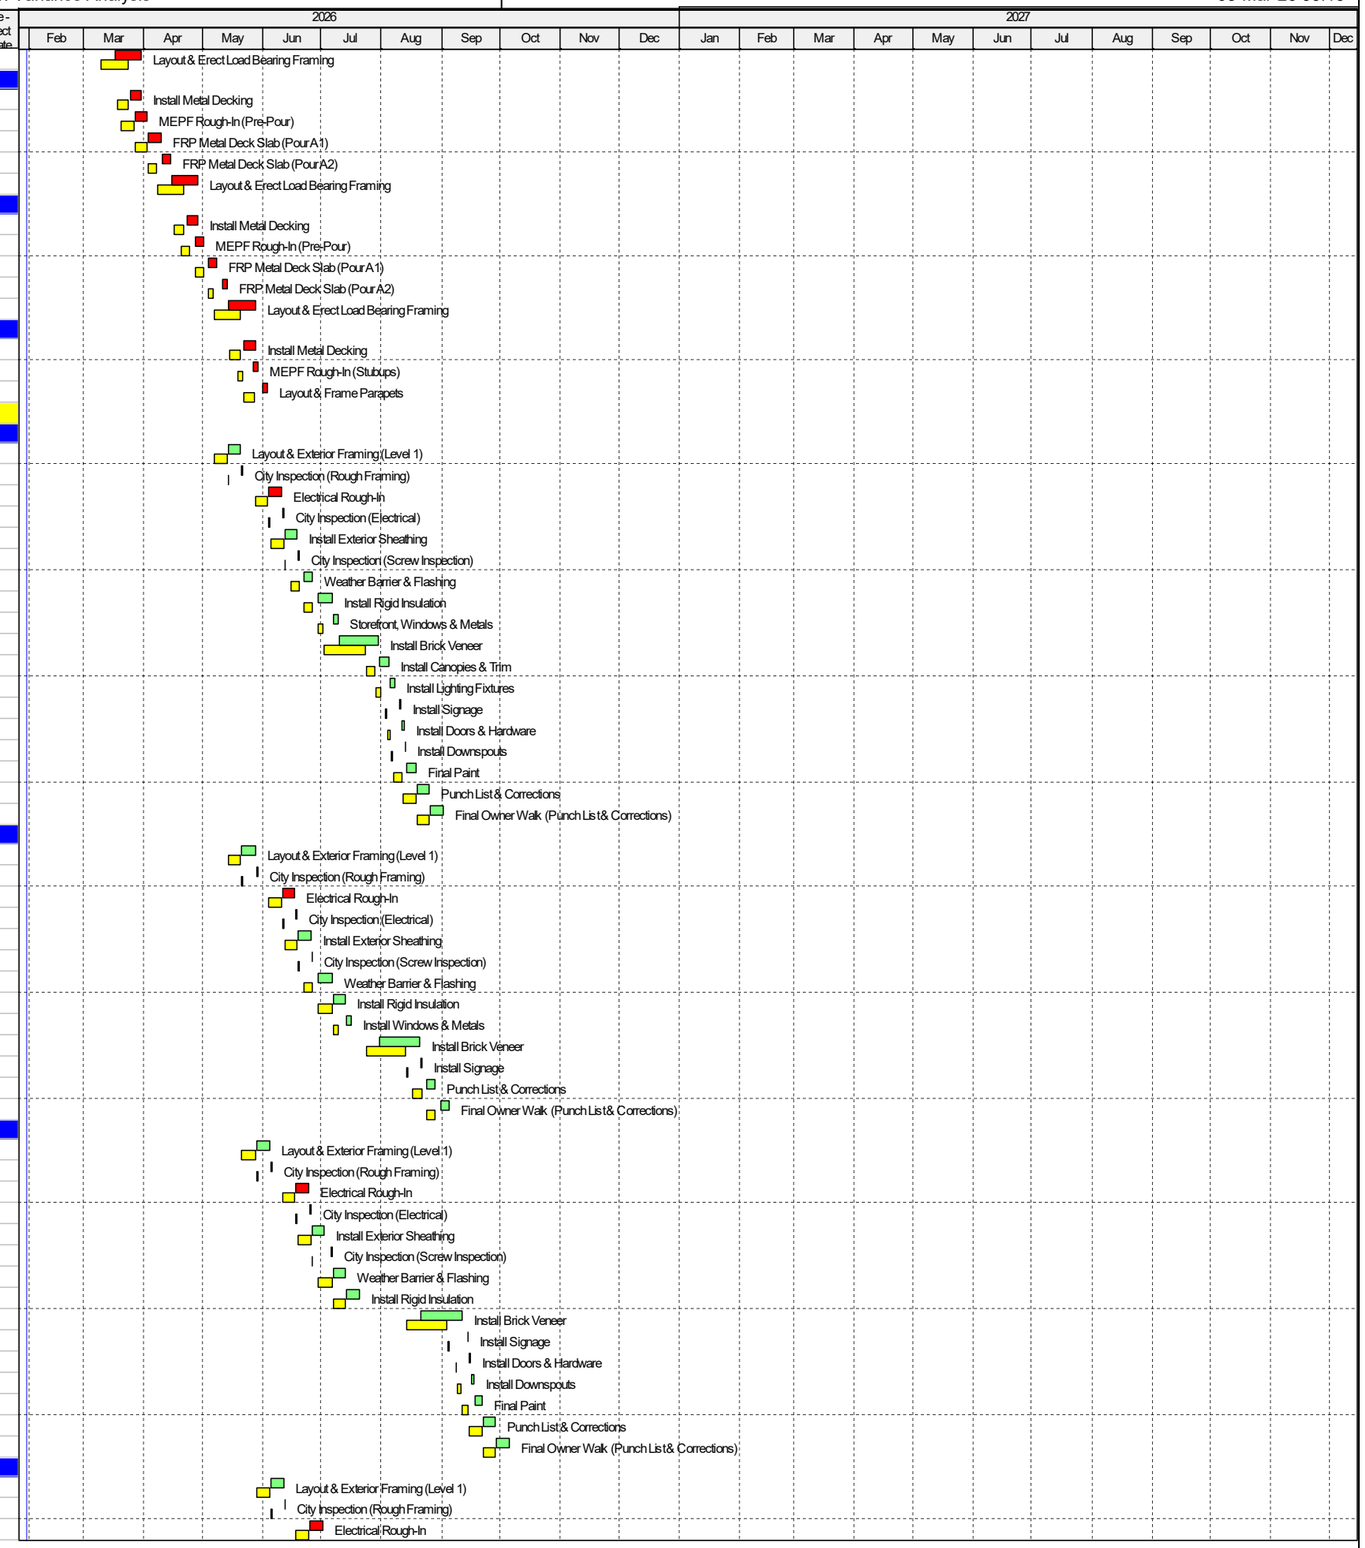

Project Baseline Bar | Remaining Work | ◇ Baseline Milestone
Actual Work | Critical Remaining Work | ◆ Milestone

TASK filter: Remaining .

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
EE-WEST-1030	City Inspection (Electrical)	1	0%	02-Jul-26	02-Jul-26	0	25-Jun-26	25-Jun-26	-5
EE-WEST-1040	Install Exterior Sheathing	5	0%	06-Jul-26	10-Jul-26	0	26-Jun-26	02-Jul-26	-5
EE-WEST-1050	City Inspection (Screw Inspection)	1	0%	13-Jul-26	13-Jul-26	0	06-Jul-26	06-Jul-26	-5
EE-WEST-1060	Weather Barrier & Flashing	5	0%	14-Jul-26	20-Jul-26	0	07-Jul-26	13-Jul-26	-5
EE-WEST-1070	Install Rigid Insulation	5	0%	21-Jul-26	27-Jul-26	0	14-Jul-26	20-Jul-26	-5
EE-WEST-1080	Install Windows & Metals	3	0%	28-Jul-26	30-Jul-26	0	21-Jul-26	23-Jul-26	-5
EE-WEST-1090	Install Brick Veneer	15	0%	14-Sep-26	02-Oct-26	23	04-Sep-26	25-Sep-26	-5
EE-WEST-1100	Install Signage	1	0%	05-Oct-26	05-Oct-26	23	28-Sep-26	28-Sep-26	-5
EE-WEST-1110	Punch List & Corrections	5	0%	06-Oct-26	12-Oct-26	23	29-Sep-26	05-Oct-26	-5
EE-WEST-1120	Final Owner Walk (Punch List & Corrections)	3	0%	13-Oct-26	15-Oct-26	62	06-Oct-26	08-Oct-26	-5
Roof		80	0%	04-Jun-26	25-Sep-26	34	28-May-26	08-Sep-26	-13
EE-ROOF-1000	Clean & Prep Metal Deck	2	0%	04-Jun-26	05-Jun-26	17	28-May-26	29-May-26	-5
EE-ROOF-1010	Stage Materials & Solar Rails (Crane)	2	0%	08-Jun-26	09-Jun-26	17	01-Jun-26	01-Jun-26	-6
EE-ROOF-1020	Layout for Penetrations, Curb Blocking, Edge Metal	2	0%	10-Jun-26	11-Jun-26	17	02-Jun-26	03-Jun-26	-6
EE-ROOF-1030	Install Blocking & Equipment Curbs	3	0%	12-Jun-26	16-Jun-26	17	04-Jun-26	08-Jun-26	-6
EE-ROOF-1040	Install Rigid Insulation	4	0%	17-Jun-26	22-Jun-26	17	09-Jun-26	12-Jun-26	-6
EE-ROOF-1050	Install Cover Board	4	0%	23-Jun-26	26-Jun-26	17	15-Jun-26	18-Jun-26	-6
EE-ROOF-1060	Install TPO Roofing System (incl. boots, termination bars)	10	0%	29-Jun-26	13-Jul-26	17	19-Jun-26	02-Jul-26	-6
EE-ROOF-1070	Install Edge Metal, Coping, Trim	5	0%	14-Jul-26	20-Jul-26	34	06-Jul-26	10-Jul-26	-6
EE-ROOF-1080	Install Roof Drains, Vents, Mechanical Curbs	5	0%	21-Jul-26	27-Jul-26	34	13-Jul-26	17-Jul-26	-6
EE-ROOF-1140	Set Rooftop Units (RTU's & Splits)	1	0%	28-Jul-26	28-Jul-26	55	20-Jul-26	20-Jul-26	-6
EE-ROOF-1150	Install Duct/Condensate/Vent Tie-Ins & Flashing	3	0%	29-Jul-26	31-Jul-26	55	21-Jul-26	23-Jul-26	-6
EE-ROOF-1090	Install Electrical Conduit & Roof Mounted Boxes	5	0%	28-Jul-26	03-Aug-26	34	20-Jul-26	24-Jul-26	-6
EE-ROOF-1160	Startup/Controls/Balancing Prep	3	0%	03-Aug-26	05-Aug-26	55	24-Jul-26	28-Jul-26	-6
EE-ROOF-1100	Install Solar Mounting Rails & Racking	3	0%	04-Aug-26	06-Aug-26	34	27-Jul-26	29-Jul-26	-6
EE-ROOF-1170	Water Test / Leak Test	1	0%	06-Aug-26	06-Aug-26	55	29-Jul-26	29-Jul-26	-6
EE-ROOF-1180	Roof Patches (If Any)	1	0%	07-Aug-26	07-Aug-26	55	30-Jul-26	30-Jul-26	-6
EE-ROOF-1190	Punch List & Corrections	3	0%	10-Aug-26	12-Aug-26	55	31-Jul-26	04-Aug-26	-6
EE-ROOF-1110	Mount Solar Panels	15	0%	07-Aug-26	27-Aug-26	34	30-Jul-26	19-Aug-26	-6
EE-ROOF-1120	Run Electrical Conduit & Inverters to Roof	5	0%	28-Aug-26	03-Sep-26	34	20-Aug-26	26-Aug-26	-6
EE-ROOF-1130	Final Electrical Tie-In (Solar Panels)	5	0%	04-Sep-26	11-Sep-26	34	27-Aug-26	02-Sep-26	-6
EE-ROOF-1200	Final Owner Walk (Punch List & Corrections)	10	0%	14-Sep-26	25-Sep-26	34	03-Sep-26	08-Sep-26	-13
Interior Build-Out		167	0%	02-Mar-26	20-Oct-26	279	25-Feb-26	12-Oct-26	-6
Level 2 Interior		44	0%	14-Jul-26	11-Sep-26	93	06-Jul-26	20-Aug-26	-16
IB-L2IN-1000	Layout & Framing (incl. backing, door frames)	5	0%	14-Jul-26	20-Jul-26	17	06-Jul-26	10-Jul-26	-6
IB-L2IN-1010	Electrical Rough-In	5	0%	21-Jul-26	27-Jul-26	17	13-Jul-26	17-Jul-26	-6
IB-L2IN-1020	Mechanical Rough-In	5	0%	21-Jul-26	27-Jul-26	17	13-Jul-26	17-Jul-26	-6
IB-L2IN-1030	Plumbing Rough-In	5	0%	21-Jul-26	27-Jul-26	17	13-Jul-26	17-Jul-26	-6
IB-L2IN-1040	Fire Supression Rough-In	5	0%	21-Jul-26	27-Jul-26	17	13-Jul-26	17-Jul-26	-6
IB-L2IN-1050	Install Insulation	2	0%	28-Jul-26	29-Jul-26	48	20-Jul-26	21-Jul-26	-6
IB-L2IN-1060	Install Drywall	4	0%	30-Jul-26	04-Aug-26	48	22-Jul-26	27-Jul-26	-6
IB-L2IN-1070	Tape & Mud Drywall	5	0%	05-Aug-26	11-Aug-26	48	28-Jul-26	03-Aug-26	-6
IB-L2IN-1080	Prep & Paint	3	0%	12-Aug-26	14-Aug-26	48	04-Aug-26	06-Aug-26	-6
IB-L2IN-1090	MEPF Trim-Out	5	0%	17-Aug-26	21-Aug-26	48	07-Aug-26	13-Aug-26	-6
IB-L2IN-1100	Install Storage Doors & Hardware	5	0%	24-Aug-26	28-Aug-26	48	14-Aug-26	20-Aug-26	-6
IB-L2IN-1110	Final Clean and Punchlist	5	0%	31-Aug-26	04-Sep-26	49			
IB-L2IN-1120	Punchlist Completion and Signoff	5	0%	07-Sep-26	11-Sep-26	93			
Level 3 Interior		41	0%	21-Jul-26	15-Sep-26	91	13-Jul-26	27-Aug-26	-13
IB-L3IN-1000	Layout & Framing (incl. backing, door frames)	5	0%	21-Jul-26	27-Jul-26	26	13-Jul-26	17-Jul-26	-6
IB-L3IN-1010	Electrical Rough-In	5	0%	28-Jul-26	03-Aug-26	46	20-Jul-26	24-Jul-26	-6
IB-L3IN-1020	Mechanical Rough-In	5	0%	28-Jul-26	03-Aug-26	46	20-Jul-26	24-Jul-26	-6
IB-L3IN-1030	Plumbing Rough-In	5	0%	28-Jul-26	03-Aug-26	46	20-Jul-26	24-Jul-26	-6
IB-L3IN-1040	Fire Supression Rough-In	5	0%	28-Jul-26	03-Aug-26	46	20-Jul-26	24-Jul-26	-6
IB-L3IN-1050	Install Insulation	2	0%	04-Aug-26	05-Aug-26	46	27-Jul-26	28-Jul-26	-6
IB-L3IN-1060	Install Drywall	4	0%	06-Aug-26	11-Aug-26	46	29-Jul-26	03-Aug-26	-6
IB-L3IN-1070	Tape & Mud Drywall	5	0%	12-Aug-26	18-Aug-26	46	04-Aug-26	10-Aug-26	-6
IB-L3IN-1080	Prep & Paint	3	0%	19-Aug-26	21-Aug-26	46	11-Aug-26	13-Aug-26	-6
IB-L3IN-1090	MEPF Trim-Out	5	0%	24-Aug-26	28-Aug-26	46	14-Aug-26	20-Aug-26	-6
IB-L3IN-1100	Install Storage Doors & Hardware	5	0%	31-Aug-26	04-Sep-26	46	21-Aug-26	27-Aug-26	-6
IB-L3IN-1110	Final Clean and Punchlist	2	0%	07-Sep-26	08-Sep-26	47			
IB-L3IN-1120	Punchlist Completion and Signoff	5	0%	09-Sep-26	15-Sep-26	91			
Unisex Restroom		28	0%	28-Jul-26	03-Sep-26	99	20-Jul-26	18-Aug-26	-12
IB-L3UN-1000	Framing (Metal Studs, Blocking)	3	0%	28-Jul-26	30-Jul-26	33	20-Jul-26	22-Jul-26	-6
IB-L3UN-1010	MEPF Rough-In	3	0%	31-Jul-26	04-Aug-26	51	23-Jul-26	27-Jul-26	-6
IB-L3UN-1020	City Inspection (Framing & MEPF Rough)	1	0%	05-Aug-26	05-Aug-26	52	28-Jul-26	28-Jul-26	-6
IB-L3UN-1030	Install Insulation	1	0%	06-Aug-26	06-Aug-26	52	29-Jul-26	29-Jul-26	-6
IB-L3UN-1040	Install Drywall	2	0%	07-Aug-26	10-Aug-26	52	30-Jul-26	31-Jul-26	-6
IB-L3UN-1050	Tape & Mud Drywall	3	0%	11-Aug-26	13-Aug-26	54	03-Aug-26	05-Aug-26	-6
IB-L3UN-1060	Painting	2	0%	14-Aug-26	17-Aug-26	54	06-Aug-26	07-Aug-26	-6
IB-L3UN-1070	Install Restroom Fixtures & Partitions	2	0%	18-Aug-26	19-Aug-26	54	10-Aug-26	11-Aug-26	-6
IB-L3UN-1080	Install Accessories (Grab Bars, Mirrors, Signs)	2	0%	20-Aug-26	21-Aug-26	54	12-Aug-26	13-Aug-26	-6

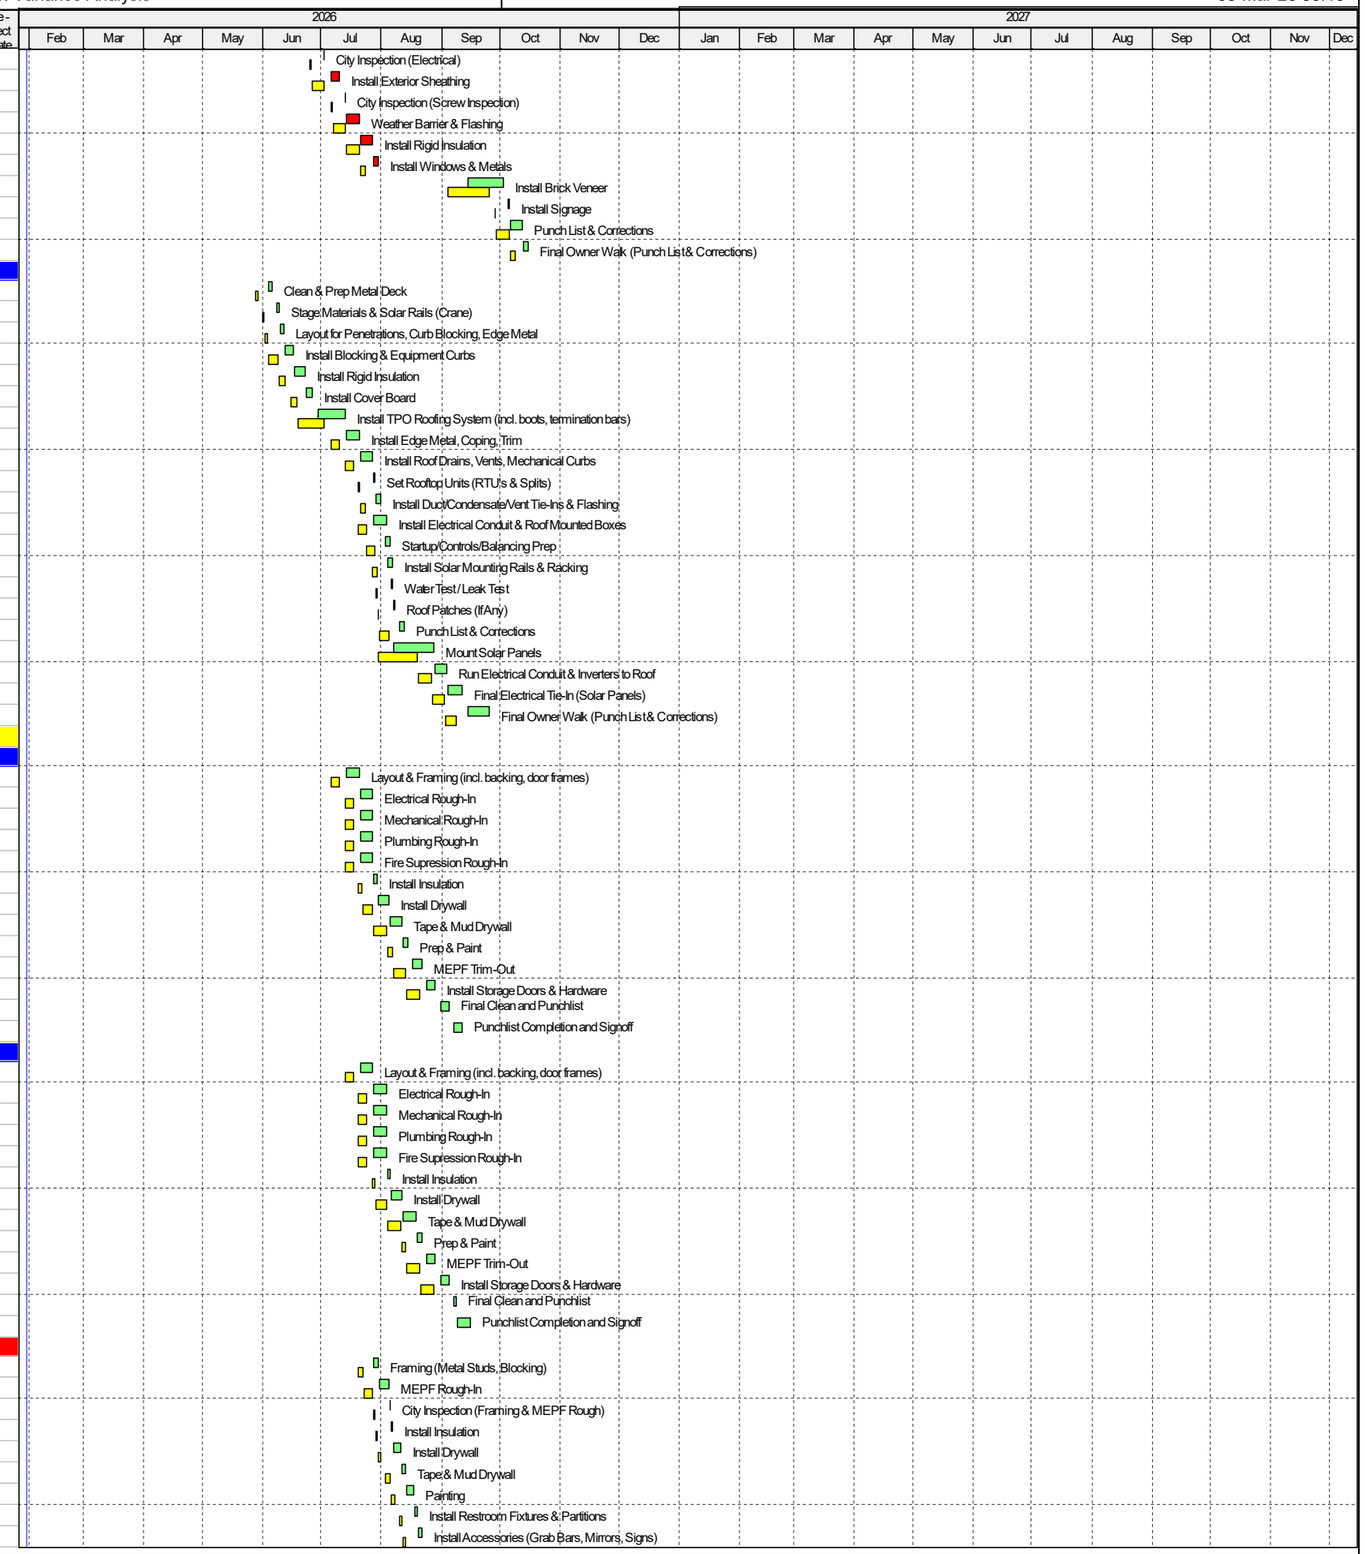

Project Baseline Bar | Remaining Work | ◇ Baseline Milestone
Actual Work | Critical Remaining Work | ◆ Milestone

TASK filter: Remaining .

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
IB-L3UN-1090	Final MEP Trim-Out	2	0%	24-Aug-26	25-Aug-26	54	14-Aug-26	17-Aug-26	-6
IB-L3UN-1100	Final Clean and Punchlist	2	0%	26-Aug-26	27-Aug-26	54	18-Aug-26	18-Aug-26	-7
IB-L3UN-1110	Punchlist Completion and Signoff	5	0%	28-Aug-26	03-Sep-26	99			
Level 4 Interior		42	0%	28-Jul-26	23-Sep-26	85	20-Jul-26	03-Sep-26	-14
IB-L4IN-1000	Layout & Framing (incl. backing, door frames)	5	0%	28-Jul-26	03-Aug-26	26	20-Jul-26	24-Jul-26	-6
IB-L4IN-1010	Electrical Rough-In	5	0%	04-Aug-26	10-Aug-26	33	27-Jul-26	31-Jul-26	-6
IB-L4IN-1020	Mechanical Rough-In	5	0%	04-Aug-26	10-Aug-26	33	27-Jul-26	31-Jul-26	-6
IB-L4IN-1030	Plumbing Rough-In	5	0%	04-Aug-26	10-Aug-26	33	27-Jul-26	31-Jul-26	-6
IB-L4IN-1040	Fire Supression Rough-In	5	0%	04-Aug-26	10-Aug-26	33	27-Jul-26	31-Jul-26	-6
IB-L4IN-1050	Install Insulation	2	0%	11-Aug-26	12-Aug-26	33	03-Aug-26	04-Aug-26	-6
IB-L4IN-1060	Install Drywall	4	0%	13-Aug-26	18-Aug-26	33	05-Aug-26	10-Aug-26	-6
IB-L4IN-1070	Tape & Mud Drywall	5	0%	19-Aug-26	25-Aug-26	33	11-Aug-26	17-Aug-26	-6
IB-L4IN-1080	Prep & Paint	3	0%	26-Aug-26	28-Aug-26	33	18-Aug-26	20-Aug-26	-6
IB-L4IN-1090	MEPF Trim-Out	5	0%	31-Aug-26	04-Sep-26	33	21-Aug-26	27-Aug-26	-6
IB-L4IN-1100	Install Storage Doors & Hardware	5	0%	08-Sep-26	14-Sep-26	41	28-Aug-26	03-Sep-26	-6
IB-L4IN-1110	Final Clean and Punchlist	2	0%	15-Sep-26	16-Sep-26	41			
IB-L4IN-1120	Punchlist Completion and Signoff	5	0%	17-Sep-26	23-Sep-26	85			
Level 1 Interior		44	0%	04-Aug-26	02-Oct-26	291	27-Jul-26	16-Sep-26	-12
IB-L1IN-1000	Layout & Framing (incl. backing, door frames)	5	0%	04-Aug-26	10-Aug-26	26	27-Jul-26	31-Jul-26	-6
IB-L1IN-1010	Electrical Rough-In	5	0%	11-Aug-26	17-Aug-26	36	03-Aug-26	07-Aug-26	-6
IB-L1IN-1020	Mechanical Rough-In	5	0%	11-Aug-26	17-Aug-26	36	03-Aug-26	07-Aug-26	-6
IB-L1IN-1030	Plumbing Rough-In	5	0%	11-Aug-26	17-Aug-26	36	03-Aug-26	07-Aug-26	-6
IB-L1IN-1040	Fire Supression Rough-In	5	0%	11-Aug-26	17-Aug-26	36	03-Aug-26	07-Aug-26	-6
IB-L1IN-1050	Install Insulation	2	0%	18-Aug-26	19-Aug-26	36	10-Aug-26	11-Aug-26	-6
IB-L1IN-1060	Install Drywall	4	0%	20-Aug-26	25-Aug-26	36	12-Aug-26	17-Aug-26	-6
IB-L1IN-1070	Tape & Mud Drywall	5	0%	26-Aug-26	01-Sep-26	36	18-Aug-26	24-Aug-26	-6
IB-L1IN-1080	Prep & Paint	3	0%	02-Sep-26	04-Sep-26	36	25-Aug-26	27-Aug-26	-6
IB-L1IN-1090	MEPF Trim-Out	5	0%	08-Sep-26	14-Sep-26	36	28-Aug-26	03-Sep-26	-6
IB-L1IN-1100	Install Storage Doors & Hardware	5	0%	15-Sep-26	21-Sep-26	36	04-Sep-26	11-Sep-26	-6
IB-L1IN-1110	Final Clean and Punchlist	2	0%	22-Sep-26	23-Sep-26	36			
IB-L1IN-1120	Punchlist Completion and Signoff	5	0%	24-Sep-26	30-Sep-26	80			
Restrooms (Mens & Womens)		29	0%	11-Aug-26	18-Sep-26	301	03-Aug-26	01-Sep-26	-13
IB-L1RR-1000	Framing (Metal Studs, Blocking)	3	0%	11-Aug-26	13-Aug-26	26	03-Aug-26	05-Aug-26	-6
IB-L1RR-1010	MEPF Rough-In	3	0%	14-Aug-26	18-Aug-26	44	06-Aug-26	10-Aug-26	-6
IB-L1RR-1020	City Inspection (Framing & MEPF Rough)	1	0%	19-Aug-26	19-Aug-26	44	11-Aug-26	11-Aug-26	-6
IB-L1RR-1030	Install Insulation	1	0%	20-Aug-26	20-Aug-26	44	12-Aug-26	12-Aug-26	-6
IB-L1RR-1040	Install Drywall	2	0%	21-Aug-26	24-Aug-26	44	13-Aug-26	14-Aug-26	-6
IB-L1RR-1050	Tape & Mud Drywall	3	0%	25-Aug-26	27-Aug-26	44	17-Aug-26	19-Aug-26	-6
IB-L1RR-1060	Painting	2	0%	28-Aug-26	31-Aug-26	44	20-Aug-26	21-Aug-26	-6
IB-L1RR-1070	Install Restroom Fixtures & Partitions	2	0%	01-Sep-26	02-Sep-26	44	24-Aug-26	25-Aug-26	-6
IB-L1RR-1080	Install Accessories (Grab Bars, Mirrors, Signs)	2	0%	03-Sep-26	04-Sep-26	44	26-Aug-26	27-Aug-26	-6
IB-L1RR-1090	Final MEP Trim-Out	2	0%	08-Sep-26	09-Sep-26	44	28-Aug-26	31-Aug-26	-6
IB-L1RR-1100	Final Clean and Punclist	2	0%	10-Sep-26	11-Sep-26	44	01-Sep-26	01-Sep-26	-7
IB-L1RR-1110	Punchlist Completion and Signoff	5	0%	14-Sep-26	18-Sep-26	301			
Management Spaces (Rental Office, Storage, Break Room)		36	0%	14-Aug-26	02-Oct-26	291	06-Aug-26	16-Sep-26	-12
IB-L1M\S-1000	Layout & Framing (incl. backing, door frames)	3	0%	14-Aug-26	18-Aug-26	26	06-Aug-26	10-Aug-26	-6
IB-L1M\S-1010	MEPF Rough-In	3	0%	19-Aug-26	21-Aug-26	32	11-Aug-26	13-Aug-26	-6
IB-L1M\S-1020	City Inspection (Framing & MEPF)	1	0%	24-Aug-26	24-Aug-26	32	14-Aug-26	14-Aug-26	-6
IB-L1M\S-1030	Install Insulation	2	0%	25-Aug-26	26-Aug-26	32	17-Aug-26	18-Aug-26	-6
IB-L1M\S-1040	Install Drywall	2	0%	27-Aug-26	28-Aug-26	32	19-Aug-26	20-Aug-26	-6
IB-L1M\S-1050	Tape & Mud Drywall	3	0%	31-Aug-26	02-Sep-26	32	21-Aug-26	25-Aug-26	-6
IB-L1M\S-1060	Painting	3	0%	03-Sep-26	08-Sep-26	32	26-Aug-26	28-Aug-26	-6
IB-L1M\S-1070	Install Ceiling Grid (Break Room)	1	0%	09-Sep-26	09-Sep-26	34	31-Aug-26	31-Aug-26	-6
IB-L1M\S-1080	Install Base Trim	1	0%	10-Sep-26	10-Sep-26	34	01-Sep-26	01-Sep-26	-6
IB-L1M\S-1090	Install Cabinets & Countertops (Break Room & Office)	3	0%	11-Sep-26	15-Sep-26	34	02-Sep-26	04-Sep-26	-6
IB-L1M\S-1100	Install Sink & Faucests (Break Room)	1	0%	16-Sep-26	16-Sep-26	34	08-Sep-26	08-Sep-26	-6
IB-L1M\S-1110	Appliances (Microwave & Fridge)	1	0%	17-Sep-26	17-Sep-26	34	09-Sep-26	09-Sep-26	-6
IB-L1M\S-1120	Interior Signage	1	0%	18-Sep-26	18-Sep-26	34	10-Sep-26	10-Sep-26	-6
IB-L1M\S-1130	MEPF Trim-Out	3	0%	21-Sep-26	23-Sep-26	34	11-Sep-26	15-Sep-26	-6
IB-L1M\S-1140	Final Clean and Punchlist	2	0%	24-Sep-26	25-Sep-26	34	16-Sep-26	16-Sep-26	-7
IB-L1M\S-1150	Punchlist Completion and Signoff	5	0%	28-Sep-26	02-Oct-26	291			
Janus Scope		60	0%	28-Jul-26	20-Oct-26	17	20-Jul-26	12-Oct-26	-6
IB-JNUS-1000	Level 2 Install (Diamond Plate, Turkey Wire, Misc.)	15	0%	28-Jul-26	17-Aug-26	17	20-Jul-26	07-Aug-26	-6
IB-JNUS-1010	Level 3 Install (Diamond Plate, Turkey Wire, Misc.)	15	0%	18-Aug-26	08-Sep-26	17	10-Aug-26	28-Aug-26	-6
IB-JNUS-1020	Level 4 Install (Diamond Plate, Turkey Wire, Misc.)	15	0%	09-Sep-26	29-Sep-26	17	31-Aug-26	21-Sep-26	-6
IB-JNUS-1030	Level 1 Install (Diamond Plate, Turkey Wire, Misc.)	15	0%	30-Sep-26	20-Oct-26	17	22-Sep-26	12-Oct-26	-6
Elevator Installation		35	0%	19-Aug-26	07-Oct-26	26	11-Aug-26	29-Sep-26	-6
EL-INST-1000	Evelvator Installation (incl. Equipment Room Buildout)	35	0%	19-Aug-26	07-Oct-26	26	11-Aug-26	29-Sep-26	-6
Stairwells		46	0%	02-Mar-26	04-May-26	187	25-Feb-26	17-Mar-26	-34
IB-STAR-1000	Install Stairs & Railings	20	0%	02-Mar-26	27-Mar-26	91	25-Feb-26	10-Mar-26	-13
IB-STAR-1010	Install Signage & Lighting	7	0%	30-Mar-26	07-Apr-26	140	11-Mar-26	13-Mar-26	-17

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: Remaining .

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
IB-STAR-1020	Install Doors & Hardware	4	0%	08-Apr-26	13-Apr-26	140	16-Mar-26	17-Mar-26	-19
IB-STAR-1030	Paint Stairs and Railings	5	0%	14-Apr-26	20-Apr-26	143			
IB-STAR-1040	Clean Stairwells and Punchlist	5	0%	21-Apr-26	27-Apr-26	143			
IB-STAR-1050	Punchlist and Signoff on Stairwells	5	0%	28-Apr-26	04-May-26	187			
Outside Primary Footprint		81	0%	31-Jul-26	23-Nov-26	35	24-Jul-26	18-Nov-26	-3
Sitework Finishes		62	0%	31-Jul-26	27-Oct-26	54	24-Jul-26	19-Oct-26	-6
SW-FIN-1040	Finish Grade Site (incl. bio ponds)	5	0%	31-Jul-26	06-Aug-26	0	24-Jul-26	30-Jul-26	-5
SW-FIN-1050	Install Irrigation Sleeves (inc. bio ponds)	2	0%	07-Aug-26	10-Aug-26	0	31-Jul-26	03-Aug-26	-5
SW-FIN-1060	Electrical Rough (Light Poles)	5	0%	11-Aug-26	17-Aug-26	0	04-Aug-26	10-Aug-26	-5
SW-FIN-1100	Install Bollards (including footings)	5	0%	18-Aug-26	24-Aug-26	0	11-Aug-26	17-Aug-26	-5
SW-FIN-1130	FRP Concrete (Hardscape & Sidewalks)	7	0%	25-Aug-26	02-Sep-26	0	18-Aug-26	26-Aug-26	-5
SW-FIN-1140	Install Irrigation	10	0%	03-Sep-26	17-Sep-26	15	27-Aug-26	10-Sep-26	-5
SW-FIN-1150	Install Asphalt (Final Coat)	1	0%	18-Sep-26	18-Sep-26	15	11-Sep-26	11-Sep-26	-5
SW-FIN-1170	Planting	10	0%	21-Sep-26	02-Oct-26	15	14-Sep-26	25-Sep-26	-5
SW-FIN-1171	FRP Dumpster Enclosure	7	0%	05-Oct-26	13-Oct-26	15	28-Sep-26	06-Oct-26	-5
SW-FIN-1180	Site Furnishings & Signage	5	0%	14-Oct-26	20-Oct-26	15	07-Oct-26	13-Oct-26	-5
SW-FIN-1190	Final Clean and Punchlist Sitework	2	0%	21-Oct-26	22-Oct-26	15	14-Oct-26	14-Oct-26	-6
SW-FIN-1200	Punch List Completion and Signoff	3	0%	23-Oct-26	27-Oct-26	54	15-Oct-26	19-Oct-26	-6
Rutland Drive Improvements		62	0%	27-Aug-26	23-Nov-26	35	27-Aug-26	18-Nov-26	-3
SW-RTLN-1000	EPSC Install (Silt Fence, Inlet Protection)	3	0%	27-Aug-26	31-Aug-26	0	27-Aug-26	31-Aug-26	0
SW-RTLN-1010	Sawcut Asphalt & Demo Existing Curb	3	0%	01-Sep-26	03-Sep-26	0	01-Sep-26	03-Sep-26	0
SW-RTLN-1020	Temp Traffic Control Setup	3	0%	04-Sep-26	09-Sep-26	0	04-Sep-26	09-Sep-26	0
SW-RTLN-1030	Relocate Mailbox / Signs / Remove Conflicts	2	0%	10-Sep-26	11-Sep-26	0	10-Sep-26	11-Sep-26	0
SW-RTLN-1040	Trench & Install Storm Pipe	8	0%	14-Sep-26	23-Sep-26	0	14-Sep-26	23-Sep-26	0
SW-RTLN-1050	Set Curb Inlets, Junction Boxes, Headwalls	6	0%	24-Sep-26	01-Oct-26	0	24-Sep-26	01-Oct-26	0
SW-RTLN-1060	Backfill / Compact Drain Trenches	3	0%	02-Oct-26	06-Oct-26	0	02-Oct-26	06-Oct-26	0
SW-RTLN-1070	Subgrade Proofrool & Undercut / Backfill (if needed)	3	0%	07-Oct-26	09-Oct-26	0	07-Oct-26	09-Oct-26	0
SW-RTLN-1080	Place Aggregate Base	4	0%	12-Oct-26	15-Oct-26	0	12-Oct-26	15-Oct-26	0
SW-RTLN-1090	City Inspections (Proofrool, Storm, Curbs)	2	0%	16-Oct-26	19-Oct-26	0	16-Oct-26	19-Oct-26	0
SW-RTLN-1100	Install Curb & Gutter	5	0%	20-Oct-26	26-Oct-26	0	20-Oct-26	26-Oct-26	0
SW-RTLN-1110	Sidewalks & ADA Ramps	4	0%	27-Oct-26	30-Oct-26	0	27-Oct-26	30-Oct-26	0
SW-RTLN-1120	First Lift Asphalt (Binder Course)	2	0%	02-Nov-26	03-Nov-26	0	02-Nov-26	03-Nov-26	0
SW-RTLN-1130	Final Grading	2	0%	04-Nov-26	05-Nov-26	0	04-Nov-26	05-Nov-26	0
SW-RTLN-1140	Final Asphalt Surface Course	1	0%	06-Nov-26	06-Nov-26	0	06-Nov-26	06-Nov-26	0
SW-RTLN-1150	Permanent Signs & Striping	2	0%	09-Nov-26	10-Nov-26	0	09-Nov-26	10-Nov-26	0
SW-RTLN-1160	Site Cleanup & Final EPSC Removal	2	0%	11-Nov-26	12-Nov-26	0	11-Nov-26	12-Nov-26	0
SW-RTLN-1170	Rutland Drive Punchlist Walk	2	0%	13-Nov-26	16-Nov-26	35	13-Nov-26	16-Nov-26	0
SW-RTLN-1180	Rutland Drive Punchlist Completion and Signoff	5	0%	17-Nov-26	23-Nov-26	35	17-Nov-26	18-Nov-26	-3
Closeout		68	0%	11-Aug-26	13-Nov-26	0	03-Aug-26	19-Nov-26	4
Commissioning		10	0%	08-Sep-26	21-Sep-26	33	28-Aug-26	03-Sep-26	-11
CO-CM-1000	Start-Up & Testing	10	0%	08-Sep-26	21-Sep-26	33	28-Aug-26	03-Sep-26	-11
Building Finals		68	0%	11-Aug-26	13-Nov-26	0	03-Aug-26	19-Nov-26	4
CO-BF-1000	Rough Fire Sprinkler Inspection	1	0%	11-Aug-26	11-Aug-26	61	03-Aug-26	03-Aug-26	-6
CO-BF-1010	Final Fire Sprinkler Inspection	1	0%	22-Sep-26	22-Sep-26	33	04-Sep-26	04-Sep-26	-11
CO-BF-1020	Electrical Final Inspection	1	0%	23-Sep-26	23-Sep-26	33	08-Sep-26	08-Sep-26	-11
CO-BF-1030	Plumbing Final Inspection	1	0%	24-Sep-26	24-Sep-26	33	09-Sep-26	09-Sep-26	-11
CO-BF-1040	Mechanical Final Inspection	1	0%	25-Sep-26	25-Sep-26	33	10-Sep-26	10-Sep-26	-11
CO-BF-1050	Fire Alarm Final Inspection	1	0%	28-Sep-26	28-Sep-26	33	11-Sep-26	11-Sep-26	-11
CO-BF-1060	Building Final Occupancy Inspection (Substantial Completion)	1	0%	13-Nov-26	13-Nov-26	0	19-Nov-26	19-Nov-26	4
Warranty Work		240	0%	03-Dec-26	15-Nov-27	0	20-Nov-26	04-Nov-27	-7
WW-WARR-1000	1st Quarter HVAC Maintenance	60	0%	03-Dec-26	03-Mar-27	0	20-Nov-26	22-Feb-27	-7
WW-WARR-1010	1st Quarter Landscape Maintenance	60	0%	03-Dec-26	03-Mar-27	0	20-Nov-26	22-Feb-27	-7
WW-WARR-1030	2nd Quarter HVAC Maintenance	60	0%	04-Mar-27	26-May-27	0	23-Feb-27	17-May-27	-7
WW-WARR-1040	2nd Quarter Landscape Maintenance	60	0%	04-Mar-27	26-May-27	0	23-Feb-27	17-May-27	-7
WW-WARR-1050	3rd Quarter HVAC Maintenance	60	0%	27-May-27	20-Aug-27	0	18-May-27	11-Aug-27	-7
WW-WARR-1060	3rd Quarter Landscape Maintenance	60	0%	27-May-27	20-Aug-27	0	18-May-27	11-Aug-27	-7
WW-WARR-1020	11-Month Warranty Walk	5	0%	04-Oct-27	08-Oct-27	26	20-Nov-26	07-Oct-27	-1
WW-WARR-1070	4th Quarter HVAC Maintenance	60	0%	23-Aug-27	15-Nov-27	0	12-Aug-27	04-Nov-27	-7
WW-WARR-1080	4th Quarter Landscape Maintenance	60	0%	23-Aug-27	15-Nov-27	0	12-Aug-27	04-Nov-27	-7

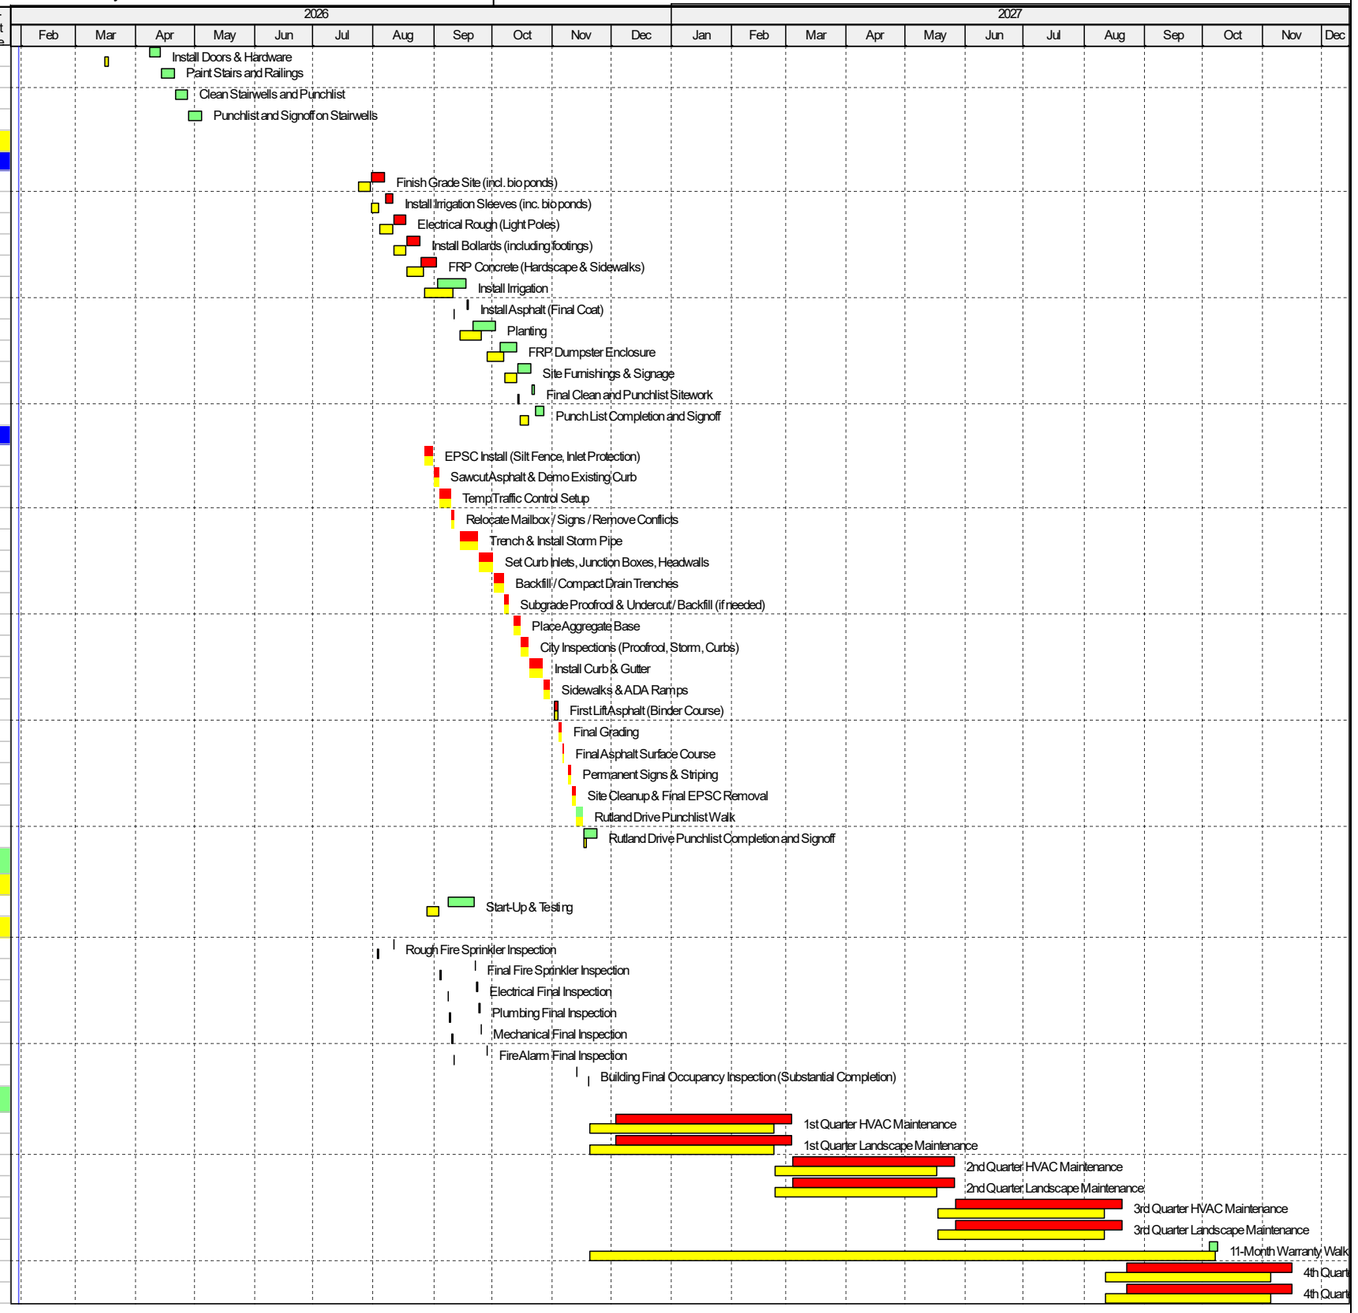

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: Remaining .

© Oracle Corporation
