	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Public Storage Selma, NC**	**263 days**	**263 days**	**0d**	**Mon 10/6/25**	**Mon 10/6/25**	**0d**	**Fri 10/9/26**	**Fri 10/9/26**	**0d**
2	Award Contract	0 days	0 days	0d	Mon 10/6/25	Mon 10/6/25	0d	Mon 10/6/25	Mon 10/6/25	0d
3	**Mobilization**	**6 days**	**6 days**	**0d**	**Mon 12/1/25**	**Mon 12/1/25**	**0d**	**Mon 12/8/25**	**Mon 12/8/25**	**0d**
4	Mobilization (Site Fence, Layout, Barricades, Etc.)	1 day	1 day	0d	Mon 1/5/26	Mon 1/5/26	0d	Mon 1/5/26	Mon 1/5/26	0d
5	SWPPP	5 days	5 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Fri 12/19/25	Fri 12/19/25	0d
6	**Demo/Site Work**	**87 days**	**84 days**	**3d**	**Mon 1/5/26**	**Mon 1/5/26**	**0d**	**Tue 5/5/26**	**Thu 4/30/26**	**3d**
7	Clearing and Grubbing	10 days	10 days	0d	Mon 1/5/26	Mon 1/5/26	0d	Fri 1/16/26	Fri 1/16/26	0d
8	Dewatering	5 days	5 days	0d	Mon 1/19/26	Mon 1/19/26	0d	Fri 1/23/26	Fri 1/23/26	0d
9	Rough Grading	18 days	18 days	0d	Mon 1/19/26	Mon 1/19/26	0d	Wed 2/11/26	Wed 2/11/26	0d
10	Storm System	21 days	21 days	0d	Mon 3/2/26	Thu 2/12/26	12d	Mon 3/30/26	Thu 3/12/26	12d
11	Sanitary Sewer	5 days	5 days	0d	Tue 3/31/26	Fri 3/13/26	12d	Mon 4/6/26	Thu 3/19/26	12d
12	Water	10 days	10 days	0d	Fri 3/20/26	Fri 3/20/26	0d	Thu 4/2/26	Thu 4/2/26	0d
13	Site Electrical	10 days	10 days	0d	Wed 4/8/26	Fri 4/3/26	3d	Tue 4/21/26	Thu 4/16/26	3d
14	Building Tie In	10 days	10 days	0d	Wed 4/22/26	Fri 4/17/26	3d	Tue 5/5/26	Thu 4/30/26	3d
15	**Building A**	**149 days**	**144 days**	**5d**	**Tue 1/27/26**	**Thu 2/5/26**	**-7d**	**Fri 8/21/26**	**Tue 8/25/26**	**-2d**
16	**Structure**	**133 days**	**104 days**	**29d**	**Tue 1/27/26**	**Thu 2/5/26**	**-7d**	**Thu 7/30/26**	**Tue 6/30/26**	**22d**
17	**First Floor**	**93 days**	**64 days**	**29d**	**Tue 1/27/26**	**Thu 2/5/26**	**-7d**	**Thu 6/4/26**	**Tue 5/5/26**	**22d**
18	Weather Delay(Snow & Ice)	12 days	5 days	7d	Tue 1/27/26	Thu 2/5/26	-7d	Wed 2/11/26	Wed 2/11/26	0d
19	Building Pad Delivery (Bldg A)	5 days	5 days	0d	Mon 3/9/26	Thu 2/12/26	17d	Fri 3/13/26	Wed 2/18/26	17d
20	Elevator Pit - Excavate	2 days	5 days	-3d	Mon 3/9/26	Thu 2/19/26	12d	Tue 3/10/26	Wed 2/25/26	9d
21	Elevator Pit - Form and Pour	10 days	10 days	0d	Tue 3/10/26	Thu 2/26/26	8d	Mon 3/23/26	Wed 3/11/26	8d
22	FRP Foundations / Foundation CMU - Area 1	7 days	7 days	0d	Mon 3/16/26	Thu 2/19/26	17d	Tue 3/24/26	Fri 2/27/26	17d
23	Concrete Retaining Walls	10 days	10 days	0d	Wed 3/25/26	Mon 3/2/26	17d	Tue 4/7/26	Fri 3/13/26	17d
24	FRP Foundations/Foundation Area 2	7 days	7 days	0d	Wed 4/8/26	Mon 3/16/26	17d	Thu 4/16/26	Tue 3/24/26	17d
25	Under Slab MEP	10 days	10 days	0d	Fri 4/3/26	Wed 3/11/26	17d	Thu 4/16/26	Tue 3/24/26	17d
26	Slab #1 Prep / Pour (North Half)	10 days	10 days	0d	Fri 4/10/26	Wed 3/18/26	17d	Thu 4/23/26	Tue 3/31/26	17d
27	CMU shafts	15 days	15 days	0d	Fri 4/24/26	Wed 4/1/26	17d	Thu 5/14/26	Tue 4/21/26	17d
28	Slab #2 Prep / Pour (South Half)	10 days	10 days	0d	Fri 4/24/26	Wed 4/1/26	17d	Thu 5/7/26	Tue 4/14/26	17d
29	Janus Framing System (North Half)	15 days	15 days	0d	Fri 4/24/26	Wed 4/1/26	17d	Thu 5/14/26	Tue 4/21/26	17d
30	Janus Framing System (South Half)	15 days	10 days	5d	Fri 5/15/26	Wed 4/22/26	17d	Thu 6/4/26	Tue 5/5/26	22d
31	**Second Floor**	**40 days**	**40 days**	**0d**	**Fri 5/22/26**	**Wed 4/22/26**	**22d**	**Thu 7/16/26**	**Tue 6/16/26**	**22d**
32	Elevated Slab #1 (North Half) Prep/Pour	5 days	5 days	0d	Fri 5/22/26	Wed 4/22/26	22d	Thu 5/28/26	Tue 4/28/26	22d
33	Elevated Slab #2 (South Half) Prep/Pour	5 days	5 days	0d	Fri 5/29/26	Wed 5/6/26	17d	Thu 6/4/26	Tue 5/12/26	17d
34	Janus Framing System (North Half)	15 days	15 days	0d	Fri 6/5/26	Wed 5/6/26	22d	Thu 6/25/26	Tue 5/26/26	22d
35	Janus Framing System (South Half)	15 days	10 days	5d	Fri 6/26/26	Wed 5/27/26	22d	Thu 7/16/26	Tue 6/9/26	27d
36	Roof Decking - Building A		5 days			Wed 6/10/26			Tue 6/16/26	
37	**Stairs**	**20 days**	**20 days**	**0d**	**Fri 5/15/26**	**Tue 5/19/26**	**-2d**	**Thu 6/11/26**	**Mon 6/15/26**	**-2d**
38	Stair #1	10 days	10 days	0d	Fri 5/15/26	Tue 5/19/26	-2d	Thu 5/28/26	Mon 6/1/26	-2d
39	Stair #2	10 days	10 days	0d	Fri 5/29/26	Tue 6/2/26	-2d	Thu 6/11/26	Mon 6/15/26	-2d
40	**Roof**	**10 days**	**10 days**	**0d**	**Fri 7/17/26**	**Wed 6/17/26**	**22d**	**Thu 7/30/26**	**Tue 6/30/26**	**22d**
41	Metal Roofing	10 days	10 days	0d	Fri 7/17/26	Wed 6/17/26	22d	Thu 7/30/26	Tue 6/30/26	22d
42	**Framing and MEP**	**50 days**	**80 days**	**-30d**	**Fri 5/29/26**	**Wed 5/6/26**	**17d**	**Thu 8/6/26**	**Tue 8/25/26**	**-13d**
43	**First Floor**	**35 days**	**65 days**	**-30d**	**Fri 5/29/26**	**Wed 5/6/26**	**17d**	**Thu 7/16/26**	**Tue 8/4/26**	**-13d**
44	Interior Framing	5 days	5 days	0d	Fri 6/5/26	Wed 5/6/26	22d	Thu 6/11/26	Tue 5/12/26	22d
45	1st Floor MEP Rough-In Area 1	20 days	20 days	0d	Fri 5/29/26	Wed 5/13/26	12d	Thu 6/25/26	Tue 6/9/26	12d
46	1st Floor MEP Rough-In Area 2	15 days	15 days	0d	Fri 6/5/26	Wed 6/10/26	-3d	Thu 6/25/26	Tue 6/30/26	-3d
47	1st Floor MEP Trim Out Area 1	10 days	10 days	0d	Fri 6/26/26	Wed 7/15/26	-13d	Thu 7/9/26	Tue 7/28/26	-13d
48	1st Floor MEP Trim Out Area 2	5 days	5 days	0d	Fri 7/10/26	Wed 7/29/26	-13d	Thu 7/16/26	Tue 8/4/26	-13d
49	**Second Floor**	**45 days**	**50 days**	**-5d**	**Fri 6/5/26**	**Wed 6/17/26**	**-8d**	**Thu 8/6/26**	**Tue 8/25/26**	**-13d**
50	Interior Framing	5 days	5 days	0d	Fri 6/5/26	Wed 6/17/26	-8d	Thu 6/11/26	Tue 6/23/26	-8d
51	2nd Floor MEP Rough-In Area 2	15 days	15 days	0d	Fri 6/26/26	Wed 7/1/26	-3d	Thu 7/16/26	Tue 7/21/26	-3d
52	2nd Floor MEP Rough-In Area 2	15 days	15 days	0d	Fri 7/17/26	Wed 7/22/26	-3d	Thu 8/6/26	Tue 8/11/26	-3d
53	2nd Floor MEP Trim Out Area 1	10 days	10 days	0d	Fri 7/17/26	Wed 8/5/26	-13d	Thu 7/30/26	Tue 8/18/26	-13d
54	2nd Floor MEP Trim Out Area 2	5 days	5 days	0d	Fri 7/31/26	Wed 8/19/26	-13d	Thu 8/6/26	Tue 8/25/26	-13d
55	**Elevator**	**30 days**	**30 days**	**0d**	**Mon 7/13/26**	**Mon 7/13/26**	**-1d**	**Fri 8/21/26**	**Mon 8/24/26**	**-1d**
56	Delivery	0 days	0 days	0d	Mon 7/13/26	Mon 7/13/26	-1d	Mon 7/13/26	Mon 7/13/26	-1d
57	Elevator 1 - First Floor	5 days	5 days	0d	Mon 7/13/26	Tue 7/14/26	-1d	Fri 7/17/26	Mon 7/20/26	-1d

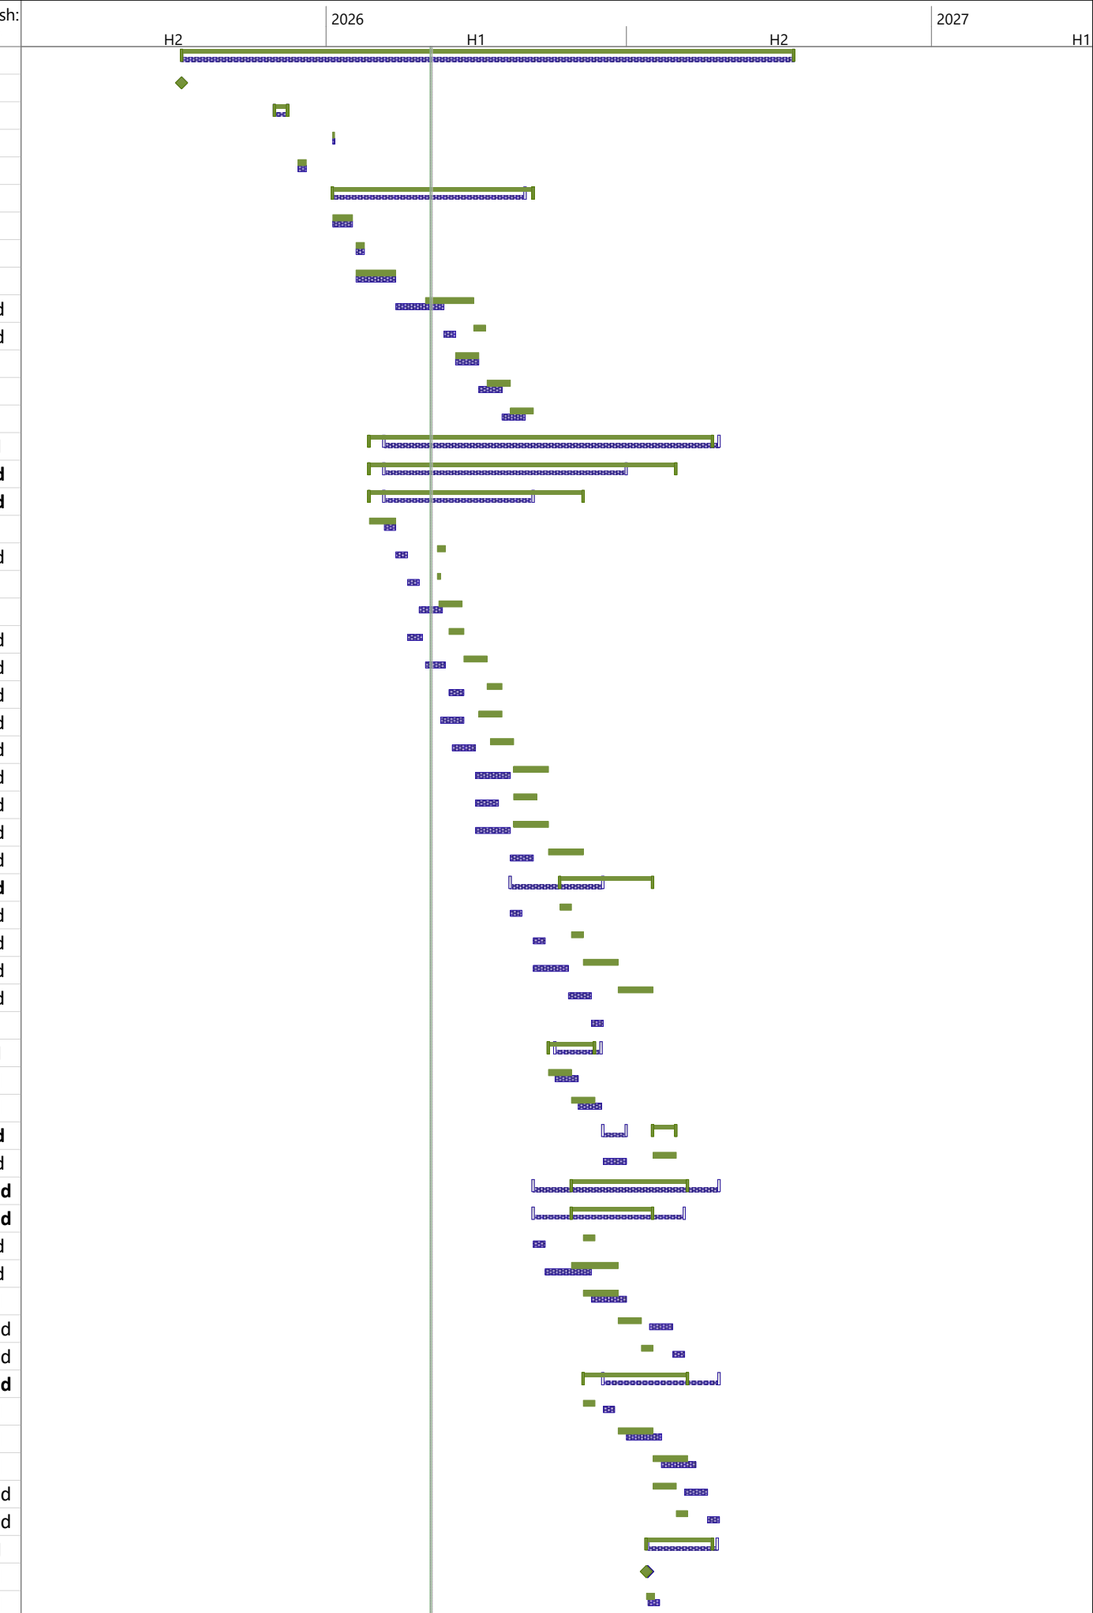

	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
58	Elevator 1 - Second Floor	5 days	5 days	0d	Mon 7/20/26	Tue 7/21/26	-1d	Fri 7/24/26	Mon 7/27/26	-1d
59	Elevator 2 - First Floor	5 days	5 days	0d	Mon 7/27/26	Tue 7/28/26	-1d	Fri 7/31/26	Mon 8/3/26	-1d
60	Elevator 2 - Second Floor	5 days	5 days	0d	Mon 8/3/26	Tue 8/4/26	-1d	Fri 8/7/26	Mon 8/10/26	-1d
61	Infill Doors	5 days	5 days	0d	Mon 8/3/26	Tue 8/4/26	-1d	Fri 8/7/26	Mon 8/10/26	-1d
62	Test / Adjust	5 days	5 days	0d	Mon 8/10/26	Tue 8/11/26	-1d	Fri 8/14/26	Mon 8/17/26	-1d
63	State Inspection	5 days	5 days	0d	Mon 8/17/26	Tue 8/18/26	-1d	Fri 8/21/26	Mon 8/24/26	-1d
64	**Exterior Finishes**	**50 days**	**50 days**	**0d**	**Fri 6/12/26**	**Wed 5/27/26**	**12d**	**Thu 8/20/26**	**Tue 8/4/26**	**12d**
65	Masonry Veneer	15 days	15 days	0d	Fri 6/12/26	Wed 5/27/26	12d	Thu 7/2/26	Tue 6/16/26	12d
66	Metal Panels Completion	15 days	15 days	0d	Fri 7/3/26	Wed 6/17/26	12d	Thu 7/23/26	Tue 7/7/26	12d
67	Sheetmetal Work (Coping, Gutters, & Downspouts)	10 days	10 days	0d	Fri 7/31/26	Wed 7/1/26	22d	Thu 8/13/26	Tue 7/14/26	22d
68	Automatic Entrance Door	5 days	5 days	0d	Fri 7/3/26	Wed 6/17/26	12d	Thu 7/9/26	Tue 6/23/26	12d
69	Exterior Paint	10 days	10 days	0d	Fri 7/24/26	Wed 7/8/26	12d	Thu 8/6/26	Tue 7/21/26	12d
70	Exterior Signage Install	10 days	10 days	0d	Fri 8/7/26	Wed 7/22/26	12d	Thu 8/20/26	Tue 8/4/26	12d
71	Canopy	10 days	10 days	0d	Fri 8/7/26	Wed 7/22/26	12d	Thu 8/20/26	Tue 8/4/26	12d
72	**Building B**	**75 days**	**99 days**	**-24d**	**Wed 3/4/26**	**Thu 2/19/26**	**9d**	**Tue 6/16/26**	**Tue 7/7/26**	**-15d**
73	**Structure**	**35 days**	**69 days**	**-34d**	**Wed 3/4/26**	**Thu 2/19/26**	**9d**	**Tue 4/21/26**	**Tue 5/26/26**	**-25d**
74	**First Floor**	**30 days**	**64 days**	**-34d**	**Wed 3/4/26**	**Thu 2/19/26**	**9d**	**Tue 4/14/26**	**Tue 5/19/26**	**-25d**
75	Building Pad Delivery (Bldg B)	3 days	5 days	-2d	Wed 3/4/26	Thu 2/19/26	9d	Fri 3/6/26	Wed 2/25/26	7d
76	FRP Foundations / Foundation CMU - Area 1	5 days	5 days	0d	Mon 3/9/26	Thu 2/26/26	7d	Fri 3/13/26	Wed 3/4/26	7d
77	FRP Foundations/Foundation Area 2		5 days			Wed 3/25/26			Tue 3/31/26	
78	Under Slab MEP	5 days	5 days	0d	Mon 3/9/26	Wed 3/25/26	-12d	Fri 3/13/26	Tue 3/31/26	-12d
79	Slab Prep / Pour	5 days	5 days	0d	Thu 3/12/26	Wed 4/15/26	-24d	Wed 3/18/26	Tue 4/21/26	-24d
80	CMU Walls	10 days	10 days	0d	Wed 3/25/26	Wed 4/22/26	-20d	Tue 4/7/26	Tue 5/5/26	-20d
81	Janus Framing System	5 days	10 days	-5d	Wed 4/8/26	Wed 5/6/26	-20d	Tue 4/14/26	Tue 5/19/26	-25d
82	Roof Decking		0 days			Tue 5/19/26			Tue 5/19/26	
83	**Roof**	**5 days**	**5 days**	**0d**	**Mon 4/6/26**	**Wed 5/20/26**	**-32d**	**Fri 4/10/26**	**Tue 5/26/26**	**-32d**
84	Metal Roofing	5 days	5 days	0d	Wed 4/15/26	Wed 5/20/26	-25d	Tue 4/21/26	Tue 5/26/26	-25d
85	**Framing and MEP**	**25 days**	**25 days**	**0d**	**Wed 4/15/26**	**Wed 5/20/26**	**-25d**	**Tue 5/19/26**	**Tue 6/23/26**	**-25d**
86	**First Floor**	**25 days**	**25 days**	**0d**	**Wed 4/15/26**	**Wed 5/20/26**	**-25d**	**Tue 5/19/26**	**Tue 6/23/26**	**-25d**
87	Interior Framing	5 days	5 days	0d	Wed 4/15/26	Wed 5/20/26	-25d	Tue 4/21/26	Tue 5/26/26	-25d
88	1st Floor MEP Rough-In Area 1	10 days	10 days	0d	Wed 4/22/26	Wed 5/27/26	-25d	Tue 5/5/26	Tue 6/9/26	-25d
89	Finishes	10 days	10 days	0d	Wed 4/22/26	Wed 5/27/26	-25d	Tue 5/5/26	Tue 6/9/26	-25d
90	1st Floor MEP Trim Out Area 1	10 days	10 days	0d	Wed 5/6/26	Wed 6/10/26	-25d	Tue 5/19/26	Tue 6/23/26	-25d
91	**Exterior Finishes**	**25 days**	**35 days**	**-10d**	**Wed 5/13/26**	**Wed 5/20/26**	**-5d**	**Tue 6/16/26**	**Tue 7/7/26**	**-15d**
92	Metal Panels Completion	5 days	15 days	-10d	Wed 5/13/26	Wed 5/20/26	-5d	Tue 5/19/26	Tue 6/9/26	-15d
93	Sheetmetal Work (Coping, Gutters, & Downspouts)	3 days	10 days	-7d	Wed 5/20/26	Wed 6/10/26	-15d	Fri 5/22/26	Tue 6/23/26	-22d
94	Automatic Entrance Door	5 days	5 days	0d	Wed 5/20/26	Wed 6/10/26	-15d	Tue 5/26/26	Tue 6/16/26	-15d
95	Exterior Paint	10 days	10 days	0d	Wed 5/20/26	Wed 6/10/26	-15d	Tue 6/2/26	Tue 6/23/26	-15d
96	Exterior Signage Install	10 days	10 days	0d	Wed 6/3/26	Wed 6/24/26	-15d	Tue 6/16/26	Tue 7/7/26	-15d
97	Canopy	10 days	10 days	0d	Wed 6/3/26	Wed 6/24/26	-15d	Tue 6/16/26	Tue 7/7/26	-15d
98	**Building C**	**48 days**	**99 days**	**-51d**	**Mon 3/2/26**	**Thu 2/26/26**	**2d**	**Wed 5/6/26**	**Tue 7/14/26**	**-49d**
99	**Structure**	**35 days**	**74 days**	**-39d**	**Mon 3/2/26**	**Thu 2/26/26**	**2d**	**Fri 4/17/26**	**Tue 6/9/26**	**-37d**
100	**First Floor**	**30 days**	**69 days**	**-39d**	**Mon 3/2/26**	**Thu 2/26/26**	**2d**	**Fri 4/10/26**	**Tue 6/2/26**	**-37d**
101	Building Pad Delivery (Bldg C)	5 days	5 days	0d	Mon 3/2/26	Thu 2/26/26	2d	Fri 3/6/26	Wed 3/4/26	2d
102	FRP Foundations / Foundation CMU - Area 1	5 days	5 days	0d	Wed 3/4/26	Thu 3/5/26	-1d	Tue 3/10/26	Wed 3/11/26	-1d
103	FRP Foundations/Foundation Area 2	5 days	5 days	0d	Wed 3/11/26	Thu 3/12/26	-1d	Tue 3/17/26	Wed 3/18/26	-1d
104	Under Slab MEP	5 days	5 days	0d	Wed 3/11/26	Thu 3/19/26	-6d	Tue 3/17/26	Wed 3/25/26	-6d
105	Slab Prep / Pour	5 days	5 days	0d	Wed 3/11/26	Thu 3/26/26	-11d	Tue 3/17/26	Wed 4/1/26	-11d
106	CMU Walls	10 days	10 days	0d	Mon 3/23/26	Wed 5/6/26	-32d	Fri 4/3/26	Tue 5/19/26	-32d
107	Janus Framing System	5 days	5 days	0d	Mon 4/6/26	Wed 5/20/26	-32d	Fri 4/10/26	Tue 5/26/26	-32d
108	Roof Decking		5 days			Wed 5/27/26			Tue 6/2/26	
109	**Roof**	**5 days**	**5 days**	**0d**	**Mon 4/13/26**	**Wed 6/3/26**	**-37d**	**Fri 4/17/26**	**Tue 6/9/26**	**-37d**
110	Metal Roofing	5 days	5 days	0d	Mon 4/13/26	Wed 6/3/26	-37d	Fri 4/17/26	Tue 6/9/26	-37d
111	**Framing and MEP**	**4 days**	**20 days**	**-16d**	**Mon 4/20/26**	**Wed 6/10/26**	**-37d**	**Thu 4/23/26**	**Tue 7/7/26**	**-53d**
112	**First Floor**	**4 days**	**20 days**	**-16d**	**Mon 4/20/26**	**Wed 6/10/26**	**-37d**	**Thu 4/23/26**	**Tue 7/7/26**	**-53d**
113	1st Floor MEP Rough-In Area 1	2 days	10 days	-8d	Mon 4/20/26	Wed 6/10/26	-37d	Tue 4/21/26	Tue 6/23/26	-45d
114	1st Floor MEP Trim Out Area 1	2 days	10 days	-8d	Wed 4/22/26	Wed 6/24/26	-45d	Thu 4/23/26	Tue 7/7/26	-53d

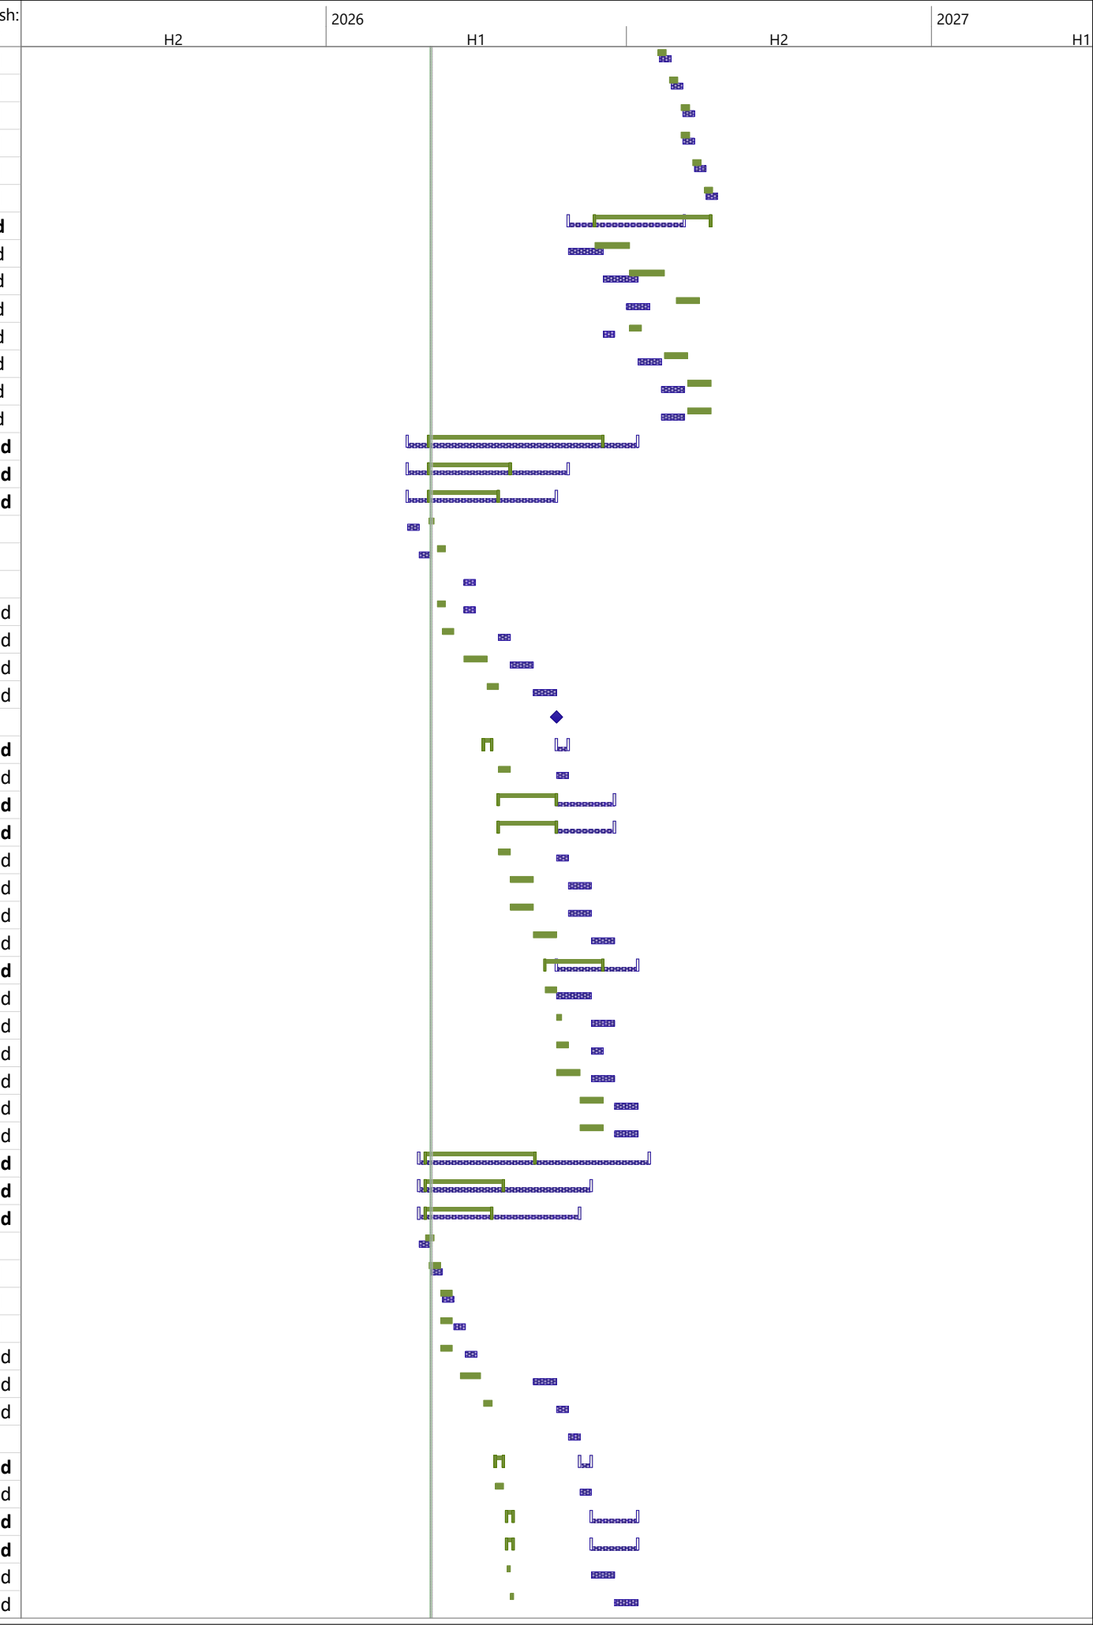
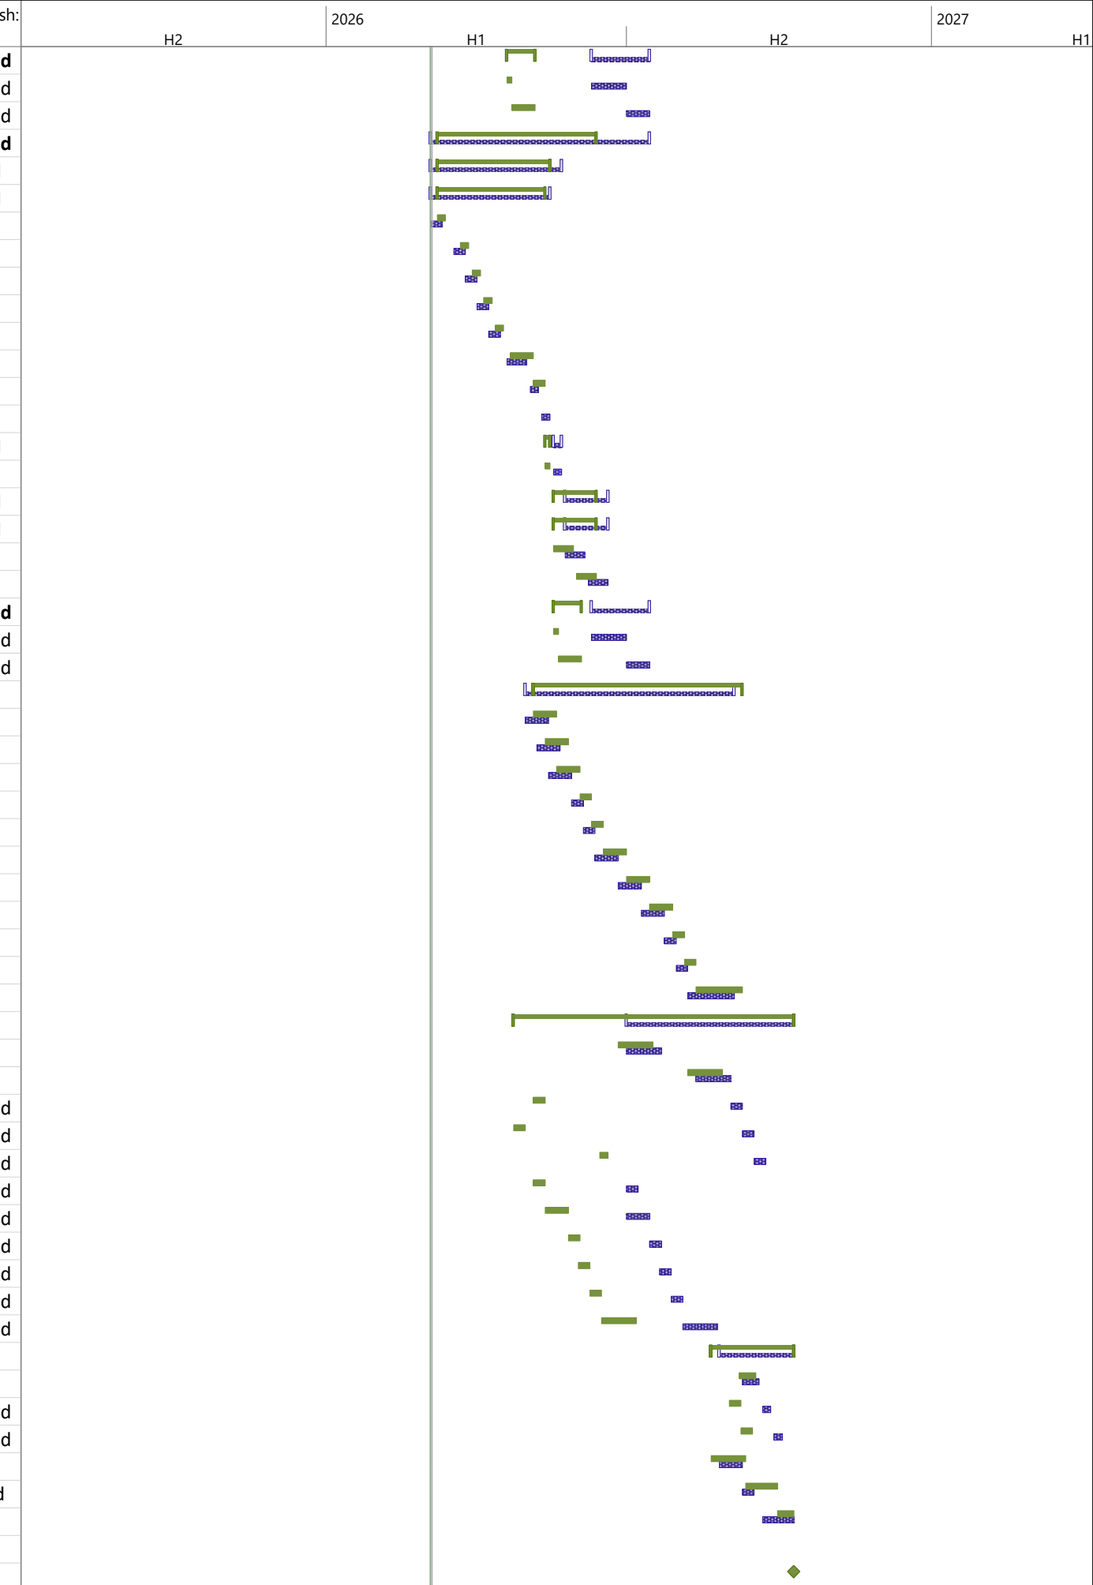
	Name	Duration: Current	Duration: Previous	Durati Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
115	**Exterior Finishes**	**13 days**	**25 days**	**-12d**	**Mon 4/20/26**	**Wed 6/10/26**	**-37d**	**Wed 5/6/26**	**Tue 7/14/26**	**-49d**
116	Metal Panels Completion	3 days	15 days	-12d	Mon 4/20/26	Wed 6/10/26	-37d	Wed 4/22/26	Tue 6/30/26	-49d
117	Exterior Signage Install	10 days	10 days	0d	Thu 4/23/26	Wed 7/1/26	-49d	Wed 5/6/26	Tue 7/14/26	-49d
118	**Building D**	**70 days**	**94 days**	**-24d**	**Mon 3/9/26**	**Thu 3/5/26**	**2d**	**Fri 6/12/26**	**Tue 7/14/26**	**-22d**
119	**Structure**	**50 days**	**57 days**	**-7d**	**Mon 3/9/26**	**Thu 3/5/26**	**2d**	**Fri 5/15/26**	**Fri 5/22/26**	**-5d**
120	**First Floor**	**47 days**	**52 days**	**-5d**	**Mon 3/9/26**	**Thu 3/5/26**	**2d**	**Tue 5/12/26**	**Fri 5/15/26**	**-3d**
121	Building Pad Delivery (Bldg D)	5 days	5 days	0d	Mon 3/9/26	Thu 3/5/26	2d	Fri 3/13/26	Wed 3/11/26	2d
122	FRP Foundations / Foundation CMU - Area 1	5 days	5 days	0d	Mon 3/23/26	Thu 3/19/26	2d	Fri 3/27/26	Wed 3/25/26	2d
123	FRP Foundations/Foundation Area 2	5 days	5 days	0d	Mon 3/30/26	Thu 3/26/26	2d	Fri 4/3/26	Wed 4/1/26	2d
124	Under Slab MEP	5 days	5 days	0d	Mon 4/6/26	Thu 4/2/26	2d	Fri 4/10/26	Wed 4/8/26	2d
125	Slab Prep / Pour	5 days	5 days	0d	Mon 4/13/26	Thu 4/9/26	2d	Fri 4/17/26	Wed 4/15/26	2d
126	CMU Walls	10 days	10 days	0d	Wed 4/22/26	Mon 4/20/26	2d	Tue 5/5/26	Fri 5/1/26	2d
127	Janus Framing System	5 days	5 days	0d	Wed 5/6/26	Mon 5/4/26	2d	Tue 5/12/26	Fri 5/8/26	2d
128	Roof Decking		5 days			Mon 5/11/26			Fri 5/15/26	
129	**Roof**	**3 days**	**5 days**	**-2d**	**Wed 5/13/26**	**Mon 5/18/26**	**-3d**	**Fri 5/15/26**	**Fri 5/22/26**	**-5d**
130	Metal Roofing	3 days	5 days	-2d	Wed 5/13/26	Mon 5/18/26	-3d	Fri 5/15/26	Fri 5/22/26	-5d
131	**Framing and MEP**	**20 days**	**20 days**	**0d**	**Mon 5/18/26**	**Mon 5/25/26**	**-5d**	**Fri 6/12/26**	**Fri 6/19/26**	**-5d**
132	**First Floor**	**20 days**	**20 days**	**0d**	**Mon 5/18/26**	**Mon 5/25/26**	**-5d**	**Fri 6/12/26**	**Fri 6/19/26**	**-5d**
133	1st Floor MEP Rough-In Area 1	10 days	10 days	0d	Mon 5/18/26	Mon 5/25/26	-5d	Fri 5/29/26	Fri 6/5/26	-5d
134	1st Floor MEP Trim Out Area 1	10 days	10 days	0d	Mon 6/1/26	Mon 6/8/26	-5d	Fri 6/12/26	Fri 6/19/26	-5d
135	**Exterior Finishes**	**13 days**	**25 days**	**-12d**	**Mon 5/18/26**	**Wed 6/10/26**	**-17d**	**Wed 6/3/26**	**Tue 7/14/26**	**-29d**
136	Metal Panels Completion	3 days	15 days	-12d	Mon 5/18/26	Wed 6/10/26	-17d	Wed 5/20/26	Tue 6/30/26	-29d
137	Exterior Signage Install	10 days	10 days	0d	Thu 5/21/26	Wed 7/1/26	-29d	Wed 6/3/26	Tue 7/14/26	-29d
138	**Site Finishes**	**90 days**	**90 days**	**0d**	**Wed 5/6/26**	**Fri 5/1/26**	**3d**	**Tue 9/8/26**	**Thu 9/3/26**	**3d**
139	Site Fine Grading	10 days	10 days	0d	Wed 5/6/26	Fri 5/1/26	3d	Tue 5/19/26	Thu 5/14/26	3d
140	Stone Base	10 days	10 days	0d	Wed 5/13/26	Fri 5/8/26	3d	Tue 5/26/26	Thu 5/21/26	3d
141	Curb / Sidewalks	10 days	10 days	0d	Wed 5/20/26	Fri 5/15/26	3d	Tue 6/2/26	Thu 5/28/26	3d
142	Binder Course Asphalt - Area 1	5 days	5 days	0d	Wed 6/3/26	Fri 5/29/26	3d	Tue 6/9/26	Thu 6/4/26	3d
143	Binder Course Asphalt - Area 2	5 days	5 days	0d	Wed 6/10/26	Fri 6/5/26	3d	Tue 6/16/26	Thu 6/11/26	3d
144	Landscaping - Area 1	10 days	10 days	0d	Wed 6/17/26	Fri 6/12/26	3d	Tue 6/30/26	Thu 6/25/26	3d
145	Landscaping - Area 2	10 days	10 days	0d	Wed 7/1/26	Fri 6/26/26	3d	Tue 7/14/26	Thu 7/9/26	3d
146	Final Pavement	10 days	10 days	0d	Wed 7/15/26	Fri 7/10/26	3d	Tue 7/28/26	Thu 7/23/26	3d
147	Line Marking/Signage	5 days	5 days	0d	Wed 7/29/26	Fri 7/24/26	3d	Tue 8/4/26	Thu 7/30/26	3d
148	As-Builts Complete & Submitted to AHJ	5 days	5 days	0d	Wed 8/5/26	Fri 7/31/26	3d	Tue 8/11/26	Thu 8/6/26	3d
149	As-Built/City Review	20 days	20 days	0d	Wed 8/12/26	Fri 8/7/26	3d	Tue 9/8/26	Thu 9/3/26	3d
150	**Interior Upfit**	**121 days**	**73 days**	**48d**	**Fri 4/24/26**	**Wed 7/1/26**	**-48d**	**Fri 10/9/26**	**Fri 10/9/26**	**0d**
151	1st Floor - Janus Unit Install	15 days	15 days	0d	Fri 6/26/26	Wed 7/1/26	-3d	Thu 7/16/26	Tue 7/21/26	-3d
152	2nd Floor - Janus Unit Install	15 days	15 days	0d	Fri 8/7/26	Wed 8/12/26	-3d	Thu 8/27/26	Tue 9/1/26	-3d
153	Bldg B Janus Install	5 days	5 days	0d	Wed 5/6/26	Wed 9/2/26	-85d	Tue 5/12/26	Tue 9/8/26	-85d
154	Bldg C Janus Install	5 days	5 days	0d	Fri 4/24/26	Wed 9/9/26	-98d	Thu 4/30/26	Tue 9/15/26	-98d
155	Bldg D Janus Install	5 days	5 days	0d	Mon 6/15/26	Wed 9/16/26	-67d	Fri 6/19/26	Tue 9/22/26	-67d
156	Drywall Hanging	5 days	5 days	0d	Wed 5/6/26	Wed 7/1/26	-40d	Tue 5/12/26	Tue 7/7/26	-40d
157	Drywall Finishing	10 days	10 days	0d	Wed 5/13/26	Wed 7/1/26	-35d	Tue 5/26/26	Tue 7/14/26	-35d
158	Paint	5 days	5 days	0d	Wed 5/27/26	Wed 7/15/26	-35d	Tue 6/2/26	Tue 7/21/26	-35d
159	Millwork	5 days	5 days	0d	Tue 6/2/26	Tue 7/21/26	-35d	Mon 6/8/26	Mon 7/27/26	-35d
160	Floor Sealer - 2nd Floor	5 days	5 days	0d	Tue 6/9/26	Tue 7/28/26	-35d	Mon 6/15/26	Mon 8/3/26	-35d
161	Floor Sealer / Polish - 1st Floor and drive ups	15 days	15 days	0d	Tue 6/16/26	Tue 8/4/26	-35d	Mon 7/6/26	Mon 8/24/26	-35d
162	**Closeout**	**36 days**	**33 days**	**3d**	**Fri 8/21/26**	**Wed 8/26/26**	**-3d**	**Fri 10/9/26**	**Fri 10/9/26**	**0d**
163	Final Clean - Bldg A	8 days	8 days	0d	Mon 9/7/26	Wed 9/9/26	-2d	Wed 9/16/26	Fri 9/18/26	-2d
164	Final Clean - Bldg B	5 days	5 days	0d	Tue 9/1/26	Mon 9/21/26	-14d	Mon 9/7/26	Fri 9/25/26	-14d
165	Final Clean - Bldg C and D	5 days	5 days	0d	Tue 9/8/26	Mon 9/28/26	-14d	Mon 9/14/26	Fri 10/2/26	-14d
166	MEP Final Inspections	15 days	10 days	5d	Fri 8/21/26	Wed 8/26/26	-3d	Thu 9/10/26	Tue 9/8/26	2d
167	Building Final Inspections	13 days	5 days	8d	Fri 9/11/26	Wed 9/9/26	2d	Tue 9/29/26	Tue 9/15/26	10d
168	Weather Days Included (20 Days)	8 days	15 days	-7d	Wed 9/30/26	Mon 9/21/26	7d	Fri 10/9/26	Fri 10/9/26	0d
169	**Substantial Completion**	**0 days**	**0 days**	**0d**	**Fri 10/9/26**	**Fri 10/9/26**	**0d**	**Fri 10/9/26**	**Fri 10/9/26**	**0d**
170	Substantial Completion	0 days	0 days	0d	Fri 10/9/26	Fri 10/9/26	0d	Fri 10/9/26	Fri 10/9/26	0d
