	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous
1	**Public Storage Willis - TX 24198**	**223 days**	**207 days**	**16d**	**Thu 9/25/25**	**Thu 9/25/25**	**0d**	**Mon 8/3/26**	**Fri 7/10/26**
2	**Pre-Construction**	**133 days**	**133 days**	**0d**	**Thu 9/25/25**	**Thu 9/25/25**	**0d**	**Mon 3/30/26**	**Mon 3/30/26**
3	Contract Signed	1 day	1 day	0d	Thu 9/25/25	Thu 9/25/25	0d	Thu 9/25/25	Thu 9/25/25
4	Building Permit	1 day	1 day	0d	Fri 1/9/26	Fri 1/9/26	0d	Fri 1/9/26	Fri 1/9/26
5	Fire Tank Permit	1 day	1 day	0d	Mon 3/30/26	Mon 3/30/26	0d	Mon 3/30/26	Mon 3/30/26
6	NTP - From PS	1 day	1 day	0d	Mon 1/12/26	Mon 1/12/26	0d	Mon 1/12/26	Mon 1/12/26
7	Approval to go Vertical by AHJ	1 day	1 day	0d	Thu 3/26/26	Wed 3/4/26	16d	Thu 3/26/26	Wed 3/4/26
8	**Procurament**	**67 days**	**70 days**	**-3d**	**Wed 3/11/26**	**Tue 2/17/26**	**16d**	**Fri 6/12/26**	**Mon 5/25/26**
9	Building Structure	2 days	2 days	0d	Wed 3/11/26	Tue 2/17/26	16d	Fri 3/13/26	Thu 2/19/26
10	Hallway System	2 days	2 days	0d	Wed 6/10/26	Tue 5/19/26	16d	Fri 6/12/26	Thu 5/21/26
11	Fire Tank Delivery	1 day	1 day	0d	Mon 5/25/26	Mon 5/25/26	0d	Mon 5/25/26	Mon 5/25/26
12	**Site Work**	**102 days**	**100 days**	**2d**	**Mon 2/2/26**	**Tue 1/13/26**	**14d**	**Tue 6/23/26**	**Mon 6/1/26**
13	**Earthwork**	**19 days**	**17 days**	**2d**	**Mon 2/2/26**	**Tue 1/13/26**	**14d**	**Thu 2/26/26**	**Wed 2/4/26**
14	Erosion Control | BMPs	3 days	3 days	0d	Mon 2/2/26	Tue 1/13/26	14d	Wed 2/4/26	Thu 1/15/26
15	Demolition & Haul Off - For Bldg Pad	4 days	4 days	0d	Mon 2/9/26	Fri 1/16/26	16d	Thu 2/12/26	Wed 1/21/26
16	Grading | Cut & Fill	5 days	5 days	0d	Fri 2/13/26	Thu 1/22/26	16d	Thu 2/19/26	Wed 1/28/26
17	Bulding Pad Preparation	5 days	5 days	0d	Fri 2/20/26	Thu 1/29/26	16d	Thu 2/26/26	Wed 2/4/26
18	**Site Utilities**	**77 days**	**93 days**	**-16d**	**Fri 2/13/26**	**Thu 1/22/26**	**16d**	**Mon 6/1/26**	**Mon 6/1/26**
19	Re-adjust existing storm	3 days	3 days	0d	Fri 2/13/26	Thu 1/22/26	16d	Tue 2/17/26	Mon 1/26/26
20	Storm Sewer	5 days	5 days	0d	Fri 2/27/26	Thu 2/5/26	16d	Thu 3/5/26	Wed 2/11/26
21	Sanitary Sewer	6 days	6 days	0d	Fri 3/6/26	Thu 2/12/26	16d	Fri 3/13/26	Thu 2/19/26
22	Water Line	6 days	6 days	0d	Mon 3/16/26	Fri 2/20/26	16d	Mon 3/23/26	Fri 2/27/26
23	Utility Approval by AHJ	2 days	2 days	0d	Tue 3/24/26	Mon 3/2/26	16d	Wed 3/25/26	Tue 3/3/26
24	**Fire Tank (By Others)**	**5 days**	**5 days**	**0d**	**Tue 5/26/26**	**Tue 5/26/26**	**0d**	**Mon 6/1/26**	**Mon 6/1/26**
25	Fire Tank Installation	5 days	5 days	0d	Tue 5/26/26	Tue 5/26/26	0d	Mon 6/1/26	Mon 6/1/26
26	**Exterior Improvements**	**66 days**	**66 days**	**0d**	**Tue 3/24/26**	**Mon 3/2/26**	**16d**	**Tue 6/23/26**	**Mon 6/1/26**
27	**Site Paving**	**22 days**	**22 days**	**0d**	**Tue 3/24/26**	**Mon 3/2/26**	**16d**	**Wed 4/22/26**	**Tue 3/31/26**
28	Paving Subgrade Prep	8 days	8 days	0d	Tue 3/24/26	Mon 3/2/26	16d	Thu 4/2/26	Wed 3/11/26
29	Fire Lane Concrete Paving	8 days	8 days	0d	Fri 4/3/26	Thu 3/12/26	16d	Tue 4/14/26	Mon 3/23/26
30	Light Duty Concrete Paving	6 days	6 days	0d	Wed 4/15/26	Tue 3/24/26	16d	Wed 4/22/26	Tue 3/31/26
31	**Detention Pond Work**	**9 days**	**9 days**	**0d**	**Fri 4/3/26**	**Thu 3/12/26**	**16d**	**Wed 4/15/26**	**Tue 3/24/26**
32	Grading | Cut	5 days	5 days	0d	Fri 4/3/26	Thu 3/12/26	16d	Thu 4/9/26	Wed 3/18/26
33	Storm Sewer	4 days	4 days	0d	Fri 4/10/26	Thu 3/19/26	16d	Wed 4/15/26	Tue 3/24/26
34	**Landscape & Irrigation**	**11 days**	**11 days**	**0d**	**Tue 6/2/26**	**Mon 5/11/26**	**16d**	**Tue 6/16/26**	**Mon 5/25/26**
35	Irrigation Installation	6 days	6 days	0d	Tue 6/2/26	Mon 5/11/26	16d	Tue 6/9/26	Mon 5/18/26
36	Landscape Installation	5 days	5 days	0d	Wed 6/10/26	Tue 5/19/26	16d	Tue 6/16/26	Mon 5/25/26
37	**Gates & Fences**	**5 days**	**5 days**	**0d**	**Wed 6/17/26**	**Tue 5/26/26**	**16d**	**Tue 6/23/26**	**Mon 6/1/26**
38	Chain Link Fence	3 days	3 days	0d	Wed 6/17/26	Tue 5/26/26	16d	Fri 6/19/26	Thu 5/28/26
39	Double Swing Gate	2 days	2 days	0d	Mon 6/22/26	Fri 5/29/26	16d	Tue 6/23/26	Mon 6/1/26
40	**Building Work**	**107 days**	**107 days**	**0d**	**Fri 2/27/26**	**Thu 2/5/26**	**16d**	**Mon 7/27/26**	**Fri 7/3/26**
41	**SOG | Foundation**	**12 days**	**12 days**	**0d**	**Fri 2/27/26**	**Thu 2/5/26**	**16d**	**Mon 3/16/26**	**Fri 2/20/26**
42	Form Board	1 day	1 day	0d	Fri 2/27/26	Thu 2/5/26	16d	Fri 2/27/26	Thu 2/5/26
43	Plumbing UG Rough-In	1 day	1 day	0d	Mon 3/2/26	Fri 2/6/26	16d	Mon 3/2/26	Fri 2/6/26
44	Electrical UFER & Service	1 day	1 day	0d	Tue 3/3/26	Mon 2/9/26	16d	Tue 3/3/26	Mon 2/9/26
45	Grade Beam Excavation	3 days	3 days	0d	Wed 3/4/26	Tue 2/10/26	16d	Fri 3/6/26	Thu 2/12/26
46	Set Poly & Termite Control	1 day	1 day	0d	Mon 3/9/26	Fri 2/13/26	16d	Mon 3/9/26	Fri 2/13/26
47	Set Rebar for GB & SOG	2 days	2 days	0d	Tue 3/10/26	Mon 2/16/26	16d	Wed 3/11/26	Tue 2/17/26
48	Pour & Finish SOG	2 days	2 days	0d	Thu 3/12/26	Wed 2/18/26	16d	Fri 3/13/26	Thu 2/19/26

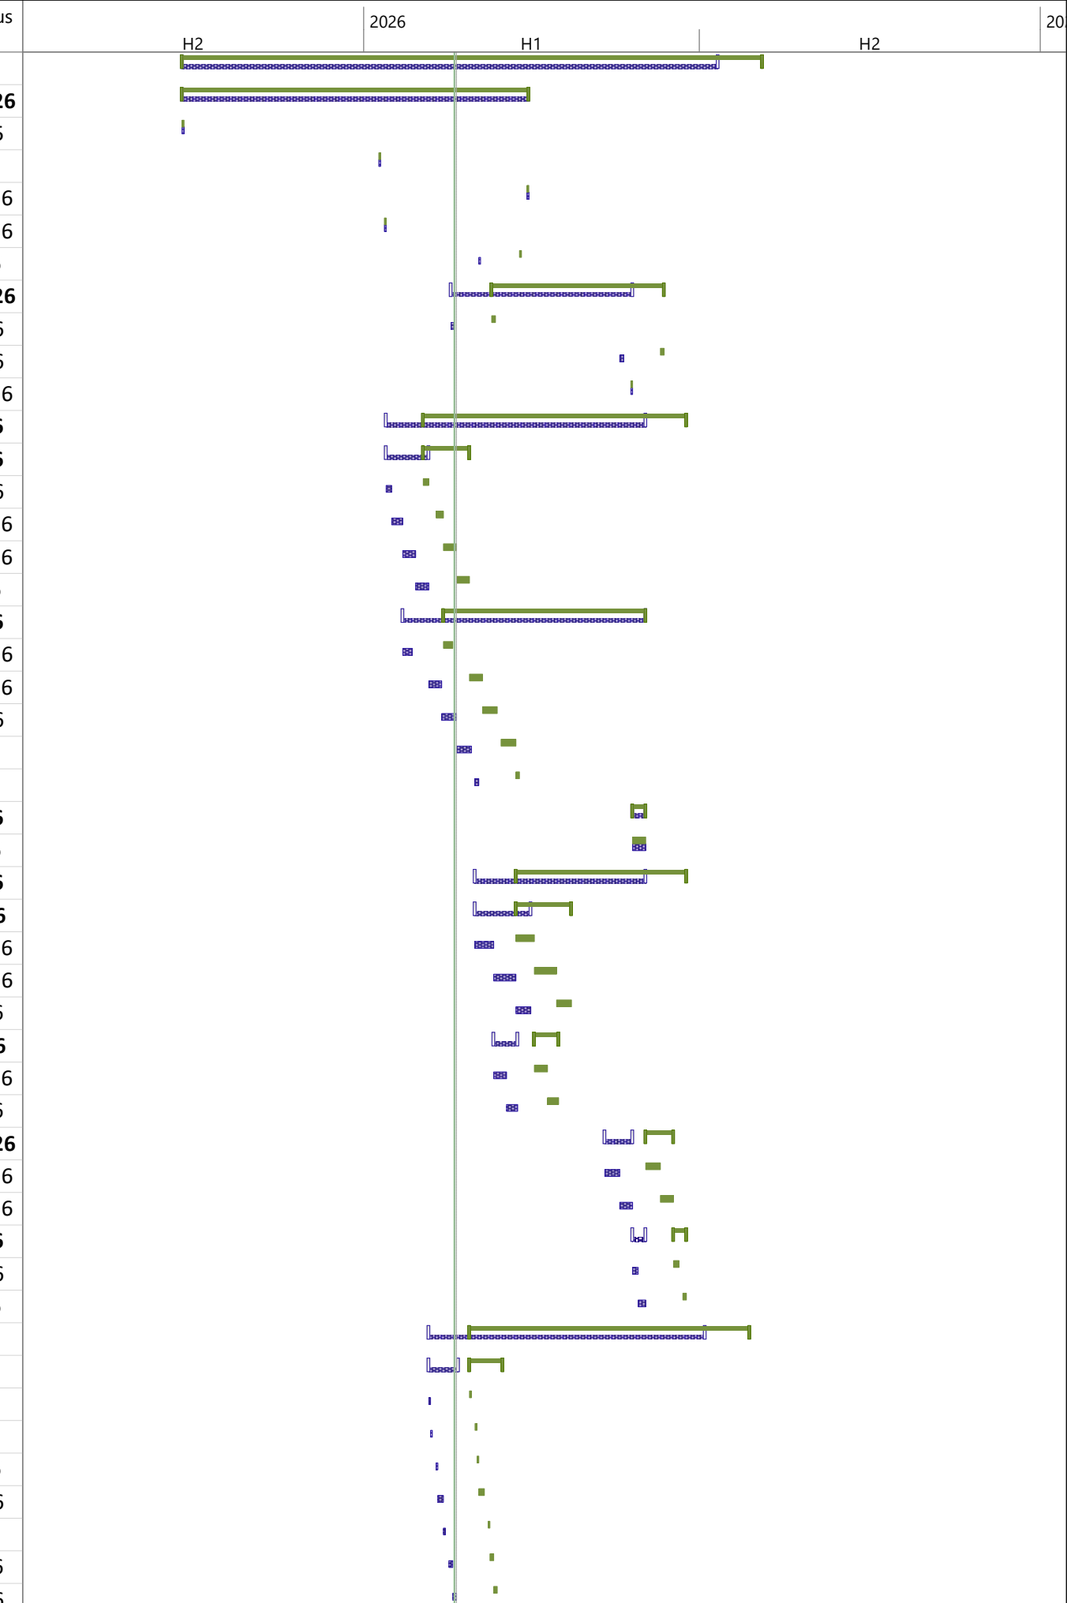
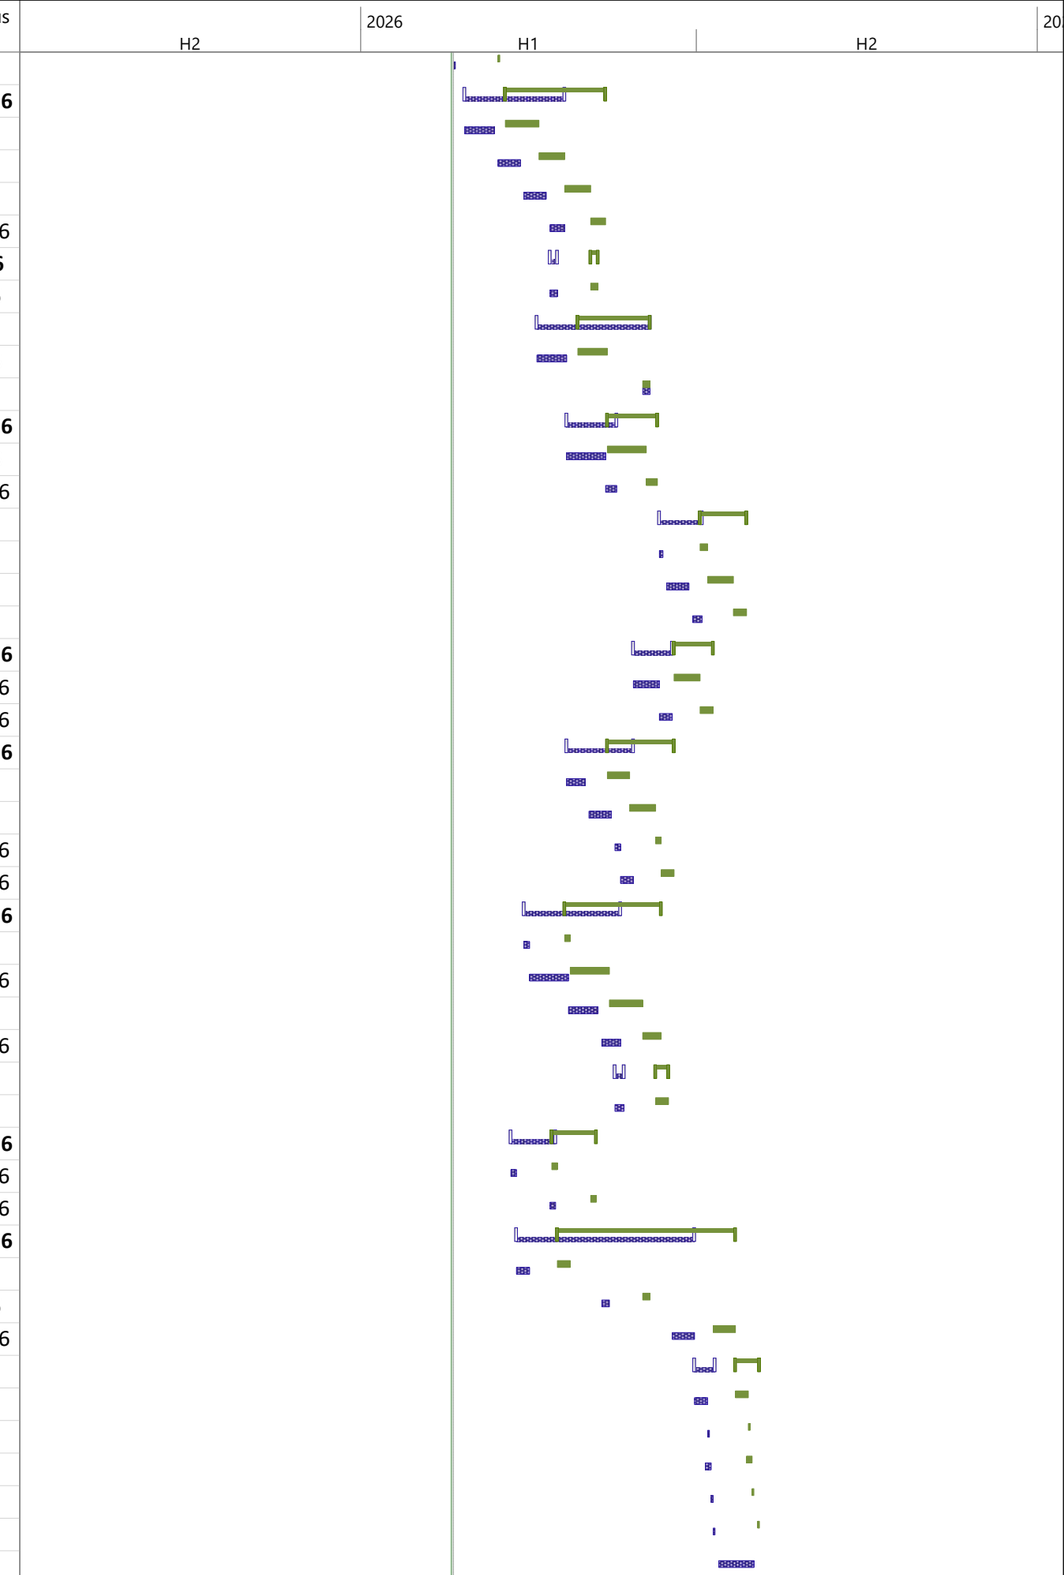
	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous
49	Joint Control Saw Cutting	1 day	1 day	0d	Mon 3/16/26	Fri 2/20/26	16d	Mon 3/16/26	Fri 2/20/26
50	**Steel Structure (Betco/Janus)**	**38 days**	**38 days**	**0d**	**Fri 3/20/26**	**Thu 2/26/26**	**16d**	**Tue 5/12/26**	**Mon 4/20/26**
51	Framing & Interior Partitions	12 days	12 days	0d	Fri 3/20/26	Thu 2/26/26	16d	Mon 4/6/26	Fri 3/13/26
52	Standing Seam Metal Roofing System	10 days	10 days	0d	Tue 4/7/26	Mon 3/16/26	16d	Mon 4/20/26	Fri 3/27/26
53	Exterior Wall Assembly	10 days	10 days	0d	Tue 4/21/26	Mon 3/30/26	16d	Mon 5/4/26	Fri 4/10/26
54	Gutter, Coping & Downpsouts	6 days	6 days	0d	Tue 5/5/26	Mon 4/13/26	16d	Tue 5/12/26	Mon 4/20/26
55	**Masonry**	**4 days**	**4 days**	**0d**	**Tue 5/5/26**	**Mon 4/13/26**	**16d**	**Fri 5/8/26**	**Thu 4/16/26**
56	Fire Pump Room	4 days	4 days	0d	Tue 5/5/26	Mon 4/13/26	16d	Fri 5/8/26	Thu 4/16/26
57	**Fire Sprinkler System**	**29 days**	**45 days**	**-16d**	**Tue 4/28/26**	**Mon 4/6/26**	**16d**	**Fri 6/5/26**	**Fri 6/5/26**
58	Sprinkler Installation	12 days	12 days	0d	Tue 4/28/26	Mon 4/6/26	16d	Wed 5/13/26	Tue 4/21/26
59	Final Adjustment and Testing	4 days	4 days	0d	Tue 6/2/26	Tue 6/2/26	0d	Fri 6/5/26	Fri 6/5/26
60	**Fire Alarm**	**19 days**	**19 days**	**0d**	**Thu 5/14/26**	**Wed 4/22/26**	**16d**	**Tue 6/9/26**	**Mon 5/18/26**
61	Fire Alarm Installation	15 days	15 days	0d	Thu 5/14/26	Wed 4/22/26	16d	Wed 6/3/26	Tue 5/12/26
62	Final Adjustment & Testing	4 days	4 days	0d	Thu 6/4/26	Wed 5/13/26	16d	Tue 6/9/26	Mon 5/18/26
63	**ERCCS - TBD subject to AHJ Review**	**17 days**	**17 days**	**0d**	**Fri 7/3/26**	**Thu 6/11/26**	**16d**	**Mon 7/27/26**	**Fri 7/3/26**
64	ERCCS Testing	2 days	2 days	0d	Fri 7/3/26	Thu 6/11/26	16d	Mon 7/6/26	Fri 6/12/26
65	Submittal and Approval by AHJ	10 days	10 days	0d	Tue 7/7/26	Mon 6/15/26	16d	Mon 7/20/26	Fri 6/26/26
66	ERCCS Installation	5 days	5 days	0d	Tue 7/21/26	Mon 6/29/26	16d	Mon 7/27/26	Fri 7/3/26
67	**Hallway System (Betco/Janus)**	**15 days**	**15 days**	**0d**	**Fri 6/19/26**	**Thu 5/28/26**	**16d**	**Thu 7/9/26**	**Wed 6/17/26**
68	Hallway System & Roll Up Doors	10 days	10 days	0d	Fri 6/19/26	Thu 5/28/26	16d	Thu 7/2/26	Wed 6/10/26
69	Wire Mesh	5 days	5 days	0d	Fri 7/3/26	Thu 6/11/26	16d	Thu 7/9/26	Wed 6/17/26
70	**Mechanical**	**26 days**	**26 days**	**0d**	**Thu 5/14/26**	**Wed 4/22/26**	**16d**	**Thu 6/18/26**	**Wed 5/27/26**
71	Line Sets & Rough In	8 days	8 days	0d	Thu 5/14/26	Wed 4/22/26	16d	Mon 5/25/26	Fri 5/1/26
72	AHUs & Duct Work	10 days	10 days	0d	Tue 5/26/26	Mon 5/4/26	16d	Mon 6/8/26	Fri 5/15/26
73	Dehumidifiers	3 days	3 days	0d	Tue 6/9/26	Mon 5/18/26	16d	Thu 6/11/26	Wed 5/20/26
74	Condensers & Final Connection	5 days	5 days	0d	Fri 6/12/26	Thu 5/21/26	16d	Thu 6/18/26	Wed 5/27/26
75	**Electrical**	**38 days**	**38 days**	**0d**	**Tue 4/21/26**	**Mon 3/30/26**	**16d**	**Thu 6/11/26**	**Wed 5/20/26**
76	Conduit, Wire	3 days	3 days	0d	Tue 4/21/26	Mon 3/30/26	16d	Thu 4/23/26	Wed 4/1/26
77	Light Installation	15 days	15 days	0d	Fri 4/24/26	Thu 4/2/26	16d	Thu 5/14/26	Wed 4/22/26
78	Gear & Riser Room Assembly	12 days	12 days	0d	Fri 5/15/26	Thu 4/23/26	16d	Mon 6/1/26	Fri 5/8/26
79	Wall Packs	8 days	8 days	0d	Tue 6/2/26	Mon 5/11/26	16d	Thu 6/11/26	Wed 5/20/26
80	**Plumbing**	**5 days**	**5 days**	**0d**	**Tue 6/9/26**	**Mon 5/18/26**	**16d**	**Mon 6/15/26**	**Fri 5/22/26**
81	Condensate Drain & Vents	5 days	5 days	0d	Tue 6/9/26	Mon 5/18/26	16d	Mon 6/15/26	Fri 5/22/26
82	**Openings (Betco/Janus)**	**18 days**	**18 days**	**0d**	**Tue 4/14/26**	**Mon 3/23/26**	**16d**	**Thu 5/7/26**	**Wed 4/15/26**
83	HM Frames	3 days	3 days	0d	Tue 4/14/26	Mon 3/23/26	16d	Thu 4/16/26	Wed 3/25/26
84	HM Doors & Hardware	3 days	3 days	0d	Tue 5/5/26	Mon 4/13/26	16d	Thu 5/7/26	Wed 4/15/26
85	**Finish-Out**	**68 days**	**68 days**	**0d**	**Fri 4/17/26**	**Thu 3/26/26**	**16d**	**Tue 7/21/26**	**Mon 6/29/26**
86	Light Gauge Framing | Electrical, Riser	5 days	5 days	0d	Fri 4/17/26	Thu 3/26/26	16d	Thu 4/23/26	Wed 4/1/26
87	Drywall Assembly	4 days	4 days	0d	Tue 6/2/26	Mon 5/11/26	16d	Fri 6/5/26	Thu 5/14/26
88	Seal Concrete in Corridors	8 days	8 days	0d	Fri 7/10/26	Thu 6/18/26	16d	Tue 7/21/26	Mon 6/29/26
89	**Post-Construction**	**9 days**	**9 days**	**0d**	**Wed 7/22/26**	**Tue 6/30/26**	**16d**	**Mon 8/3/26**	**Fri 7/10/26**
90	Final Clean-Up	5 days	5 days	0d	Wed 7/22/26	Tue 6/30/26	16d	Tue 7/28/26	Mon 7/6/26
91	Punch List - TBD - Proposed Date	1 day	1 day	0d	Wed 7/29/26	Tue 7/7/26	16d	Wed 7/29/26	Tue 7/7/26
92	Final Inspections	3 days	3 days	0d	Tue 7/28/26	Mon 7/6/26	16d	Thu 7/30/26	Wed 7/8/26
93	CO/TCO	1 day	1 day	0d	Fri 7/31/26	Thu 7/9/26	16d	Fri 7/31/26	Thu 7/9/26
94	Substantial Completion	1 day	1 day	0d	Mon 8/3/26	Fri 7/10/26	16d	Mon 8/3/26	Fri 7/10/26
95	15 Weather Days in Contract		15 days			Mon 7/13/26			Fri 7/31/26
