Public Storage Willis - TX24198

ID	Task Name	Duration	Start	Finish	% Complete
1	**Public Storage Willis - TX 24198**	**223 days**	**Thu 9/25/25**	**Mon 8/3/26**	**2%**
2	**Pre-Construction**	**133 days**	**Thu 9/25/25**	**Mon 3/30/26**	**60%**
3	Contract Signed	1 day	Thu 9/25/25	Thu 9/25/25	100%
4	Building Permit	1 day	Fri 1/9/26	Fri 1/9/26	100%
5	Fire Tank Permit	1 day	Mon 3/30/26	Mon 3/30/26	0%
6	NTP - From PS	1 day	Mon 1/12/26	Mon 1/12/26	100%
7	Approval to go Vertical by AHJ	1 day	Thu 3/26/26	Thu 3/26/26	0%
8	**Procurement**	**67 days**	**Wed 3/11/26**	**Fri 6/12/26**	**0%**
9	Building Structure	2 days	Wed 3/11/26	Fri 3/13/26	0%
10	Hallway System	2 days	Wed 6/10/26	Fri 6/12/26	0%
11	Fire Tank Delivery	1 day	Mon 5/25/26	Mon 5/25/26	0%
12	**Site Work**	**102 days**	**Mon 2/2/26**	**Tue 6/23/26**	**3%**
13	**Earthwork**	**19 days**	**Mon 2/2/26**	**Thu 2/26/26**	**18%**
14	Erosion Control | BMPs	3 days	Mon 2/2/26	Wed 2/4/26	100%
15	Demolition & Haul Off - For Bldg Pad	4 days	Mon 2/9/26	Thu 2/12/26	0%
16	Grading | Cut & Fill	5 days	Fri 2/13/26	Thu 2/19/26	0%
17	Bulding Pad Preparation	5 days	Fri 2/20/26	Thu 2/26/26	0%
18	**Site Utilities**	**77 days**	**Fri 2/13/26**	**Mon 6/1/26**	**0%**
19	Re-adjust existing storm	3 days	Fri 2/13/26	Tue 2/17/26	0%
20	Storm Sewer	5 days	Fri 2/27/26	Thu 3/5/26	0%
21	Sanitary Sewer	6 days	Fri 3/6/26	Fri 3/13/26	0%
22	Water Line	6 days	Mon 3/16/26	Mon 3/23/26	0%
23	Utility Approval by AHJ	2 days	Tue 3/24/26	Wed 3/25/26	0%
24	**Fire Tank (By Others)**	**5 days**	**Tue 5/26/26**	**Mon 6/1/26**	**0%**
25	Fire Tank Installation	5 days	Tue 5/26/26	Mon 6/1/26	0%
26	**Exterior Improvements**	**66 days**	**Tue 3/24/26**	**Tue 6/23/26**	**0%**
27	**Site Paving**	**22 days**	**Tue 3/24/26**	**Wed 4/22/26**	**0%**
28	Paving Subgrade Prep	8 days	Tue 3/24/26	Thu 4/2/26	0%
29	Fire Lane Concrete Paving	8 days	Fri 4/3/26	Tue 4/14/26	0%
30	Light Duty Concrete Paving	6 days	Wed 4/15/26	Wed 4/22/26	0%
31	**Detention Pond Work**	**9 days**	**Fri 4/3/26**	**Wed 4/15/26**	**0%**

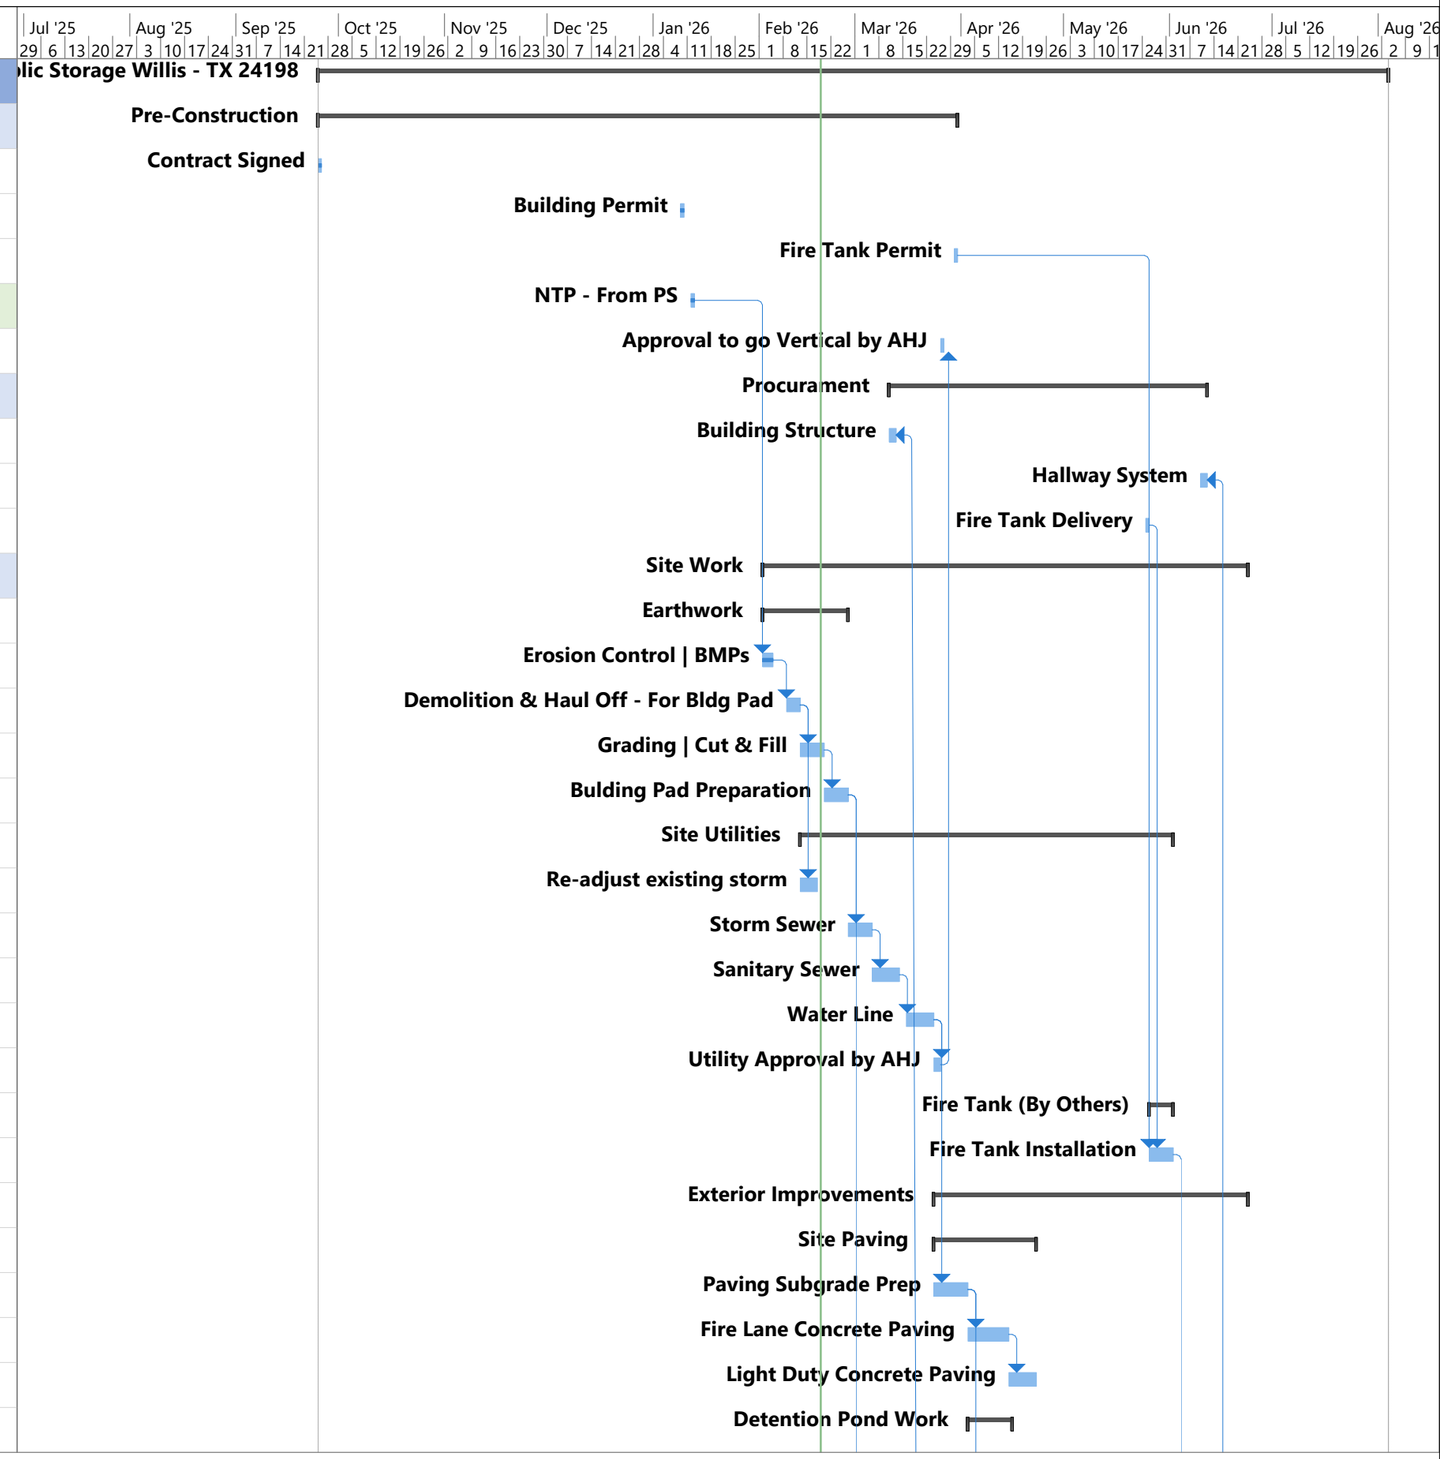

Public Storage Willis - TX24198

ID	Task Name	Duration	Start	Finish	% Complete
32	Grading | Cut	5 days	Fri 4/3/26	Thu 4/9/26	0%
33	Storm Sewer	4 days	Fri 4/10/26	Wed 4/15/26	0%
34	**Landscape & Irrigation**	**11 days**	**Tue 6/2/26**	**Tue 6/16/26**	**0%**
35	Irrigation Installation	6 days	Tue 6/2/26	Tue 6/9/26	0%
36	Landscape Installation	5 days	Wed 6/10/26	Tue 6/16/26	0%
37	**Gates & Fences**	**5 days**	**Wed 6/17/26**	**Tue 6/23/26**	**0%**
38	Chain Link Fence	3 days	Wed 6/17/26	Fri 6/19/26	0%
39	Double Swing Gate	2 days	Mon 6/22/26	Tue 6/23/26	0%
40	**Building Work**	**107 days**	**Fri 2/27/26**	**Mon 7/27/26**	**0%**
41	**SOG | Foundation**	**12 days**	**Fri 2/27/26**	**Mon 3/16/26**	**0%**
42	Form Board	1 day	Fri 2/27/26	Fri 2/27/26	0%
43	Plumbing UG Rough-In	1 day	Mon 3/2/26	Mon 3/2/26	0%
44	Electrical UFER & Service	1 day	Tue 3/3/26	Tue 3/3/26	0%
45	Grade Beam Excavation	3 days	Wed 3/4/26	Fri 3/6/26	0%
46	Set Poly & Termite Control	1 day	Mon 3/9/26	Mon 3/9/26	0%
47	Set Rebar for GB & SOG	2 days	Tue 3/10/26	Wed 3/11/26	0%
48	Pour & Finish SOG	2 days	Thu 3/12/26	Fri 3/13/26	0%
49	Joint Control Saw Cutting	1 day	Mon 3/16/26	Mon 3/16/26	0%
50	**Steel Structure (Betco/Janus)**	**38 days**	**Fri 3/20/26**	**Tue 5/12/26**	**0%**
51	Framing & Interior Partitions	12 days	Fri 3/20/26	Mon 4/6/26	0%
52	Standing Seam Metal Roofing System	10 days	Tue 4/7/26	Mon 4/20/26	0%
53	Exterior Wall Assembly	10 days	Tue 4/21/26	Mon 5/4/26	0%
54	Gutter, Coping & Downpsouts	6 days	Tue 5/5/26	Tue 5/12/26	0%
55	**Masonry**	**4 days**	**Tue 5/5/26**	**Fri 5/8/26**	**0%**
56	Fire Pump Room	4 days	Tue 5/5/26	Fri 5/8/26	0%
57	**Fire Sprinkler System**	**29 days**	**Tue 4/28/26**	**Fri 6/5/26**	**0%**
58	Sprinkler Installation	12 days	Tue 4/28/26	Wed 5/13/26	0%
59	Final Adjustment and Testing	4 days	Tue 6/2/26	Fri 6/5/26	0%
60	**Fire Alarm**	**19 days**	**Thu 5/14/26**	**Tue 6/9/26**	**0%**
61	Fire Alarm Installation	15 days	Thu 5/14/26	Wed 6/3/26	0%
62	Final Adjustment & Testing	4 days	Thu 6/4/26	Tue 6/9/26	0%

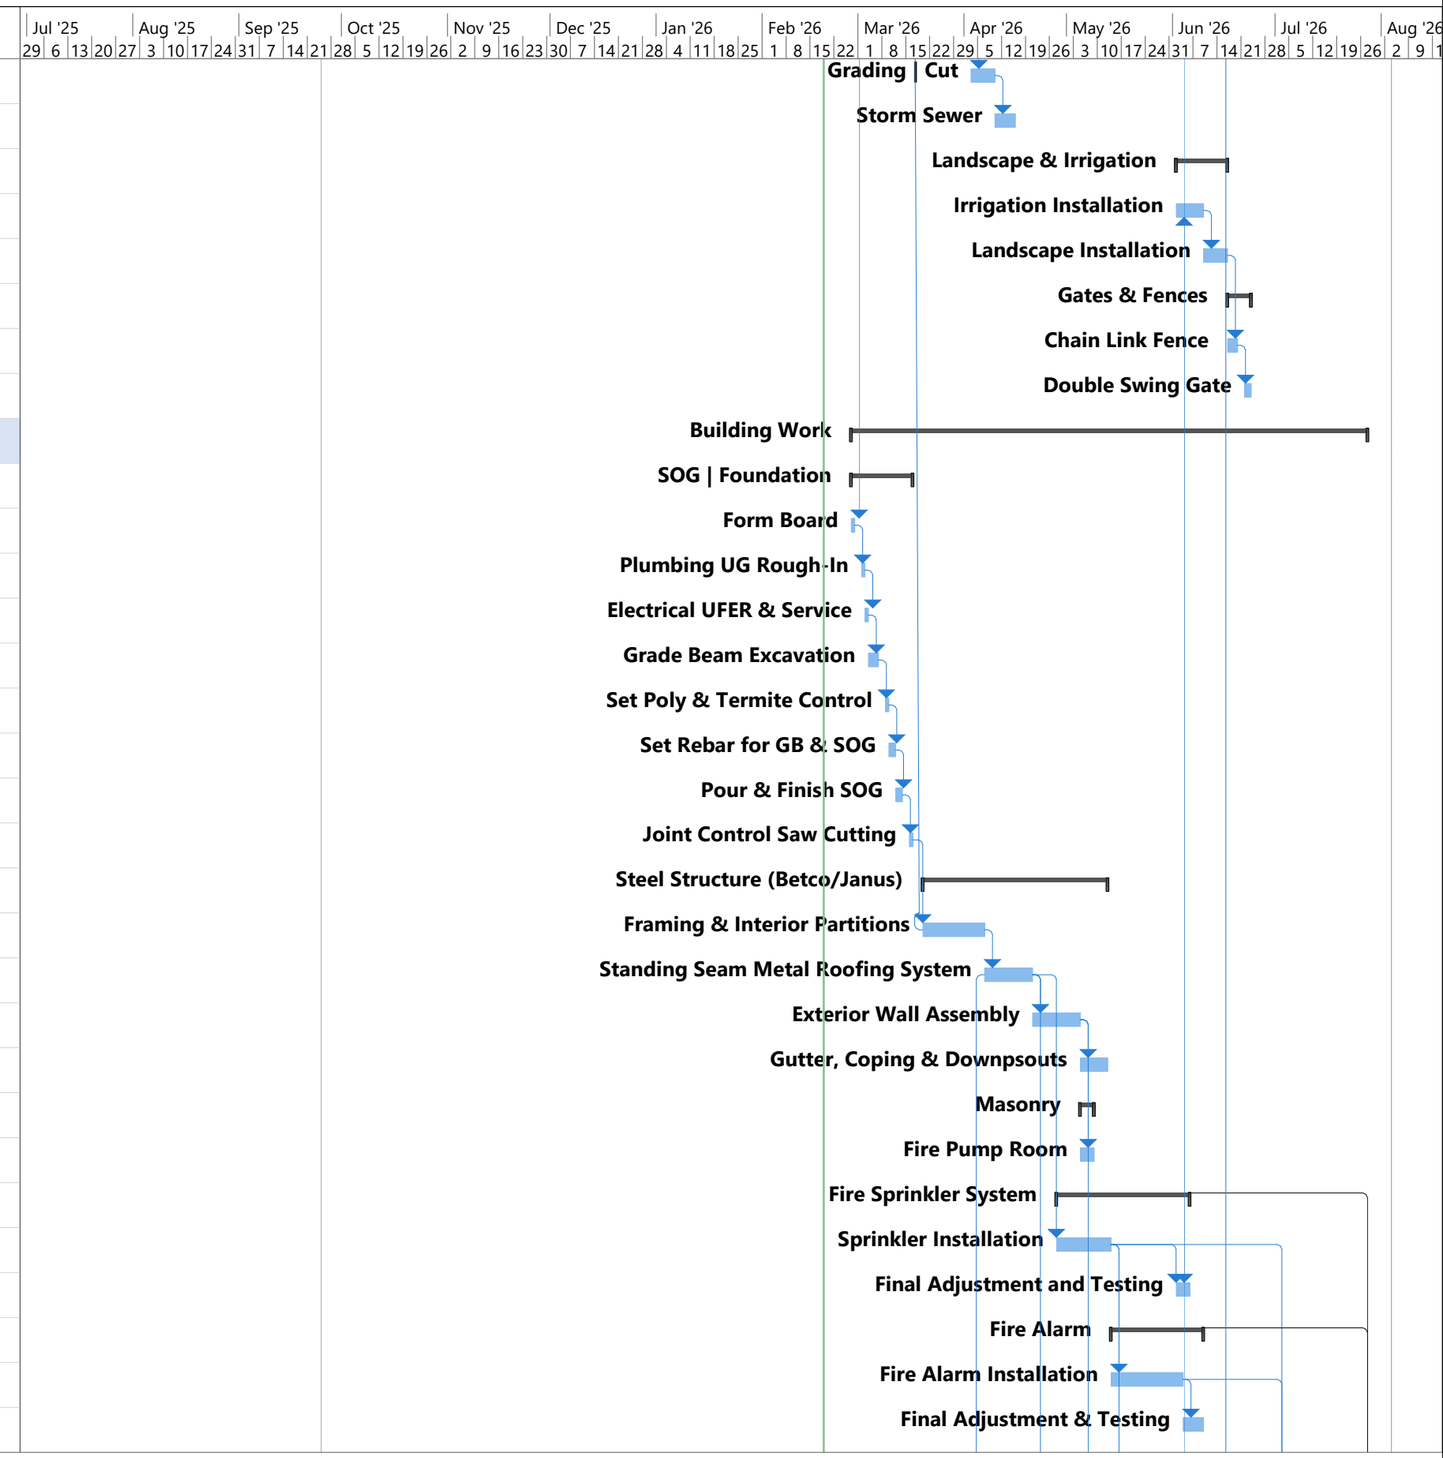

Public Storage Willis - TX24198

ID	Task Name	Duration	Start	Finish	% Complete
63	**ERCCS - TBD subject to AHJ Review**	**17 days**	**Fri 7/3/26**	**Mon 7/27/26**	**0%**
64	ERCCS Testing	2 days	Fri 7/3/26	Mon 7/6/26	0%
65	Submittal and Approval by AHJ	10 days	Tue 7/7/26	Mon 7/20/26	0%
66	ERCCS Installation	5 days	Tue 7/21/26	Mon 7/27/26	0%
67	**Hallway System (Betco/Janus)**	**15 days**	**Fri 6/19/26**	**Thu 7/9/26**	**0%**
68	Hallway System & Roll Up Doors	10 days	Fri 6/19/26	Thu 7/2/26	0%
69	Wire Mesh	5 days	Fri 7/3/26	Thu 7/9/26	0%
70	**Mechanical**	**26 days**	**Thu 5/14/26**	**Thu 6/18/26**	**0%**
71	Line Sets & Rough In	8 days	Thu 5/14/26	Mon 5/25/26	0%
72	AHUs & Duct Work	10 days	Tue 5/26/26	Mon 6/8/26	0%
73	Dehumidifiers	3 days	Tue 6/9/26	Thu 6/11/26	0%
74	Condensers & Final Connection	5 days	Fri 6/12/26	Thu 6/18/26	0%
75	**Electrical**	**38 days**	**Tue 4/21/26**	**Thu 6/11/26**	**0%**
76	Conduit, Wire	3 days	Tue 4/21/26	Thu 4/23/26	0%
77	Light Installation	15 days	Fri 4/24/26	Thu 5/14/26	0%
78	Gear & Riser Room Assembly	12 days	Fri 5/15/26	Mon 6/1/26	0%
79	Wall Packs	8 days	Tue 6/2/26	Thu 6/11/26	0%
80	**Plumbing**	**5 days**	**Tue 6/9/26**	**Mon 6/15/26**	**0%**
81	Condensate Drain & Vents	5 days	Tue 6/9/26	Mon 6/15/26	0%
82	**Openings (Betco/Janus)**	**18 days**	**Tue 4/14/26**	**Thu 5/7/26**	**0%**
83	HM Frames	3 days	Tue 4/14/26	Thu 4/16/26	0%
84	HM Doors & Hardware	3 days	Tue 5/5/26	Thu 5/7/26	0%
85	**Finish-Out**	**68 days**	**Fri 4/17/26**	**Tue 7/21/26**	**0%**
86	Light Gauge Framing | Electrical, Riser	5 days	Fri 4/17/26	Thu 4/23/26	0%
87	Drywall Assembly	4 days	Tue 6/2/26	Fri 6/5/26	0%
88	Seal Concrete in Corridors	8 days	Fri 7/10/26	Tue 7/21/26	0%
89	**Post-Construction**	**9 days**	**Wed 7/22/26**	**Mon 8/3/26**	**0%**
90	Final Clean-Up	5 days	Wed 7/22/26	Tue 7/28/26	0%
91	Punch List - TBD - Proposed Date	1 day	Wed 7/29/26	Wed 7/29/26	0%
92	Final Inspections	3 days	Tue 7/28/26	Thu 7/30/26	0%
93	CO/TCO	1 day	Fri 7/31/26	Fri 7/31/26	0%

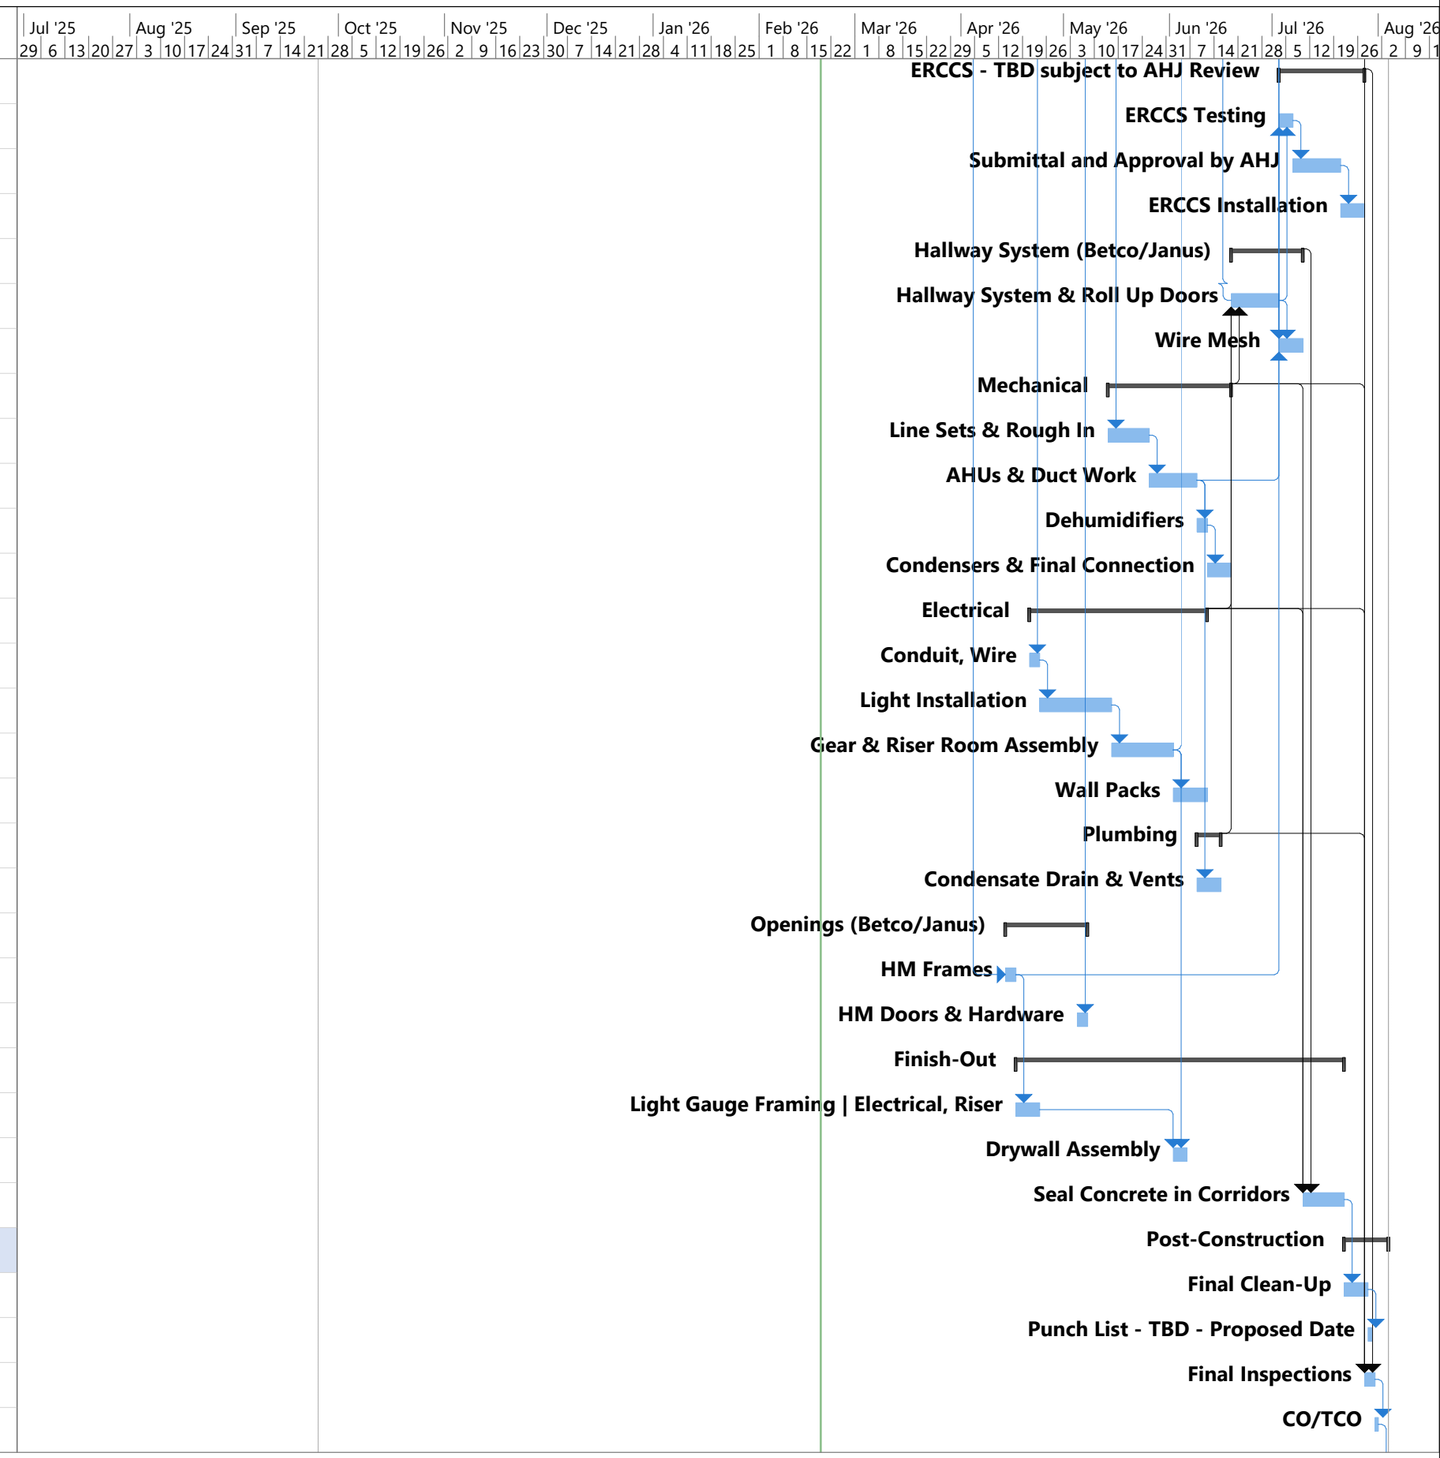

Public Storage Willis - TX24198

ID	Task Name	Duration	Start	Finish	% Complete
94	Substantial Completion	1 day	Mon 8/3/26	Mon 8/3/26	0%
