#	Activity ID	Activity Name	Original Duration	Start	Finish
1	**Public Storage at Marksheffel and Barnes - CUR**				
2	**Project Summary**				
3	**Contract Milestones**				
4	33172	Proposals/Bids Due	0	18-Jul-24 A	
5	33182	Interviews	0	22-Jul-24 A	
6	33192	Award Contract	0	26-Jul-24 A	
7	NTP	Initial Notice to Proceed - Site Not in Compliance Per Contract	0	14-Jan-25 A	
8	SC	Project SC - Before Weather Impacts	0	04-Mar-26	
9	PSC	Project Substantially Complete - After Weather Impacts	0		12-Mar-26*
10	PSC0002	Project Open	0		12-Mar-26
11	**Construction Milestones**				
12	1004	Permit Approved	0	21-Jan-25 A	
13	1005	Start Construction	0		22-Jan-25 A
14	1007	Start of Foundations	0		17-Mar-25 A
15	1008	Start of Elevated Structure	0		07-May-25 A
16	1012	Stair Cores Complete to Roof	0		30-May-25 A
17	1010	Structure Complete	0		07-Jan-26
18	1016	Building Dry In	0		07-Jan-26
19	1015	Exterior Work Complete	0		12-Jan-26
20	1020	DAS Room Completion	5	20-Jan-26	26-Jan-26
21	**Schedule Impacts**				
22	Weather Delays				
23	36286	Weather Delay 3/19/2025	1	19-Mar-25 A	19-Mar-25 A
24	cmu	Weather Delay 5/6/2025	1	06-May-25 A	06-May-25 A
25	A1210	Weather Delay 8/25/2025 - 8/29/2025	5	25-Aug-25 A	29-Aug-25 A
26	1027	Contract Weather Days - 10 Days	7	04-Mar-26	12-Mar-26
27	Project Impacts				
28	Owner Added Scope Impacts				
29	Pond Construction By Owner				
30	35668	Pond Construction Per Owner	40	20-Jan-25 A	05-Mar-25 A
31	35686	Pond Contractor Permit Pulled	1	06-Mar-25 A	06-Mar-25 A
32	35676	North Pond Retaining Wall Completed by Owner	30	07-Mar-25 A	11-Jun-25 A
33	BMP Installation and Certification By Owner				
34	35706	Repair and Install BMPS By Owner (not completed by owner)	25	20-Jan-25 A	12-Feb-25 A
35	CSU Scheduling Impact				
36	35708	CSU Domestic Tap Installation	20	07-Apr-25 A	02-May-25 A
37	Impacts Correspondence				
38	35926	W.E.O. Notification of Delayed Mobilization Due to Weather	1	14-Jan-25 A	14-Jan-25 A
39	35946	Initial NTP From Owner	1	14-Jan-25 A	14-Jan-25 A
40	35956	W.E.O. Notification of Site Condition Impacting start of work	1	22-Jan-25 A	22-Jan-25 A
41	35966	W.E.O. Notification of Continued Site Impacts	1	28-Jan-25 A	28-Jan-25 A
42	35976	W.E.O. Notification of Erosion Control and Pond Work Impacts	1	30-Jan-25 A	30-Jan-25 A
43	Owner Over-Ex and Pad Certification By Owner				
44	35726	Owner Over-Ex Complete and Pad Certification Email	1	16-Jan-25 A	16-Jan-25 A
45	Design Impacts				
46	Bulletin #3				
47	36047	Delivery of Bulletin #3 with South Footer Structural	1	13-Mar-25 A	13-Mar-25 A
48	Structural Design Changes				
49	36056	Revised Rebar Shop Submittal (Added and Revised Footers)	27	14-Mar-25 A	27-Mar-25 A
50	36076	Revised Structural Steel Submittal (Columns and Canopy Connectio	28	14-Mar-25 A	10-Apr-25 A

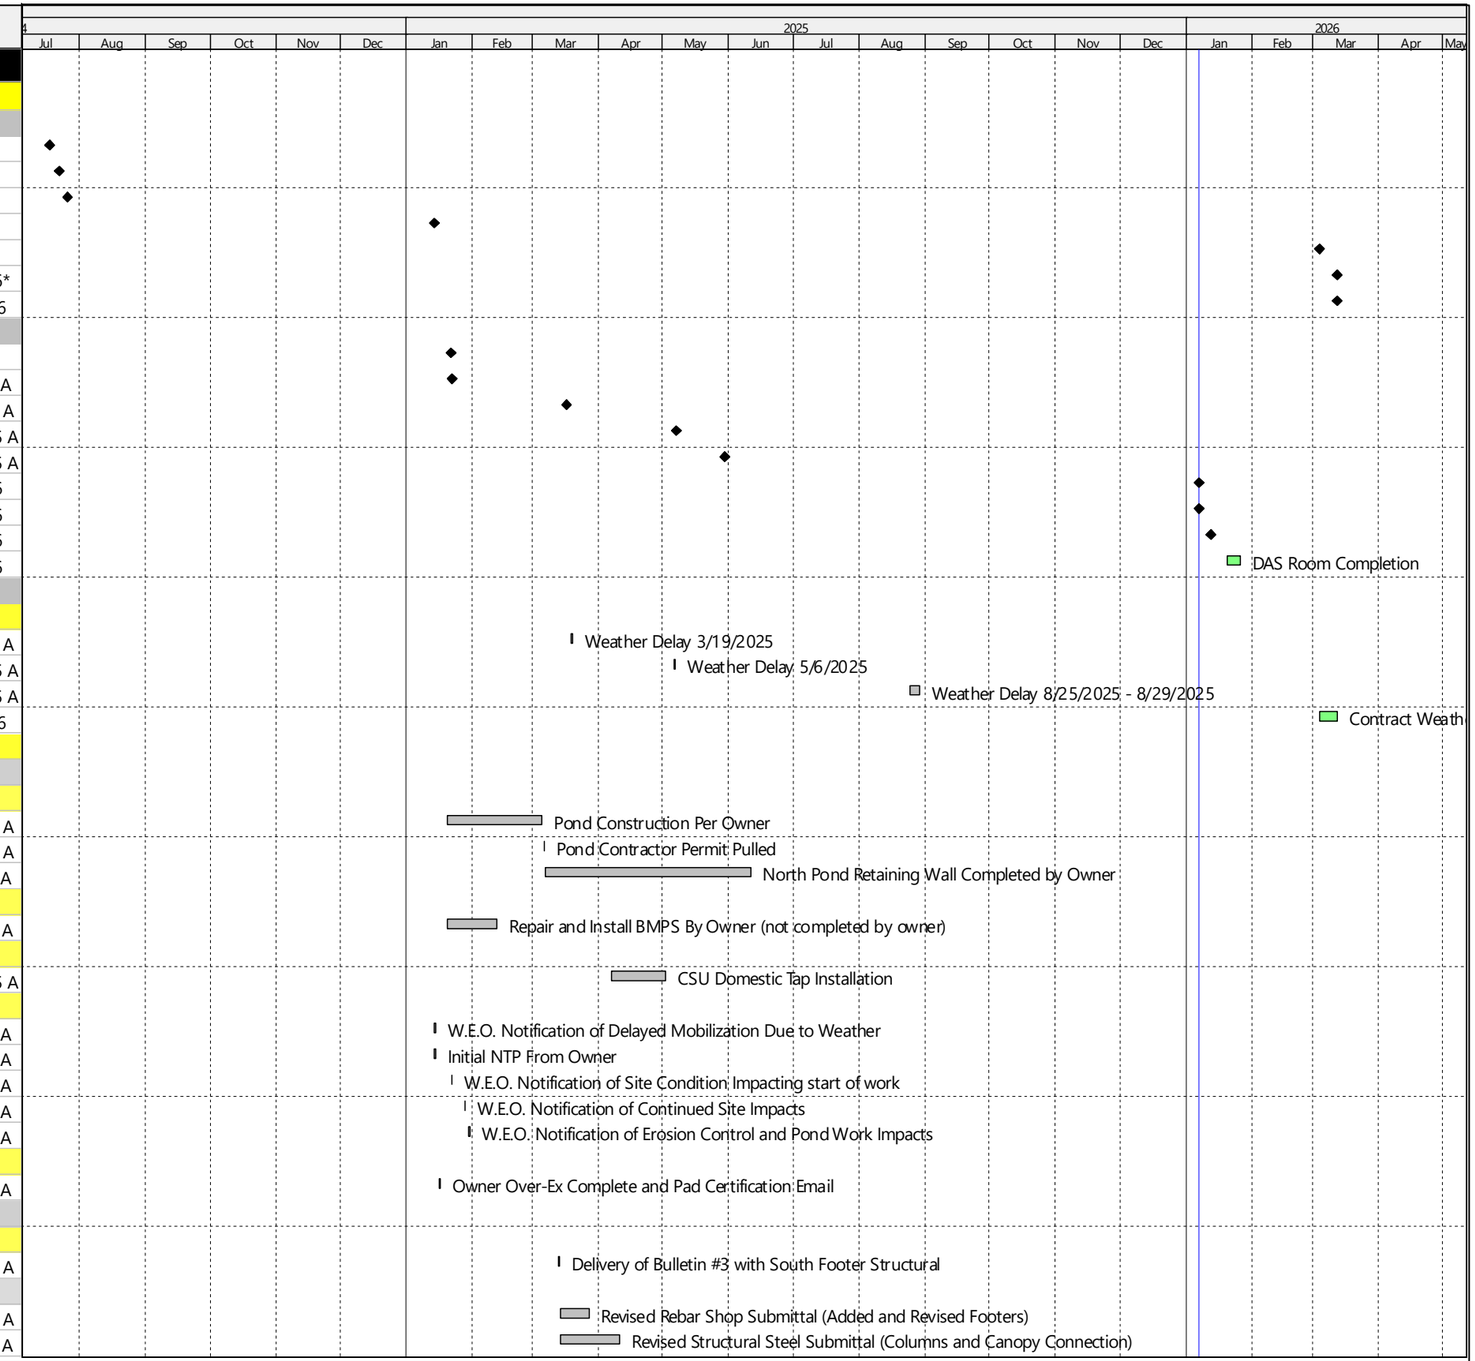

Project: Public Storage at Marksheffel and Barnes - CUR

Print Layout: #DE-03-Client Print View

TASK filter: All Activities

W·E·O'NEIL EST. 1925

#	Activity ID	Activity Name	Original Duration	Start	Finish
51	36057	Design Review Rebar Shop Revision	1	01-Apr-25 A	08-Apr-25 A
52	36058	Structural Steel Embed Procurement	5	11-Apr-25 A	17-Apr-25 A
53	36067	Design Review Steel Submittal	10	11-Apr-25 A	24-Apr-25 A
54		Machine Room			
55		Machine Room Redesign			
56	37156	Delay- Machine Room RFI - Work stopped (includes RBD review)	10	06-Nov-25 A	20-Nov-25 A
57		**Pre-Construciton**			
58		**Procurement**			
59	34952	Contracting of Early Trades	128	26-Jul-24 A	28-Jan-25 A
60	32922	Electric Room MDP	434	16-Aug-24 A	29-Oct-25 A
61	34992	Owner's Enabling Contract Work	96	26-Aug-24 A	13-Jan-25 A
62	32912	Elevator (By Owner)	166	29-Aug-24 A	12-Jan-26
63		**Additional Scope Per Owner - Required For Project Start**			
64		W.E. O'Neil BMP Install and Permitting - Owner Approved			
65	35846	Owner Approval/Direction To Install Stormwater BMP's (OAC Meetir	1	13-Feb-25 A	13-Feb-25 A
66	35856	W.E. O'neil Subcontractor Agreements	7	14-Feb-25 A	24-Feb-25 A
67	35876	BMP Install	3	25-Feb-25 A	27-Feb-25 A
68	35886	CSU Stormwater Permitting	15	25-Feb-25 A	14-Mar-25 A
69	35866	CSU Stormwater Inspection	0		17-Mar-25 A
70		W.E. O'Neil Site Prep - Owner Approved			
71	35906	Owner Approval/Direction to Grade Site Per GEC (Email - 2/3)	1	03-Feb-25 A	03-Feb-25 A
72	35896	Grading per GEC Plan	12	05-Feb-25 A	10-Feb-25 A
73	35986	Cold Weather Delay (High below freezing)	4	11-Feb-25 A	14-Feb-25 A
74	35996	Grading Per GEC Plan Continued	1	17-Feb-25 A	17-Feb-25 A
75	36006	Cold Weather Delay (High Below Freezing	2	18-Feb-25 A	19-Feb-25 A
76	36016	Grading Per GEC Plan Continued	1	20-Feb-25 A	20-Feb-25 A
77		**Construction**			
78		**Mobilization**			
79	32932	Mobilization and Survey	5	22-Jan-25 A	28-Jan-25 A
80		**Site Development**			
81		Site Infrastructure			
82	35273	Install Sewer	4	25-Mar-25 A	04-Apr-25 A
83	33103	Install Fire Connection	5	07-Apr-25 A	11-Apr-25 A
84	33113	Install Fire Connection	3	21-Apr-25 A	23-Apr-25 A
85	33093	Sewer Camera and Final Connection	3	25-Apr-25 A	29-Apr-25 A
86	36736	Discovered unmarked gas, city tap rescheduled	10	05-May-25 A	06-Jun-25 A
87	36746	Install Domestic Water (City Install Domestic Tap - 5/2)	2	06-Jun-25 A	08-Jul-25 A
88	33092	Install Domestic Water (City Install Domestic Tap - 5/2)	1	06-Jun-25 A	06-Jun-25 A
89	33102	Install Storm Main (Pond to STA: 2+42.32)	6	04-Aug-25 A	08-Aug-25 A
90	1050	Install Storm Secondary	5	15-Aug-25 A	19-Sep-25 A
91		Site Civil			
92	1053	Electrical Main Conduit and Transformer Prep (PRECONSTRUCTION)	1	17-Feb-25 A	17-Feb-25 A
93	1055	CSU Electrical Inspection	1	18-Feb-25 A	18-Feb-25 A
94	35433	Electrical Trench Backfill and Recompaction	2	19-Feb-25 A	20-Feb-25 A
95	1054	Transformer Installation (By CSU - Lead Time Scheduling Included)	12	21-Feb-25 A	11-Mar-25 A
96	36666	CSU Meter Install (start of temp power)	5	12-Mar-25 A	28-Mar-25 A
97	35283	Electrical Main to Building	10	02-Dec-25 A	11-Dec-25 A
98		Paving			
99	35363	Survey - Grid Line K, South	1	12-Sep-25 A	12-Sep-25 A
100	35393	Survey - Grid Line K, North	1	12-Sep-25 A	12-Sep-25 A

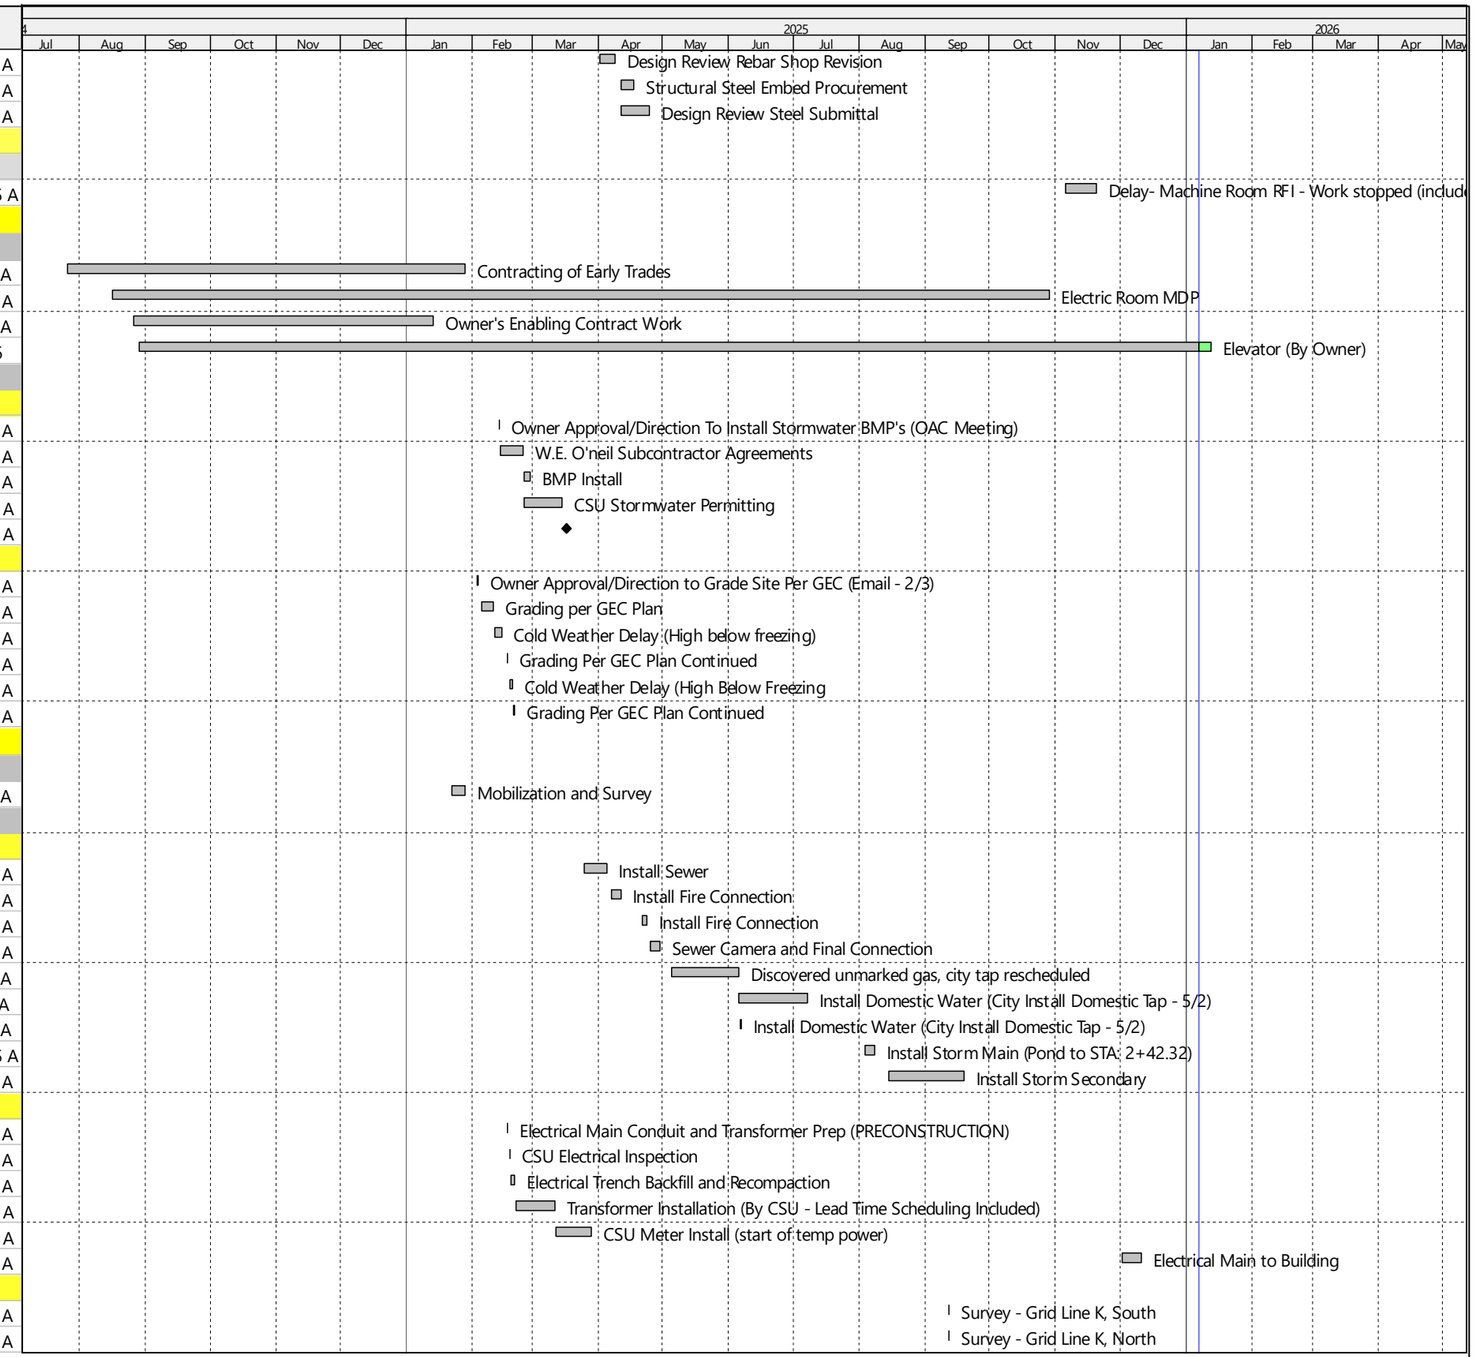

Project: Public Storage at Marksheffel and Barnes - CUR

Print Layout: #DE-03-Client Print View

TASK filter: All Activities

W·E·O'NEIL EST. 1925

#	Activity ID	Activity Name	Original Duration	Start	Finish
101	1180	Irrigation sleeving	2	18-Sep-25 A	18-Sep-25 A
102	35313	Survey - Trash Enclosure	1	19-Sep-25 A	19-Sep-25 A
103	35323	Excavate - Trash Enclosure	1	19-Sep-25 A	19-Sep-25 A
104	35413	FRPS Curb, Gutter - Grid Line K, North	3	22-Sep-25 A	23-Sep-25 A
105	35383	FRPS Curb and gutter - Grid Line K, South	3	23-Sep-25 A	23-Sep-25 A
106	35333	FRPS Footer - Trash Enclosure	3	23-Sep-25 A	24-Sep-25 A
107	35343	FRPS Stem Wall - Trash Enclosure	3	24-Sep-25 A	25-Sep-25 A
108	35373	Finish Grade - Grid Line K, South	3	25-Sep-25 A	10-Oct-25 A
109	35403	Finish Grade - Grid Line K, North	3	25-Sep-25 A	10-Oct-25 A
110	35353	Backfill and compact - Trash Enclosure	1	26-Sep-25 A	26-Sep-25 A
111	35384	FRPS Sidewalk - Grid Line K, South	3	29-Sep-25 A	30-Sep-25 A
112	35414	FRPS Sidewalk and Ballards - Grid Line K, North	2	30-Sep-25 A	01-Oct-25 A
113	35443	FRPS Trash Enclosure Slab	2	07-Oct-25 A	09-Oct-25 A
114	36026	Asphalt Btm and Top	4	13-Oct-25 A	16-Oct-25 A
115	35344	Trash Enclosure Masonry	3	10-Nov-25 A	19-Dec-25 A
116	1130	Trash Enclosure Gates	2	09-Jan-26	12-Jan-26
117	**Foundation**				
118	35012	Excavate Footers	3	17-Mar-25 A	19-Mar-25 A
119	35022	Excavate Footers	3	20-Mar-25 A	24-Mar-25 A
120	35003	FRPS All Grade Beams and Footers	6	24-Mar-25 A	28-Mar-25 A
121	35004	FRPS Stem Walls	10	27-Mar-25 A	11-Apr-25 A
122	35263	Underground Plumbing Excavate, Install and Inspect	5	31-Mar-25 A	04-Apr-25 A
123	35493	Fire Sprinkler Riser Excavate, Install and Inspect (delayed start due tc	2	04-Apr-25 A	07-Apr-25 A
124	35483	Underground Plumbing Backfill and Recompact	2	07-Apr-25 A	08-Apr-25 A
125	35023	Foundation Dampproof and Insulation - East, North and West	4	07-Apr-25 A	10-Apr-25 A
126	35013	FRPS All Grade Beams and Footers	1	09-Apr-25 A	09-Apr-25 A
127	35005	FRPS Stem Walls	3	10-Apr-25 A	15-Apr-25 A
128	35134	Backfill and Ground Prep - SOG Area 1	5	16-Apr-25 A	18-Apr-25 A
129	1067	Foundation Dampproof and Insulation - South Wall	3	16-Apr-25 A	18-Apr-25 A
130	35183	SOG FRPS - Area 1	8	21-Apr-25 A	29-Apr-25 A
131	36706	Backfill and Ground Prep - SOG Area 2	3	24-Apr-25 A	28-Apr-25 A
132	35253	SOG FRPS - Area 2 .SOG FRPS - Area 1	8	30-Apr-25 A	09-May-25 A
133	35135	Backfill and Ground Prep - SOG Area 3	5	12-Jun-25 A	16-Jun-25 A
134	35243	Backfill and Ground Prep - SOG Area 4	2	13-Jun-25 A	17-Jun-25 A
135	36716	SOG FRPS - Area 3	7	16-Jun-25 A	23-Jun-25 A
136	35233	SOG FRPS - Area 4	7	30-Jun-25 A	07-Jul-25 A
137	**Superstructure**				
138	Structural Metal Framing and Deck				
139	Level 2 Deck (level 1 Walls)				
140	L2 A1				
141	33283	Erect Frame and Decking - L2 A1 (moblize 2 days prior with material	7	13-May-25 A	23-May-25 A
142	A1000	Erect Frame and Decking - L2 A1	5	15-May-25 A	23-May-25 A
143	L2 A2				
144	33492	Erect Frame and Decking - L2 A2	7	13-May-25 A	05-Jun-25 A
145	A1010	Erect Frame and Decking - L2 A2	5	27-May-25 A	04-Jun-25 A
146	36796	Stop Work - Steel Submit Review and Fabrication	7	05-Jun-25 A	26-Jun-25 A
147	36166	Resume - Erect Frame and Decking - L2 A2	1	26-Jun-25 A	26-Jun-25 A
148	L2 A3				
149	36096	Erect Frame and Decking - L2 A3	4	26-Jun-25 A	07-Jul-25 A
150	L2 A4				

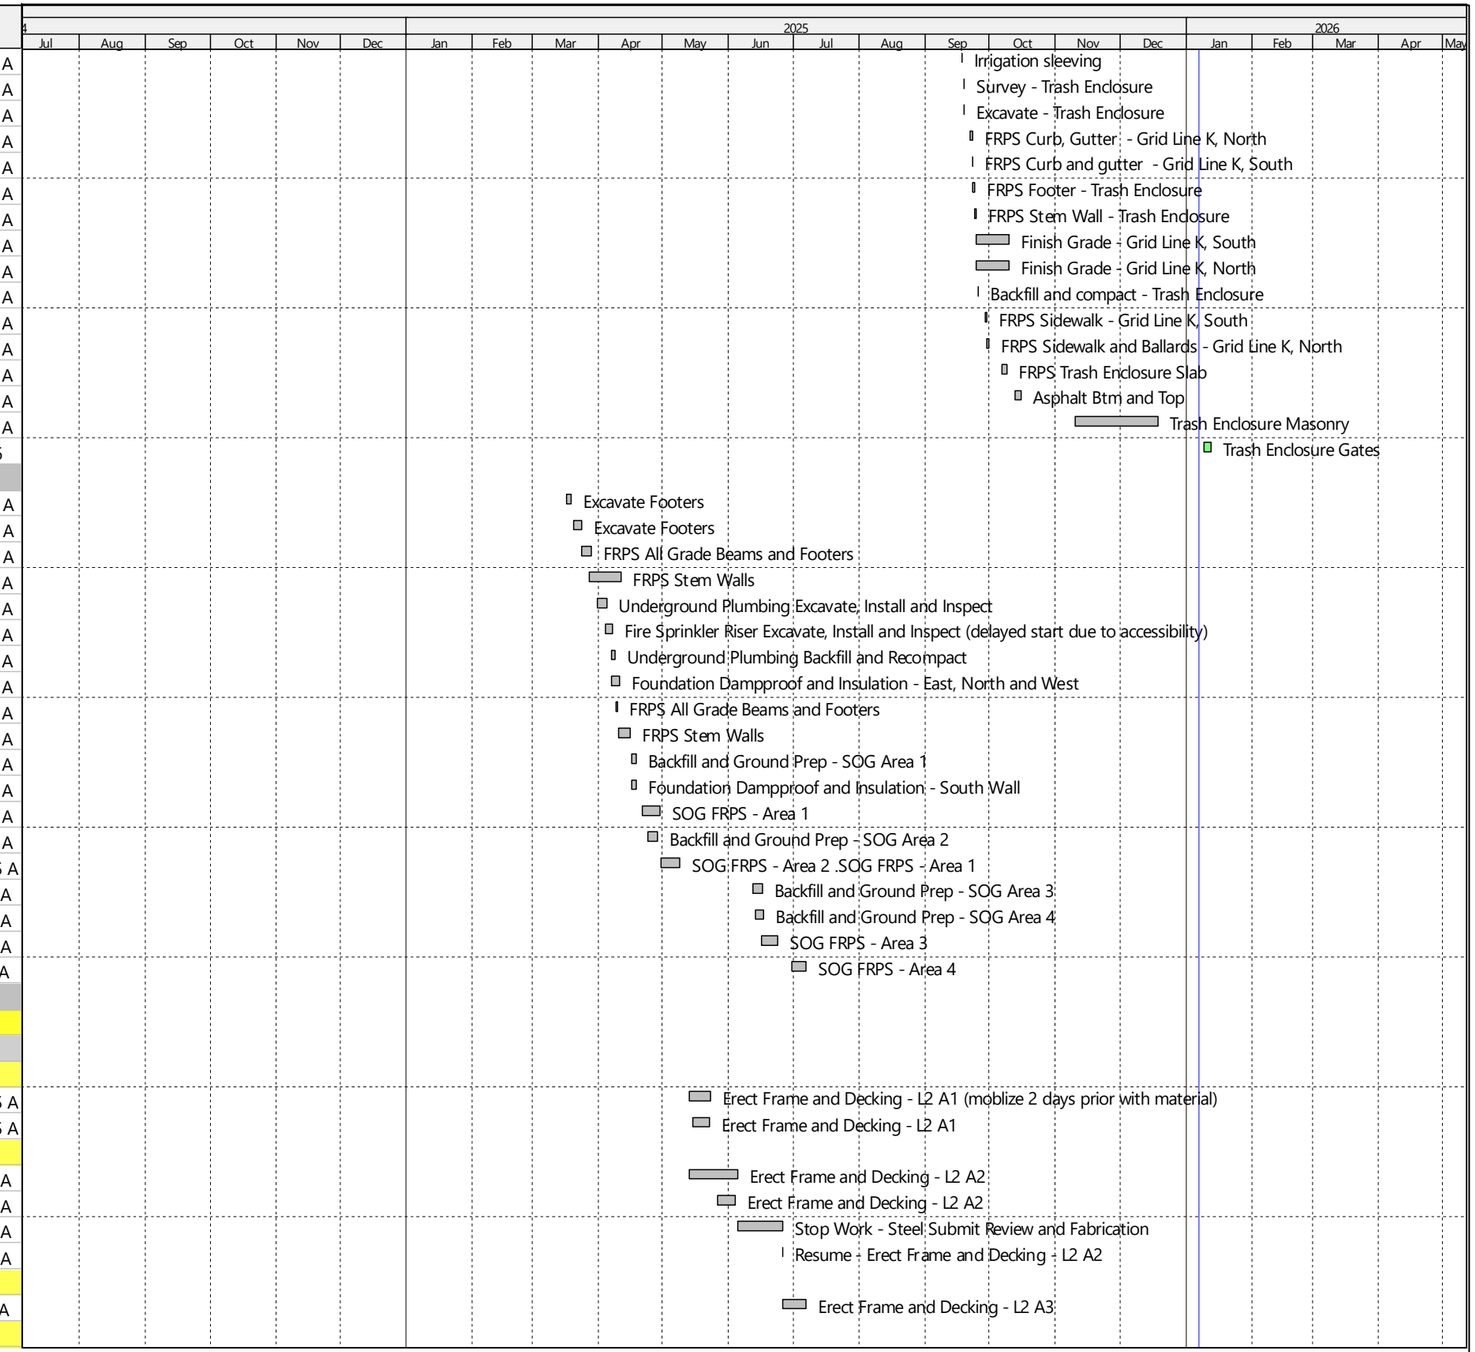

Project: Public Storage at Marksheffel and Barnes - CUR

Print Layout: #DE-03-Client Print View

TASK filter: All Activities

W·E·O'NEIL EST. 1925

#	Activity ID	Activity Name	Original Duration	Start	Finish
151	36756	Erect Frame and Decking - L2 A4	4	08-Jul-25 A	21-Jul-25 A
152		Level 2 Concrete			
153		Pour 1 (Gridline A-J)			
154	A1020	WWF and Pour Prep	2	11-Jul-25 A	11-Jul-25 A
155	A1040	Form, Pour, Strip	2	14-Jul-25 A	15-Jul-25 A
156		Pour 2 (Gridline J-Q)			
157	A1050	WWF and Pour Prep	2	14-Jul-25 A	15-Jul-25 A
158	A1070	Form, Pour, Strip	2	18-Jul-25 A	21-Jul-25 A
159		Pour 3 (Gridline Q-U)			
160	A1080	WWF and Pour Prep	2	21-Jul-25 A	21-Jul-25 A
161	A1100	Form, Pour, Strip	2	22-Jul-25 A	23-Jul-25 A
162		Level 3 Deck (Level 2 Walls)			
163		L3 A1			
164	33233	Erect Frame and Decking - L3 A1	7	15-Jul-25 A	24-Jul-25 A
165		L3 A2			
166	33562	Erect Frame and Decking - L3 A2	7	21-Jul-25 A	25-Jul-25 A
167		L3 A3			
168	36176	Erect Frame and Decking - L3 A3	5	25-Jul-25 A	30-Jul-25 A
169		Level 3 Concrete			
170		Pour 1 (Gridline A-J)			
171	A1110	Rebar and Pour Prep	2	31-Jul-25 A	01-Aug-25 A
172	A1130	Form, Pour, Strip	2	04-Aug-25 A	05-Aug-25 A
173		Pour 2 (Gridline J-Q)			
174	A1140	Rebar and Pour Prep	2	06-Aug-25 A	08-Aug-25 A
175	A1160	Form, Pour, Strip	2	11-Aug-25 A	13-Aug-25 A
176		Pour 3 (Gridline Q-U)			
177	A1170	Rebar and Pour Prep	2	13-Aug-25 A	13-Aug-25 A
178	A1190	Form, Pour, Strip	2	14-Aug-25 A	15-Aug-25 A
179		Roof Deck (Level 3 Walls)			
180		Roof Area 1			
181	36376	Erect Walls - RA1	5	08-Aug-25 A	15-Aug-25 A
182	36396	Install Curbs and Roof Supports - RA1	2	28-Aug-25 A	29-Aug-25 A
183	36406	Decking Closure - RA1	2	01-Sep-25 A	03-Sep-25 A
184		Roof Area 2			
185	36326	Erect Walls - RA2	5	15-Aug-25 A	22-Aug-25 A
186	36346	Install Curbs and Roof Supports - RA2	2	28-Aug-25 A	29-Aug-25 A
187	36356	Decking Closure - RA2	2	03-Sep-25 A	05-Sep-25 A
188		Roof Area 3			
189	36426	Erect Walls - RA3	5	18-Aug-25 A	29-Aug-25 A
190	36446	Install Curbs and Roof Supports - RA3	2	29-Aug-25 A	02-Sep-25 A
191	36456	Decking Closure - RA3	2	05-Sep-25 A	08-Sep-25 A
192		CMU Cores			
193	1072	CMU Mobilization	5	07-Apr-25 A	11-Apr-25 A
194	1073	CMU Elevator Core	8	14-Apr-25 A	23-Apr-25 A
195	35143	CMU Stair B (additional grouting - 5 days per Bulletin #3.CMU Stair	13	24-Apr-25 A	23-May-25 A
196	35153	CMU Stair A	17	07-May-25 A	30-May-25 A
197	35144	Steel Stair Install - Stair B	8	19-Jun-25 A	11-Jul-25 A
198	35173	Steel Stair Install - Stair A	8	14-Jul-25 A	17-Jul-25 A
199	35163	Elevator Shaft Hoist beams and Spreader Tubes	3	26-Aug-25 A	03-Sep-25 A
200		**Exterior Skin**			

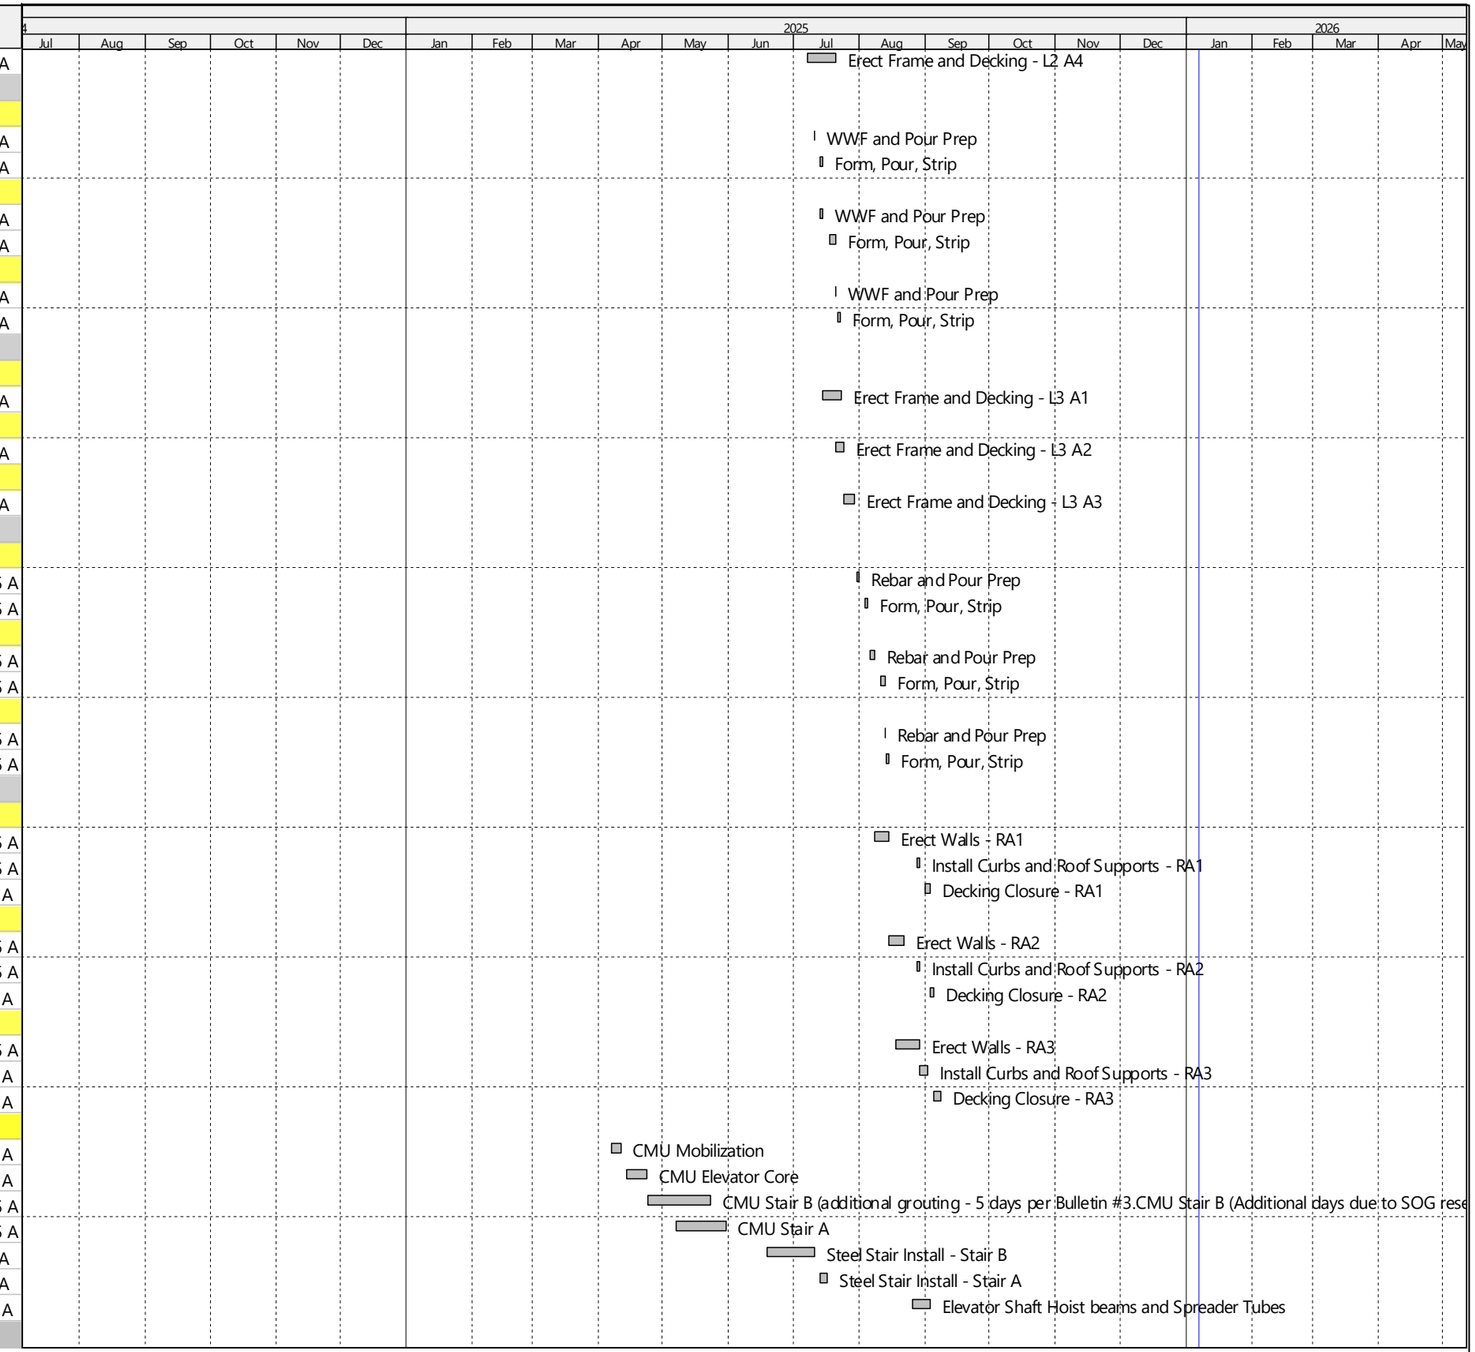

Project: Public Storage at Marksheffel and Barnes - CUR

Print Layout: #DE-03-Client Print View

TASK filter: All Activities

W·E·O'NEIL EST. 1925

#	Activity ID	Activity Name	Original Duration	Start	Finish
201		Roofing			
202	1076	Backing and Blocking (parapet cap, nailers and signage supports)	5	10-Sep-25 A	26-Sep-25 A
203	1075	Roof Install	5	30-Sep-25 A	10-Oct-25 A
204		South Elevation			
205	36526	Sheathing	4	22-Sep-25 A	25-Sep-25 A
206	36556	Exterior Metal Panel	5	22-Sep-25 A	16-Oct-25 A
207	36536	Air/Weather Barrier	2	26-Sep-25 A	01-Oct-25 A
208	36546	Masonry Veneer	15	01-Oct-25 A	10-Oct-25 A
209	36566	EIFS	10	21-Oct-25 A	04-Nov-25 A
210	33425	Storefront Install	3	11-Nov-25 A	14-Jan-26
211	33426	Canopy Install	3	06-Jan-26 A	19-Jan-26
212		West Elevation			
213	36476	Sheathing	4	26-Sep-25 A	03-Oct-25 A
214	36486	Air/Weather Barrier	2	03-Oct-25 A	10-Oct-25 A
215	36496	Masonry Veneer	8	10-Oct-25 A	21-Oct-25 A
216	36506	Exterior Metal Panel	5	22-Oct-25 A	10-Nov-25 A
217	36516	EIFS	10	30-Oct-25 A	20-Nov-25 A
218		North Elevation			
219	36296	Sheathing	4	02-Oct-25 A	10-Oct-25 A
220	36466	Exterior Metal Panel	5	14-Oct-25 A	22-Oct-25 A
221	36306	Air/Weather Barrier and Insulation	3	21-Oct-25 A	23-Oct-25 A
222	33332	Masonry Veneer	8	22-Oct-25 A	30-Oct-25 A
223	34802	EIFS	8	18-Nov-25 A	10-Dec-25 A
224		East Elevation			
225	36626	Exterior Metal Panel	5	02-Oct-25 A	16-Oct-25 A
226	36596	Sheathing	4	06-Oct-25 A	15-Oct-25 A
227	36606	Air/Weather Barrier	2	23-Oct-25 A	24-Oct-25 A
228	36616	Masonry Veneer	8	30-Oct-25 A	07-Nov-25 A
229	36676	Storefront Install	3	11-Nov-25 A	09-Jan-26
230	36636	EIFS	8	20-Nov-25 A	15-Dec-25 A
231	36686	Canopy Install	3	12-Jan-26	14-Jan-26
232		**Rough-In**			
233		Level 1 - Rough-In Work			
234	33692	Fire Suppression - Level 1	15	23-Jul-25 A	30-Oct-25 A
235	33642	Mechanical Rough-In - Level 1	65	02-Sep-25 A	06-Nov-25 A
236	33632	Interior Wall Framing - Level 1	5	10-Oct-25 A	28-Oct-25 A
237	33652	Electrical Rough In - Level 1	29	10-Oct-25 A	22-Dec-25 A
238	33672	Plumbing Rough-In - Level 1	8	15-Oct-25 A	19-Nov-25 A
239	33762	Machine Room Build out	5	03-Nov-25 A	06-Nov-25 A
240	33702	Fire Alarm Rough In - Level 1	5	20-Nov-25 A	22-Dec-25 A
241	33682	Machine Room RFI - Work Commenced	10	21-Nov-25 A	31-Dec-25 A
242		Level 2 - Rough-In Work			
243	33742	Fire Suppression - Level 2	15	01-Aug-25 A	12-Nov-25 A
244	33712	Mechanical Rough-In - Level 2	7	11-Aug-25 A	06-Nov-25 A
245	33732	Plumbing Rough-In - Level 2	5	23-Oct-25 A	11-Nov-25 A
246	33722	Electrical Rough-In - Level 2	15	29-Oct-25 A	22-Dec-25 A
247	33752	Fire Alarm Rough In - Level 2	5	20-Nov-25 A	22-Dec-25 A
248		Level 3 - Rough-In Work			
249	33812	Fire Suppression - Level 3	15	24-Sep-25 A	20-Nov-25 A
250	33802	Mechanical Rough-In - Level 3	7	25-Sep-25 A	13-Nov-25 A

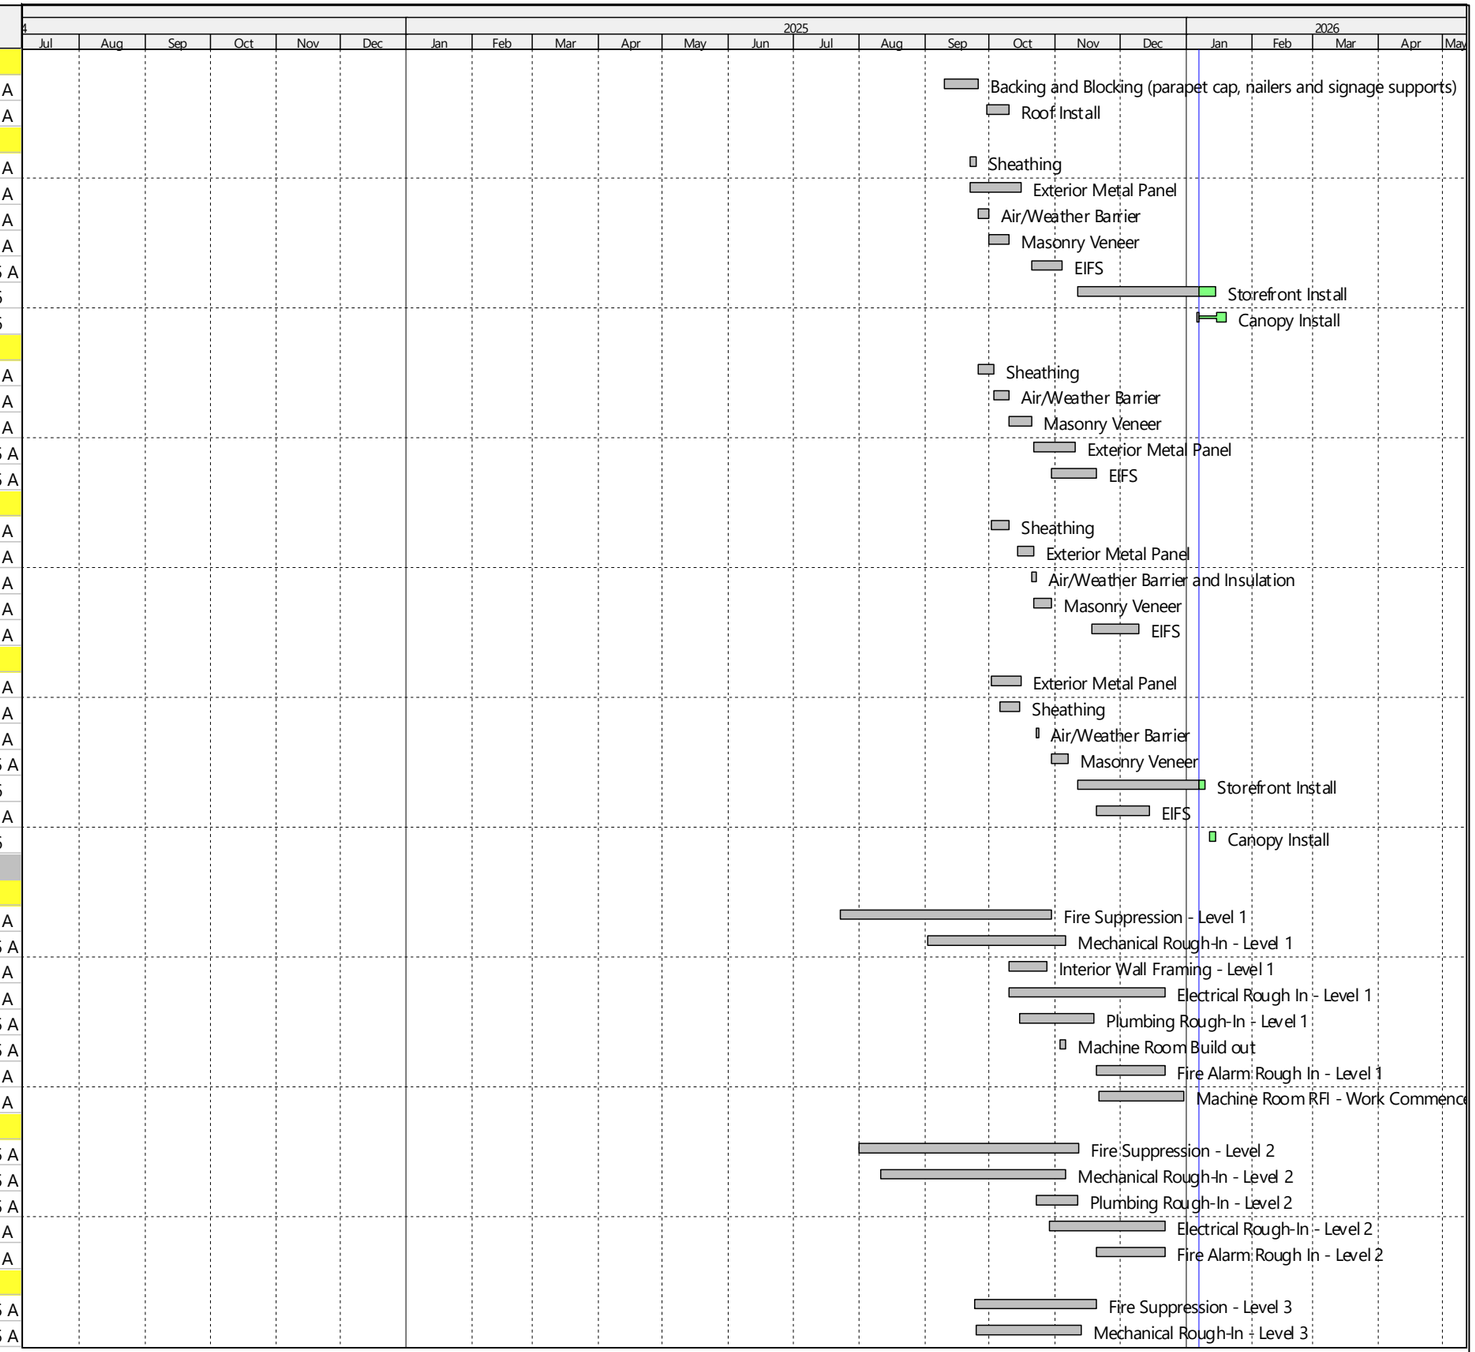

Project: Public Storage at Marksheffel and Barnes - CUR

Print Layout: #DE-03-Client Print View

TASK filter: All Activities

W·E·O'NEIL EST. 1925

#	Activity ID	Activity Name	Original Duration	Start	Finish
251	33792	Plumbing Rough-In - Level 3	5	27-Oct-25 A	01-Dec-25 A
252	33822	Interior Wall Framing - Level 3 RR	5	28-Oct-25 A	30-Oct-25 A
253	33832	Fire Alarm Rough-In - Level 3	5	20-Nov-25 A	22-Dec-25 A
254	33782	Electrical Rough-In - Level 3	21	18-Dec-25 A	16-Jan-26
255	**Janus Scope**				
256	33842	Level 1 - JS	10	20-Oct-25 A	12-Nov-25 A
257	33852	Level 2 - JS	15	13-Nov-25 A	17-Dec-25 A
258	33862	Level 3 - JS	15	15-Dec-25 A	07-Jan-26 A
259	33872	Level 1 - JS Mesh	5	07-Jan-26	13-Jan-26
260	33922	Level 2 - JS Mesh	5	14-Jan-26	20-Jan-26
261	33932	Level 3 - JS Mesh	5	21-Jan-26	27-Jan-26
262	**Elevators**				
263	33882	Elevator Installation	20	13-Jan-26	09-Feb-26
264	33902	1st FLR - Elevator Infill and Lobby Finishes	2	15-Jan-26	16-Jan-26
265	33912	2nd FLR - Elevator Infill and Lobby Finishes	2	19-Jan-26	20-Jan-26
266	33892	3rd FLR - Elevator Infill and Lobby Finishes	2	21-Jan-26	22-Jan-26
267	**Interiors**				
268	Storage Areas				
269	Level 1 - Interiors				
270	34942	Electrical Pulls	5	22-Dec-25 A	22-Dec-25 A
271	34922	Paint Deck	5	23-Dec-25 A	31-Dec-25 A
272	34902	Mechanical Trim	2	29-Dec-25 A	06-Jan-26 A
273	34892	Lighting Trim	5	05-Jan-26 A	30-Jan-26
274	34882	Flooring	2	08-Jan-26	09-Jan-26
275	34912	Plumbing Trim	5	12-Jan-26	16-Jan-26
276	Level 2 -Interiors				
277	34852	Electrical Pulls	5	22-Dec-25 A	22-Dec-25 A
278	34862	Flooring	2	07-Jan-26 A	23-Jan-26
279	34832	Lighting Trim	3	02-Feb-26	04-Feb-26
280	34842	Mechanical Trim	2	16-Feb-26	17-Feb-26
281	Level 3 - Interiors				
282	1092	Electrical Pulls	5	30-Dec-25 A	23-Jan-26
283	1083	Flooring	2	28-Jan-26	29-Jan-26
284	1084	Lighting Trim	3	05-Feb-26	09-Feb-26
285	1085	Mechanical Trim	2	18-Feb-26	19-Feb-26
286	Level 3 Restrooms				
287	37036	Drywall - RR	13	16-Dec-25 A	06-Jan-26 A
288	37006	Doors & Hardware - RR	2	19-Dec-25 A	08-Jan-26
289	36946	Flooring - RR	1	07-Jan-26	07-Jan-26
290	36956	Prime & Paint 1st Coat - RR	2	09-Jan-26	12-Jan-26
291	36976	Light Fixtures - RR	2	13-Jan-26	14-Jan-26
292	37026	Mechanical Trim Out - RR	3	13-Jan-26	15-Jan-26
293	37016	Electrical Trim Out - RR	2	15-Jan-26	16-Jan-26
294	36986	Plumbing Trim Out - RR	2	19-Jan-26	20-Jan-26
295	36996	Final Coat Paint - RR	1	21-Jan-26	21-Jan-26
296	36966	Install Appliances - RR	2	22-Jan-26	23-Jan-26
297	Level 1 Office				
298	1096	Flooring - Office	2	01-Dec-25 A	04-Dec-25 A
299	34932	Drywall - Office	10	10-Dec-25 A	19-Dec-25 A
300	1106	Doors & Hardware - Office	2	19-Dec-25 A	08-Jan-26

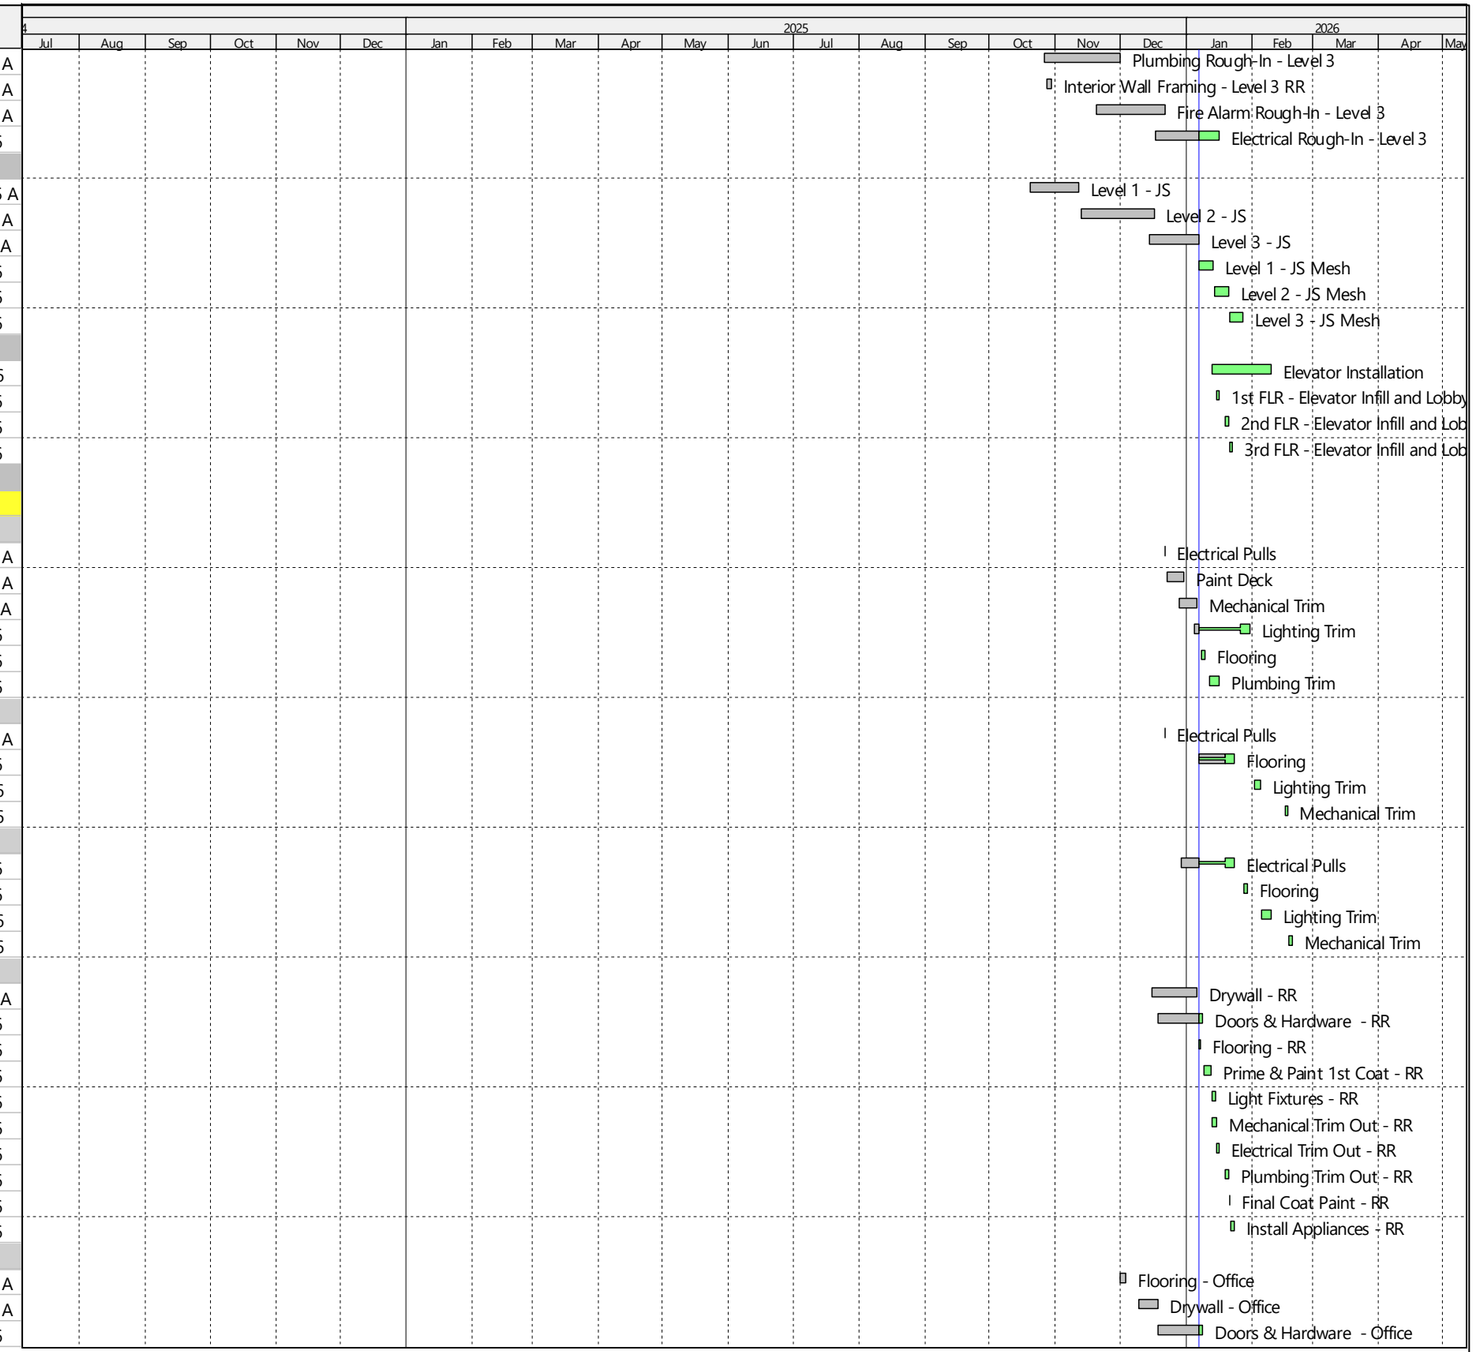

Project: Public Storage at Marksheffel and Barnes - CUR

Print Layout: #DE-03-Client Print View

TASK filter: All Activities

W·E·O'NEIL EST. 1925

#	Activity ID	Activity Name	Original Duration	Start	Finish
301	1097	Prime & Paint 1st Coat - Office	2	23-Dec-25 A	29-Dec-25 A
302	1107	Final Coat Paint - Office	2	30-Dec-25 A	31-Dec-25 A
303	1095	Millwork - Office	2	02-Jan-26 A	02-Jan-26 A
304	1100	Light Fixtures - Office	2	05-Jan-26 A	08-Jan-26
305	1104	Electrical Trim Out - Office	2	07-Jan-26	08-Jan-26
306	1105	Plumbing Trim Out - Office	2	09-Jan-26	12-Jan-26
307	1099	Install Appliances - Office	1	13-Jan-26	13-Jan-26
308	1103	Mechanical Trim Out - Office	2	26-Jan-26	27-Jan-26
309	Level 1 Restroom				
310	36926	Drywall - RR	8	03-Dec-25 A	12-Dec-25 A
311	36896	Doors & Hardware - RR	2	18-Dec-25 A	08-Jan-26
312	36826	Prime & Paint 1st Coat - RR	2	23-Dec-25 A	29-Dec-25 A
313	36866	Final Coat Paint - RR	1	30-Dec-25 A	31-Dec-25 A
314	36846	Light Fixtures - RR	2	05-Jan-26 A	06-Jan-26 A
315	36906	Electrical Trim Out - RR	2	06-Jan-26 A	08-Jan-26
316	36916	Mechanical Trim Out - RR	2	07-Jan-26	08-Jan-26
317	36856	Plumbing Trim Out - RR	2	09-Jan-26	12-Jan-26
318	36836	Install Appliances - RR	2	13-Jan-26	14-Jan-26
319	36816	Flooring - RR	1	30-Jan-26	30-Jan-26
320	DAS Equipment Room				
321	37136	Drywall	10	10-Dec-25 A	19-Dec-25 A
322	37046	Doors & Hardware	2	18-Dec-25 A	22-Dec-25 A
323	37076	Prime & Paint 1st Coat	2	24-Dec-25 A	26-Dec-25 A
324	37126	Final Coat Paint	1	02-Jan-26 A	05-Jan-26 A
325	37146	Hard lid Ceiling Install	5	09-Jan-26	15-Jan-26
326	37086	Light Fixtures	2	16-Jan-26	19-Jan-26
327	37096	Electrical Trim Out	2	16-Jan-26	19-Jan-26
328	37106	Mechanical Trim Out	2	16-Jan-26	19-Jan-26
329	**Final Sitework**				
330	Hardscapes				
331	1140	Detention Pond Fencing	3	14-Aug-25 A	26-Sep-25 A
332	1129	Sidewalks	5	30-Sep-25 A	19-Nov-25 A
333	1131	Striping and Signage	1	11-Dec-25 A	11-Dec-25 A
334	Landscapes				
335	1179	Irrigation Systems	5	07-Jan-26	13-Jan-26
336	1189	Plantings	5	14-Jan-26	20-Jan-26
337	**Closeout**				
338	1112	Fire Alarm Programing/Testing	5	19-Jan-26	23-Jan-26
339	1114	WEO Overall / Final Punch List Work	5	02-Feb-26	06-Feb-26
340	1115	Develop Owner Punch Lists	5	09-Feb-26	13-Feb-26
341	1111	Commissioning	3	20-Feb-26	24-Feb-26
342	1113	Final Inspections	5	25-Feb-26	03-Mar-26

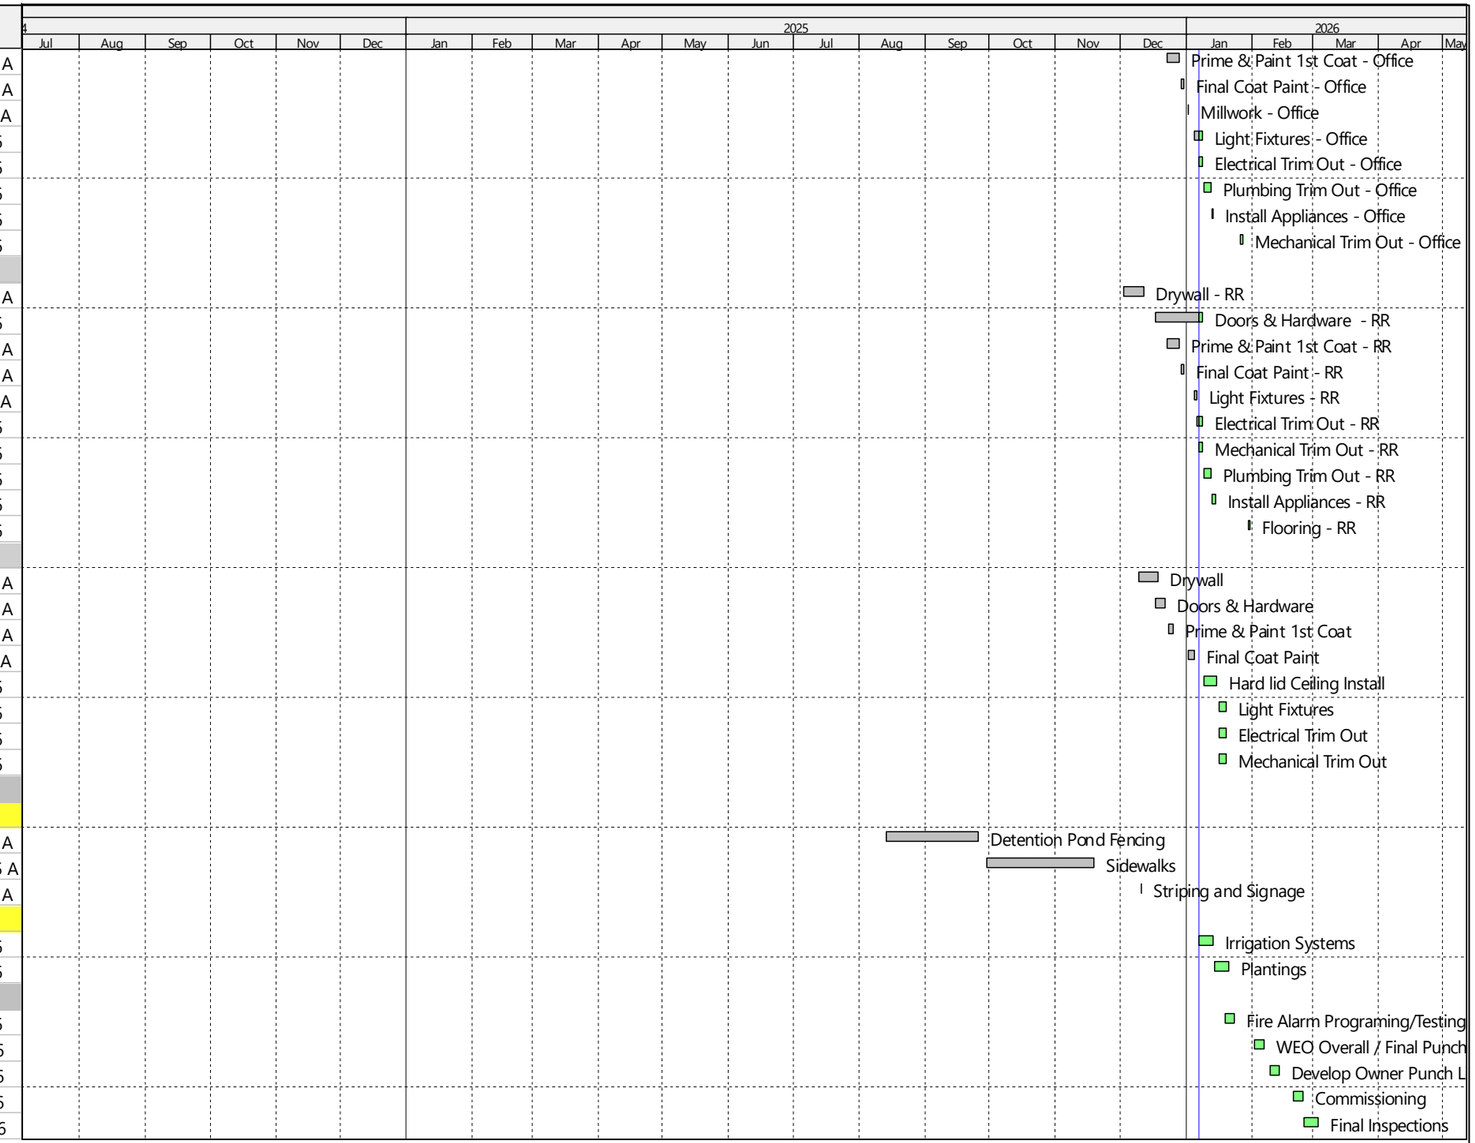

Project: Public Storage at Marksheffel and Barnes - CUR

Print Layout: #DE-03-Client Print View

TASK filter: All Activities

W·E·O'NEIL EST. 1925
