Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

# Public Storage Dashboard

Data Date: 1/7/2026

| Type | Project | Region | Responsible |
|---|---|---|---|
| Construction | Colorado Springs, CO | West Coast | Mark Buckner |

| Baseline Completion Date | Current Completion Date | Schedule Variance | Schedule Compression |
|---|---|---|---|
| 2/6/2026 | 3/12/2026 | -34 Baseline<br>0 Previous | Remaining Work Compression: 29% — Alert |

## Milestone Variance

| Milestone | Baseline Milestone Date | Previous Milestone Date | Current Milestone Date | Current Baseline Variance | Delta from Last Month | Activity Name | Status Indicator |
|---|---|---|---|---|---|---|---|
| NTP | 1/14/2025 | 1/14/2025 | 1/14/2025 | 0 | 0 | Initial Notice to Proceed - Site Not in Compliance Per Contract | On Track – Gaining |
| Foundation Complete | 4/14/2025 | 4/18/2025 | 4/18/2025 | -4 | 0 | Foundation Dampproof and Insulation - South Wall | Delayed – Gaining |
| Hardscape/Landscape Complete | 11/4/2025 | 12/9/2025 | 12/11/2025 | -37 | -2 | Striping and Signage | Delayed – Slipping |
| 1st Floor Finishes Complete | 9/19/2025 | 1/22/2026 | 1/6/2026 | -109 | 16 | Mechanical Trim | Delayed – Gaining |
| Structure Top Out | 7/25/2025 | 12/5/2025 | 1/7/2026 | -166 | -33 | Structure Complete | Delayed – Slipping |
| Weather Tight | 8/22/2025 | 12/5/2025 | 1/7/2026 | -138 | -33 | Building Dry In | Delayed – Slipping |
| Elevator Complete | 4/11/2025 | 12/15/2025 | 1/12/2026 | -276 | -28 | Elevator (By Owner) | Delayed – Slipping |
| 2nd Floor Finishes Complete | 10/10/2025 | 2/5/2026 | 2/17/2026 | -130 | -12 | Mechanical Trim | Delayed – Slipping |
| 3rd Floor Finishes Complete | 11/7/2025 | 2/12/2026 | 2/19/2026 | -104 | -7 | Mechanical Trim | Delayed – Slipping |
| Contract Completion | 2/6/2026 | 3/12/2026 | 3/12/2026 | -34 | 0 | Project Substantially Complete - After Weather Impacts | Delayed – Gaining |

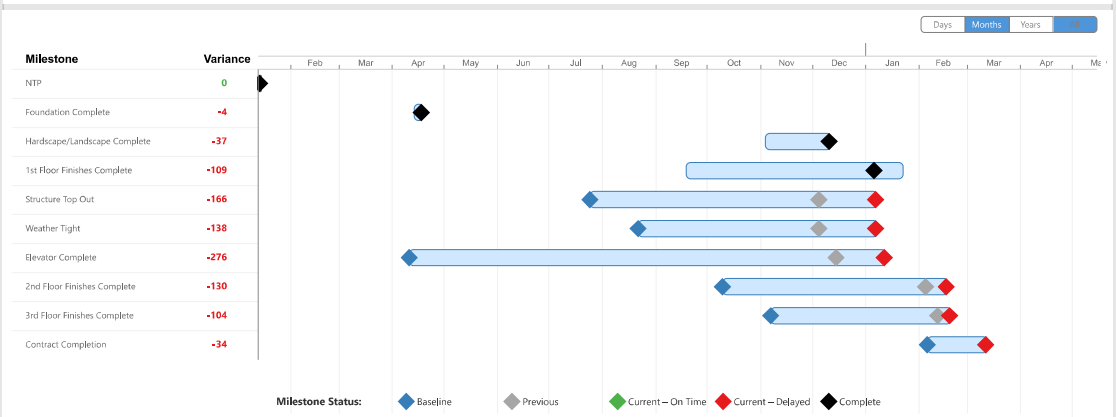


## Baseline Variance

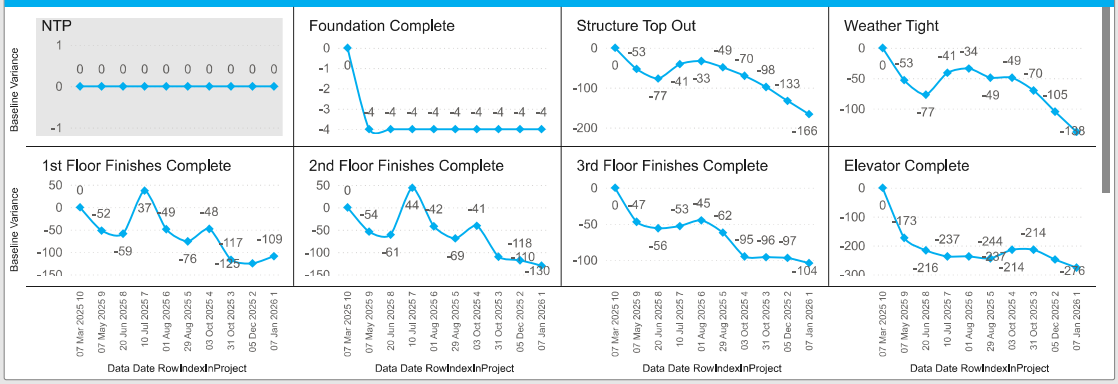


## Schedule Performance Summary

**Summary**

The current state of the project schedule is cause for concern, highlighted by low scores in critical areas such as Schedule Validation, Execution Practices, Work Compression, and Change Management. These factors collectively suggest a lack of control and potential for future delays or quality issues. Priority should be given to addressing the areas in ALERT status to stabilize the project schedule and restore confidence in on-time, on-spec project delivery. This requires immediate action to correct the underlying issues within the project planning and execution phases.

**Schedule Health Score: 79 — Warning**

The Schedule Health score is significantly below industry standards, indicating serious shortcomings in schedule quality. This could lead to inaccurate critical path calculation, reducing the reliability of schedule forecasts. It's recommended to review and rectify the detected scheduling issues urgently.

**Execution Score: 51.00 — Warning**

The execution score is just above the alert threshold but still well below optimal levels, suggesting the project team's schedule adherence and planning could be improved. Enhancing short-term planning and execution practices is advised to improve this metric.

**Remaining Work Compression: 29% — Alert**

There is a high level of compression in the remaining work, far exceeding acceptable limits. This indicates the project team is trying to complete significantly more tasks in shorter durations, which might compromise the quality and feasibility of project deliverables. A review of project milestones and work allocation is necessary to mitigate overcompression.

**Schedule Change Index: 25.00 — Alert**

The schedule has experienced frequent and significant changes, which is a clear indication of planning instability. This can result in unreliable forecasts and a potentially reactive rather than proactive approach to project management. It is recommended to stabilize the schedule through enhanced planning and control measures.

Powered By STELIC INSIGHT • ACTION • IMPACT
