01 All Activities

Activity ID	Activity Name	OD	RD	% Complete	Start	Finish	Total Float
CO25103 - Colorada Springs - Marksheffel & Barnes Rd (solar)(CAN) (CLO) - T		75	37	50.67%	28-Jan-26 A	21-May-26	0
Project Summary		55	27	50.91%	06-Feb-26	07-May-26	10
Contract Milestones		7	7	0%	15-Apr-26	23-Apr-26	20
SC	Project SC - Before Weather Impacts	0	0	0%	15-Apr-26		-54
PSC	Project Substantially Complete - After Weather Impacts	0	0	0%		23-Apr-26*	-54
PSC0002	Project Open	0	0	0%		23-Apr-26	20
Construction Milestones		0	0	0%	01-Apr-26	01-Apr-26	27
1010	Structure Complete	0	0	0%		01-Apr-26	27
1015	Exterior Work Complete	0	0	0%		01-Apr-26	27
1016	Building Dry In	0	0	0%		01-Apr-26	-37
Schedule Impacts		55	17	69.09%	06-Feb-26	07-May-26	0
Weather Delays		7	7	0%	15-Apr-26	23-Apr-26	-54
1027	Contract Weather Days - 10 Days	7	7	0%	15-Apr-26	23-Apr-26	-54
Project Impacts		16	17	0%	06-Feb-26	07-May-26	0
Landscape delay due to frozen ground		16	17	0%	06-Feb-26	07-May-26	0
A1230	Delay - North and West Frozen Ground	16	17	0%	06-Feb-26	07-May-26	0
Construction		72	37	48.61%	28-Jan-26	21-May-26	0
Elevators		11	11	0%	06-Apr-26	20-Apr-26	18
33902	Schindler Fronts/Finshes Level 1	2	2	0%	06-Apr-26	07-Apr-26	18
33912	Schindler Fronts/Finshes Level 2	2	2	0%	08-Apr-26	09-Apr-26	18
33892	Schindler Fronts/Finshes Level 3	2	2	0%	10-Apr-26	13-Apr-26	18
33962	Schindler Adjuster - Final corrections w/ schedule 2 week lead time	11	11	0%	06-Apr-26	20-Apr-26	18
Final Sitework		24	10	58.33%	10-Mar-26	21-May-26	0
Landscapes		24	10	58.33%	10-Mar-26	21-May-26	0
1199	Irrigation Systems North and West	5	5	0%	10-Mar-26	14-May-26	0
1189	Plantings	5	5	0%	15-May-26	21-May-26	0
Closeout		54	19	64.81%	28-Jan-26	27-Apr-26	18
1111	Project Commissioning	5	5	0%	01-Apr-26	07-Apr-26	-54
1112	Fire Alarm Programing/Testing	5	5	0%	28-Jan-26	07-Apr-26	32
1114	WEO Overall / Final Punch List Work	5	5	0%	01-Apr-26	07-Apr-26	27
1113	Final Inspections	5	5	0%	08-Apr-26	14-Apr-26	-54
1115	Develop Owner Punch Lists	5	5	0%	08-Apr-26	14-Apr-26	27
1123	Elevator Commisioning	5	5	0%	14-Apr-26	20-Apr-26	18
1133	Elevator Final Inspections	5	5	0%	21-Apr-26	27-Apr-26	18

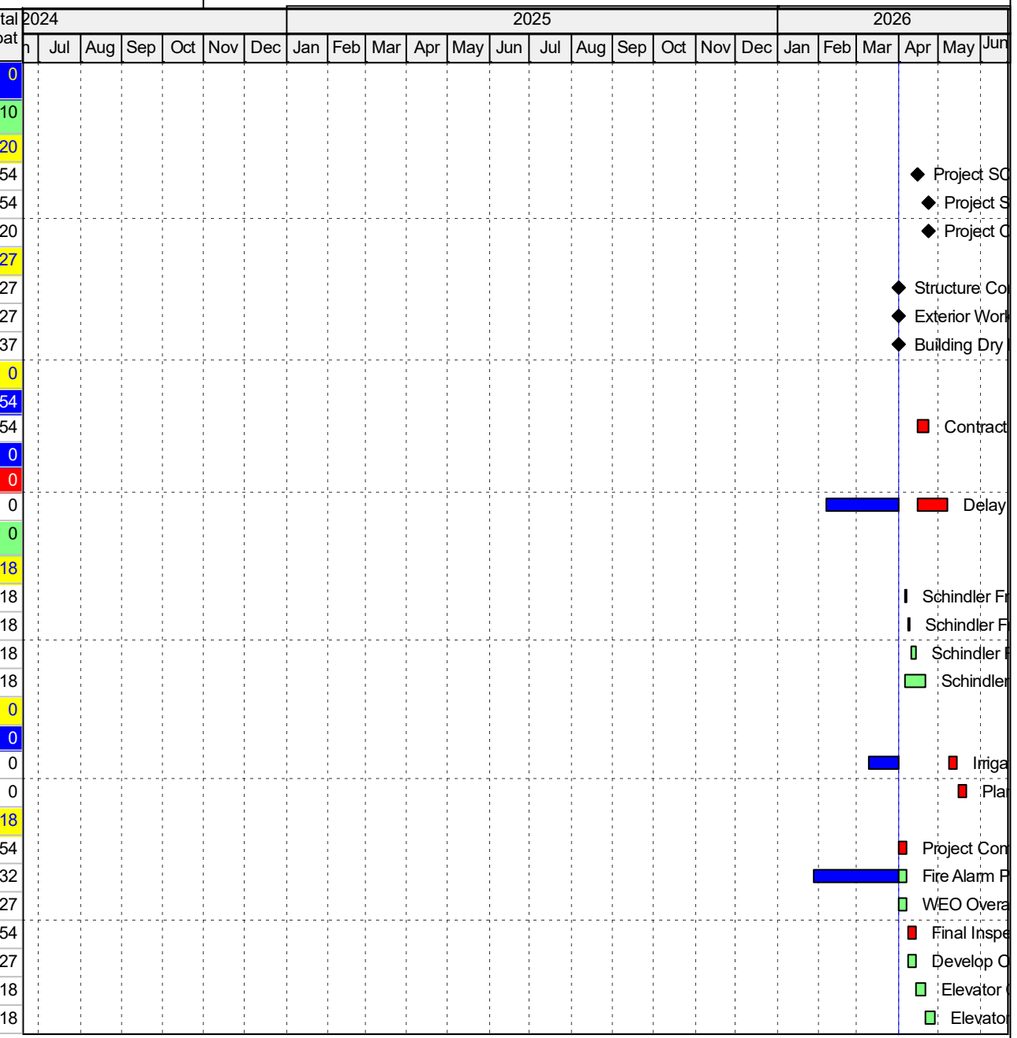

Actual Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work

CO25103 - Colorada Springs - Marksheffel Barnes Rd (solar)(CAN) (CLO) -

Filter: TASK filter: Remaining .
Project ID: CS-UP12 Data Date: 01-Apr-26 Run Date: 02-Apr-26 05:45
