Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
CO25103 - Colorada Springs - Marksheffel & Barnes Rd (solar)(CAN) (		37	0%	28-Jan-26A	21-May-26	0	28-Jan-26	05-Mar-26	-55
Project Summary		27	0%	06-Feb-26A	07-May-26	10	30-Jan-26	02-Mar-26	-48
Contract Milestones		7	0%	15-Apr-26	23-Apr-26	20	20-Feb-26	02-Mar-26	-38
SC	Project SC - Before Weather Impacts	0	100%	15-Apr-26		-54	20-Feb-26		-38
PSC	Project Substantially Complete - After Weather Impacts	0	100%		23-Apr-26*	-54		02-Mar-26	-38
PSC0002	Project Open	0	100%		23-Apr-26	20		02-Mar-26	-38
Construction Milestones		0	0%	01-Apr-26	01-Apr-26	27	30-Jan-26	13-Feb-26	-32
1010	Structure Complete	0	100%		01-Apr-26	27		30-Jan-26	-43
1015	Exterior Work Complete	0	100%		01-Apr-26	27		13-Feb-26	-32
1016	Building Dry In	0	100%		01-Apr-26	-37		30-Jan-26	-43
Schedule Impacts		17	0%	06-Feb-26A	07-May-26	0	20-Feb-26	02-Mar-26	-48
Weather Delays		7	0%	15-Apr-26	23-Apr-26	-54	20-Feb-26	02-Mar-26	-38
1027	Contract Weather Days - 10 Days	7	100%	15-Apr-26	23-Apr-26	-54	20-Feb-26	02-Mar-26	-38
Project Impacts		17	0%	06-Feb-26A	07-May-26	0			
Landscape delay due to frozen ground		17	0%	06-Feb-26A	07-May-26	0			
A1230	Delay - North and West Frozen Ground	17	0%	06-Feb-26A	07-May-26	0			
Construction		37	0%	28-Jan-26A	21-May-26	0	28-Jan-26	05-Mar-26	-55
Elevators		11	0%	06-Apr-26	20-Apr-26	18	04-Feb-26	11-Feb-26	-48
33902	Schindler Fronts/Finshes Level 1	2	100%	06-Apr-26	07-Apr-26	18	04-Feb-26	05-Feb-26	-43
33912	Schindler Fronts/Finshes Level 2	2	100%	08-Apr-26	09-Apr-26	18	06-Feb-26	09-Feb-26	-43
33892	Schindler Fronts/Finshes Level 3	2	100%	10-Apr-26	13-Apr-26	18	10-Feb-26	11-Feb-26	-43
33962	Schindler Adjuster - Final corrections w/ schedule 2 week lead time	11	0%	06-Apr-26	20-Apr-26	18			
Final Sitework		10	0%	10-Mar-26A	21-May-26	0	27-Feb-26	05-Mar-26	-55
Landscapes		10	0%	10-Mar-26A	21-May-26	0	27-Feb-26	05-Mar-26	-55
1199	Irrigation Systems North and West	5	0%	10-Mar-26A	14-May-26	0			
1189	Plantings	5	100%	15-May-26	21-May-26	0	27-Feb-26	05-Mar-26	-55
Closeout		19	0%	28-Jan-26A	27-Apr-26	18	28-Jan-26	27-Feb-26	-41
1111	Project Commissioning	5	100%	01-Apr-26	07-Apr-26	-54	06-Feb-26	12-Feb-26	-38
1112	Fire Alarm Programing/Testing	5	100%	28-Jan-26A	07-Apr-26	32	28-Jan-26	06-Feb-26	-42
1114	WEO Overall / Final Punch List Work	5	100%	01-Apr-26	07-Apr-26	27	16-Feb-26	20-Feb-26	-32
1113	Final Inspections	5	100%	08-Apr-26	14-Apr-26	-54	13-Feb-26	19-Feb-26	-38
1115	Develop Owner Punch Lists	5	100%	08-Apr-26	14-Apr-26	27	23-Feb-26	27-Feb-26	-32
1123	Elevator Commisioning	5	100%	14-Apr-26	20-Apr-26	18	12-Feb-26	18-Feb-26	-43
1133	Elevator Final Inspections	5	100%	21-Apr-26	27-Apr-26	18	19-Feb-26	25-Feb-26	-43

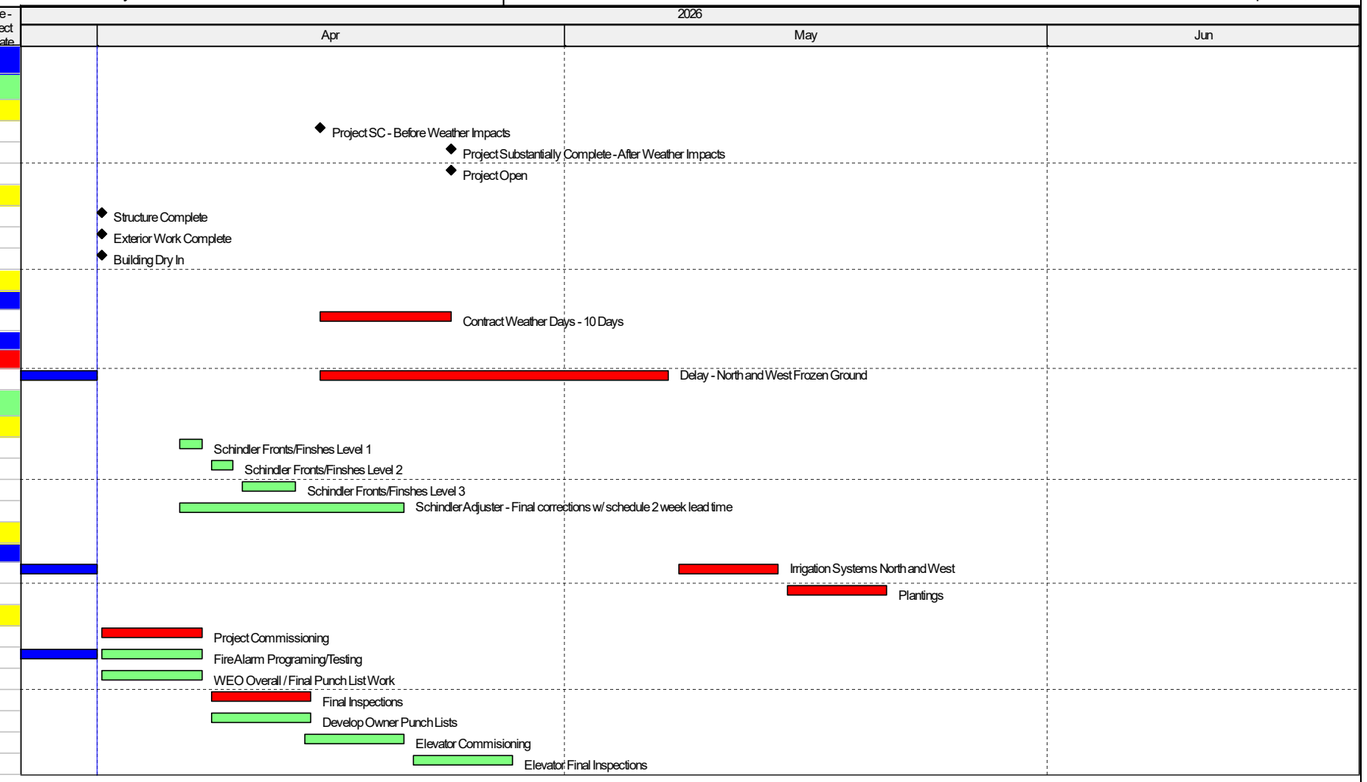

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: Remaining .

© Oracle Corporation
