Activity ID	Activity Name	OD	RD	Start	Finish	TF
Public Storage Fairfax VA - DEC 2025						
Public Storage Fairfax VA						
Milestones						
MIL-1000	Notice to Proceed (05.05.25)	0	0	05-May-25 A		
MIL-1010	Weathertight - Main Building	0	0		16-Apr-26	42
MIL-1020	Permanent Power	0	0	06-May-26		61
MIL-1030	Substantial Completion (08.19.26)	0	0		19-Aug-26*	0
MIL-1040	Final Completion - Main Building	0	0		11-Sep-26*	8
Preconstruction						
Procurement						
PROC-1000	Precon Construction	1	0	05-May-25 A	05-May-25 A	
PROC-1010	Contractor Procurement	60	0	06-May-25 A	07-Nov-25 A	
Long Lead Items						
PROC-1020	Elevator Submittal	23	0	12-Jun-25 A	14-Jul-25 A	
PROC-1030	Brick Submittal and Fabrication	60	0	01-Jul-25 A	19-Sep-25 A	
PROC-1120	Ferguson Tank Submittal	20	0	29-Jul-25 A	15-Oct-25 A	
PROC-1040	Switchgear Submittal	15	0	31-Jul-25 A	20-Aug-25 A	
PROC-1050	Light Fixtures Submittal	20	0	04-Aug-25 A	29-Aug-25 A	
PROC-1060	Switchgear Fabrication	30	0	21-Aug-25 A	30-Sep-25 A	
PROC-1070	Light Fixtures Fabrication	20	0	01-Sep-25 A	25-Sep-25 A	
PROC-1110	HVAC Equipment Submittal	20	0	15-Sep-25 A	30-Sep-25 A	
PROC-1080	Glass Field Measurement and Fabrication - Office	45	0	15-Sep-25 A	22-Dec-25 A	
PROC-1130	HVAC Equipment Fabrication	70	30	20-Oct-25 A	11-Feb-26	29
PROC-1090	Fire Pump Submittal	40	1	27-Oct-25 A	01-Jan-26	129
PROC-1140	Ferguson Tank Fabrication	15	0	27-Oct-25 A	21-Nov-25 A	
PROC-1100	Elevator Fabrication	50	50	01-Jan-26	11-Mar-26	40
PROC-1150	Fire Pump Fabrication	20	20	02-Jan-26	29-Jan-26	129
Construction						
Site Work						
SITE-1020	Mobilization	1	0	05-May-25 A	05-May-25 A	
SITE-1000	Erosion Control Phase I	4	0	06-May-25 A	09-May-25 A	
SITE-1010	Stormwater Management Ponds Phase I	10	0	03-Nov-25 A	21-Nov-25 A	
SITE-1030	Stormwater Management Ponds Phase II	10	10	23-Mar-26	03-Apr-26	103
Site Work - Main Building						
SITE-MB-1010	Demo/Clear Site - Main Building	10	0	12-May-25 A	23-May-25 A	
SITE-MB-1020	Rough Grading - Main Building	10	0	26-May-25 A	06-Jun-25 A	
SITE-MB-1030	Building Pad Delivery - Main Building	35	0	09-Jun-25 A	25-Jul-25 A	
SITE-MB-1040	Domestic & Fire Water Online - Main Building	27	0	28-Jul-25 A	02-Sep-25 A	
SITE-MB-1050	Storm Structures and Pipe - Main Building	30	10	03-Nov-25 A	14-Jan-26	114
SITE-MB-1070	Fine Grading - Main Building	15	15	01-Jan-26	21-Jan-26	31
SITE-MB-1060	Sanitary Sewer - Main Building	10	10	01-Apr-26*	14-Apr-26	60
SITE-MB-1100	Curb and Gutter - Main Building	7	7	08-May-26	18-May-26	36
SITE-MB-1120	Stone Base Parking Lot - Main Building	10	10	19-May-26	01-Jun-26	36
SITE-MB-1080	Sidewalk - Main Building	10	10	08-Jul-26	21-Jul-26	0
SITE-MB-1130	Paving (Includes SHA Work) - Main Building	11	11	22-Jul-26	05-Aug-26	0

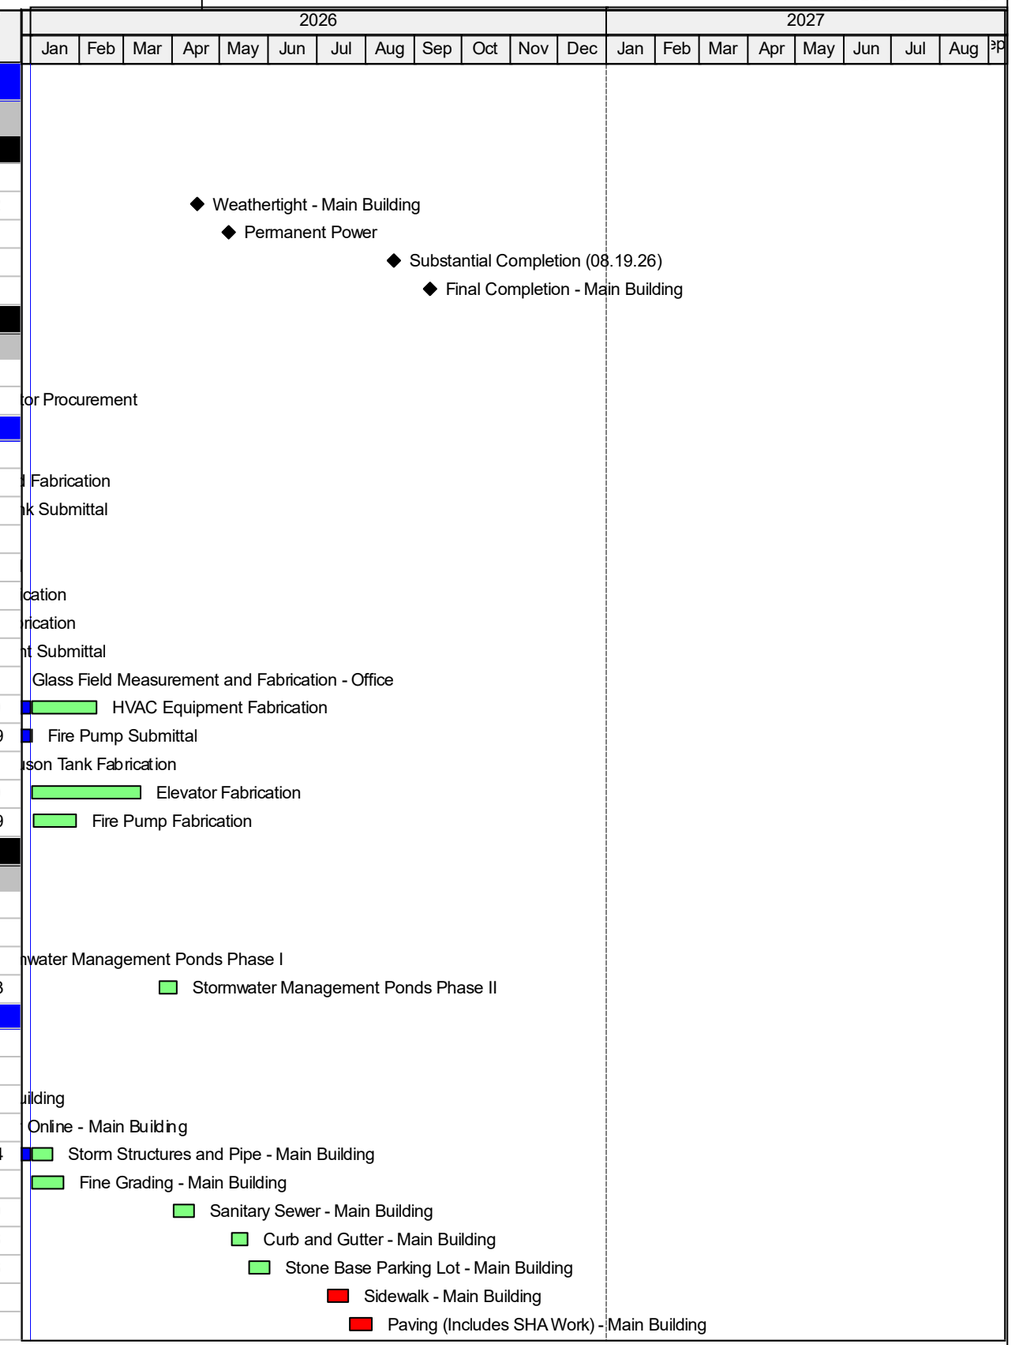

Activity ID	Activity Name	OD	RD	Start	Finish	TF
SITE-MB-1090	Landscape - Main Building	10	10	06-Aug-26	19-Aug-26	0
SITE-MB-1140	Line Striping - Main Building	2	2	06-Aug-26	07-Aug-26	8
Site Work - Office						
SITE-OFF-1000	Demo/Clear Site - Office Building	10	0	12-May-25 A	23-May-25 A	
SITE-OFF-1010	Rough Grading - Office Building	10	0	26-May-25 A	06-Jun-25 A	
SITE-OFF-1020	Building Pad Delivery - Office Building	35	0	09-Jun-25 A	25-Jul-25 A	
SITE-OFF-1060	Fine Grading - Office Building	6	6	01-Jan-26	08-Jan-26	152
SITE-OFF-1030	Domestic & Fire Water Online - Office Building	10	10	01-Jan-26	14-Jan-26	148
SITE-OFF-1080	Landscape - Office Building	1	1	09-Jan-26	09-Jan-26	163
SITE-OFF-1090	Curb and Gutter - Office Building	1	1	15-Jan-26	15-Jan-26	148
SITE-OFF-1110	Stone Base Parking Lot - Office Building	1	1	16-Jan-26	16-Jan-26	149
SITE-OFF-1070	Sidewalk - Office Building	2	2	16-Jan-26	19-Jan-26	148
SITE-OFF-1120	Paving - Office Building	2	2	20-Jan-26	21-Jan-26	148
SITE-OFF-1100	Misc Exterior Items (Vehicle Gate Operator) - Office Building	3	3	22-Jan-26	26-Jan-26	152
SITE-OFF-1130	Line Striping - Office Building	1	1	22-Jan-26	22-Jan-26	148
Main Building						
Substructure						
CON-MB-1000	UG Electric Rough In	10	0	04-Aug-25 A	27-Aug-25 A	
CON-MB-1010	UG Plumbing Roughin	8	0	18-Aug-25 A	27-Aug-25 A	
CON-MB-1020	Prep/Pour SOG 1/2	12	0	27-Aug-25 A	10-Sep-25 A	
CON-MB-1030	Prep/Pour SOG 2/2	18	0	29-Aug-25 A	22-Sep-25 A	
CON-MB-1040	Foundation Waterproofing	5	5	20-Jan-26	26-Jan-26	10
Superstructure						
First Floor Superstructure						
CON-MB-L1-1040	Structural Steel Columns & Beams - 1st Floor	18	0	29-Sep-25 A	28-Oct-25 A	
CON-MB-L1-1060	Metal Decking - 2nd floor	4	0	23-Oct-25 A	28-Oct-25 A	
CON-MB-L1-1090	Exterior & Interior Framing - 1st Floor	10	7	28-Oct-25 A	09-Jan-26	10
CON-MB-L1-1070	Prep/Pour SOD - 2nd Floor	8	0	29-Oct-25 A	01-Nov-25 A	
Second Floor Superstructure						
CON-MB-L2-1000	Structural Steel Columns & Beams - 2nd Floor	14	0	04-Nov-25 A	21-Nov-25 A	
CON-MB-L2-1010	Metal Decking 3rd Floor	4	0	24-Nov-25 A	27-Nov-25 A	
CON-MB-L2-1020	Prep/Pour SOD - 3rd floor	8	0	28-Nov-25 A	04-Dec-25 A	
CON-MB-L2-1040	Exterior & Interior Framing - 2nd Floor	10	10	22-Jan-26	04-Feb-26	4
Third Floor Superstructure						
CON-MB-L3-1000	Structural Steel Columns & Beams - 3rd Floor	14	0	01-Dec-25 A	19-Dec-25 A	
CON-MB-L3-1010	Metal Decking - 4th Floor	4	0	19-Dec-25 A	23-Dec-25 A	
CON-MB-L3-1020	Prep & Pour SOD - 4th Floor	8	3	22-Dec-25 A	05-Jan-26	0
CON-MB-L3-1040	Exterior & Interior Framing - 3rd Floor	10	10	03-Feb-26	16-Feb-26	50
Fourth Floor Superstructure						
CON-MB-L4-1000	Structural Steel Columns & Beams - 4th Floor	14	14	06-Jan-26	23-Jan-26	0
CON-MB-L4-1010	Metal Decking - 5th Floor	4	4	26-Jan-26	29-Jan-26	0
CON-MB-L4-1020	Prep & Pour SOD - 5th Floor	4	4	30-Jan-26	04-Feb-26	0
CON-MB-L4-1030	Exterior & Interior Framing - 4th Floor	10	10	17-Feb-26	02-Mar-26	0
Fifth Floor Superstructure						
CON-MB-L5-1000	Structural Steel Columns & Beams - 5th Floor	14	14	05-Feb-26	24-Feb-26	9
CON-MB-L5-1010	Framing & Metal Decking - Roof	10	10	25-Feb-26	10-Mar-26	9
CON-MB-L5-1050	Exterior & Interior Framing - 5th Floor	10	10	06-Apr-26	17-Apr-26	9

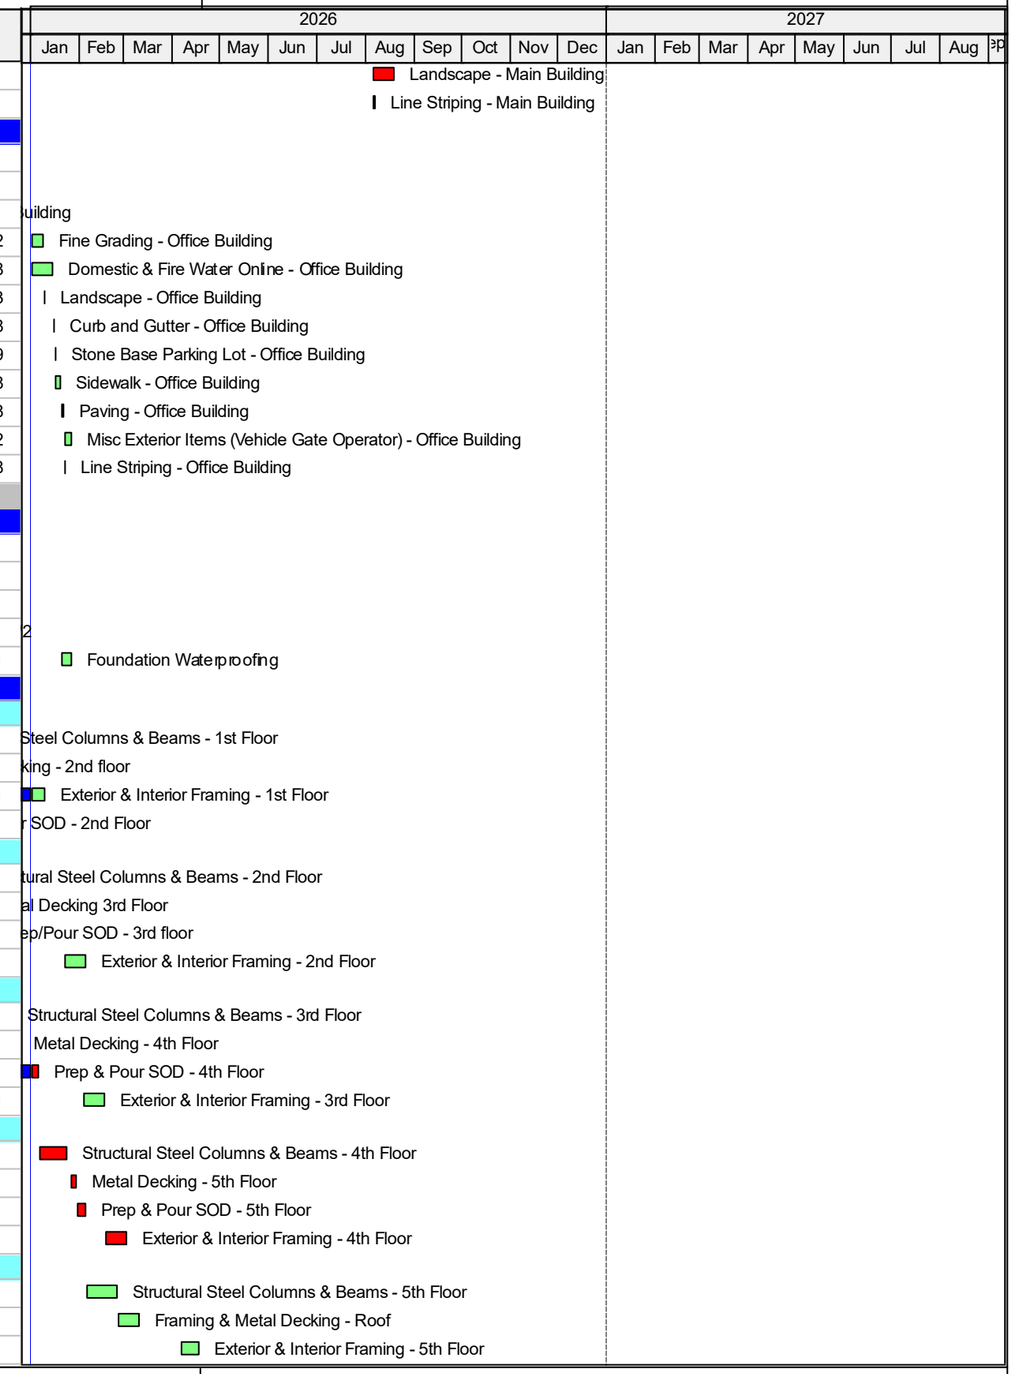

Activity ID	Activity Name	OD	RD	Start	Finish	TF
Interior Finishes						
CON-MB-2020	Winterization	5	0	22-Dec-25 A	29-Dec-25 A	
CON-MB-2000	Grind/Seal Floors (Full Building)	10	10	05-Jun-26	18-Jun-26	29
CON-MB-2010	Final Cleaning (Full Building)	15	15	09-Jun-26	29-Jun-26	37
Elevator						
CON-ELEV-1000	Elevator 3 CMU Shaft	12	0	15-Sep-25 A	30-Sep-25 A	
CON-ELEV-1010	Elevator 1/2 CMU Shaft	14	0	01-Oct-25 A	17-Oct-25 A	
CON-ELEV-1020	Elevator Install	65	65	01-Apr-26	30-Jun-26	26
Stair Shafts						
CON-STAIR-1000	Stair Tower B CMU	25	0	15-Sep-25 A	24-Oct-25 A	
CON-STAIR-1010	Stair Tower A CMU	10	0	03-Oct-25 A	17-Oct-25 A	
CON-STAIR-1020	Stair Stringers and Pans	10	5	29-Dec-25 A	07-Jan-26	143
CON-STAIR-1030	Doors & HW - Stairs	2	2	08-Jan-26	09-Jan-26	143
CON-STAIR-1040	Prep/Paint - Stairs	2	2	12-Jan-26	13-Jan-26	161
First Floor Interior Finishes						
CON-MB-L1-1130	Fireproofing Structural Steel - 1st Floor	8	7	12-Dec-25 A	09-Jan-26	2
CON-MB-L1-1140	OH & Wall Plumbing Rough In - 1st Floor	3	3	12-Jan-26	14-Jan-26	68
CON-MB-L1-1150	Electric & Low Voltage OH & Wall Rough In - 1st Floor	10	10	12-Jan-26	23-Jan-26	61
CON-MB-L1-1170	Sprinkler Rough In - 1st Floor	10	10	12-Jan-26	23-Jan-26	143
CON-MB-L1-1160	HVAC Rough In - 1st Floor	3	3	12-Feb-26	16-Feb-26	45
CON-MB-L1-1180	OH & Wall MEP Inspections - 1st Floor	2	2	17-Feb-26	18-Feb-26	45
CON-MB-L1-1270	Janus Wall Panels - 1st Floor	15	15	13-Mar-26	02-Apr-26	29
CON-MB-L1-1190	Hang & Finish Drywall - 1st Floor	7	7	17-Apr-26	27-Apr-26	80
CON-MB-L1-1200	Doors & HW - 1st Floor	2	2	28-Apr-26	29-Apr-26	102
CON-MB-L1-1210	Prep/Paint Walls & Ceilings - 1st Floor	2	2	28-Apr-26	29-Apr-26	80
CON-MB-L1-1220	Plumbing Fixtures - 1st Floor	2	2	30-Apr-26	01-May-26	83
CON-MB-L1-1230	Diffusers - 1st Floor	5	5	30-Apr-26	06-May-26	80
CON-MB-L1-1240	Light Fixtures - 1st Floor	5	5	30-Apr-26	06-May-26	80
Second Floor Interior Finishes						
CON-MB-L2-1090	Fireproofing Structural Steel - 2nd Floor	8	8	12-Jan-26	21-Jan-26	2
CON-MB-L2-1100	Electric OH & Wall Rough In - 2nd Floor	10	10	05-Feb-26	18-Feb-26	29
CON-MB-L2-1060	Doors & HW - 2nd Floor	2	2	05-Feb-26	06-Feb-26	141
CON-MB-L2-1120	Sprinkler Rough In - 2nd Floor	10	10	05-Feb-26	18-Feb-26	125
CON-MB-L2-1080	Prep/Paint Walls - 2nd Floor	2	2	09-Feb-26	10-Feb-26	141
CON-MB-L2-1110	HVAC Rough In - 2nd Floor	5	5	12-Feb-26	18-Feb-26	29
CON-MB-L2-1140	OH & Wall MEP Inspections - 2nd Floor	1	1	19-Feb-26	19-Feb-26	29
CON-MB-L2-1070	Janus Wall Panels - 2nd Floor	15	15	20-Feb-26	12-Mar-26	29
CON-MB-L2-1150	Diffusers - 2nd Floor	5	5	20-Feb-26	26-Feb-26	146
CON-MB-L2-1160	Light Fixtures - 2nd Floor	5	5	20-Feb-26	26-Feb-26	146
Third Floor Interior Finishes						
CON-MB-L3-1060	Fire Proofing Structural Steel - 3rd Floor	8	8	22-Jan-26	02-Feb-26	2
CON-MB-L3-1070	OH & Wall Plumbing Rough In - 3rd Floor	3	3	17-Feb-26	19-Feb-26	57
CON-MB-L3-1080	Electric & Low Voltage OH & Wall Rough In - 3rd Floor	10	10	17-Feb-26	02-Mar-26	50
CON-MB-L3-1090	HVAC Rough In - 3rd Floor	5	5	17-Feb-26	23-Feb-26	55
CON-MB-L3-1100	Sprinkler Rough In - 3rd Floor	10	10	17-Feb-26	02-Mar-26	117
CON-MB-L3-1120	OH & Wall MEP Inspections - 3rd Floor	2	2	03-Mar-26	04-Mar-26	50

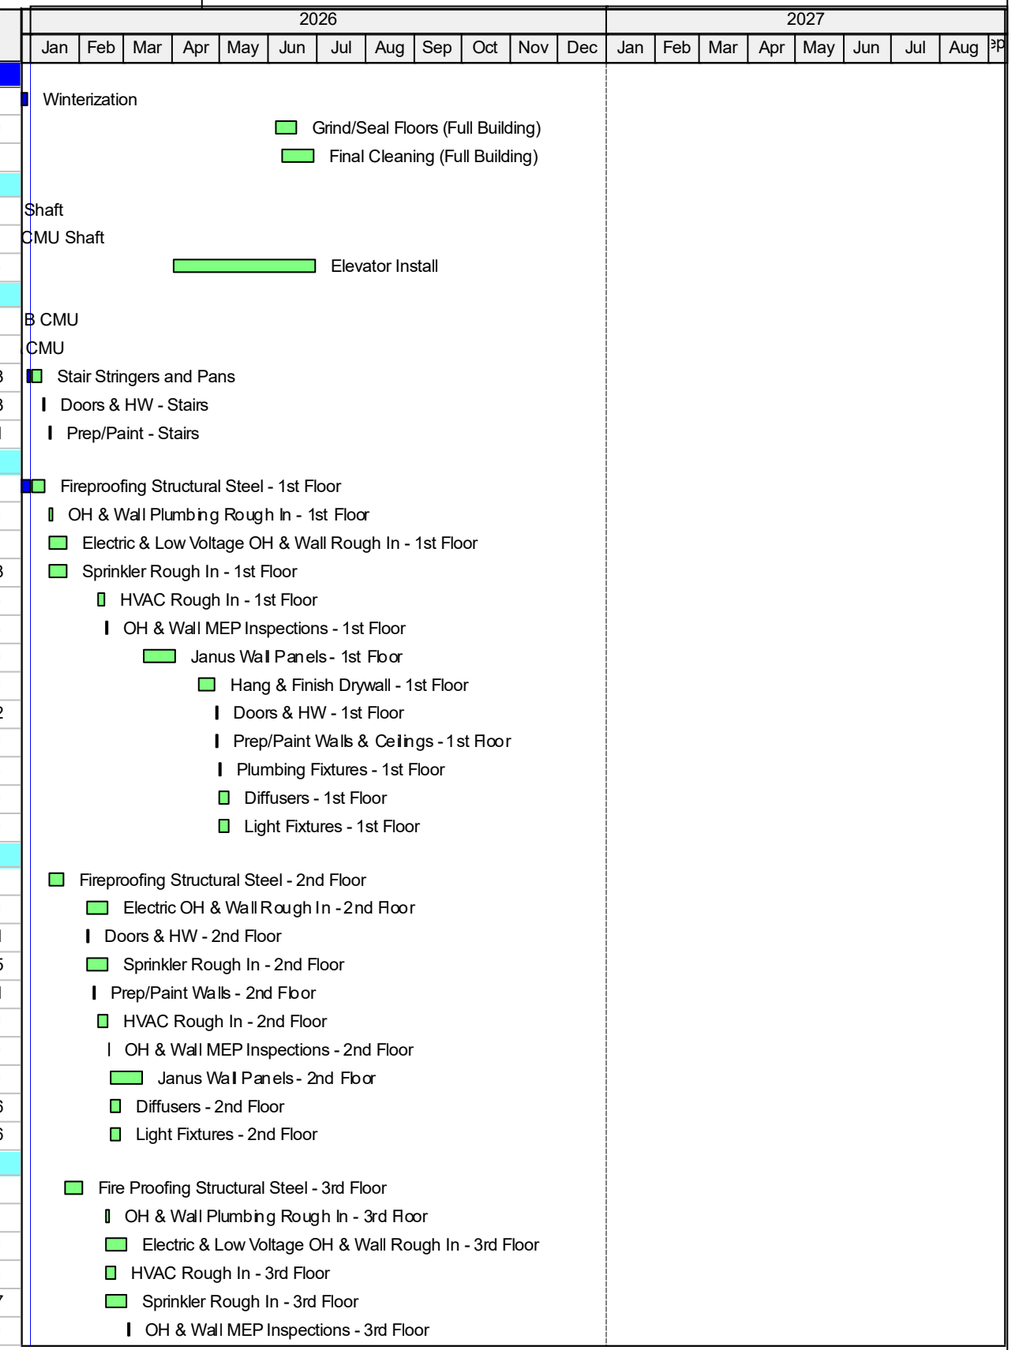

Activity ID	Activity Name	OD	RD	Start	Finish	TF
CON-MB-L3-1150	Janus Wall Panels - 3rd Floor	15	15	03-Apr-26	23-Apr-26	29
CON-MB-L3-1130	Hang/Finish Drywall - 3rd Floor	7	7	17-Apr-26	27-Apr-26	69
CON-MB-L3-1140	Prep/Paint Walls & Ceilings - 3rd Floor	3	3	28-Apr-26	30-Apr-26	69
CON-MB-L3-1160	Plumbing Fixtures - 3rd Floor	4	4	01-May-26	06-May-26	70
CON-MB-L3-1170	Diffusers - 3rd Floor	5	5	01-May-26	07-May-26	69
CON-MB-L3-1180	Light Fixtures - 3rd Floor	5	5	01-May-26	07-May-26	69
Fourth Floor Interior Finishes						
CON-MB-L4-1050	Fire Proofing Structural Steel - 4th Floor	8	8	05-Feb-26	16-Feb-26	0
CON-MB-L4-1060	Electric OH & Wall Rough In - 4th Floor	10	10	03-Mar-26	16-Mar-26	56
CON-MB-L4-1070	HVAC Rough In - 4th Floor	5	5	03-Mar-26	09-Mar-26	61
CON-MB-L4-1080	Sprinkler Rough In - 4th Floor	10	10	03-Mar-26	16-Mar-26	107
CON-MB-L4-1100	OH & Wall MEP Inspections - 4th Floor	1	1	17-Mar-26	17-Mar-26	56
CON-MB-L4-1110	Prep/Paint Walls - 4th Floor	2	2	18-Mar-26	19-Mar-26	104
CON-MB-L4-1120	Diffusers - 4th Floor	5	5	18-Mar-26	24-Mar-26	101
CON-MB-L4-1130	Light Fixtures - 4th Floor	5	5	18-Mar-26	24-Mar-26	101
CON-MB-L4-1140	Janus Wall Panels - 4th Floor	15	15	24-Apr-26	14-May-26	29
Fifth Floor Interior Finishes						
CON-MB-L5-1040	Fire Proofing Structural Steel - 5th Floor	8	8	01-Apr-26	10-Apr-26	9
CON-MB-L5-1060	Electric & Low Voltage OH & Wall Rough In - 5th Floor	10	10	20-Apr-26	01-May-26	30
CON-MB-L5-1070	OH & Wall Plumbing Rough In - 5th Floor	3	3	20-Apr-26	22-Apr-26	37
CON-MB-L5-1080	HVAC Rough In - 5th Floor	5	5	20-Apr-26	24-Apr-26	35
CON-MB-L5-1090	Sprinkler Rough In - 5th Floor	10	10	20-Apr-26	01-May-26	73
CON-MB-L5-1110	OH & Wall MEP Inspections - 5th Floor	1	1	04-May-26	04-May-26	30
CON-MB-L5-1120	Hang/Finish Drywall - 5th Floor	7	7	05-May-26	13-May-26	30
CON-MB-L5-1130	Prep/Paint Walls - 5th Floor	2	2	14-May-26	15-May-26	86
CON-MB-L5-1170	Janus Wall Panels - 5th Floor	15	15	15-May-26	04-Jun-26	29
CON-MB-L5-1140	Plumbing Fixtures - 5th Floor	4	4	18-May-26	21-May-26	86
CON-MB-L5-1150	Diffusers - 5th Floor	1	1	18-May-26	18-May-26	89
CON-MB-L5-1160	Light Fixtures - 5th Floor	1	1	18-May-26	18-May-26	89
Switchgear Room						
CON-POW-1000	Switchgear Room Enclosure	10	10	20-Jan-26	02-Feb-26	61
CON-POW-1010	Install Switchgear Equipment	15	15	03-Feb-26	23-Feb-26	61
CON-POW-1020	Switchgear Lights and Power	15	15	24-Feb-26	16-Mar-26	61
CON-POW-1030	City Inspection	1	1	17-Mar-26	17-Mar-26	61
CON-POW-1040	Dominion Primary	20	20	18-Mar-26	14-Apr-26	61
CON-POW-1050	Dominion Transformer	5	5	15-Apr-26	21-Apr-26	61
CON-POW-1060	Dominion Secondary	5	5	22-Apr-26	28-Apr-26	61
CON-POW-1070	Power Activation	5	5	29-Apr-26	05-May-26	61
Exterior Finishes						
CON-MB-L1-1250	Exterior Sheathing - 1st Floor	6	6	12-Jan-26	19-Jan-26	10
CON-MB-L2-1050	Exterior Sheathing - 2nd Floor	6	6	27-Jan-26	03-Feb-26	4
CON-MB-L1-1280	Perimeter Waterproofing - 1st Floor	3	3	04-Feb-26	06-Feb-26	4
CON-MB-L3-1050	Exterior Sheathing - 3rd Floor	6	6	06-Feb-26	13-Feb-26	55
CON-MB-L5-1100	Brick Facade - 1st Floor	30	30	09-Feb-26	20-Mar-26	4
CON-MB-L4-1040	Exterior Sheathing - 4th Floor	6	6	20-Feb-26	27-Feb-26	0
CON-MB-L1-1260	Perimeter Waterproofing West Elevation (Excluding 5th Floor)	4	4	02-Mar-26	05-Mar-26	0

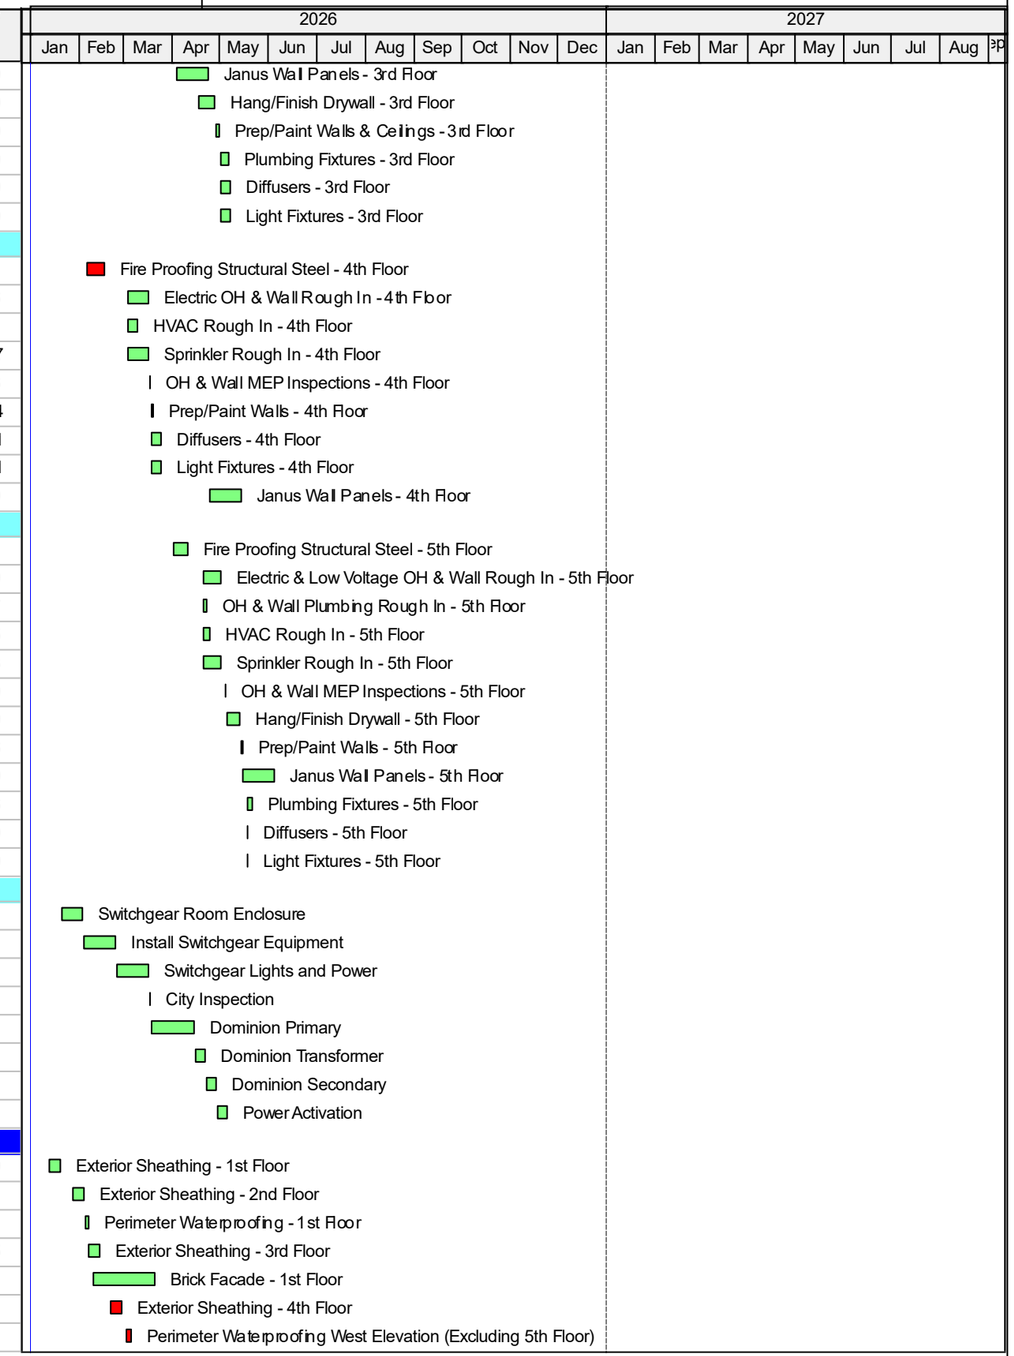

Activity ID	Activity Name	OD	RD	Start	Finish	TF
CON-MB-EXT-1000	Brick West Elevation (Excluding 5th Floor)	20	20	06-Mar-26	02-Apr-26	0
CON-MB-L2-1280	Perimeter Waterproofing North Elevation (Excluding 5th Floor)	4	4	06-Mar-26	11-Mar-26	16
CON-MB-EXT-1130	Storefront	20	20	23-Mar-26	17-Apr-26	66
CON-MB-EXT-1020	Brick North and West Elevations (5th Floor)	25	25	03-Apr-26	07-May-26	0
CON-MB-EXT-1040	Stucco West Elevation	15	15	03-Apr-26	23-Apr-26	25
CON-MB-L5-1030	Exterior Sheathing - 5th Floor	6	6	09-Apr-26	16-Apr-26	9
CON-MB-L2-1310	Perimeter Waterproofing West/North Elevations (5th Floor)	2	2	17-Apr-26	20-Apr-26	9
CON-MB-EXT-1150	Canopies	7	7	20-Apr-26	28-Apr-26	66
CON-MB-L2-1290	Perimeter Waterproofing East Elevation	4	4	21-Apr-26	24-Apr-26	9
CON-MB-EXT-1070	Glass West Elevation	7	7	24-Apr-26	04-May-26	41
CON-MB-L2-1300	Perimeter Waterproofing South Elevation	4	4	27-Apr-26	30-Apr-26	30
CON-MB-EXT-1090	Glass North Elevation	7	7	05-May-26	13-May-26	41
CON-MB-EXT-1030	Brick East Elevation	25	25	08-May-26	11-Jun-26	0
CON-MB-EXT-1060	Stucco North Elevation	7	7	08-May-26	18-May-26	15
CON-MB-EXT-1110	Glass East Elevation	7	7	14-May-26	22-May-26	41
CON-MB-EXT-1080	Stucco East Elevation	14	14	19-May-26	05-Jun-26	15
CON-MB-EXT-1140	Glass South Elevation	7	7	25-May-26	02-Jun-26	41
CON-MB-EXT-1100	Stucco South Elevation	7	7	08-Jun-26	16-Jun-26	15
CON-MB-EXT-1050	Brick South Elevation	18	18	12-Jun-26	07-Jul-26	0
CON-MB-EXT-1120	Swing Doors/ Automatic Sliding Entrance	4	4	08-Jul-26	13-Jul-26	12
Roofing						
CON-MB-L5-1020	Roof Insulation & TPO	15	15	11-Mar-26	31-Mar-26	9
Office Building						
Structure - Office						
CON-OFF-1000	Prep/Pour SOG - Office Building	5	0	21-Jul-25 A	22-Jul-25 A	
CON-OFF-1010	Structural Steel - Office Building	2	0	30-Sep-25 A	30-Sep-25 A	
CON-OFF-1030	Interior/Exterior Framing - Office Building	8	0	10-Oct-25 A	22-Oct-25 A	
CON-OFF-1070	Framing Inspection - Office Building	1	0	22-Oct-25 A	22-Oct-25 A	
CON-OFF-1050	Roof Decking - Office Building	1	0	27-Oct-25 A	27-Oct-25 A	
CON-OFF-1020	Foundation Waterproofing - Office Building	2	0	31-Oct-25 A	02-Dec-25 A	
Interior Finishes - Office						
CON-OFF-1080	MEP Rough In - Office Building	3	0	03-Dec-25 A	12-Dec-25 A	
CON-OFF-1090	MEP Inspections - Office Building	1	2	29-Dec-25 A	02-Jan-26	143
CON-OFF-1100	Hang/Finish Drywall - Office Building	3	3	05-Jan-26	07-Jan-26	143
CON-OFF-1110	Doors, Frames & Hardware - Office Building	2	2	08-Jan-26	09-Jan-26	143
CON-OFF-1120	Prep/Paint Walls - Office Building	2	2	12-Jan-26	13-Jan-26	143
CON-OFF-1130	Flooring - Office Building	5	5	14-Jan-26	20-Jan-26	143
CON-OFF-1140	MEP Finishes, Fixtures, Accessories - Office Building	2	2	21-Jan-26	22-Jan-26	143
CON-OFF-1150	Millwork - Office Building	2	2	21-Jan-26	22-Jan-26	147
CON-OFF-1220	Final Cleaning - Office Building	1	1	23-Jan-26	23-Jan-26	147
Exterior Finishes - Office						
CON-OFF-1040	Roofing - Office Building	2	0	29-Oct-25 A	29-Oct-25 A	
CON-OFF-1060	Exterior Sheathing/Waterproofing - Office Building	3	3	29-Dec-25 A	05-Jan-26	151
CON-OFF-1160	Store Front & Windows - Office Building	3	3	06-Jan-26	08-Jan-26	153
CON-OFF-1170	Brick Facade - Office Building	5	5	06-Jan-26	12-Jan-26	151
Final Inspections & Close Out						

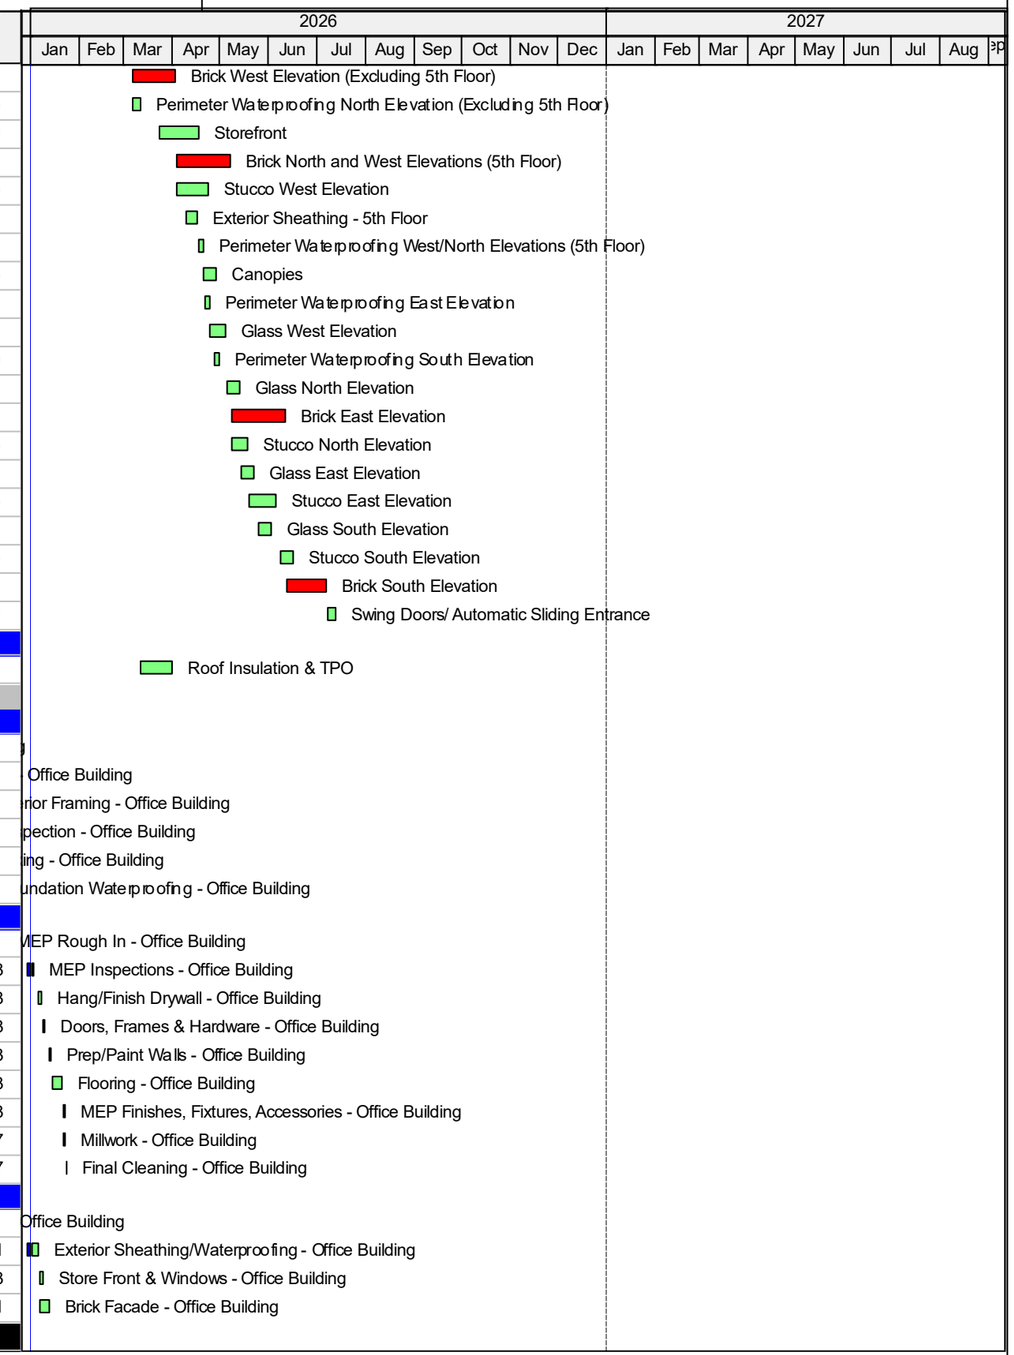
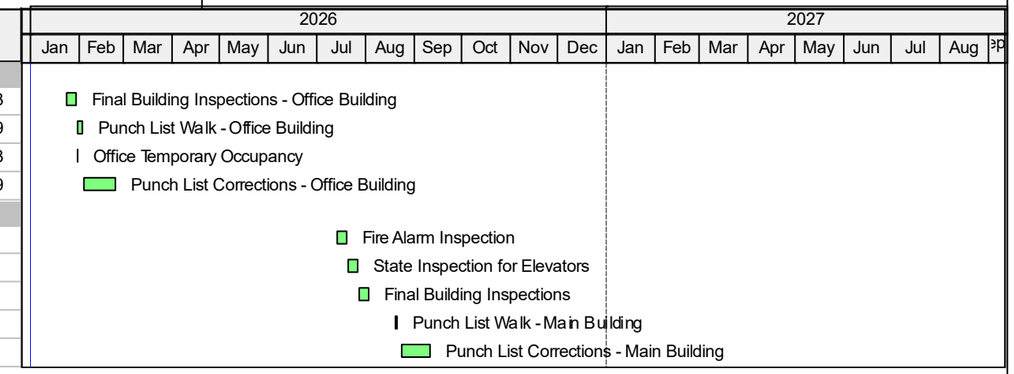
Activity ID	Activity Name	OD	RD	Start	Finish	TF
Office Building						
CLO-OFF-1030	Final Building Inspections - Office Building	5	5	23-Jan-26	29-Jan-26	143
CLO-OFF-1040	Punch List Walk - Office Building	2	2	30-Jan-26	02-Feb-26	149
CLO-OFF-1000	Office Temporary Occupancy	1	1	30-Jan-26	30-Jan-26*	143
CLO-OFF-1050	Punch List Corrections - Office Building	15	15	03-Feb-26	23-Feb-26	149
Main Building						
CLO-MB-1000	Fire Alarm Inspection	5	5	14-Jul-26	20-Jul-26	12
CLO-MB-1010	State Inspection for Elevators	5	5	21-Jul-26	27-Jul-26	12
CLO-MB-1020	Final Building Inspections	5	5	28-Jul-26	03-Aug-26	12
CLO-MB-1040	Punch List Walk - Main Building	2	2	20-Aug-26	21-Aug-26	5
CLO-MB-1050	Punch List Corrections - Main Building	15	15	24-Aug-26	11-Sep-26	5
