PSFVA-UP04 - Public Storage Fairfax VA - DEC 2025

01 LONGEST PATH

DATA DATE: 31-Dec-25
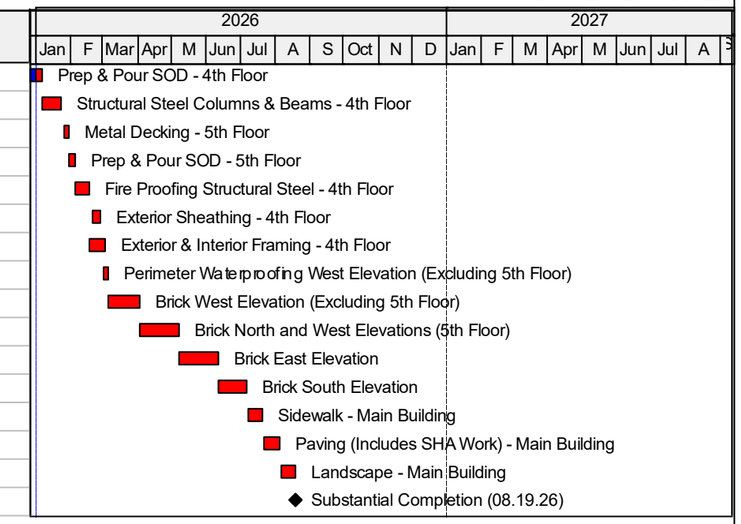
Activity ID	Activity Name	OD	RD	% Complete	Start	Finish	TF
CON-MB-L3-1020	Prep & Pour SOD - 4th Floor	8	3	62.5%	22-Dec-25 A	05-Jan-26	0
CON-MB-L4-1000	Structural Steel Columns & Beams - 4th Floor	14	14	0%	06-Jan-26	23-Jan-26	0
CON-MB-L4-1010	Metal Decking - 5th Floor	4	4	0%	26-Jan-26	29-Jan-26	0
CON-MB-L4-1020	Prep & Pour SOD - 5th Floor	4	4	0%	30-Jan-26	04-Feb-26	0
CON-MB-L4-1050	Fire Proofing Structural Steel - 4th Floor	8	8	0%	05-Feb-26	16-Feb-26	0
CON-MB-L4-1040	Exterior Sheathing - 4th Floor	6	6	0%	20-Feb-26	27-Feb-26	0
CON-MB-L4-1030	Exterior & Interior Framing - 4th Floor	10	10	0%	17-Feb-26	02-Mar-26	0
CON-MB-L1-1260	Perimeter Waterproofing West Elevation (Excluding 5th Floor)	4	4	0%	02-Mar-26	05-Mar-26	0
CON-MB-EXT-1000	Brick West Elevation (Excluding 5th Floor)	20	20	0%	06-Mar-26	02-Apr-26	0
CON-MB-EXT-1020	Brick North and West Elevations (5th Floor)	25	25	0%	03-Apr-26	07-May-26	0
CON-MB-EXT-1030	Brick East Elevation	25	25	0%	08-May-26	11-Jun-26	0
CON-MB-EXT-1050	Brick South Elevation	18	18	0%	12-Jun-26	07-Jul-26	0
SITE-MB-1080	Sidewalk - Main Building	10	10	0%	08-Jul-26	21-Jul-26	0
SITE-MB-1130	Paving (Includes SHA Work) - Main Building	11	11	0%	22-Jul-26	05-Aug-26	0
SITE-MB-1090	Landscape - Main Building	10	10	0%	06-Aug-26	19-Aug-26	0
MIL-1030	Substantial Completion (08.19.26)	0	0	0%		19-Aug-26*	0
