Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
VA18231 - Fairfax - Lee Hwy (land) - 08239- 2025.12.31 UP03		182	0%	05-May-25A	11-Sep-26	5	05-May-25	15-Sep-26	2
Public Storage Fairfax VA		182	0%	05-May-25A	11-Sep-26	5	05-May-25	15-Sep-26	2
Milestones		106	0%	05-May-25A	11-Sep-26	5	05-May-25	15-Sep-26	2
MIL-1000	Notice to Proceed (05.05.25)	0	100%	05-May-25A			05-May-25		0
MIL-1010	Weathertight - Main Building	0	0%		16-Apr-26	42		09-Apr-26	-5
MIL-1020	Permanent Power	0	0%	06-May-26		61	26-Mar-26		-29
MIL-1030	Substantial Completion (08.19.26)	0	0%		19-Aug-26*	0		19-Aug-26	0
MIL-1040	Final Completion - Main Building	0	0%		11-Sep-26*	8		15-Sep-26	4
Preconstruction		50	0%	05-May-25A	11-Mar-26	137	05-May-25	13-Feb-26	-18
Procurement		50	0%	05-May-25A	11-Mar-26	137	05-May-25	13-Feb-26	-18
PROC-1000	Precon Construction	0	100%	05-May-25A	05-May-25A		05-May-25	05-May-25	0
PROC-1010	Contractor Procurement	0	100%	06-May-25A	07-Nov-25A		06-May-25	07-Nov-25	0
Long Lead Items		50	0%	12-Jun-25A	11-Mar-26	106	12-Jun-25	13-Feb-26	-18
PROC-1020	Elevator Submittal	0	100%	12-Jun-25A	14-Jul-25A		12-Jun-25	14-Jul-25	0
PROC-1030	Brick Submittal and Fabrication	0	100%	01-Jul-25A	19-Sep-25A		01-Jul-25	19-Sep-25	0
PROC-1120	Ferguson Tank Submital	0	100%	29-Jul-25A	15-Oct-25A		29-Jul-25	15-Oct-25	0
PROC-1040	Switchgear Submittal	0	100%	31-Jul-25A	20-Aug-25A		31-Jul-25	20-Aug-25	0
PROC-1050	Light Fixtures Submittal	0	100%	04-Aug-25A	29-Aug-25A		04-Aug-25	29-Aug-25	0
PROC-1060	Switchgear Fabrication	0	100%	21-Aug-25A	30-Sep-25A		21-Aug-25	30-Sep-25	0
PROC-1070	Light Fixtures Fabrication	0	100%	01-Sep-25A	25-Sep-25A		01-Sep-25	25-Sep-25	0
PROC-1110	HVAC Equipment Submittal	0	100%	15-Sep-25A	30-Sep-25A		15-Sep-25	30-Sep-25	0
PROC-1080	Glass Field Measurement and Fabrication - Office	0	100%	15-Sep-25A	22-Dec-25A		15-Sep-25	19-Dec-25	-1
PROC-1130	HVAC Equipment Fabrication	30	81.54%	20-Oct-25A	11-Feb-26	29	20-Oct-25	16-Jan-26	-18
PROC-1090	Fire Pump Submittal	1	100%	27-Oct-25A	01-Jan-26	129	27-Oct-25	01-Dec-25	-23
PROC-1140	Ferguson Tank Fabrication	0	100%	27-Oct-25A	21-Nov-25A		27-Oct-25	21-Nov-25	0
PROC-1100	Elevator Fabrication	50	54.29%	01-Jan-26	11-Mar-26	40	10-Nov-25	13-Feb-26	-18
PROC-1150	Fire Pump Fabrication	20	73.33%	02-Jan-26	29-Jan-26	129	02-Dec-25	12-Jan-26	-13
Construction		165	0%	05-May-25A	19-Aug-26	22	05-May-25	14-Aug-26	-3
Site Work		165	0%	05-May-25A	19-Aug-26	5	05-May-25	14-Aug-26	-3
SITE-1020	Mobilization	0	100%	05-May-25A	05-May-25A		05-May-25	05-May-25	0
SITE-1000	Erosion Control Phase I	0	100%	06-May-25A	09-May-25A		06-May-25	09-May-25	0
SITE-1010	Stormwater Management Ponds Phase I	0	100%	03-Nov-25A	21-Nov-25A		24-Nov-25	05-Dec-25	10
SITE-1030	Stormwater Management Ponds Phase II	10	0%	23-Mar-26	03-Apr-26	103			
Site Work - Main Building		165	0%	12-May-25A	19-Aug-26	0	12-May-25	14-Aug-26	-3
SITE-MB-1010	Demo/Clear Site - Main Building	0	100%	12-May-25A	23-May-25A		12-May-25	23-May-25	0
SITE-MB-1020	Rough Grading - Main Building	0	100%	26-May-25A	06-Jun-25A		26-May-25	06-Jun-25	0
SITE-MB-1030	Building Pad Delivery - Main Building	0	100%	09-Jun-25A	25-Jul-25A		09-Jun-25	25-Jul-25	0
SITE-MB-1040	Domestic & Fire Water Online - Main Building	0	100%	28-Jul-25A	02-Sep-25A		28-Jul-25	02-Sep-25	0
SITE-MB-1050	Storm Structures and Pipe - Main Building	10	100%	03-Nov-25A	14-Jan-26	114	03-Nov-25	12-Dec-25	-23
SITE-MB-1070	Fine Grading - Main Building	15	20%	01-Jan-26	21-Jan-26	31	29-Dec-25	16-Jan-26	-3
SITE-MB-1060	Sanitary Sewer - Main Building	10	100%	01-Apr-26*	14-Apr-26	60	15-Dec-25	26-Dec-25	-77
SITE-MB-1100	Curb and Gutter - Main Building	7	0%	08-May-26	18-May-26	36	22-May-26	01-Jun-26	10
SITE-MB-1120	Stone Base Parking Lot - Main Building	10	0%	19-May-26	01-Jun-26	36	02-Jun-26	15-Jun-26	10
SITE-MB-1080	Sidewalk - Main Building	10	0%	08-Jul-26	21-Jul-26	0	13-Jul-26	17-Jul-26	-2
SITE-MB-1130	Paving (Includes SHA Work) - Main Building	11	0%	22-Jul-26	05-Aug-26	0	20-Jul-26	31-Jul-26	-3
SITE-MB-1090	Landscape - Main Building	10	0%	06-Aug-26	19-Aug-26	0	03-Aug-26	14-Aug-26	-3
SITE-MB-1140	Line Striping - Main Building	2	0%	06-Aug-26	07-Aug-26	8	03-Aug-26	04-Aug-26	-3
Site Work - Office		18	0%	12-May-25A	26-Jan-26	152	12-May-25	03-Dec-25	-38
SITE-OFF-1000	Demo/Clear Site - Office Building	0	100%	12-May-25A	23-May-25A		12-May-25	23-May-25	0
SITE-OFF-1010	Rough Grading - Office Building	0	100%	26-May-25A	06-Jun-25A		26-May-25	06-Jun-25	0
SITE-OFF-1020	Building Pad Delivery - Office Building	0	100%	09-Jun-25A	25-Jul-25A		09-Jun-25	25-Jul-25	0
SITE-OFF-1060	Fine Grading - Office Building	6	100%	01-Jan-26	08-Jan-26	152	10-Nov-25	17-Nov-25	-38
SITE-OFF-1030	Domestic & Fire Water Online - Office Building	10	100%	01-Jan-26	14-Jan-26	148	10-Nov-25	21-Nov-25	-38
SITE-OFF-1080	Landscape - Office Building	1	100%	09-Jan-26	09-Jan-26	163	18-Nov-25	18-Nov-25	-38
SITE-OFF-1090	Curb and Gutter - Office Building	1	100%	15-Jan-26	15-Jan-26	148	24-Nov-25	24-Nov-25	-38
SITE-OFF-1110	Stone Base Parking Lot - Office Building	1	100%	16-Jan-26	16-Jan-26	149	25-Nov-25	25-Nov-25	-38
SITE-OFF-1070	Sidewalk - Office Building	2	100%	16-Jan-26	19-Jan-26	148	25-Nov-25	26-Nov-25	-38
SITE-OFF-1120	Paving - Office Building	2	100%	20-Jan-26	21-Jan-26	148	27-Nov-25	28-Nov-25	-38
SITE-OFF-1100	Misc Exterior Items (Vehicle Gate Operator) - Office Building	3	100%	22-Jan-26	26-Jan-26	152	01-Dec-25	03-Dec-25	-38
SITE-OFF-1130	Line Striping - Office Building	1	100%	22-Jan-26	22-Jan-26	148	01-Dec-25	01-Dec-25	-38
Main Building		138	0%	04-Aug-25A	13-Jul-26	49	04-Aug-25	29-Jul-26	12
Substructure		5	0%	04-Aug-25A	26-Jan-26	10	04-Aug-25	26-Nov-25	-43
CON-MB-1000	UG Electric Rough In	0	100%	04-Aug-25A	27-Aug-25A		04-Aug-25	27-Aug-25	0
CON-MB-1010	UG Plumbing Roughin	0	100%	18-Aug-25A	27-Aug-25A		18-Aug-25	27-Aug-25	0
CON-MB-1020	Prep/Pour SOG 1/2	0	100%	27-Aug-25A	10-Sep-25A		27-Aug-25	10-Sep-25	0
CON-MB-1030	Prep/Pour SOG 2/2	0	100%	29-Aug-25A	22-Sep-25A		29-Aug-25	22-Sep-25	0
CON-MB-1040	Foundation Waterproofing	5	100%	20-Jan-26	26-Jan-26	10	20-Nov-25	26-Nov-25	-43
Superstructure		77	0%	29-Sep-25A	17-Apr-26	9	29-Sep-25	02-Apr-26	-11
First Floor Superstructure		7	0%	29-Sep-25A	09-Jan-26	10	29-Sep-25	11-Nov-25	-43
CON-MB-L1-10	Structural Steel Columns & Beams - 1st Floor	0	100%	29-Sep-25A	28-Oct-25A		29-Sep-25	28-Oct-25	0
CON-MB-L1-10	Metal Decking - 2nd floor	0	100%	23-Oct-25A	28-Oct-25A		23-Oct-25	28-Oct-25	0

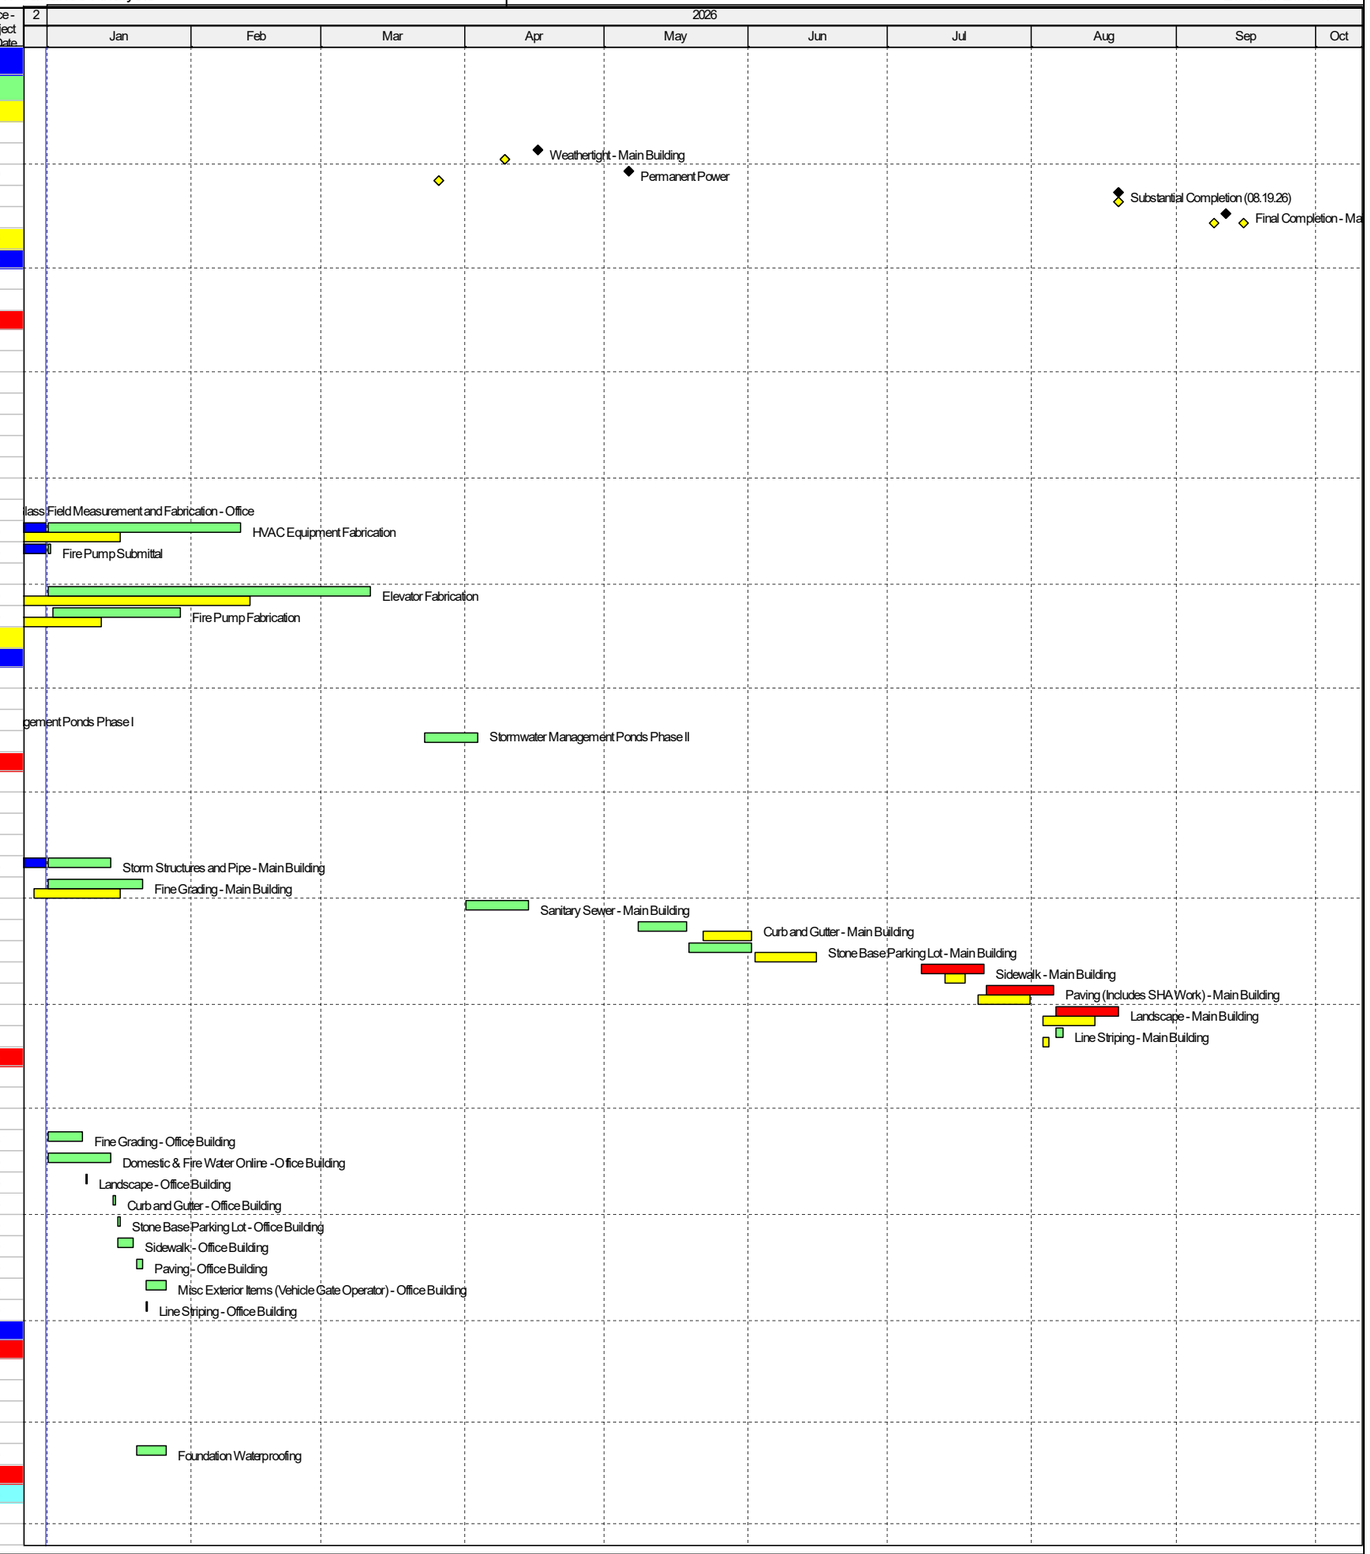

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
CON-MB-L1-10	Exterior & Interior Framing - 1st Floor	7	100%	28-Oct-25A	09-Jan-26	10	28-Oct-25	11-Nov-25	-43
CON-MB-L1-10	Prep/Pour SOD - 2nd Floor	0	100%	29-Oct-25A	01-Nov-25A		29-Oct-25	03-Nov-25	1
Second Floor Superstructure		10	0%	04-Nov-25A	04-Feb-26	4	04-Nov-25	23-Dec-25	-31
CON-MB-L2-10	Structural Steel Columns & Beams - 2nd Floor	0	100%	04-Nov-25A	21-Nov-25A		04-Nov-25	21-Nov-25	0
CON-MB-L2-10	Metal Decking 3rd Floor	0	100%	24-Nov-25A	27-Nov-25A		24-Nov-25	27-Nov-25	0
CON-MB-L2-10	Prep/Pour SOD - 3rd floor	0	100%	28-Nov-25A	04-Dec-25A		28-Nov-25	09-Dec-25	3
CON-MB-L2-10	Exterior & Interior Framing - 2nd Floor	10	100%	22-Jan-26	04-Feb-26	4	10-Dec-25	23-Dec-25	-31
Third Floor Superstructure		33	0%	01-Dec-25A	16-Feb-26	50	10-Dec-25	28-Jan-26	-13
CON-MB-L3-10	Structural Steel Columns & Beams - 3rd Floor	0	100%	01-Dec-25A	19-Dec-25A		10-Dec-25	29-Dec-25	6
CON-MB-L3-10	Metal Decking - 4th Floor	0	50%	19-Dec-25A	23-Dec-25A		30-Dec-25	02-Jan-26	8
CON-MB-L3-10	Prep & Pour SOD - 4th Floor	3	0%	22-Dec-25A	05-Jan-26	0	05-Jan-26	14-Jan-26	7
CON-MB-L3-10	Exterior & Interior Framing - 3rd Floor	10	0%	03-Feb-26	16-Feb-26	50	15-Jan-26	28-Jan-26	-13
Fourth Floor Superstructure		40	0%	06-Jan-26	02-Mar-26	0	15-Jan-26	27-Feb-26	-1
CON-MB-L4-10	Structural Steel Columns & Beams - 4th Floor	14	0%	06-Jan-26	23-Jan-26	0	15-Jan-26	03-Feb-26	7
CON-MB-L4-10	Metal Decking - 5th Floor	4	0%	26-Jan-26	29-Jan-26	0	04-Feb-26	09-Feb-26	7
CON-MB-L4-10	Prep & Pour SOD - 5th Floor	4	0%	30-Jan-26	04-Feb-26	0	10-Feb-26	13-Feb-26	7
CON-MB-L4-10	Exterior & Interior Framing - 4th Floor	10	0%	17-Feb-26	02-Mar-26	0	16-Feb-26	27-Feb-26	-1
Fifth Floor Superstructure		52	0%	05-Feb-26	17-Apr-26	9	16-Feb-26	02-Apr-26	-11
CON-MB-L5-10	Structural Steel Columns & Beams - 5th Floor	14	0%	05-Feb-26	24-Feb-26	9	16-Feb-26	05-Mar-26	7
CON-MB-L5-10	Framing & Metal Decking - Roof	10	0%	25-Feb-26	10-Mar-26	9	06-Mar-26	19-Mar-26	7
CON-MB-L5-10	Exterior & Interior Framing - 5th Floor	10	0%	06-Apr-26	17-Apr-26	9	20-Mar-26	02-Apr-26	-11
Interior Finishes		129	0%	15-Sep-25A	30-Jun-26	58	15-Sep-25	14-Jul-26	10
CON-MB-2020	Winterization	0	0%	22-Dec-25A	29-Dec-25A				
CON-MB-2000	Grind/Seal Floors (Full Building)	10	0%	05-Jun-26	18-Jun-26	29	22-Jun-26	03-Jul-26	11
CON-MB-2010	Final Cleaning (Full Building)	15	0%	09-Jun-26	29-Jun-26	37	24-Jun-26	14-Jul-26	11
Elevator		65	0%	15-Sep-25A	30-Jun-26	26	15-Sep-25	09-Jul-26	7
CON-ELEV-100	Elevator 3 CMU Shaft	0	100%	15-Sep-25A	30-Sep-25A		15-Sep-25	30-Sep-25	0
CON-ELEV-101	Elevator 1/2 CMU Shaft	0	100%	01-Oct-25A	17-Oct-25A		03-Nov-25	20-Nov-25	24
CON-ELEV-102	Elevator Install	65	0%	01-Apr-26	30-Jun-26	26	10-Apr-26	09-Jul-26	7
Stair Shafts		9	0%	15-Sep-25A	13-Jan-26	161	15-Sep-25	20-Nov-25	-38
CON-STAIR-10	Stair Tower B CMU	0	100%	15-Sep-25A	24-Oct-25A		15-Sep-25	24-Oct-25	0
CON-STAIR-10	Stair Tower A CMU	0	100%	03-Oct-25A	17-Oct-25A		03-Oct-25	17-Oct-25	0
CON-STAIR-10	Stair Stringers and Pans	5	100%	29-Dec-25A	07-Jan-26	143	03-Nov-25	14-Nov-25	-38
CON-STAIR-10	Doors & HW - Stairs	2	100%	08-Jan-26	09-Jan-26	143	17-Nov-25	18-Nov-25	-38
CON-STAIR-10	Prep/Paint - Stairs	2	100%	12-Jan-26	13-Jan-26	161	19-Nov-25	20-Nov-25	-38
First Floor Interior Finishes		90	0%	12-Dec-25A	06-May-26	97	15-Jan-26	29-Apr-26	-5
CON-MB-L1-11	Fireproofing Structural Steel - 1st Floor	7	0%	12-Dec-25A	09-Jan-26	2	15-Jan-26	26-Jan-26	11
CON-MB-L1-11	OH & Wall Plumbing Rough In- 1st Floor	3	0%	12-Jan-26	14-Jan-26	68	27-Jan-26	29-Jan-26	11
CON-MB-L1-11	Electric & Low Voltage OH & Wall Rough In - 1st Floor	10	0%	12-Jan-26	23-Jan-26	61	27-Jan-26	09-Feb-26	11
CON-MB-L1-11	Sprinkler Rough In - 1st Floor	10	0%	12-Jan-26	23-Jan-26	143	27-Jan-26	09-Feb-26	11
CON-MB-L1-11	HVAC Rough In - 1st Floor	3	0%	12-Feb-26	16-Feb-26	45	27-Jan-26	29-Jan-26	-12
CON-MB-L1-11	OH & Wall MEP Inspections - 1st Floor	2	0%	17-Feb-26	18-Feb-26	45	10-Feb-26	11-Feb-26	-5
CON-MB-L1-12	Janus Wall Panels - 1st Floor	15	0%	13-Mar-26	02-Apr-26	29	16-Mar-26	03-Apr-26	1
CON-MB-L1-11	Hang & Finish Drywall - 1st Floor	7	0%	17-Apr-26	27-Apr-26	80	10-Apr-26	20-Apr-26	-5
CON-MB-L1-12	Doors & HW - 1st Floor	2	0%	28-Apr-26	29-Apr-26	102	21-Apr-26	22-Apr-26	-5
CON-MB-L1-12	Prep/Paint Walls & Ceilings - 1st Floor	2	0%	28-Apr-26	29-Apr-26	80	21-Apr-26	22-Apr-26	-5
CON-MB-L1-12	Plumbing Fixtures - 1st Floor	2	0%	30-Apr-26	01-May-26	83	23-Apr-26	24-Apr-26	-5
CON-MB-L1-12	Diffusers - 1st Floor	5	0%	30-Apr-26	06-May-26	80	23-Apr-26	29-Apr-26	-5
CON-MB-L1-12	Light Fixtures - 1st Floor	5	0%	30-Apr-26	06-May-26	80	23-Apr-26	29-Apr-26	-5
Second Floor Interior Finishes		44	0%	12-Jan-26	12-Mar-26	136	24-Dec-25	13-Mar-26	1
CON-MB-L2-10	Fireproofing Structural Steel - 2nd Floor	8	0%	12-Jan-26	21-Jan-26	2	27-Jan-26	05-Feb-26	11
CON-MB-L2-11	Electric OH & Wall Rough In- 2nd Floor	10	0%	05-Feb-26	18-Feb-26	29	06-Feb-26	19-Feb-26	1
CON-MB-L2-10	Doors & HW - 2nd Floor	2	100%	05-Feb-26	06-Feb-26	141	24-Dec-25	25-Dec-25	-31
CON-MB-L2-11	Sprinkler Rough In - 2nd Floor	10	0%	05-Feb-26	18-Feb-26	125	06-Feb-26	19-Feb-26	1
CON-MB-L2-10	Prep/Paint Walls - 2nd Floor	2	100%	09-Feb-26	10-Feb-26	141	26-Dec-25	29-Dec-25	-31
CON-MB-L2-111	HVAC Rough In - 2nd Floor	5	0%	12-Feb-26	18-Feb-26	29	06-Feb-26	12-Feb-26	-4
CON-MB-L2-11	OH & Wall MEP Inspections - 2nd Floor	1	0%	19-Feb-26	19-Feb-26	29	20-Feb-26	20-Feb-26	1
CON-MB-L2-10	Janus Wall Panels -2nd Floor	15	0%	20-Feb-26	12-Mar-26	29	23-Feb-26	13-Mar-26	1
CON-MB-L2-11	Diffusers - 2nd Floor	5	0%	20-Feb-26	26-Feb-26	146	23-Feb-26	27-Feb-26	1
CON-MB-L2-11	Light Fixtures - 2nd Floor	5	0%	20-Feb-26	26-Feb-26	146	23-Feb-26	27-Feb-26	1
Third Floor Interior Finishes		76	0%	22-Jan-26	07-May-26	69	06-Feb-26	30-Apr-26	-5
CON-MB-L3-10	Fire Proofing Structural Steel - 3rd Floor	8	0%	22-Jan-26	02-Feb-26	2	06-Feb-26	17-Feb-26	11
CON-MB-L3-10	OH & Wall Plumbing Rough In- 3rd Floor	3	0%	17-Feb-26	19-Feb-26	57	18-Feb-26	20-Feb-26	1
CON-MB-L3-10	Electric & Low Voltage OH & Wall Rough In - 3rd Floor	10	0%	17-Feb-26	02-Mar-26	50	18-Feb-26	03-Mar-26	1
CON-MB-L3-10	HVAC Rough In - 3rd Floor	5	0%	17-Feb-26	23-Feb-26	55	18-Feb-26	24-Feb-26	1
CON-MB-L3-11	Sprinkler Rough In - 3rd Floor	10	0%	17-Feb-26	02-Mar-26	117	18-Feb-26	03-Mar-26	1
CON-MB-L3-11	OH & Wall MEP Inspections - 3rd Floor	2	0%	03-Mar-26	04-Mar-26	50	04-Mar-26	05-Mar-26	1
CON-MB-L3-11	Janus Wall Panels -3rd Floor	15	0%	03-Apr-26	23-Apr-26	29	06-Apr-26	24-Apr-26	1
CON-MB-L3-11	Hang/Finish Drywall - 3rd Floor	7	0%	17-Apr-26	27-Apr-26	69	10-Apr-26	20-Apr-26	-5
CON-MB-L3-11	Prep/Paint Walls & Ceilings - 3rd Floor	3	0%	28-Apr-26	30-Apr-26	69	21-Apr-26	23-Apr-26	-5
CON-MB-L3-11	Plumbing Fixtures - 3rd Floor	4	0%	01-May-26	06-May-26	70	24-Apr-26	29-Apr-26	-5
CON-MB-L3-11	Diffusers - 3rd Floor	5	0%	01-May-26	07-May-26	69	24-Apr-26	30-Apr-26	-5

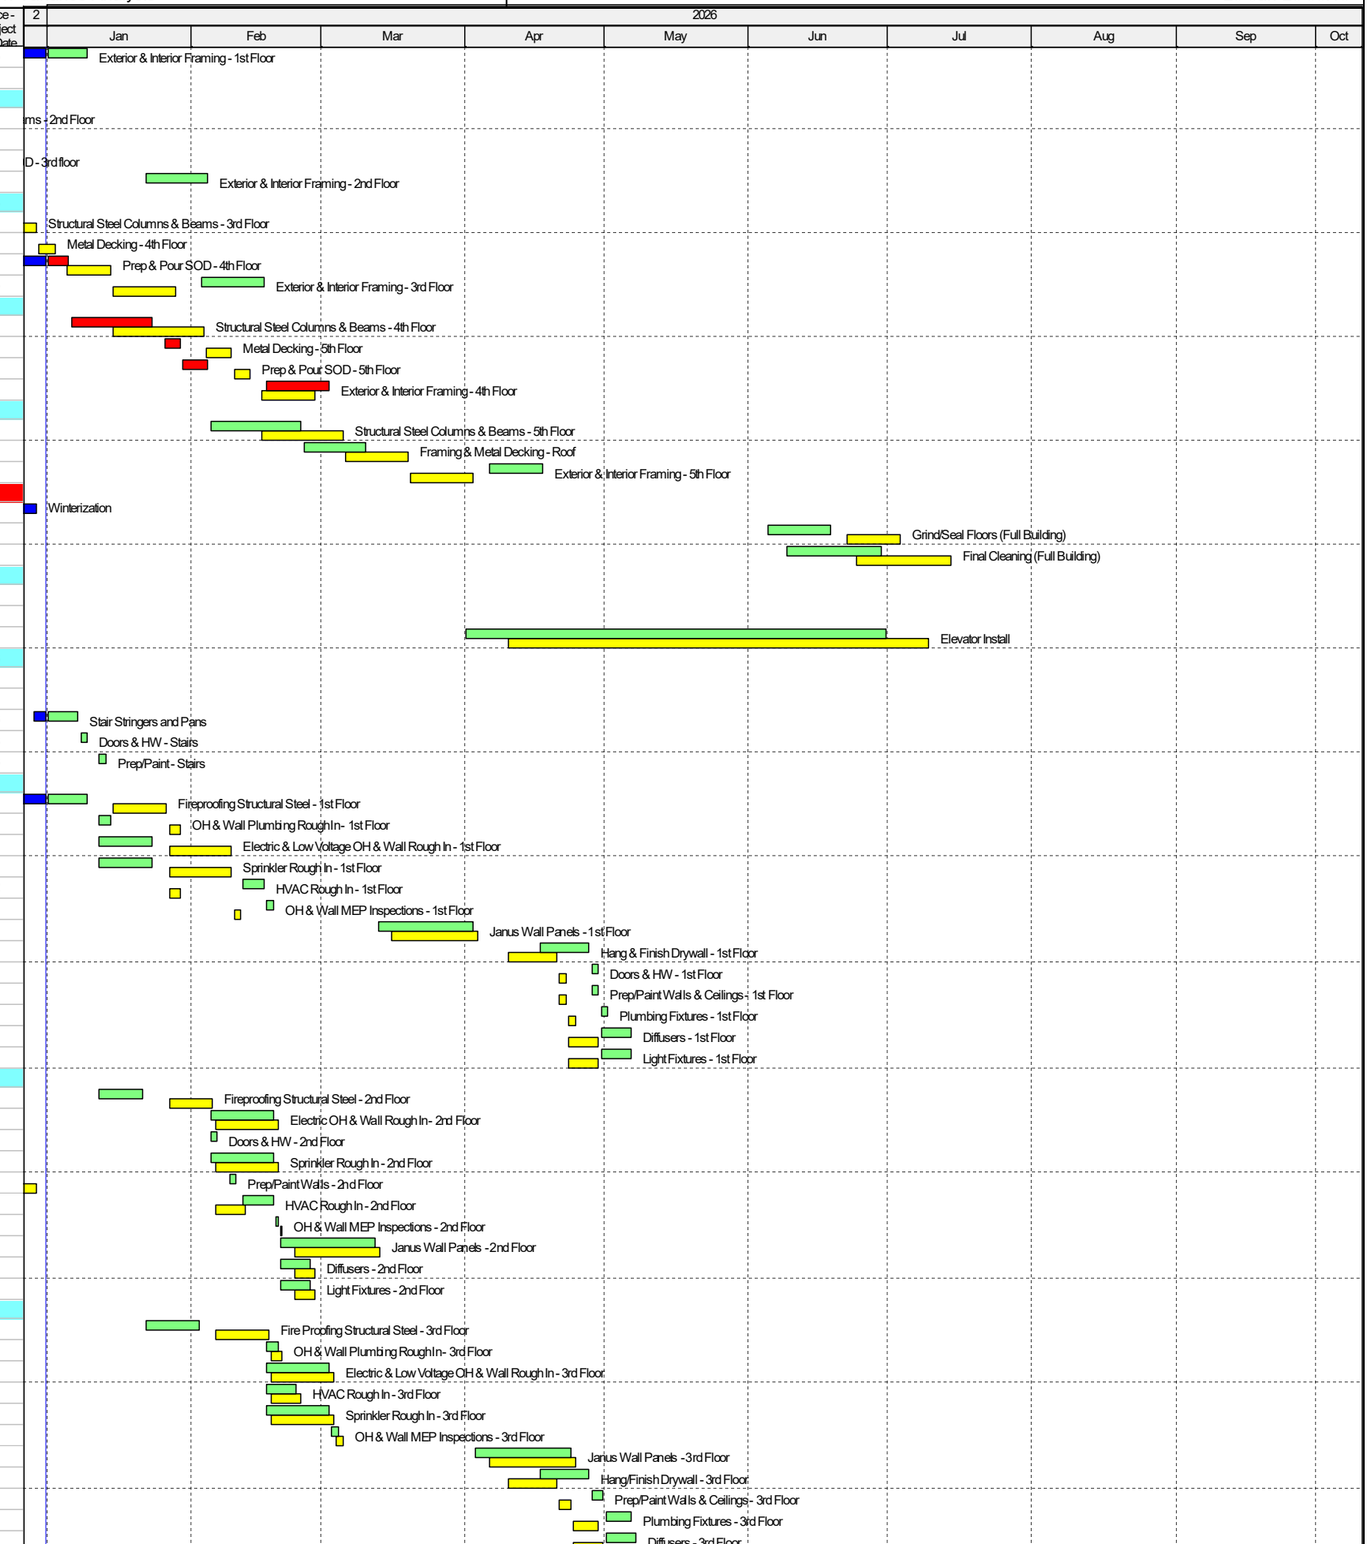

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
CON-MB-L3-11	Light Fixtures - 3rd Floor	5	0%	01-May-26	07-May-26	69	24-Apr-26	30-Apr-26	-5
Fourth Floor Interior Finishes		71	0%	05-Feb-26	14-May-26	64	10-Apr-26	29-May-26	11
CON-MB-L4-10	Fire Proofing Structural Steel - 4th Floor	8	0%	05-Feb-26	16-Feb-26	0	10-Apr-26	21-Apr-26	46
CON-MB-L4-10	Electric OH & Wall Rough In - 4th Floor	10	0%	03-Mar-26	16-Mar-26	56	24-Apr-26	07-May-26	38
CON-MB-L4-10	HVAC Rough In - 4th Floor	5	0%	03-Mar-26	09-Mar-26	61	24-Apr-26	30-Apr-26	38
CON-MB-L4-10	Sprinkler Rough In - 4th Floor	10	0%	03-Mar-26	16-Mar-26	107	24-Apr-26	07-May-26	38
CON-MB-L4-11	OH & Wall MEP Inspections - 4th Floor	1	0%	17-Mar-26	17-Mar-26	56	08-May-26	08-May-26	38
CON-MB-L4-111	Prep/Paint Walls - 4th Floor	2	0%	18-Mar-26	19-Mar-26	104	11-May-26	12-May-26	38
CON-MB-L4-11	Diffusers - 4th Floor	5	0%	18-Mar-26	24-Mar-26	101	11-May-26	15-May-26	38
CON-MB-L4-11	Light Fixtures - 4th Floor	5	0%	18-Mar-26	24-Mar-26	101	11-May-26	15-May-26	38
CON-MB-L4-11	Janus Wall Panels -4th Floor	15	0%	24-Apr-26	14-May-26	29	11-May-26	29-May-26	11
Fifth Floor Interior Finishes		47	0%	01-Apr-26	04-Jun-26	76	22-Apr-26	19-Jun-26	11
CON-MB-L5-10	Fire Proofing Structural Steel - 5th Floor	8	0%	01-Apr-26	10-Apr-26	9	22-Apr-26	01-May-26	15
CON-MB-L5-10	Electric & Low Voltage OH & Wall Rough In - 5th Floor	10	0%	20-Apr-26	01-May-26	30	04-May-26	15-May-26	10
CON-MB-L5-10	OH & Wall Plumbing Rough In - 5th Floor	3	0%	20-Apr-26	22-Apr-26	37	04-May-26	06-May-26	10
CON-MB-L5-10	HVAC Rough In - 5th Floor	5	0%	20-Apr-26	24-Apr-26	35	04-May-26	08-May-26	10
CON-MB-L5-10	Sprinkler Rough In - 5th Floor	10	0%	20-Apr-26	01-May-26	73	04-May-26	15-May-26	10
CON-MB-L5-111	OH & Wall MEP Inspections - 5th Floor	1	0%	04-May-26	04-May-26	30	18-May-26	18-May-26	10
CON-MB-L5-11	Hang/Finish Drywall - 5th Floor	7	0%	05-May-26	13-May-26	30	19-May-26	27-May-26	10
CON-MB-L5-11	Prep/Paint Walls - 5th Floor	2	0%	14-May-26	15-May-26	86	28-May-26	29-May-26	10
CON-MB-L5-11	Janus Wall Panels -5th Floor	15	0%	15-May-26	04-Jun-26	29	01-Jun-26	19-Jun-26	11
CON-MB-L5-11	Plumbing Fixtures - 5th Floor	4	0%	18-May-26	21-May-26	86	01-Jun-26	04-Jun-26	10
CON-MB-L5-11	Diffusers - 5th Floor	1	0%	18-May-26	18-May-26	89	01-Jun-26	01-Jun-26	10
CON-MB-L5-11	Light Fixtures - 5th Floor	1	0%	18-May-26	18-May-26	89	01-Jun-26	01-Jun-26	10
Switchgear Room		76	0%	20-Jan-26	05-May-26	61	10-Dec-25	25-Mar-26	-29
CON-POW-100	Switchgear Room Enclosure	10	100%	20-Jan-26	02-Feb-26	61	10-Dec-25	23-Dec-25	-29
CON-POW-101	Install Switchgear Equipment	15	40%	03-Feb-26	23-Feb-26	61	24-Dec-25	13-Jan-26	-29
CON-POW-102	Switchgear Lights and Power	15	0%	24-Feb-26	16-Mar-26	61	14-Jan-26	03-Feb-26	-29
CON-POW-103	City Inspection	1	0%	17-Mar-26	17-Mar-26	61	04-Feb-26	04-Feb-26	-29
CON-POW-104	Dominion Primary	20	0%	18-Mar-26	14-Apr-26	61	05-Feb-26	04-Mar-26	-29
CON-POW-105	Dominion Transformer	5	0%	15-Apr-26	21-Apr-26	61	05-Mar-26	11-Mar-26	-29
CON-POW-106	Dominion Secondary	5	0%	22-Apr-26	28-Apr-26	61	12-Mar-26	18-Mar-26	-29
CON-POW-107	Power Activation	5	0%	29-Apr-26	05-May-26	61	19-Mar-26	25-Mar-26	-29
Exterior Finishes		131	0%	12-Jan-26	13-Jul-26	12	12-Nov-25	29-Jul-26	12
CON-MB-L1-125	Exterior Sheathing - 1st Floor	6	100%	12-Jan-26	19-Jan-26	10	12-Nov-25	19-Nov-25	-43
CON-MB-L2-105	Exterior Sheathing - 2nd Floor	6	100%	27-Jan-26	03-Feb-26	4	15-Dec-25	22-Dec-25	-31
CON-MB-L1-128	Perimeter Waterproofing - 1st Floor	3	0%	04-Feb-26	06-Feb-26	4			
CON-MB-L3-105	Exterior Sheathing - 3rd Floor	6	0%	06-Feb-26	13-Feb-26	55	20-Jan-26	27-Jan-26	-13
CON-MB-L5-110	Brick Facade - 1st Floor	30	0%	09-Feb-26	20-Mar-26	4			
CON-MB-L4-104	Exterior Sheathing - 4th Floor	6	0%	20-Feb-26	27-Feb-26	0	19-Feb-26	26-Feb-26	-1
CON-MB-L1-126	Perimeter Waterproofing West Elevation (Excluding 5th Floor)	4	0%	02-Mar-26	05-Mar-26	0	27-Mar-26	01-Apr-26	19
CON-MB-EXT-1	Brick West Elevation (Excluding 5th Floor)	20	0%	06-Mar-26	02-Apr-26	0	02-Apr-26	27-Apr-26	17
CON-MB-L2-128	Perimeter Waterproofing North Elevation (Excluding 5th Floor)	4	0%	06-Mar-26	11-Mar-26	16	02-Apr-26	07-Apr-26	19
CON-MB-EXT-11	Storefront	20	0%	23-Mar-26	17-Apr-26	66	23-Jun-26	20-Jul-26	66
CON-MB-EXT-1	Brick North and West Elevations (5th Floor)	25	0%	03-Apr-26	07-May-26	0	28-Apr-26	21-May-26	10
CON-MB-EXT-1	Stucco West Elevation	15	0%	03-Apr-26	23-Apr-26	25	28-Apr-26	05-May-26	8
CON-MB-L5-103	Exterior Sheathing - 5th Floor	6	0%	09-Apr-26	16-Apr-26	9	25-Mar-26	01-Apr-26	-11
CON-MB-L2-131	Perimeter Waterproofing West/North Elevations (5th Floor)	2	0%	17-Apr-26	20-Apr-26	9			
CON-MB-EXT-11	Canopies	7	0%	20-Apr-26	28-Apr-26	66	21-Jul-26	29-Jul-26	66
CON-MB-L2-129	Perimeter Waterproofing East Elevation	4	0%	21-Apr-26	24-Apr-26	9	08-Apr-26	13-Apr-26	-9
CON-MB-EXT-1	Glass West Elevation	7	0%	24-Apr-26	04-May-26	41	06-May-26	14-May-26	8
CON-MB-L2-130	Perimeter Waterproofing South Elevation	4	0%	27-Apr-26	30-Apr-26	30	14-Apr-26	17-Apr-26	-9
CON-MB-EXT-1	Glass North Elevation	7	0%	05-May-26	13-May-26	41	15-May-26	25-May-26	8
CON-MB-EXT-1	Brick East Elevation	25	0%	08-May-26	11-Jun-26	0	22-May-26	16-Jun-26	3
CON-MB-EXT-1	Stucco North Elevation	7	0%	08-May-26	18-May-26	15	22-May-26	29-May-26	9
CON-MB-EXT-11	Glass East Elevation	7	0%	14-May-26	22-May-26	41	26-May-26	03-Jun-26	8
CON-MB-EXT-1	Stucco East Elevation	14	0%	19-May-26	05-Jun-26	15	01-Jun-26	08-Jun-26	1
CON-MB-EXT-11	Glass South Elevation	7	0%	25-May-26	02-Jun-26	41	04-Jun-26	12-Jun-26	8
CON-MB-EXT-11	Stucco South Elevation	7	0%	08-Jun-26	16-Jun-26	15	09-Jun-26	16-Jun-26	0
CON-MB-EXT-1	Brick South Elevation	18	0%	12-Jun-26	07-Jul-26	0	17-Jun-26	10-Jul-26	3
CON-MB-EXT-11	Swing Doors/Automatic Sliding Entrance	4	0%	08-Jul-26	13-Jul-26	12	13-Jul-26	16-Jul-26	3
Roofing		15	0%	11-Mar-26	31-Mar-26	9	20-Mar-26	09-Apr-26	7
CON-MB-L5-102	Roof Insulation & TPO	15	0%	11-Mar-26	31-Mar-26	9	20-Mar-26	09-Apr-26	7
Office Building		17	0%	21-Jul-25A	23-Jan-26	147	21-Jul-25	25-Dec-25	-21
Structure - Office		0	0%	21-Jul-25A	02-Dec-25A		21-Jul-25	04-Nov-25	-20
CON-OFF-1000	Prep/Pour SOG - Office Building	0	100%	21-Jul-25A	22-Jul-25A		21-Jul-25	22-Jul-25	0
CON-OFF-1010	Structural Steel - Office Building	0	100%	30-Sep-25A	30-Sep-25A		30-Sep-25	30-Sep-25	0
CON-OFF-1030	Interior/Exterior Framing - Office Building	0	100%	10-Oct-25A	22-Oct-25A		10-Oct-25	22-Oct-25	0
CON-OFF-1070	Framing Inspection - Office Building	0	100%	22-Oct-25A	22-Oct-25A		22-Oct-25	22-Oct-25	0
CON-OFF-1050	Roof Decking - Office Building	0	100%	27-Oct-25A	27-Oct-25A		27-Oct-25	27-Oct-25	0
CON-OFF-1020	Foundation Waterproofing - Office Building	0	100%	31-Oct-25A	02-Dec-25A		31-Oct-25	04-Nov-25	-20

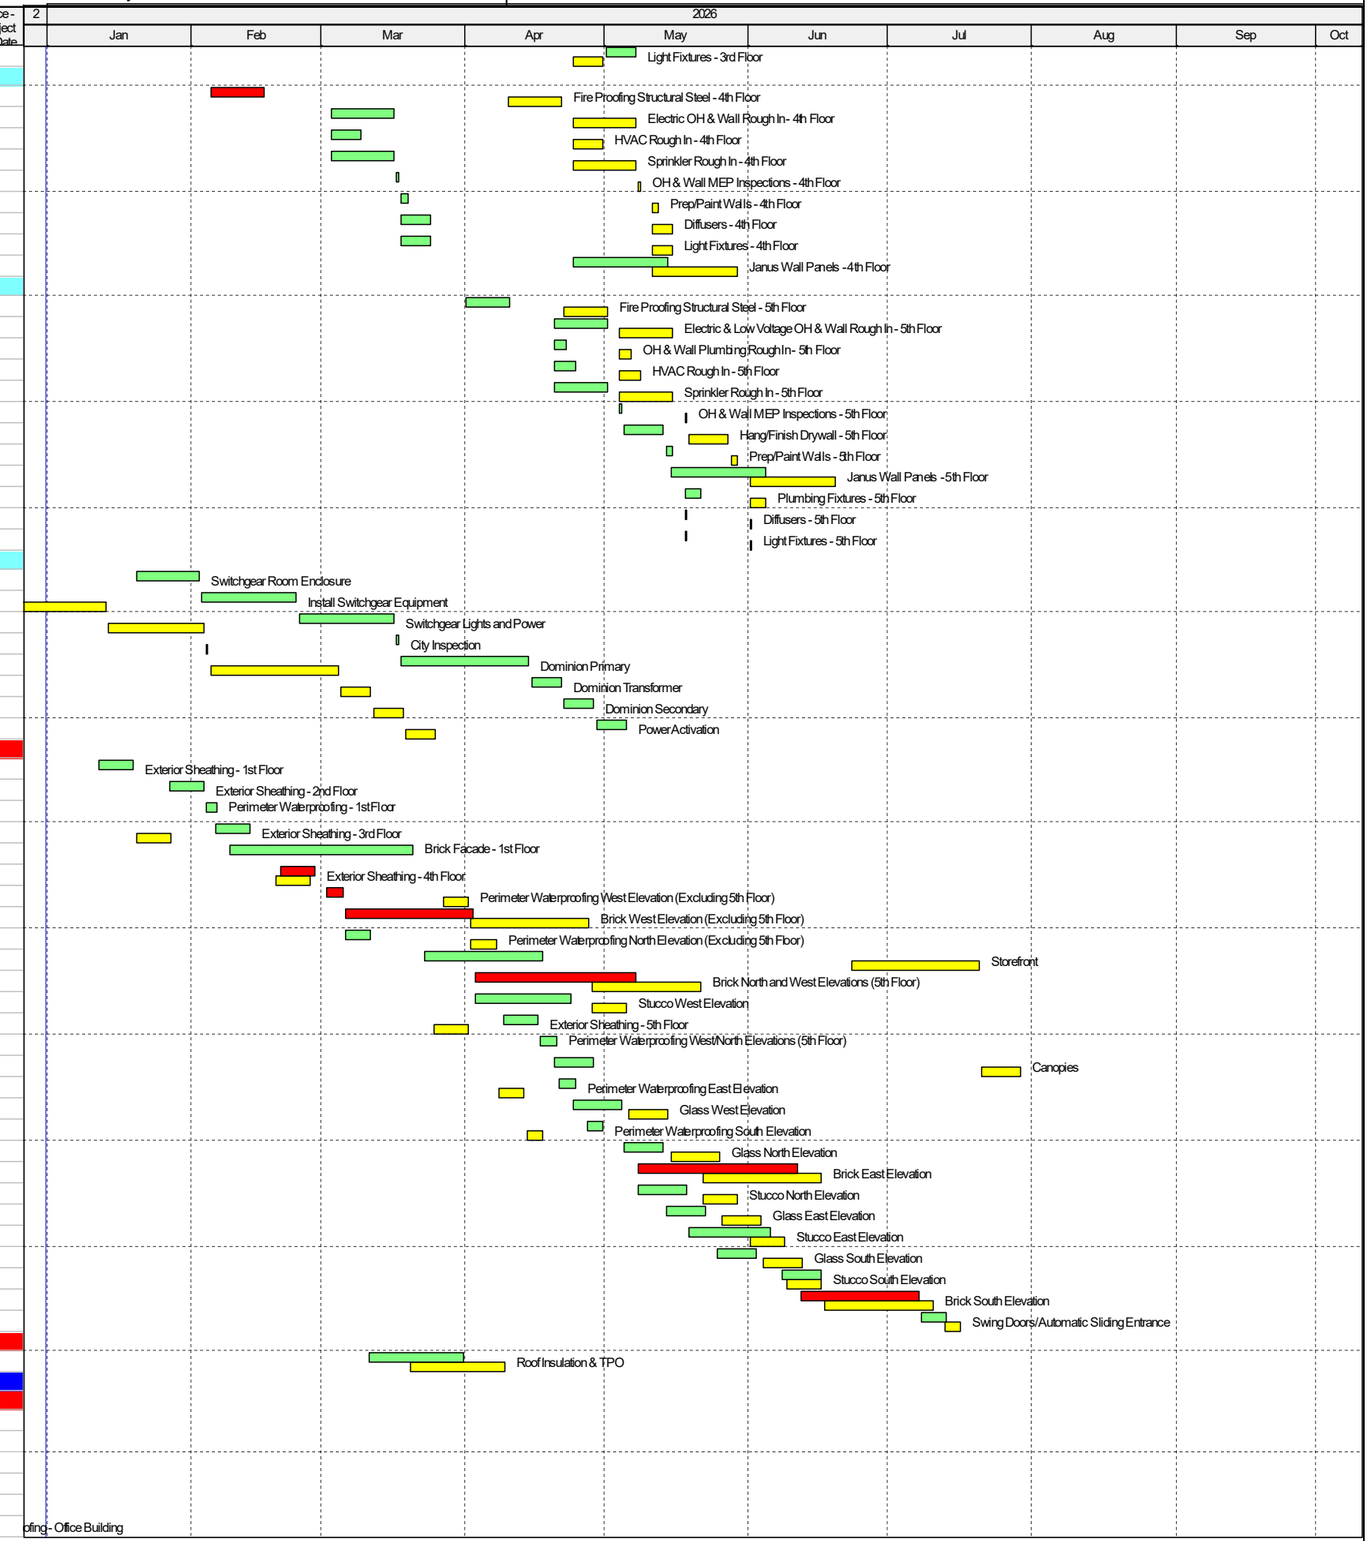

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
Interior Finishes - Office		**17**	**0%**	**03-Dec-25A**	**23-Jan-26**	**147**	**05-Nov-25**	**25-Dec-25**	**-21**
CON-OFF-1080	MEP Rough In - Office Building	0	100%	03-Dec-25A	12-Dec-25A		05-Nov-25	07-Nov-25	-25
CON-OFF-1090	MEP Inspections - Office Building	2	100%	29-Dec-25A	02-Jan-26	143	10-Nov-25	10-Nov-25	-39
CON-OFF-1100	Hang/Finish Drywall - Office Building	3	100%	05-Jan-26	07-Jan-26	143	11-Nov-25	13-Nov-25	-39
CON-OFF-1110	Doors, Frames & Hardware - Office Building	2	100%	08-Jan-26	09-Jan-26	143	14-Nov-25	17-Nov-25	-39
CON-OFF-1120	Prep/Paint Walls - Office Building	2	100%	12-Jan-26	13-Jan-26	143	18-Nov-25	19-Nov-25	-39
CON-OFF-1130	Flooring - Office Building	5	100%	14-Jan-26	20-Jan-26	143	20-Nov-25	26-Nov-25	-39
CON-OFF-1140	MEP Finishes, Fixtures,Accessories - Office Building	2	100%	21-Jan-26	22-Jan-26	143	27-Nov-25	28-Nov-25	-39
CON-OFF-1150	Millwork - Office Building	2	100%	21-Jan-26	22-Jan-26	147	27-Nov-25	28-Nov-25	-39
CON-OFF-1220	Final Cleaning - Office Building	1	100%	23-Jan-26	23-Jan-26	147	25-Dec-25	25-Dec-25	-21
Exterior Finishes - Office		**8**	**0%**	**29-Oct-25A**	**12-Jan-26**	**151**	**29-Oct-25**	**24-Dec-25**	**-13**
CON-OFF-1040	Roofing - Office Building	0	100%	29-Oct-25A	29-Oct-25A		29-Oct-25	29-Oct-25	0
CON-OFF-1060	Exterior Sheathing/Waterproofing - Office Building	3	100%	29-Dec-25A	05-Jan-26	151	03-Nov-25	05-Nov-25	-43
CON-OFF-1160	Store Front & Windows - Office Building	3	100%	06-Jan-26	08-Jan-26	153	22-Dec-25	24-Dec-25	-11
CON-OFF-1170	Brick Facade - Office Building	5	100%	06-Jan-26	12-Jan-26	151	06-Nov-25	12-Nov-25	-43
Final Inspections & Close Out		**166**	**0%**	**23-Jan-26**	**11-Sep-26**	**5**	**25-Dec-25**	**08-Sep-26**	**-3**
Office Building		**22**	**0%**	**23-Jan-26**	**23-Feb-26**	**149**	**25-Dec-25**	**23-Jan-26**	**-21**
CLO-OFF-1030	Final Building Inspections - Office Building	5	100%	23-Jan-26	29-Jan-26	143	25-Dec-25	31-Dec-25	-21
CLO-OFF-1040	Punch List Walk - Office Building	2	0%	30-Jan-26	02-Feb-26	149	01-Jan-26	02-Jan-26	-21
CLO-OFF-1000	Office Temporary Occupancy	1	0%	30-Jan-26	30-Jan-26*	143	01-Jan-26	01-Jan-26	-21
CLO-OFF-1050	Punch List Corrections - Office Building	15	0%	03-Feb-26	23-Feb-26	149	05-Jan-26	23-Jan-26	-21
Main Building		**44**	**0%**	**14-Jul-26**	**11-Sep-26**	**5**	**30-Jul-26**	**08-Sep-26**	**-3**
CLO-MB-1000	Fire Alarm Inspection	5	0%	14-Jul-26	20-Jul-26	12	30-Jul-26	05-Aug-26	12
CLO-MB-1010	State Inspection for Elevators	5	0%	21-Jul-26	27-Jul-26	12	06-Aug-26	12-Aug-26	12
CLO-MB-1020	Final Building Inspections	5	0%	28-Jul-26	03-Aug-26	12	13-Aug-26	19-Aug-26	12
CLO-MB-1040	Punch List Walk - Main Building	2	0%	20-Aug-26	21-Aug-26	5	17-Aug-26	18-Aug-26	-3
CLO-MB-1050	Punch List Corrections - Main Building	15	0%	24-Aug-26	11-Sep-26	5	19-Aug-26	08-Sep-26	-3

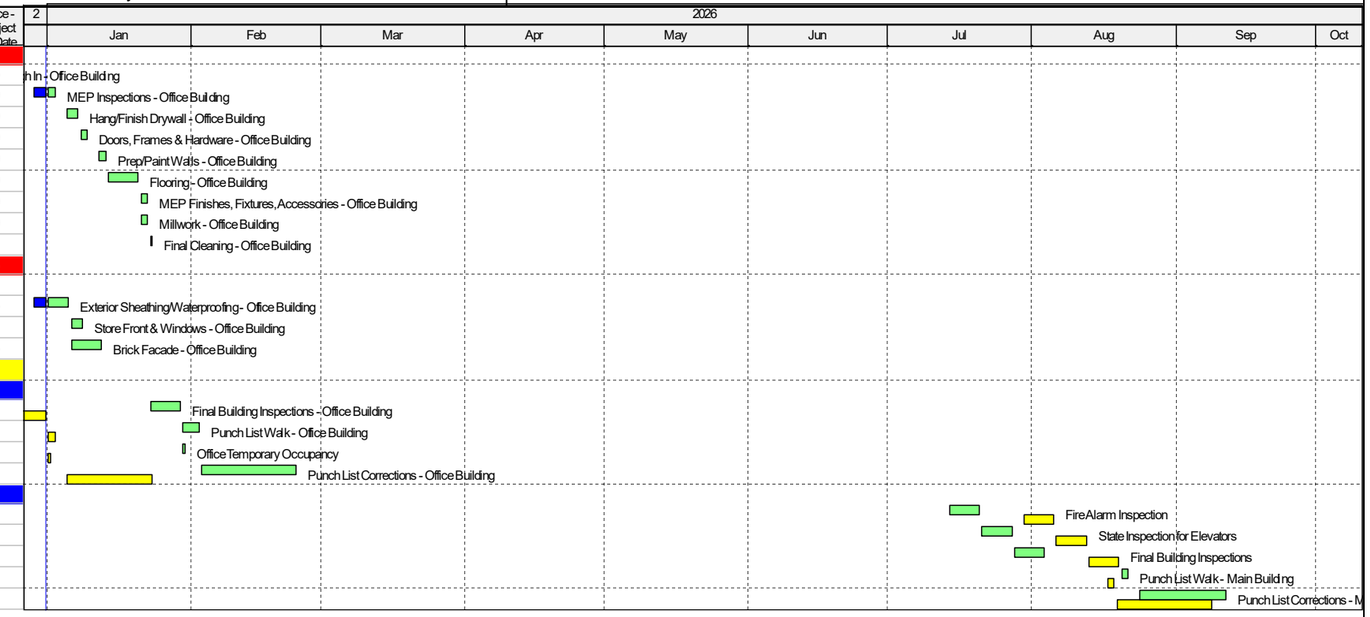

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation
