Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

Public Storage Dashboard

Data Date: 1/31/2026

Type	Project	Region	Responsible
Construction	Fairfax, VA	East Coast	Ross Kremers

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
8/19/2026	8/12/2026	7 Baseline 7 Previous	Remaining Work Compression: 11.00% — WARNING

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	5/5/2025	5/5/2025	5/5/2025	0	0	Notice To Proceed (05.05.25)	On Track – Gaining
Foundation Complete	9/22/2025	9/22/2025	9/22/2025	0	0	Prep/Pour Sog 2/2	On Track – Gaining
2nd Floor Finishes Complete	5/21/2026	2/26/2026	2/25/2026	85	1	Light Fixtures - 2Nd Floor	On Track – Gaining
4th Floor Finishes Complete	5/11/2026	3/24/2026	4/8/2026	33	-15	Light Fixtures - 4Th Floor	On Track – Slipping
Weather Tight	4/1/2026	4/16/2026	5/1/2026	-30	-15	Weathertight - Main Building	Delayed – Slipping
Structure Top Out	3/25/2026	4/17/2026	5/4/2026	-40	-17	Exterior & Interior Framing - 5Th Floor	Delayed – Slipping
Permanent Power	3/24/2026	5/6/2026	5/20/2026	-57	-14	Permanent Power	Delayed – Slipping
3rd Floor Finishes Complete	5/29/2026	5/7/2026	5/22/2026	7	-15	Light Fixtures - 3Rd Floor	On Track – Slipping
1st Floor Finishes Complete	6/11/2026	5/6/2026	5/25/2026	17	-19	Light Fixtures - 1St Floor	On Track – Slipping
5th Floor Finishes Complete	5/7/2026	5/18/2026	6/2/2026	-26	-15	Light Fixtures - 5Th Floor	Delayed – Slipping
Elevator Complete	7/1/2026	6/30/2026	7/15/2026	-14	-15	Elevator Install	Delayed – Slipping
Hardscape/Landscape Complete	8/14/2026	8/19/2026	8/12/2026	2	7	Landscape - Main Building	On Track – Gaining
Contract Completion	8/19/2026	8/19/2026	8/12/2026	7	7	Substantial Completion (08.19.26)	On Track – Gaining

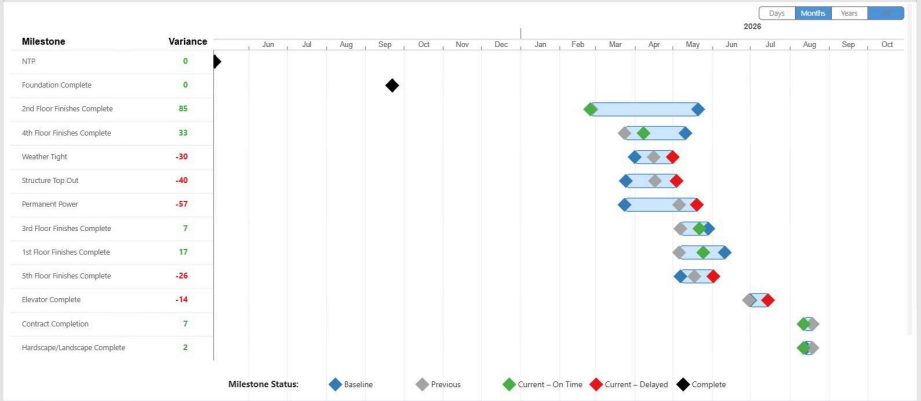

Baseline Variance

Schedule Performance Summary

Summary

The schedule is experiencing serious performance and quality degradation, with critical path slippage, excessive compression, and poor execution control all present. These indicators point toward heightened risk of significant delay and potential compromise of project and contractual objectives. Immediate intervention is required—focusing on restoring execution discipline, validating schedule quality, and reassessing compressed activities—to regain control and reduce schedule uncertainty.

Schedule Validation Score: 82.00% — WARNING
The SV Score is below the PASS threshold, indicating moderate schedule quality risks such as open-ended logic or constraint issues. Recommended action: review and address underlying logic and constraint defects to improve reliability.

Schedule Change Index: 6.00% — WARNING
There has been a moderate volume of activity logic/date changes, reflecting some schedule volatility. Monitor for persistent changes and reinforce baseline discipline to enhance predictability.

Critical Path Compression: 14.00% — ALERT
Excessive compression efforts have been applied to the critical path, suggesting the project team is making aggressive adjustments that may strain resources or compromise quality. Assess feasibility of the current plan and validate critical path logic for realism.

Execution Score: 38.00% — ALERT
Execution discipline is severely lacking, with less than half of expected near-term activities progressing as planned. Immediate corrective action is needed to improve schedule usage in daily/weekly planning cycles.

Remaining Work Compression: 11.00% — WARNING
The percentage of remaining activities with shortened durations is elevated, indicating possible over-compression that may threaten future performance. Cautiously review remaining work plans and resource allocations.

Critical Path Variance: 48.00% — ALERT
The critical path duration has lengthened substantially compared to baseline, signaling high risk of major project delay. Perform root cause analysis and develop a recovery plan targeting critical activities.

Powered By STELIC INSIGHT • ACTION • IMPACT
