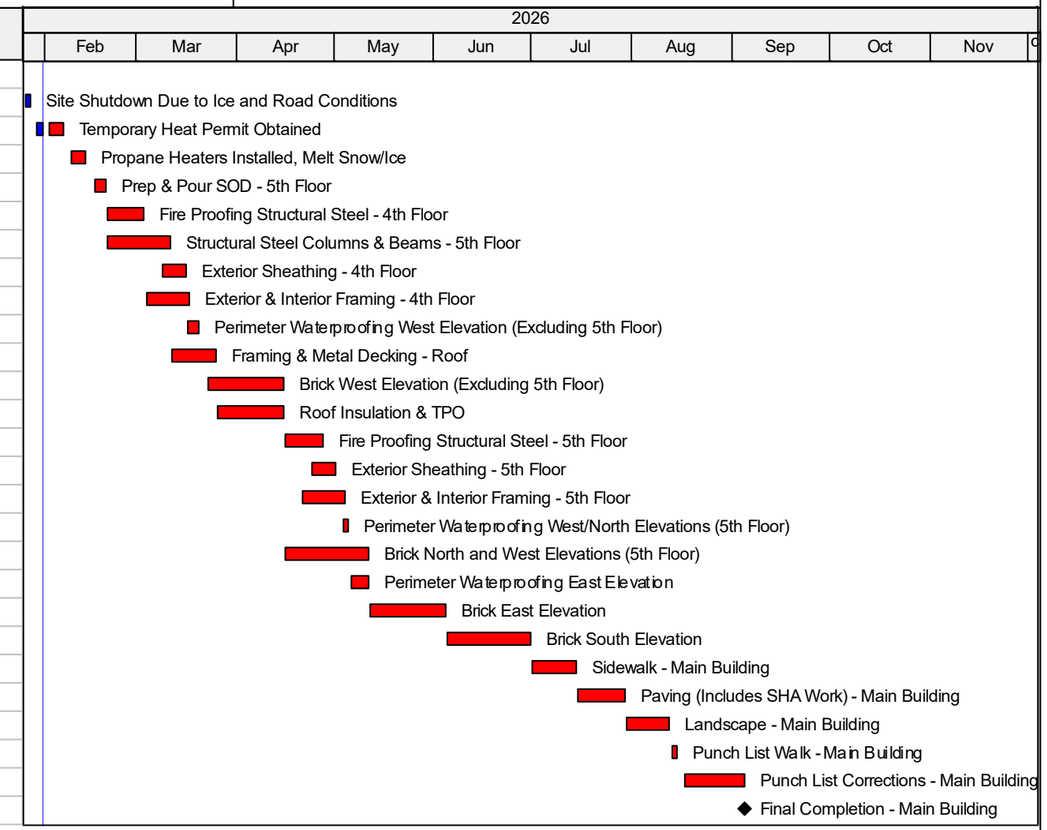Activity ID	Activity Name	OD	RD	% Complete	Start	Finish	TF
MIL-1000	Notice to Proceed (05.05.25)	0	0	100%	05-May-25 A		
FRAG01-1000	Site Shutdown Due to Ice and Road Conditions	2	0	100%	26-Jan-26 A	27-Jan-26 A	
FRAG01-1020	Temporary Heat Permit Obtained	7	5	28.57%	29-Jan-26 A	06-Feb-26	-12
FRAG01-1030	Propane Heaters Installed, Melt Snow/Ice	5	5	0%	09-Feb-26	13-Feb-26	-12
CON-MB-L4-1020	Prep & Pour SOD - 5th Floor	4	4	0%	16-Feb-26	19-Feb-26	-12
CON-MB-L4-1050	Fire Proofing Structural Steel - 4th Floor	8	8	0%	20-Feb-26	03-Mar-26	-12
CON-MB-L5-1000	Structural Steel Columns & Beams - 5th Floor	14	14	0%	20-Feb-26	11-Mar-26	-12
CON-MB-L4-1040	Exterior Sheathing - 4th Floor	6	6	0%	09-Mar-26	16-Mar-26	-12
CON-MB-L4-1030	Exterior & Interior Framing - 4th Floor	10	10	0%	04-Mar-26	17-Mar-26	-12
CON-MB-L1-1260	Perimeter Waterproofing West Elevation (Excluding 5th Floor)	4	4	0%	17-Mar-26	20-Mar-26	-12
CON-MB-L5-1010	Framing & Metal Decking - Roof	10	10	0%	12-Mar-26	25-Mar-26	-12
CON-MB-EXT-1000	Brick West Elevation (Excluding 5th Floor)	18	18	0%	23-Mar-26	15-Apr-26	-12
CON-MB-L5-1020	Roof Insulation & TPO	15	15	0%	26-Mar-26	15-Apr-26	-12
CON-MB-L5-1040	Fire Proofing Structural Steel - 5th Floor	8	8	0%	16-Apr-26	27-Apr-26	-12
CON-MB-L5-1030	Exterior Sheathing - 5th Floor	6	6	0%	24-Apr-26	01-May-26	-12
CON-MB-L5-1050	Exterior & Interior Framing - 5th Floor	10	10	0%	21-Apr-26	04-May-26	-12
CON-MB-L2-1310	Perimeter Waterproofing West/North Elevations (5th Floor)	2	2	0%	04-May-26	05-May-26	-12
CON-MB-EXT-1020	Brick North and West Elevations (5th Floor)	18	18	0%	16-Apr-26	11-May-26	-12
CON-MB-L2-1290	Perimeter Waterproofing East Elevation	4	4	0%	06-May-26	11-May-26	-12
CON-MB-EXT-1030	Brick East Elevation	18	18	0%	12-May-26	04-Jun-26	-12
CON-MB-EXT-1050	Brick South Elevation	18	18	0%	05-Jun-26	30-Jun-26	-12
SITE-MB-1080	Sidewalk - Main Building	10	10	0%	01-Jul-26	14-Jul-26	-12
SITE-MB-1130	Paving (Includes SHA Work) - Main Building	11	11	0%	15-Jul-26	29-Jul-26	-12
SITE-MB-1090	Landscape - Main Building	10	10	0%	30-Jul-26	12-Aug-26	-12
CLO-MB-1040	Punch List Walk - Main Building	2	2	0%	13-Aug-26	14-Aug-26	-12
CLO-MB-1050	Punch List Corrections - Main Building	15	15	0%	17-Aug-26	04-Sep-26	-12
MIL-1040	Final Completion - Main Building	0	0	0%		04-Sep-26*	-16
