Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
VA18231 - Fairfax - Lee Hwy (land) - 08239- 2026.02.28 UP05		138	0%	27-Oct-25A	09-Sep-26	7	27-Oct-25	04-Sep-26	-3
Public Storage Fairfax VA		138	0%	27-Oct-25A	09-Sep-26	7	27-Oct-25	04-Sep-26	-3
Milestones		94	0%	30-Apr-26	09-Sep-26	7	01-May-26	04-Sep-26	-3
MIL-1010	Weathertight - Main Building	0	0%		30-Apr-26	35		01-May-26	1
MIL-1020	Permanent Power	0	0%	17-Jun-26		34	20-May-26		-20
MIL-1030	Substantial Completion (08.24.26)	0	0%		17-Aug-26*	7		12-Aug-26	-5
MIL-1040	Final Completion - Main Building	0	0%		09-Sep-26*	10		04-Sep-26	-5
Preconstruction		21	0%	27-Oct-25A	30-Mar-26	90	27-Oct-25	06-Mar-26	-16
Procurement		21	0%	27-Oct-25A	30-Mar-26	90	27-Oct-25	06-Mar-26	-16
Long Lead Items		21	0%	27-Oct-25A	30-Mar-26	90	27-Oct-25	06-Mar-26	-16
PROC-1090	Fire Pump Submittal	1	100%	27-Oct-25A	02-Mar-26	90	27-Oct-25	02-Feb-26	-20
PROC-1100	Elevator Fabrication	20	92.75%	05-Jan-26A	27-Mar-26	31	02-Dec-25	06-Mar-26	-15
PROC-1150	Fire Pump Fabrication	20	95%	03-Mar-26	30-Mar-26	90	03-Feb-26	02-Mar-26	-20
Fragnets		0	0%			0			
Fragnet 01 - Weather Impact January 2026		0	0%			0			
Fragnet 02 - Weather Impact February 2026		0	0%			0			
Construction		121	0%	03-Nov-25A	17-Aug-26	7	03-Nov-25	12-Aug-26	-3
Site Work		121	0%	03-Nov-25A	17-Aug-26	7	03-Nov-25	12-Aug-26	-3
SITE-1030	Stormwater Management Ponds Phase II	10	0%	24-Apr-26	07-May-26	79	27-Mar-26	10-Apr-26	-20
Site Work - Main Building		121	0%	03-Nov-25A	17-Aug-26	5	03-Nov-25	12-Aug-26	-3
SITE-MB-1050	Storm Structures and Pipe - Main Building	10	100%	03-Nov-25A	13-Mar-26	83	03-Nov-25	11-Feb-26	-23
SITE-MB-1070	Fine Grading - Main Building	15	100%	02-Mar-26	20-Mar-26	16	16-Dec-25	11-Feb-26	-28
SITE-MB-1060	Sanitary Sewer - Main Building	10	100%	01-Apr-26*	14-Apr-26	71	11-Feb-26	25-Feb-26	-35
SITE-MB-1100	Curb and Gutter - Main Building	7	0%	27-May-26	04-Jun-26	34	12-May-26	20-May-26	-11
SITE-MB-1120	Stone Base Parking Lot - Main Building	10	0%	05-Jun-26	18-Jun-26	34	21-May-26	03-Jun-26	-11
SITE-MB-1080	Sidewalk - Main Building	10	0%	16-Jul-26	29-Jul-26	5	01-Jul-26	14-Jul-26	-11
SITE-MB-1090	Landscape - Main Building	10	0%	16-Jul-26	29-Jul-26	18	30-Jul-26	12-Aug-26	10
SITE-MB-1130	Paving (Includes SHA Work) - Main Building	11	0%	30-Jul-26	13-Aug-26	5	15-Jul-26	29-Jul-26	-11
SITE-MB-1140	Line Striping - Main Building	2	0%	14-Aug-26	17-Aug-26	5	30-Jul-26	31-Jul-26	-11
Site Work - Office		18	0%	02-Mar-26	25-Mar-26	110	16-Dec-25	25-May-26	42
SITE-OFF-1060	Fine Grading - Office Building	6	100%	02-Mar-26	09-Mar-26	110	16-Dec-25	16-Jan-26	-36
SITE-OFF-1080	Landscape - Office Building	1	100%	10-Mar-26	10-Mar-26	121	02-Feb-26	02-Feb-26	-26
SITE-OFF-1030	Domestic & Fire Water Online - Office Building	10	100%	02-Mar-26	13-Mar-26	106	02-Feb-26	13-Feb-26	-20
SITE-OFF-1090	Curb and Gutter - Office Building	1	100%	16-Mar-26	16-Mar-26	106	16-Feb-26	16-Feb-26	-20
SITE-OFF-1110	Stone Base Parking Lot - Office Building	1	100%	17-Mar-26	17-Mar-26	107	17-Dec-25	17-Dec-25	-64
SITE-OFF-1070	Sidewalk - Office Building	2	100%	17-Mar-26	18-Mar-26	106	04-Feb-26	05-Feb-26	-29
SITE-OFF-1120	Paving - Office Building	2	100%	19-Mar-26	20-Mar-26	106	18-Dec-25	03-Feb-26	-33
SITE-OFF-1130	Line Striping - Office Building	1	100%	23-Mar-26	23-Mar-26	106	04-Feb-26	04-Feb-26	-33
SITE-OFF-1100	Misc Exterior Items (Vehicle Gate Operator) - Office Building	3	0%	23-Mar-26	25-Mar-26	110	20-May-26	25-May-26	42
Main Building		102	0%	05-Jan-26A	21-Jul-26	26	12-Jan-26	15-Jul-26	-4
Substructure		5	0%	03-Mar-26	09-Mar-26	5	03-Feb-26	10-Feb-26	-20
CON-MB-1040	Foundation Waterproofing	5	100%	03-Mar-26	09-Mar-26	5	03-Feb-26	10-Feb-26	-20
Superstructure		45	0%	02-Feb-26A	01-May-26	17	13-Jan-26	04-May-26	1
First Floor Superstructure		0	0%			0			
Second Floor Superstructure		1	0%	02-Feb-26A	02-Mar-26	5	13-Jan-26	03-Feb-26	-19
CON-MB-L2-1040	Exterior & Interior Framing - 2nd Floor	1	100%	02-Feb-26A	02-Mar-26	5	13-Jan-26	03-Feb-26	-19
Third Floor Superstructure		10	0%	05-Mar-26	18-Mar-26	31	12-Feb-26	25-Feb-26	-15
CON-MB-L3-1040	Exterior & Interior Framing - 3rd Floor	10	100%	05-Mar-26	18-Mar-26	31	12-Feb-26	25-Feb-26	-15
Fourth Floor Superstructure		10	0%	17-Mar-26	30-Mar-26	7	04-Mar-26	17-Mar-26	-9
CON-MB-L4-1030	Exterior & Interior Framing - 4th Floor	10	0%	17-Mar-26	30-Mar-26	7	04-Mar-26	17-Mar-26	-9
Fifth Floor Superstructure		45	0%	16-Feb-26A	01-May-26	17	20-Feb-26	04-May-26	1
CON-MB-L5-1000	Structural Steel Columns & Beams - 5th Floor	7	42.86%	16-Feb-26A	10-Mar-26	17	20-Feb-26	11-Mar-26	1
CON-MB-L5-1010	Framing & Metal Decking - Roof	10	0%	11-Mar-26	24-Mar-26	17	12-Mar-26	25-Mar-26	1
CON-MB-L5-1050	Exterior & Interior Framing - 5th Floor	10	0%	20-Apr-26	01-May-26	17	21-Apr-26	04-May-26	1
Interior Finishes		101	0%	19-Feb-26A	20-Jul-26	27	19-Jan-26	15-Jul-26	-3
CON-MB-2000	Grind/Seal Floors (Full Building)	10	0%	26-Jun-26	09-Jul-26	17	19-Jun-26	02-Jul-26	-5
CON-MB-2010	Final Cleaning (Full Building)	15	0%	30-Jun-26	20-Jul-26	25	23-Jun-26	13-Jul-26	-5
Elevator		65	0%	15-Apr-26	14-Jul-26	19	16-Apr-26	15-Jul-26	1
CON-ELEV-1020	Elevator Install	65	0%	15-Apr-26	14-Jul-26	19	16-Apr-26	15-Jul-26	1
Stair Shafts		4	0%	15-Apr-26	20-Apr-26	92	02-Feb-26	05-Feb-26	-52
CON-STAIR-1030	Doors & HW - Stairs	2	100%	15-Apr-26	16-Apr-26	77	02-Feb-26	03-Feb-26	-52
CON-STAIR-1040	Prep/Paint - Stairs	2	100%	17-Apr-26	20-Apr-26	92	04-Feb-26	05-Feb-26	-52
First Floor Interior Finishes		60	0%	02-Mar-26	22-May-26	68	10-Feb-26	25-May-26	1
CON-MB-L1-1180	OH & Wall MEP Inspections - 1st Floor	2	100%	02-Mar-26	03-Mar-26	39	10-Feb-26	11-Feb-26	-14
CON-MB-L1-1270	Janus Wall Panels - 1st Floor	15	0%	03-Apr-26	23-Apr-26	17	12-Mar-26	01-Apr-26	-16
CON-MB-L1-1190	Hang & Finish Drywall - 1st Floor	7	0%	01-May-26	11-May-26	68	04-May-26	12-May-26	1
CON-MB-L1-1200	Doors & HW - 1st Floor	2	0%	12-May-26	13-May-26	68	13-May-26	14-May-26	1
CON-MB-L1-1210	Prep/Paint Walls & Ceilings - 1st Floor	2	0%	14-May-26	15-May-26	68	15-May-26	18-May-26	1
CON-MB-L1-1220	Plumbing Fixtures - 1st Floor	2	0%	18-May-26	19-May-26	71	19-May-26	20-May-26	1
CON-MB-L1-1230	Diffusers - 1st Floor	5	0%	18-May-26	22-May-26	68	19-May-26	25-May-26	1
CON-MB-L1-1240	Light Fixtures - 1st Floor	5	0%	18-May-26	22-May-26	68	19-May-26	25-May-26	1
Second Floor Interior Finishes		24	0%	19-Feb-26A	02-Apr-26	104	19-Jan-26	11-Mar-26	-16

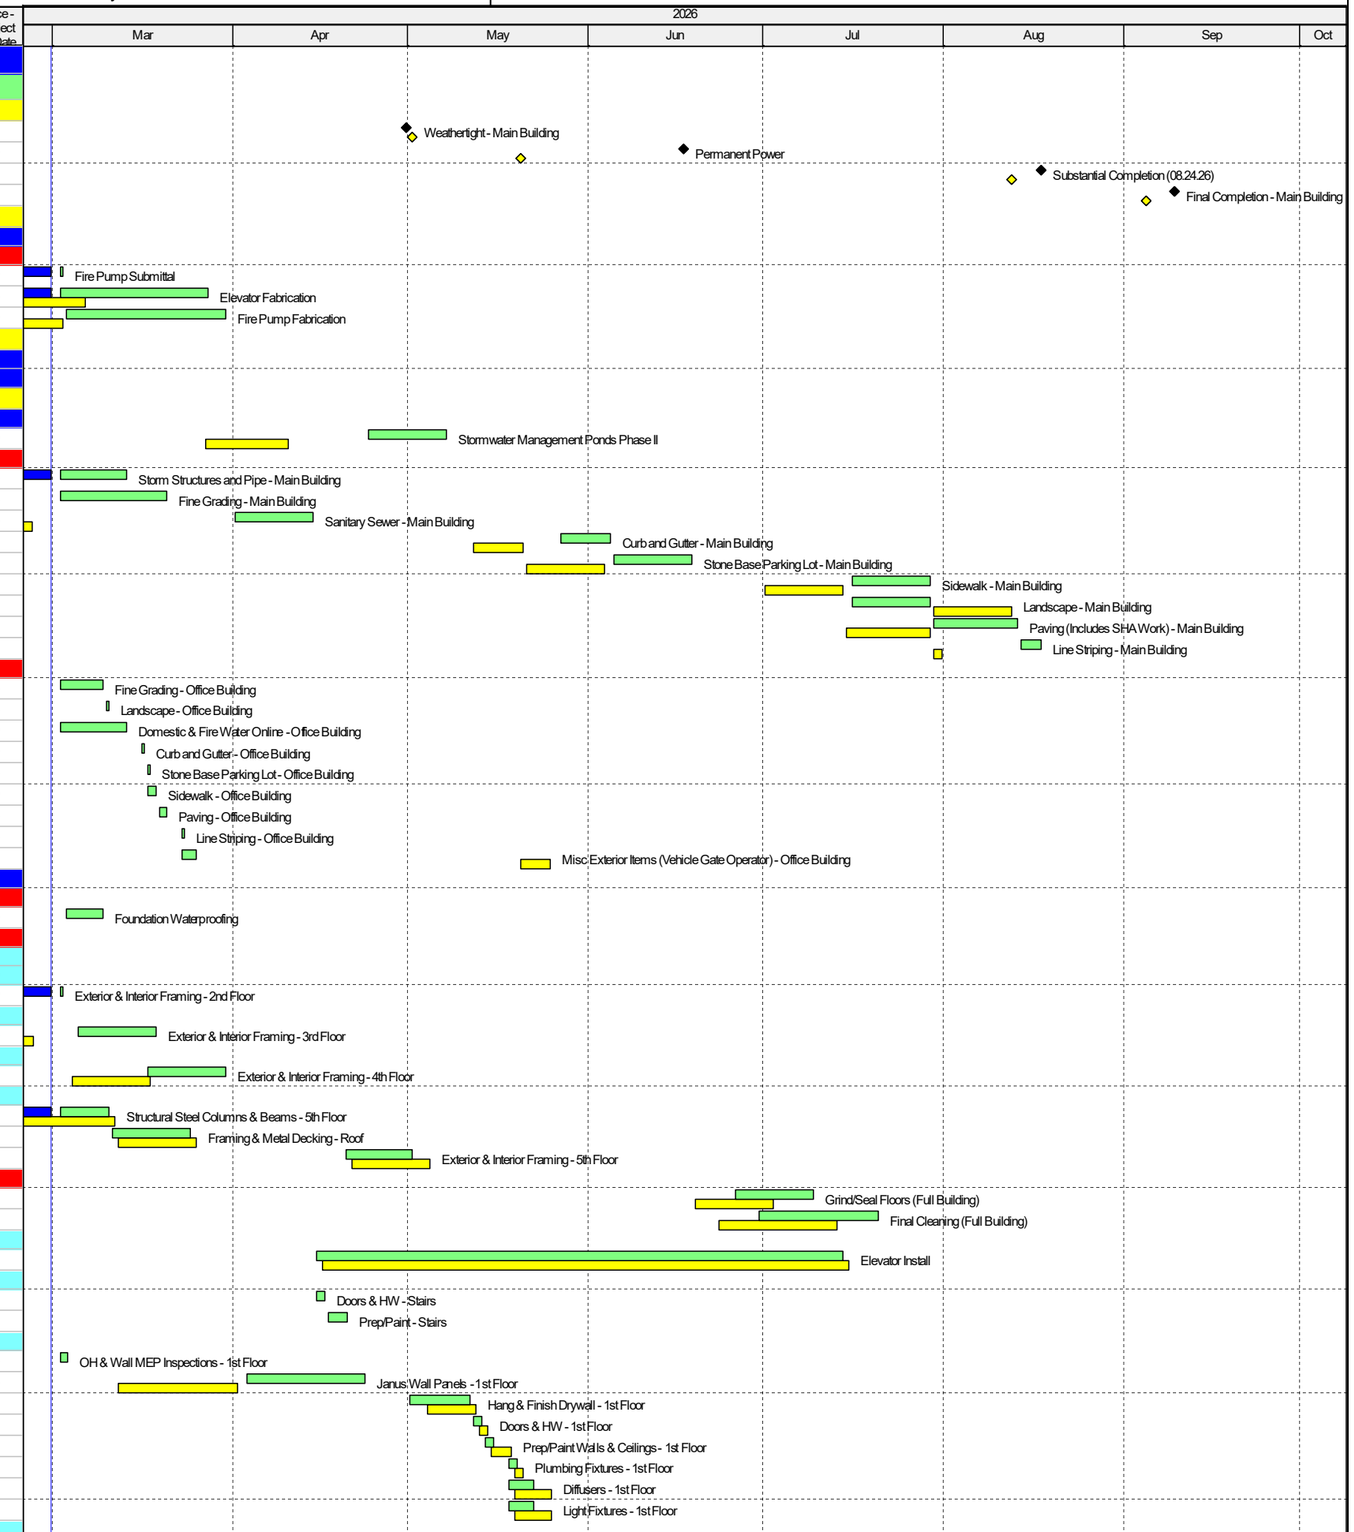

Project Baseline Bar | Remaining Work | ◇ Baseline Milestone
Actual Work | Critical Remaining Work | ◆ Milestone

TASK filter: Remaining .

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
CON-MB-L2-1110	HVAC Rough In - 2nd Floor	2	100%	19-Feb-26A	03-Mar-26	23	19-Jan-26	05-Feb-26	-18
CON-MB-L2-1060	Doors & HW - 2nd Floor	2	100%	03-Mar-26	04-Mar-26	123	04-Feb-26	05-Feb-26	-19
CON-MB-L2-1080	Prep/Paint Walls - 2nd Floor	2	100%	05-Mar-26	06-Mar-26	123	06-Feb-26	09-Feb-26	-19
CON-MB-L2-1100	Electric OH & Wall Rough In- 2nd Floor	8	100%	26-Feb-26A	11-Mar-26	17	04-Feb-26	17-Feb-26	-16
CON-MB-L2-1140	OH & Wall MEP Inspections - 2nd Floor	1	100%	12-Mar-26	12-Mar-26	17	18-Feb-26	18-Feb-26	-16
CON-MB-L2-1120	Sprinkler Rough In - 2nd Floor	10	100%	03-Mar-26	16-Mar-26	110	04-Feb-26	17-Feb-26	-19
CON-MB-L2-1150	Diffusers - 2nd Floor	5	100%	13-Mar-26	19-Mar-26	114	19-Feb-26	25-Feb-26	-16
CON-MB-L2-1160	Light Fixtures - 2nd Floor	5	100%	13-Mar-26	19-Mar-26	114	19-Feb-26	25-Feb-26	-16
CON-MB-L2-1070	Janus Wall Panels - 2nd Floor	15	46.67%	13-Mar-26	02-Apr-26	17	19-Feb-26	11-Mar-26	-16
Third Floor Interior Finishes		59	0%	23-Feb-26A	21-May-26	62	02-Feb-26	22-May-26	1
CON-MB-L3-1060	Fire Proofing Structural Steel - 3rd Floor	3	100%	23-Feb-26A	04-Mar-26	7	02-Feb-26	11-Feb-26	-15
CON-MB-L3-1070	OH & Wall Plumbing Rough In- 3rd Floor	3	66.67%	19-Mar-26	23-Mar-26	38	26-Feb-26	02-Mar-26	-15
CON-MB-L3-1090	HVAC Rough In - 3rd Floor	5	40%	19-Mar-26	25-Mar-26	36	26-Feb-26	04-Mar-26	-15
CON-MB-L3-1080	Electric & Low Voltage OH & Wall Rough In - 3rd Floor	10	20%	19-Mar-26	01-Apr-26	31	26-Feb-26	11-Mar-26	-15
CON-MB-L3-1100	Sprinkler Rough In - 3rd Floor	10	20%	19-Mar-26	01-Apr-26	98	26-Feb-26	11-Mar-26	-15
CON-MB-L3-1120	OH & Wall MEP Inspections - 3rd Floor	2	0%	02-Apr-26	03-Apr-26	31	12-Mar-26	13-Mar-26	-15
CON-MB-L3-1130	Hang/Finish Drywall - 3rd Floor	7	0%	01-May-26	11-May-26	62	04-May-26	12-May-26	1
CON-MB-L3-1140	Prep/Paint Walls & Ceilings - 3rd Floor	3	0%	12-May-26	14-May-26	62	13-May-26	15-May-26	1
CON-MB-L3-1150	Janus Wall Panels - 3rd Floor	15	0%	24-Apr-26	14-May-26	17	02-Apr-26	22-Apr-26	-16
CON-MB-L3-1160	Plumbing Fixtures - 3rd Floor	4	0%	15-May-26	20-May-26	63	18-May-26	21-May-26	1
CON-MB-L3-1170	Diffusers - 3rd Floor	5	0%	15-May-26	21-May-26	62	18-May-26	22-May-26	1
CON-MB-L3-1180	Light Fixtures - 3rd Floor	5	0%	15-May-26	21-May-26	62	18-May-26	22-May-26	1
Fourth Floor Interior Finishes		66	0%	05-Mar-26	04-Jun-26	52	20-Feb-26	13-May-26	-16
CON-MB-L4-1050	Fire Proofing Structural Steel - 4th Floor	8	75%	05-Mar-26	16-Mar-26	7	20-Feb-26	03-Mar-26	-9
CON-MB-L4-1070	HVAC Rough In - 4th Floor	5	0%	31-Mar-26	06-Apr-26	44	18-Mar-26	24-Mar-26	-9
CON-MB-L4-1060	Electric OH & Wall Rough In- 4th Floor	10	0%	31-Mar-26	13-Apr-26	39	18-Mar-26	31-Mar-26	-9
CON-MB-L4-1080	Sprinkler Rough In - 4th Floor	10	0%	31-Mar-26	13-Apr-26	90	18-Mar-26	31-Mar-26	-9
CON-MB-L4-1100	OH & Wall MEP Inspections - 4th Floor	1	0%	14-Apr-26	14-Apr-26	39	01-Apr-26	01-Apr-26	-9
CON-MB-L4-1110	Prep/Paint Walls - 4th Floor	2	0%	15-Apr-26	16-Apr-26	87	02-Apr-26	03-Apr-26	-9
CON-MB-L4-1120	Diffusers - 4th Floor	5	0%	15-Apr-26	21-Apr-26	84	02-Apr-26	08-Apr-26	-9
CON-MB-L4-1130	Light Fixtures - 4th Floor	5	0%	15-Apr-26	21-Apr-26	84	02-Apr-26	08-Apr-26	-9
CON-MB-L4-1140	Janus Wall Panels - 4th Floor	15	0%	15-May-26	04-Jun-26	17	23-Apr-26	13-May-26	-16
Fifth Floor Interior Finishes		52	0%	15-Apr-26	25-Jun-26	44	16-Apr-26	18-Jun-26	-5
CON-MB-L5-1040	Fire Proofing Structural Steel - 5th Floor	8	0%	15-Apr-26	24-Apr-26	17	16-Apr-26	27-Apr-26	1
CON-MB-L5-1070	OH & Wall Plumbing Rough In- 5th Floor	3	0%	04-May-26	06-May-26	30	05-May-26	07-May-26	1
CON-MB-L5-1080	HVAC Rough In - 5th Floor	5	0%	04-May-26	08-May-26	28	05-May-26	11-May-26	1
CON-MB-L5-1060	Electric & Low Voltage OH & Wall Rough In - 5th Floor	10	0%	04-May-26	15-May-26	23	05-May-26	18-May-26	1
CON-MB-L5-1090	Sprinkler Rough In - 5th Floor	10	0%	04-May-26	15-May-26	66	05-May-26	18-May-26	1
CON-MB-L5-1110	OH & Wall MEP Inspections - 5th Floor	1	0%	18-May-26	18-May-26	23	19-May-26	19-May-26	1
CON-MB-L5-1120	Hang/Finish Drywall - 5th Floor	7	0%	19-May-26	27-May-26	23	20-May-26	28-May-26	1
CON-MB-L5-1130	Prep/Paint Walls - 5th Floor	2	0%	28-May-26	29-May-26	59	29-May-26	01-Jun-26	1
CON-MB-L5-1150	Diffusers - 5th Floor	1	0%	01-Jun-26	01-Jun-26	62	02-Jun-26	02-Jun-26	1
CON-MB-L5-1160	Light Fixtures - 5th Floor	1	0%	01-Jun-26	01-Jun-26	62	02-Jun-26	02-Jun-26	1
CON-MB-L5-1140	Plumbing Fixtures - 5th Floor	4	0%	01-Jun-26	04-Jun-26	59	02-Jun-26	05-Jun-26	1
CON-MB-L5-1170	Janus Wall Panels - 5th Floor	15	0%	05-Jun-26	25-Jun-26	17	29-May-26	18-Jun-26	-5
Switchgear Room		76	0%	03-Mar-26	16-Jun-26	34	03-Feb-26	20-May-26	-20
CON-POW-1000	Switchgear Room Enclosure	10	100%	03-Mar-26	16-Mar-26	34	03-Feb-26	17-Feb-26	-20
CON-POW-1010	Install Switchgear Equipment	15	58.67%	17-Mar-26	06-Apr-26	34	17-Feb-26	10-Mar-26	-20
CON-POW-1020	Switchgear Lights and Power	15	0%	07-Apr-26	27-Apr-26	34	10-Mar-26	31-Mar-26	-20
CON-POW-1030	City Inspection	1	0%	28-Apr-26	28-Apr-26	34	31-Mar-26	01-Apr-26	-20
CON-POW-1040	Dominion Primary	20	0%	29-Apr-26	26-May-26	34	01-Apr-26	29-Apr-26	-20
CON-POW-1050	Dominion Transformer	5	0%	27-May-26	02-Jun-26	34	29-Apr-26	06-May-26	-20
CON-POW-1060	Dominion Secondary	5	0%	03-Jun-26	09-Jun-26	34	06-May-26	13-May-26	-20
CON-POW-1070	Power Activation	5	0%	10-Jun-26	16-Jun-26	34	13-May-26	20-May-26	-20
Exterior Finishes		102	0%	05-Jan-26A	21-Jul-26	9	12-Jan-26	06-Jul-26	-11
CON-MB-L1-1250	Exterior Sheathing - 1st Floor	1	100%	05-Jan-26A	02-Mar-26	5	12-Jan-26	03-Feb-26	-20
CON-MB-L2-1050	Exterior Sheathing - 2nd Floor	6	100%	02-Mar-26	09-Mar-26	5	02-Feb-26	09-Feb-26	-20
CON-MB-L1-1280	Perimeter Waterproofing - 1st Floor	3	100%	10-Mar-26	12-Mar-26	5	10-Feb-26	13-Feb-26	-20
CON-MB-L3-1050	Exterior Sheathing - 3rd Floor	6	100%	10-Mar-26	17-Mar-26	51	17-Feb-26	24-Feb-26	-15
CON-MB-L4-1040	Exterior Sheathing - 4th Floor	6	0%	20-Mar-26	27-Mar-26	7	09-Mar-26	16-Mar-26	-9
CON-MB-L1-1260	Perimeter Waterproofing West Elevation (Excluding 5th Floor)	4	0%	30-Mar-26	02-Apr-26	7	17-Mar-26	20-Mar-26	-9
CON-MB-L2-1280	Perimeter Waterproofing North Elevation (Excluding 5th Floor)	4	0%	03-Apr-26	08-Apr-26	21	23-Mar-26	26-Mar-26	-9
CON-MB-L5-1100	Brick Facade - 1st Floor	30	36%	13-Mar-26	23-Apr-26	5	13-Feb-26	27-Mar-26	-20
CON-MB-L5-1030	Exterior Sheathing - 5th Floor	6	0%	23-Apr-26	30-Apr-26	17	24-Apr-26	01-May-26	1
CON-MB-EXT-1000	Brick West Elevation (Excluding 5th Floor)	18	0%	07-Apr-26	30-Apr-26	5	23-Mar-26	15-Apr-26	-11
CON-MB-L2-1310	Perimeter Waterproofing West/North Elevations (5th Floor)	2	0%	01-May-26	04-May-26	17	04-May-26	05-May-26	1
CON-MB-L2-1290	Perimeter Waterproofing East Elevation	4	0%	05-May-26	08-May-26	17	06-May-26	11-May-26	1
CON-MB-L2-1300	Perimeter Waterproofing South Elevation	4	0%	11-May-26	14-May-26	31	12-May-26	15-May-26	1
CON-MB-EXT-1130	Storefront	20	0%	24-Apr-26	21-May-26	45	27-Mar-26	24-Apr-26	-20
CON-MB-EXT-1040	Stucco West Elevation	15	0%	01-May-26	21-May-26	16	16-Apr-26	06-May-26	-11
CON-MB-EXT-1020	Brick North and West Elevations (5th Floor)	18	0%	01-May-26	26-May-26	5	16-Apr-26	11-May-26	-11

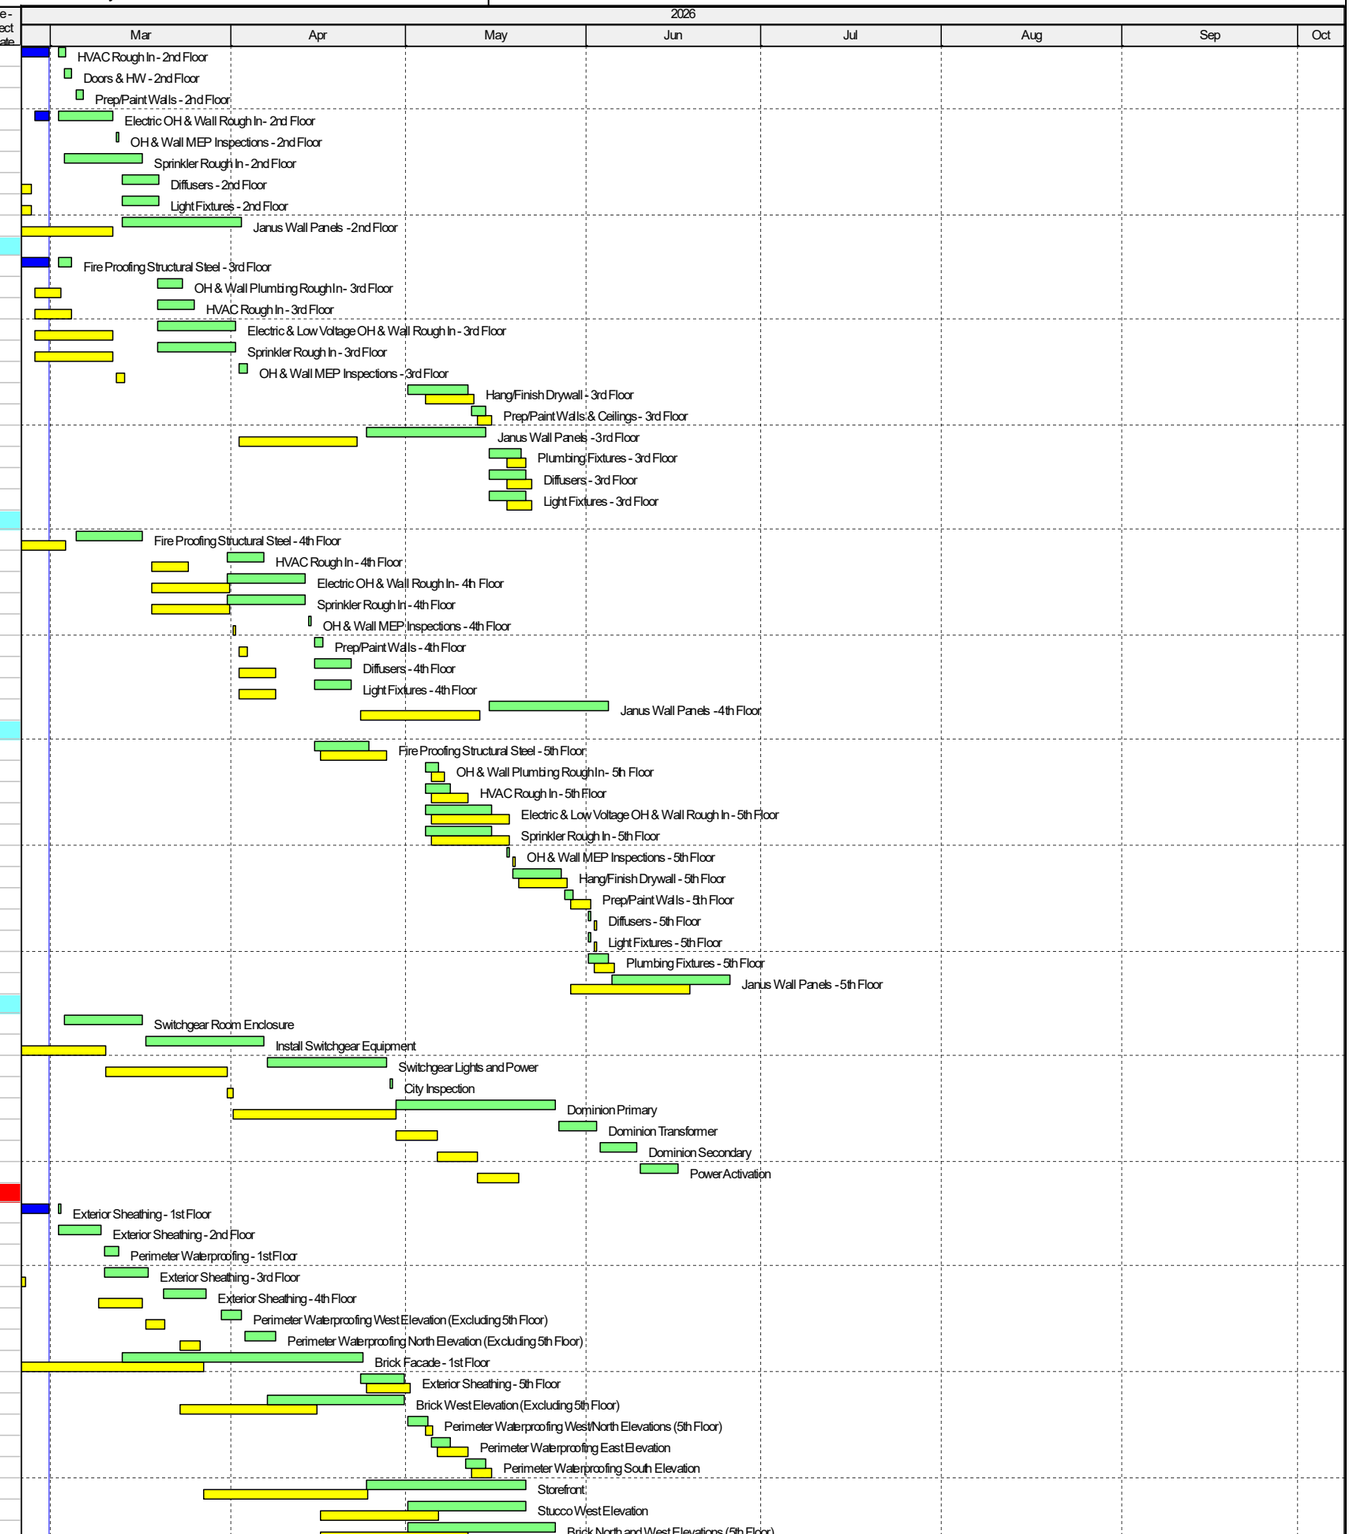

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: Remaining .

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BLProject Start	BLProject Finish	Variance - BLProject Finish Date
CON-MB-EXT-1150	Canopies	7	0%	22-May-26	01-Jun-26	45	24-Apr-26	05-May-26	-20
CON-MB-EXT-1070	Glass West Elevation	7	0%	22-May-26	01-Jun-26	24	07-May-26	15-May-26	-11
CON-MB-EXT-1060	Stucco North Elevation	7	0%	27-May-26	04-Jun-26	13	12-May-26	20-May-26	-11
CON-MB-EXT-1090	Glass North Elevation	7	0%	02-Jun-26	10-Jun-26	24	18-May-26	26-May-26	-11
CON-MB-EXT-1030	Brick East Elevation	18	0%	27-May-26	19-Jun-26	5	12-May-26	04-Jun-26	-11
CON-MB-EXT-1110	Glass East Elevation	7	0%	11-Jun-26	19-Jun-26	24	27-May-26	04-Jun-26	-11
CON-MB-EXT-1080	Stucco East Elevation	14	0%	05-Jun-26	24-Jun-26	13	21-May-26	09-Jun-26	-11
CON-MB-EXT-1140	Glass South Elevation	7	0%	22-Jun-26	30-Jun-26	24	05-Jun-26	15-Jun-26	-11
CON-MB-EXT-1100	Stucco South Elevation	7	0%	25-Jun-26	03-Jul-26	13	10-Jun-26	18-Jun-26	-11
CON-MB-EXT-1050	Brick South Elevation	18	0%	22-Jun-26	15-Jul-26	5	05-Jun-26	30-Jun-26	-11
CON-MB-EXT-1120	Swing Doors/Automatic Sliding Entrance	4	0%	16-Jul-26	21-Jul-26	9	01-Jul-26	06-Jul-26	-11
Roofing		15	0%	25-Mar-26	14-Apr-26	17	26-Mar-26	15-Apr-26	1
CON-MB-L5-1020	Roof Insulation & TPO	15	0%	25-Mar-26	14-Apr-26	17	26-Mar-26	15-Apr-26	1
Office Building		17	0%	29-Dec-25A	24-Mar-26	105	10-Dec-25	17-Feb-26	-25
Structure - Office		0	0%			0			
Interior Finishes - Office		17	0%	29-Dec-25A	24-Mar-26	105	29-Dec-25	17-Feb-26	-25
CON-OFF-1090	MEP Inspections - Office Building	2	100%	29-Dec-25A	03-Mar-26	101	29-Dec-25	23-Jan-26	-27
CON-OFF-1100	Hang/Finish Drywall - Office Building	3	100%	04-Mar-26	06-Mar-26	101	31-Dec-25	30-Jan-26	-25
CON-OFF-1110	Doors, Frames & Hardware - Office Building	2	100%	09-Mar-26	10-Mar-26	101	08-Jan-26	02-Feb-26	-27
CON-OFF-1120	Prep/Paint Walls - Office Building	2	100%	11-Mar-26	12-Mar-26	101	02-Feb-26	04-Feb-26	-27
CON-OFF-1130	Flooring - Office Building	5	100%	13-Mar-26	19-Mar-26	101	04-Feb-26	11-Feb-26	-27
CON-OFF-1140	MEP Finishes, Fixtures, Accessories - Office Building	2	100%	20-Mar-26	23-Mar-26	101	11-Feb-26	13-Feb-26	-27
CON-OFF-1150	Millwork - Office Building	2	100%	20-Mar-26	23-Mar-26	105	11-Feb-26	13-Feb-26	-27
CON-OFF-1220	Final Cleaning - Office Building	1	100%	24-Mar-26	24-Mar-26	105	17-Feb-26	17-Feb-26	-25
Exterior Finishes - Office		8	0%	29-Dec-25A	11-Mar-26	109	10-Dec-25	02-Feb-26	-27
CON-OFF-1060	Exterior Sheathing/Waterproofing - Office Building	3	100%	29-Dec-25A	04-Mar-26	109	10-Dec-25	16-Dec-25	-56
CON-OFF-1160	Store Front & Windows - Office Building	3	100%	05-Mar-26	09-Mar-26	111	30-Dec-25	08-Jan-26	-42
CON-OFF-1170	Brick Facade - Office Building	5	100%	05-Mar-26	11-Mar-26	109	17-Dec-25	02-Feb-26	-27
Final Inspections & Close Out		122	0%	24-Mar-26	09-Sep-26	7	13-Feb-26	04-Sep-26	-3
Office Building		22	0%	24-Mar-26	22-Apr-26	107	13-Feb-26	17-Jun-26	39
CLO-OFF-1030	Final Building Inspections - Office Building	5	100%	24-Mar-26	30-Mar-26	101	13-Feb-26	20-Feb-26	-27
CLO-OFF-1000	Office Temporary Occupancy	1	100%	31-Mar-26	31-Mar-26*	101	20-Feb-26	23-Feb-26	-27
CLO-OFF-1040	Punch List Walk - Office Building	2	0%	31-Mar-26	01-Apr-26	107	25-May-26	27-May-26	39
CLO-OFF-1050	Punch List Corrections - Office Building	15	0%	02-Apr-26	22-Apr-26	107	27-May-26	17-Jun-26	39
Main Building		36	0%	22-Jul-26	09-Sep-26	7	07-Jul-26	04-Sep-26	-3
CLO-MB-1000	Fire Alarm Inspection	5	0%	22-Jul-26	28-Jul-26	9	07-Jul-26	13-Jul-26	-11
CLO-MB-1010	State Inspection for Elevators	5	0%	29-Jul-26	04-Aug-26	9	16-Jul-26	22-Jul-26	-9
CLO-MB-1020	Final Building Inspections	5	0%	05-Aug-26	11-Aug-26	9	23-Jul-26	29-Jul-26	-9
CLO-MB-1040	Punch List Walk - Main Building	2	0%	18-Aug-26	19-Aug-26	7	13-Aug-26	14-Aug-26	-3
CLO-MB-1050	Punch List Corrections - Main Building	15	0%	20-Aug-26	09-Sep-26	7	17-Aug-26	04-Sep-26	-3

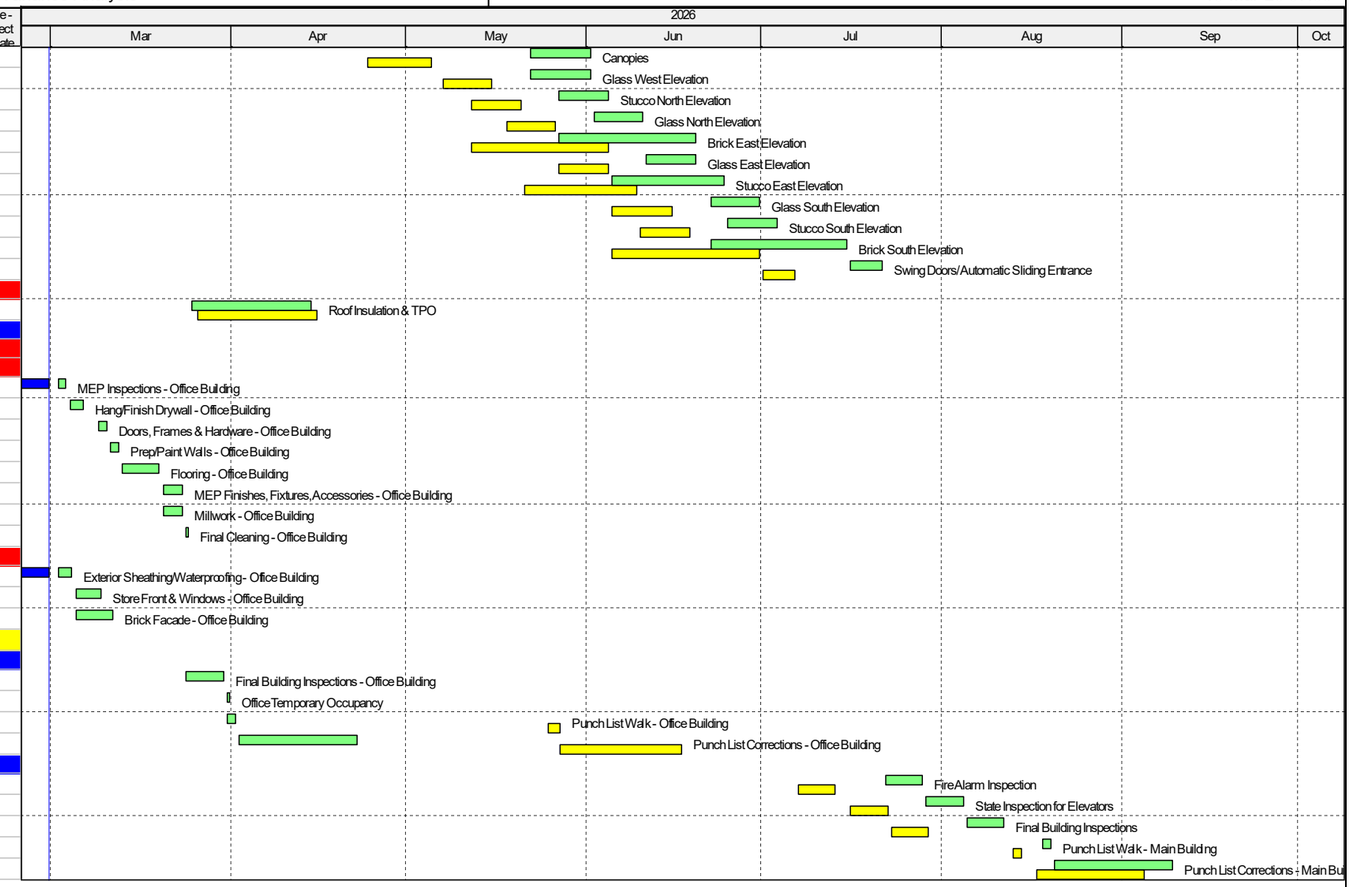

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: Remaining .

© Oracle Corporation
