Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

# Public Storage Dashboard

Data Date: 1/2/2026

| Type | Project | Region | Responsible |
|---|---|---|---|
| Construction | Mt Juliet, TN | Central | Brendan Blair |

| Baseline Completion Date | Current Completion Date | Schedule Variance | Schedule Compression |
|---|---|---|---|
| 11/30/2026 | 12/16/2026 | -16 Baseline<br>0 Previous | Remaining Work Compression: 1%— Normal |

## Milestone Variance

| Milestone | Baseline Milestone Date | Previous Milestone Date | Current Milestone Date | Current Baseline Variance | Delta from Last Month | Activity Name | Status Indicator |
|---|---|---|---|---|---|---|---|
| NTP | 9/11/2025 | 9/11/2025 | 9/11/2025 | 0 | 0 | Notice To Proceed | On Track – Gaining |
| Foundation Complete | 2/16/2026 | 2/4/2026 | 1/27/2026 | 20 | 8 | Footings & Foundation Cip Walls (Includes Elevator Pit) | On Track – Gaining |
| Structure Top Out | 6/5/2026 | 5/26/2026 | 5/27/2026 | 9 | -1 | Structure Complete | On Track – Slipping |
| Weather Tight | 7/14/2026 | 7/1/2026 | 7/2/2026 | 12 | -1 | Building Dry In | On Track – Slipping |
| 1st Floor Finishes Complete | 8/31/2026 | 9/10/2026 | 9/11/2026 | -11 | -1 | Install Storage Doors & Hardware | Delayed – Slipping |
| 2nd Floor Finishes Complete | 8/31/2026 | 8/19/2026 | 8/20/2026 | 11 | -1 | Install Storage Doors & Hardware | On Track – Slipping |
| 3rd Floor Finishes Complete | 9/8/2026 | 8/26/2026 | 8/27/2026 | 12 | -1 | Install Storage Doors & Hardware | On Track – Slipping |
| 4th Floor Finishes Complete | 8/17/2026 | 9/2/2026 | 9/3/2026 | -17 | -1 | Install Storage Doors & Hardware | Delayed – Slipping |
| Elevator Complete | 9/17/2026 | 9/28/2026 | 9/29/2026 | -12 | -1 | Evelvator Installation (Incl. Equipment Room Buildout) | Delayed – Slipping |
| Hardscape/Landscape Complete | 10/26/2026 | 11/17/2026 | 11/18/2026 | -23 | -1 | Final Owner Punch List | Delayed – Slipping |
| Contract Completion | 11/30/2026 | 12/16/2026 | 12/16/2026 | -16 | 0 | Project Sustainability Complete - After Weather Impacts | Delayed – Gaining |

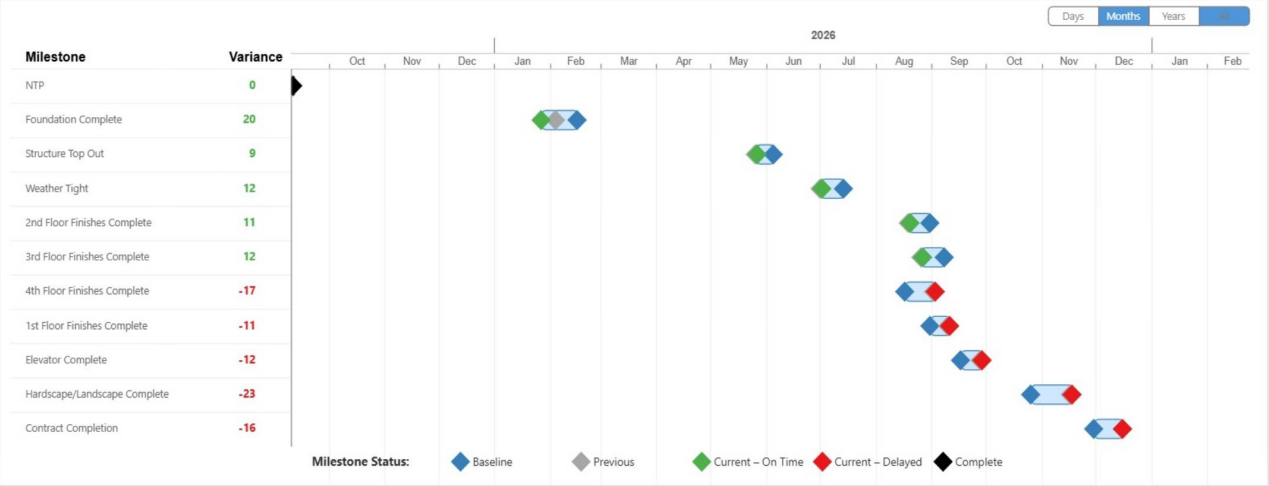


## Baseline Variance

## Schedule Performance Summary

**Summary**

There are significant risks to schedule quality and project execution, as highlighted by critical deficiencies in both scheduling discipline and update accuracy. Immediate management focus should be placed on correcting schedule logic, enhancing field planning processes, and closely monitoring progress to avoid further deterioration in forecast reliability and project outcomes.

**Schedule Validation Score: 73.00 — ALERT**

The SV Score is significantly below the acceptable threshold, indicating serious deficiencies in schedule quality and technical soundness. This compromises the reliability of the critical path and overall forecast accuracy. Immediate review and correction of schedule logic, constraints, and network integrity are strongly recommended.

**Execution Score: 48.00 — ALERT**

Execution practices are critically weak, reflecting poor use of the schedule for managing and planning near-term work. This raises the risk of uncoordinated field activities and further schedule slippage. Immediate actions are needed to improve schedule updating and work planning discipline.

**Finish Variance: 3.00 — WARNING**

The project is experiencing some slippage compared to the baseline finish date, though still within a moderate risk range. Continued monitoring and prompt mitigation of emerging delays are necessary to prevent compounding impacts.

**Remaining Work Compression: 1%— Normal**

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is mea… by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Microsoft Power BI
