Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

Public Storage Dashboard

Data Date: 2/24/2026

Type	Project	Region	Responsible
Construction	Mt Juliet, TN	Central	Brendan Blair

Baseline Completion Date	Current Completion Date	Schedule Variance	Work Compression
11/30/2026	12/1/2026	-1 days Prev: -2 days | Trend: 1 days ▲ Recovering	Remaining Work Compression: 5.00% — NORMAL

Critical Path Status & Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	9/11/2025	9/11/2025	9/11/2025	0	0	Notice To Proceed	On Track – Gaining
Foundation Complete	2/16/2026	2/17/2026	3/6/2026	-18	-17	Footings & Foundation Cip Walls (Includes Elevator Pit)	Delayed – Slipping
Structure Top Out	6/5/2026	6/3/2026	7/1/2026	-26	-28	Structure Complete	Delayed – Slipping
Weather Tight	7/14/2026	7/13/2026	8/10/2026	-27	-28	Building Dry In	Delayed – Slipping
1st Floor Finishes Complete	8/31/2026	9/21/2026	9/28/2026	-28	-7	Install Storage Doors & Hardware	Delayed – Slipping
2nd Floor Finishes Complete	8/31/2026	8/28/2026	9/14/2026	-14	-17	Install Storage Doors & Hardware	Delayed – Slipping
3rd Floor Finishes Complete	9/8/2026	9/4/2026	9/14/2026	-6	-10	Install Storage Doors & Hardware	Delayed – Slipping
4th Floor Finishes Complete	8/17/2026	9/14/2026	9/14/2026	-28	0	Install Storage Doors & Hardware	Delayed – Slipping
Elevator Complete	9/17/2026	10/7/2026	10/14/2026	-27	-7	Evelvator Installation (Incl. Equipment Room Buildout)	Delayed – Slipping
Hardscape/Landscape Complete	10/26/2026	11/23/2026	11/3/2026	-8	20	Rutland Drive Punchlist Completion And Signoff	Delayed – Gaining
Contract Completion	11/30/2026	12/2/2026	12/1/2026	-1	1	Project Substantial Completion With Weather Projection	Delayed – Gaining

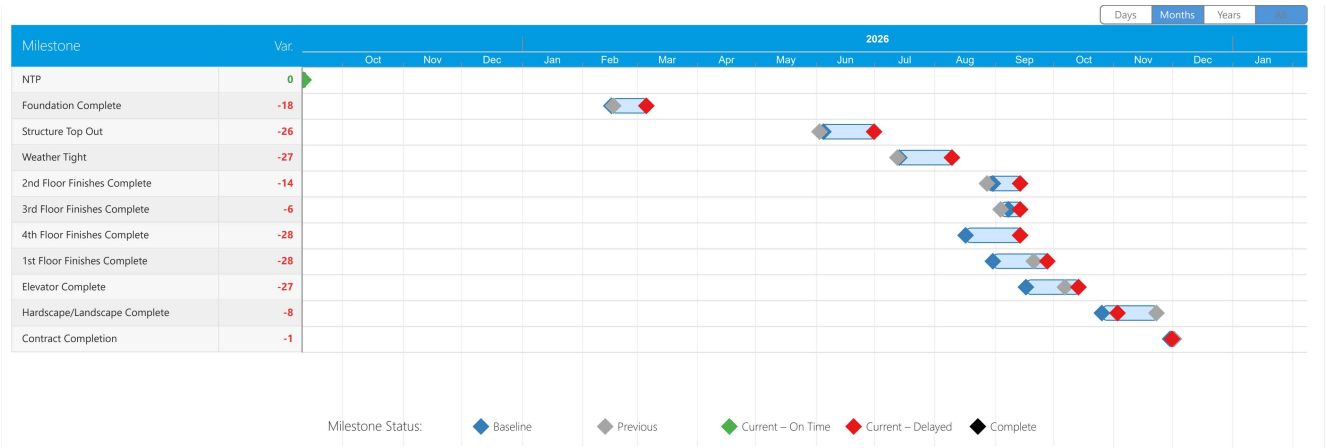

Baseline Variance Trends — Critical Milestones

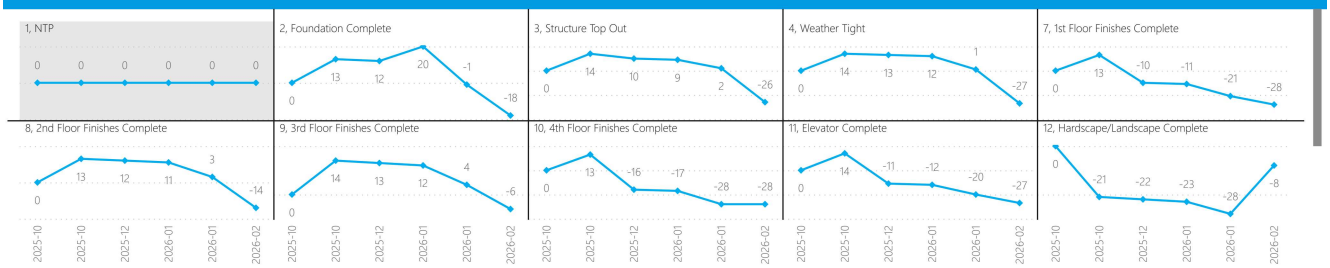

Schedule Performance Summary

Summary: Overall, the schedule exhibits serious risks stemming from low schedule quality, lack of execution discipline, and significant extension of the critical path. Immediate focus is needed on schedule validation, enforcement… planning rigor, and critical path recovery actions to prevent further decline in schedule reliability.

Critical Path Compression: 7.0% — WARNING

Notable manipulation of the critical path has occurred to compensate for slippage. While not yet excessive, closer review is warranted to avoid introducing over-optimism or strain on future execution

Critical Path Variance: 116.00% — ALERT

The critical path has extended sharply compared to baseline, indicating substantial risk of further project delays unless driving factors are addressed.

Execution Score: 33.0% — ALERT

Schedule utilization for managing near-term work is significantly deficient. Actual project execution is not being driven by the baseline plan, increasing the risk of uncoordinated activities and missed targets

Remaining Work Compression: 5.00% — ALERT

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is measured by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Schedule Validation Score:71.00% — ALERT

The schedule's technical quality is poor, with widespread validation issues such as logic gaps or improper constraints. Immediate remediation is recommended to improve forecasting reliability

Powered By STELIC INSIGHT • ACTION • IMPACT
