Public Storage Anaheim Proposal Schedule 5/27/25 gw

ID		Unique ID	Task Name	Duration	Start	Finish
1		**354**	**Grading & Building Slab Construction**	**295 days**	**Mon 25/09/08**	**Fri 26/11/06**
2		361	Commencement Date 9/8/2025	1 day	Mon 25/09/08	Mon 25/09/08
3		358	HBI Mobilization	8 days	Tue 25/09/09	Thu 25/09/18
4		461	Install Temp Fencing & BMP's	3 days	Fri 25/09/19	Tue 25/09/23
5		363	Identify & Cap Existing Utilities to Limits	3 days	Fri 25/09/19	Tue 25/09/23
6		366	Install Fire line Modifications	7 days	Wed 25/09/24	Thu 25/10/02
7		462	Surface Demo Existing Phase II areas	12 days	Fri 25/10/03	Mon 25/10/20
8		349	O/X & Grading for Bldg pad	12 days	Tue 25/10/21	Wed 25/11/05
9		13	**Certify Pad / Pad Delivery Date**	2 days	Thu 25/11/06	Fri 25/11/07
10		369	Building Permit required	0 days	Fri 25/11/07	Fri 25/11/07
11		16	Underslab Electrical & Plumbing	6 days	Mon 25/11/10	Mon 25/11/17
12		177	Building Foundations & Pre-lim CMU/Forms	10 days	Mon 25/11/10	Fri 25/11/21
13		368	Elevator Pit Form & Pour	10 days	Mon 25/11/10	Fri 25/11/21
14		367	Slab Base Material Import & Grading	5 days	Mon 25/11/24	Tue 25/12/02
15		17	Slab Vapor Barrier & Reinforcing	10 days	Mon 25/12/01	Fri 25/12/12
16		213	Slab on Grade Pour North	4 days	Tue 25/12/09	Fri 25/12/12
17		371	Slab on Grade Pour South	4 days	Mon 25/12/15	Thu 25/12/18
18		**409**	**Site Wet Utilities**	**21 days**	**Mon 25/11/10**	**Wed 25/12/10**
19		413	Storm Drain Piping & Catch Basins from Phase 1 Stubs	6 days	Mon 25/11/10	Mon 25/11/17
20		423	Extend Sewer Laterals to building	5 days	Tue 25/11/18	Mon 25/11/24
21		424	Extend Fire / Domestic Water Service to Building	10 days	Tue 25/11/25	Wed 25/12/10
22		425	**Domestic & Fire Water Services Completion**	0 days	Wed 25/12/10	Wed 25/12/10
23		**414**	**Site Dry Utilities**	**8 days**	**Tue 25/11/18**	**Mon 25/12/01**
24		415	Extend Power & Lov Voltage conduits to Bldg from Stul	5 days	Tue 25/11/18	Mon 25/11/24
25		416	Install Generac & Site lighting Conduits	3 days	Tue 25/11/25	Mon 25/12/01
26		**417**	**Onsite improvements For Early Base Pave**	**22 days**	**Thu 25/12/11**	**Wed 26/01/14**
27		418	Grade for Curb & Gutter	4 days	Thu 25/12/11	Tue 25/12/16
28		422	Install Irrigation Sleeves	1 day	Wed 25/12/17	Wed 25/12/17
29		419	Place Curb & Gutter	4 days	Thu 25/12/18	Tue 25/12/23
30		420	Grade & Pour Walks	5 days	Mon 25/12/22	Tue 25/12/30
31		421	Agg Base Import & AC Base Paving	10 days	Wed 25/12/31	Wed 26/01/14
32		**426**	**Vertical Building Construction**	**211 days**	**Mon 25/12/15**	**Thu 26/10/15**
33		250	CMU Walls to 14'-8" North	15 days	Mon 25/12/15	Wed 26/01/07
34		370	CMU Walls to 14'-8" South	15 days	Thu 26/01/08	Wed 26/01/28
35		251	Structural Steel Framing & Metal Deck to 2nd floor N.	7 days	Thu 26/01/08	Fri 26/01/16
36		372	Structural Steel Framing & Metal Deck to 2nd floor S.	7 days	Fri 26/01/23	Mon 26/02/02
37		252	Rebar, Hangars & Deck2 Pour North	7 days	Mon 26/01/19	Tue 26/01/27
38		373	Rebar, Hangars & Deck2 Pour South	7 days	Tue 26/02/03	Wed 26/02/11
39		378	CMU Walls to 25'-4" North	10 days	Thu 26/01/29	Wed 26/02/11
40		379	CMU Walls to 25'-4" South	10 days	Thu 26/02/12	Thu 26/02/26
41		375	2nd floor Shear walls North @ 15k/week	12 days	Thu 26/01/29	Fri 26/02/13
42		380	3rd Floor Decking North @ 5k/day	7 days	Tue 26/02/10	Thu 26/02/19
43		381	Rebar, Hangars & Deck Pour3 North	5 days	Fri 26/02/20	Thu 26/02/26
44		376	2nd floor Shear walls South @ 15k/week	12 days	Thu 26/02/12	Mon 26/03/02
45		377	3rd Floor Decking South@ 5k/day	7 days	Thu 26/02/26	Fri 26/03/06
46		374	Rebar, Hangars & Deck3 Pour South	5 days	Mon 26/03/09	Fri 26/03/13
47		382	CMU Walls to 36' North	10 days	Fri 26/02/27	Thu 26/03/12
48		383	CMU Walls to 36' South	10 days	Mon 26/03/16	Fri 26/03/27
49		384	3rd floor Shear walls North @ 15k/week	12 days	Fri 26/02/27	Mon 26/03/16
50		385	4th Floor Decking North @ 5k/day	7 days	Fri 26/03/13	Mon 26/03/23
51		386	Rebar, Hangars & Deck Pour4 North	5 days	Tue 26/03/24	Mon 26/03/30
52		387	3rd floor Shear walls South @ 15k/week	12 days	Mon 26/03/16	Tue 26/03/31
53		388	4th Floor Decking South@ 5k/day	7 days	Fri 26/03/27	Mon 26/04/06
54		389	Rebar, Hangars & Deck4 Pour South	5 days	Tue 26/04/07	Mon 26/04/13
55		390	CMU Walls to 46'-8" North	10 days	Tue 26/03/31	Mon 26/04/13
56		391	CMU Walls to 46'-8" South	10 days	Tue 26/04/14	Mon 26/04/27
57		392	4th floor Shear walls North @ 15k/week	12 days	Tue 26/03/31	Wed 26/04/15
58		393	5th Floor Decking North @ 5k/day	7 days	Mon 26/04/13	Tue 26/04/21
59		394	Rebar, Hangars & Deck Pour5 North	5 days	Wed 26/04/22	Tue 26/04/28
60		395	4th floor Shear walls South @ 15k/week	12 days	Tue 26/04/14	Wed 26/04/29
61		396	5th Floor Decking South@ 5k/day	7 days	Mon 26/04/27	Tue 26/05/05
62		397	Rebar, Hangars & Deck5 Pour South	7 days	Wed 26/05/06	Thu 26/05/14
63		398	CMU Walls to 57'-4" North	10 days	Wed 26/04/29	Tue 26/05/12
64		399	CMU Walls to 57'-4" South	10 days	Fri 26/05/15	Fri 26/05/29
65		400	5th floor Shear walls North @ 15k/week	14 days	Wed 26/04/29	Mon 26/05/18
66		406	Roof Equipment Structural	3 days	Thu 26/05/14	Mon 26/05/18
67		401	Roof Decking North @ 5k/day	7 days	Tue 26/05/19	Thu 26/05/28
68		402	Roof Drains, Screens & Curbs	10 days	Fri 26/05/29	Thu 26/06/11
69		403	5th floor Shear walls South @ 15k/week	12 days	Fri 26/05/15	Tue 26/06/02
70		407	Roof Equipment Structural	3 days	Fri 26/05/29	Tue 26/06/02
71		404	Roof Decking South@ 5k/day	7 days	Wed 26/06/03	Thu 26/06/11
72		405	Roof insulation Crickets & TPO	7 days	Fri 26/06/12	Mon 26/06/22
73		217	**Building Temporarily Water Tight**	0 days	Mon 26/06/22	Mon 26/06/22
74		62	Set rooftop Equipment & hook up	3 days	Tue 26/06/23	Thu 26/06/25
75		64	Elevator Construction Car #1	20 days	Tue 26/06/23	Wed 26/07/22
76		460	CMU infill @ Elevator Openings	10 days	Thu 26/07/09	Wed 26/07/22
77		65	Elevator Construction Car #2	20 days	Thu 26/07/23	Wed 26/08/19
78		458	CMU infill @ Elevator Openings	10 days	Thu 26/08/06	Wed 26/08/19
79		432	Elevator Construction Car #3	20 days	Thu 26/08/20	Thu 26/09/17
80		348	CMU infill @ Elevator Openings	10 days	Thu 26/09/03	Thu 26/09/17
81		194	State Elevator inspection Lead Time & Approval	20 days	Fri 26/09/18	Thu 26/10/15
82		445	Remove Man Lift	2 days	Fri 26/09/18	Mon 26/09/21
83		446	Infill Framing @ Manlift Landings	7 days	Mon 26/09/21	Tue 26/09/29
84		447	Sheathing Lift Leave Out Area	5 days	Mon 26/09/28	Fri 26/10/02
85		448	Finishes @ Infilled Landings	5 days	Mon 26/10/05	Fri 26/10/09
86		**146**	**Building Interior**	**194 days**	**Wed 26/01/28**	**Mon 26/11/02**
87		83	Layout & Install Overhead Hangars 1st fl	2 days	Wed 26/01/28	Thu 26/01/29
88		195	Spray Applied Fireproofing - 1st Floor	10 days	Fri 26/01/30	Thu 26/02/12
89		86	Overhead P, M, & E 1st fl	15 days	Tue 26/02/10	Tue 26/03/03

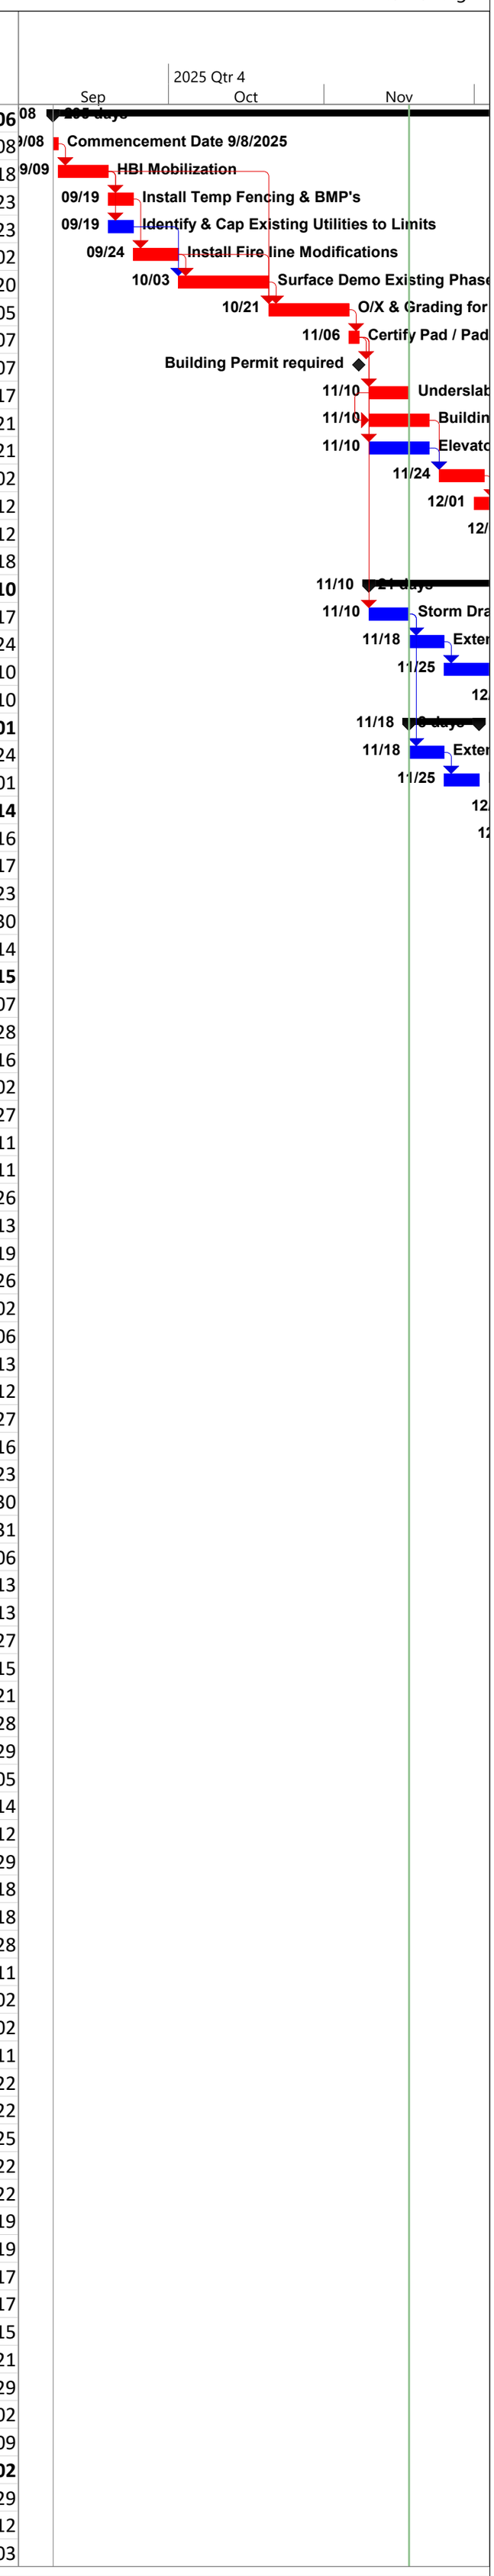

ID		Unique ID	Task Name	Duration	Start	Finish
90		87	Unit Partitions / Hallway System & Doors 1st floor	25 days	Wed 26/02/25	Tue 26/03/31
91		296	Finish Electrical 1st Fl	10 days	Wed 26/04/01	Tue 26/04/14
92		88	Instal Generator and Related Systems	35 days	Wed 26/04/15	Wed 26/06/03
93		91	Overhead M/E/P 2nd Fl	15 days	Mon 26/03/16	Fri 26/04/03
94		92	Unit Partitions / Hallway System & Doors 2nd Floor	20 days	Mon 26/04/06	Fri 26/05/01
95		297	Finish Electrical 2nd Fl	10 days	Mon 26/05/04	Fri 26/05/15
96		96	Overhead M/E/P 3rd Fl	15 days	Mon 26/04/06	Fri 26/04/24
97		97	Unit partitions /Hallway System & Doors 3rd Floor	20 days	Mon 26/05/04	Mon 26/06/01
98		298	Finish Electrical 3rd Fl	10 days	Tue 26/06/02	Mon 26/06/15
99		101	Overhead M/E/P 4th Fl	15 days	Wed 26/04/29	Tue 26/05/19
100		102	Unit Partitions /Hallway System & Doors 4th Floor	20 days	Tue 26/06/02	Mon 26/06/29
101		299	Finish Electrical 4th Fl	5 days	Tue 26/06/30	Wed 26/07/08
102		295	Overhead M/E/P 5th Fl	15 days	Fri 26/05/29	Thu 26/06/18
103		293	Unit Partitions & Hallway System & Doors 5th Floor	20 days	Tue 26/06/30	Wed 26/07/29
104		341	Hallway Systems after Scaffold Removal	5 days	Thu 26/07/30	Wed 26/08/05
105		300	Finish Electrical 5th Fl & Roof Equipment	11 days	Thu 26/07/23	Thu 26/08/06
106		220	**Overhead Doors, Liner & Demising Panels Comp.**	0 days	Wed 26/07/29	Wed 26/07/29
107		118	Elev. Lobby Framing	5 days	Thu 26/07/30	Wed 26/08/05
108		119	Elev. Lobby M/E/P Rough in	5 days	Tue 26/08/04	Mon 26/08/10
109		120	Elev. Lobby Drywall	10 days	Tue 26/08/11	Mon 26/08/24
110		164	Install HM Doors & Hardware	5 days	Tue 26/08/25	Mon 26/08/31
111		121	Lobby Fixtures & Finishes	10 days	Tue 26/08/25	Tue 26/09/08
112		165	Finish Painting in Storage areas	10 days	Tue 26/09/01	Tue 26/09/15
113		450	Building Signage per plan	5 days	Wed 26/09/16	Tue 26/09/22
114		166	Final Clean up & Seal floors	20 days	Wed 26/09/23	Tue 26/10/20
115		455	Owner Arch. Punch list & Completion	14 days	Wed 26/10/14	Mon 26/11/02
116		**434**	**Building Exterior**	**76 days**	**Mon 26/06/01**	**Thu 26/09/17**
117		435	Install Scaffolding at Building Perimeter	3 days	Mon 26/06/01	Wed 26/06/03
118		436	Exterior Metal Frame Sheathing & WRB @ Tower	10 days	Thu 26/06/04	Wed 26/06/17
119		437	Metal Panel Siding @ Tower	5 days	Thu 26/06/18	Wed 26/06/24
120		438	Storefront/Curtainwall	5 days	Thu 26/06/25	Wed 26/07/01
121		439	Glass Lead Time	10 days	Thu 26/07/02	Fri 26/07/17
122		440	Install Glass	5 days	Mon 26/07/20	Fri 26/07/24
123		441	Install Auto Sliders & Mapes Canopy	10 days	Thu 26/09/03	Thu 26/09/17
124		442	EIFS WRB, Foam/Brown & Finish	50 days	Thu 26/06/04	Fri 26/08/14
125		443	Exterior Sheet metal, Sealants, & Painting	10 days	Mon 26/08/17	Fri 26/08/28
126		444	Remove Scaffolding	3 days	Mon 26/08/31	Wed 26/09/02
127		**133**	**Onsite improvements**	**26 days**	**Thu 26/09/03**	**Fri 26/10/09**
128		137	Grade & Pour Walks	5 days	Thu 26/09/03	Thu 26/09/10
129		451	Site Fencing & Gates	5 days	Fri 26/09/11	Thu 26/09/17
130		138	Landscape Irrigation and Planting	10 days	Fri 26/09/18	Thu 26/10/01
131		139	Striping & Signage	3 days	Wed 26/09/30	Fri 26/10/02
132		245	Owner Civil Punch list & Completion	5 days	Mon 26/10/05	Fri 26/10/09
133		**141**	**Accumulative Inspections & C of O**	**20 days**	**Mon 26/10/12**	**Fri 26/11/06**
134		452	Final Grading Inspections	2 days	Mon 26/10/12	Tue 26/10/13
135		453	Final Public Works Inspections	2 days	Wed 26/10/14	Thu 26/10/15
136		234	Life Safety Inspection	2 days	Fri 26/10/16	Mon 26/10/19
137		353	MEP Final Inspections	2 days	Fri 26/10/16	Mon 26/10/19
138		454	Final Planning & Zoning Inspection	2 days	Fri 26/10/16	Mon 26/10/19
139		235	Building Final Inspection	2 days	Tue 26/10/20	Wed 26/10/21
140		456	Rain Days Included	10 days	Thu 26/10/22	Wed 26/11/04
141		236	Certificate Of Occupancy	2 days	Thu 26/11/05	Fri 26/11/06
142		305	**Open Date**	0 days	Fri 26/11/06	Fri 26/11/06

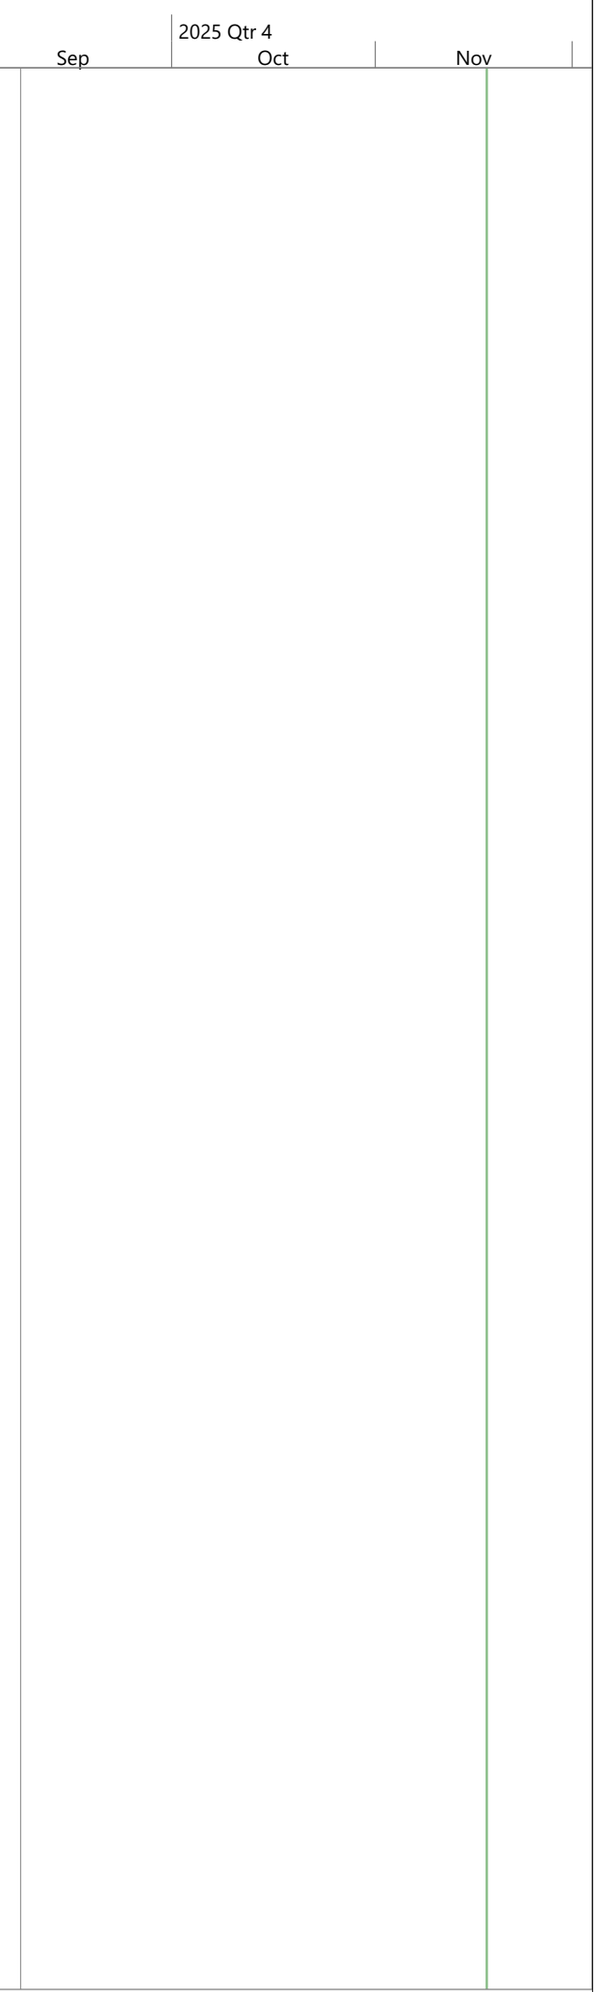

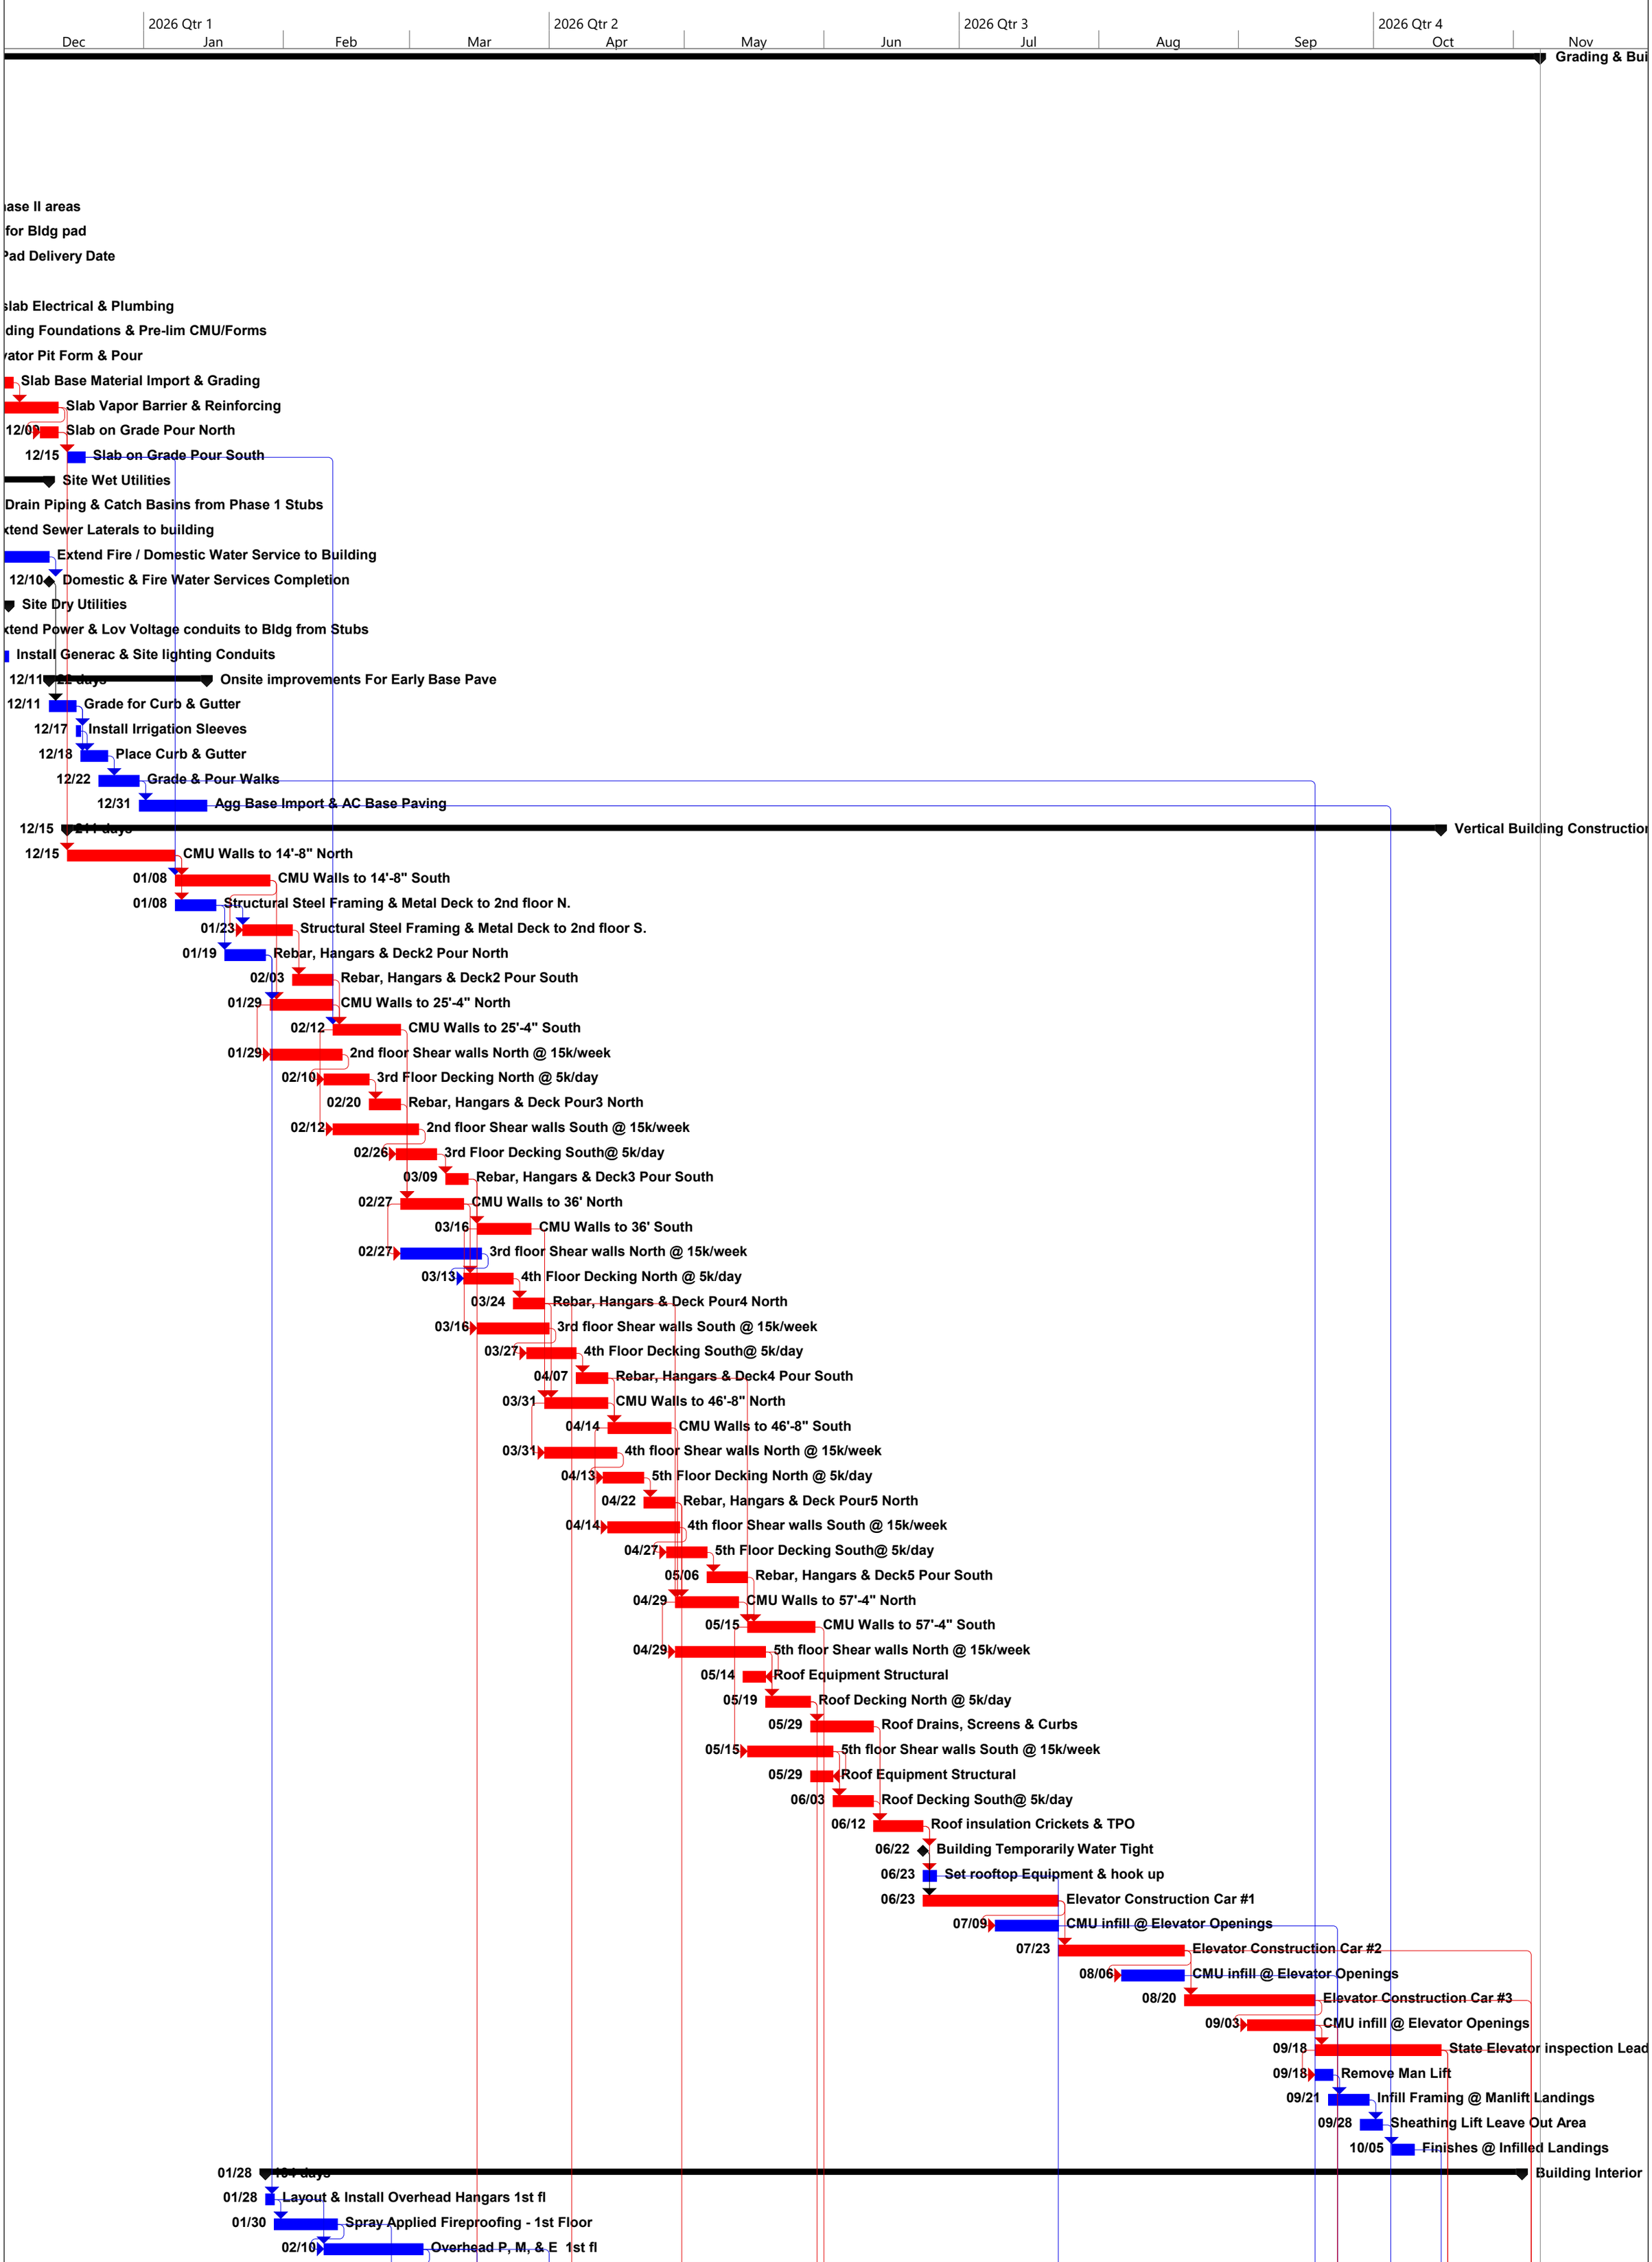
2026 Qtr 1
2026 Qtr 2
2026 Qtr 3
2026 Qtr 4
Dec
Jan
Feb
Mar
Apr
May
Jun
Jul
Aug
Sep
Oct
Nov
Grading & Bui
ase II areas
for Bldg pad
Pad Delivery Date
slab Electrical & Plumbing
ding Foundations & Pre-lim CMU/Forms
vator Pit Form & Pour
Slab Base Material Import & Grading
Slab Vapor Barrier & Reinforcing
12/03 Slab on Grade Pour North
12/15 Slab on Grade Pour South
Site Wet Utilities
Drain Piping & Catch Basins from Phase 1 Stubs
xtend Sewer Laterals to building
Extend Fire / Domestic Water Service to Building
12/10 Domestic & Fire Water Services Completion
Site Dry Utilities
xtend Power & Lov Voltage conduits to Bldg from Stubs
Install Generac & Site lighting Conduits
12/11 22 days Onsite improvements For Early Base Pave
12/11 Grade for Curb & Gutter
12/17 Install Irrigation Sleeves
12/18 Place Curb & Gutter
12/22 Grade & Pour Walks
12/31 Agg Base Import & AC Base Paving
12/15 211 days Vertical Building Constructio
12/15 CMU Walls to 14'-8" North
01/08 CMU Walls to 14'-8" South
01/08 Structural Steel Framing & Metal Deck to 2nd floor N.
01/23 Structural Steel Framing & Metal Deck to 2nd floor S.
01/19 Rebar, Hangars & Deck2 Pour North
02/03 Rebar, Hangars & Deck2 Pour South
01/29 CMU Walls to 25'-4" North
02/12 CMU Walls to 25'-4" South
01/29 2nd floor Shear walls North @ 15k/week
02/10 3rd Floor Decking North @ 5k/day
02/20 Rebar, Hangars & Deck Pour3 North
02/12 2nd floor Shear walls South @ 15k/week
02/26 3rd Floor Decking South@ 5k/day
03/09 Rebar, Hangars & Deck3 Pour South
02/27 CMU Walls to 36' North
03/16 CMU Walls to 36' South
02/27 3rd floor Shear walls North @ 15k/week
03/13 4th Floor Decking North @ 5k/day
03/24 Rebar, Hangars & Deck Pour4 North
03/16 3rd floor Shear walls South @ 15k/week
03/27 4th Floor Decking South@ 5k/day
04/07 Rebar, Hangars & Deck4 Pour South
03/31 CMU Walls to 46'-8" North
04/14 CMU Walls to 46'-8" South
03/31 4th floor Shear walls North @ 15k/week
04/13 5th Floor Decking North @ 5k/day
04/22 Rebar, Hangars & Deck Pour5 North
04/14 4th floor Shear walls South @ 15k/week
04/27 5th Floor Decking South@ 5k/day
05/06 Rebar, Hangars & Deck5 Pour South
04/29 CMU Walls to 57'-4" North
05/15 CMU Walls to 57'-4" South
04/29 5th floor Shear walls North @ 15k/week
05/14 Roof Equipment Structural
05/19 Roof Decking North @ 5k/day
05/29 Roof Drains, Screens & Curbs
05/15 5th floor Shear walls South @ 15k/week
05/29 Roof Equipment Structural
06/03 Roof Decking South@ 5k/day
06/12 Roof insulation Crickets & TPO
06/22 Building Temporarily Water Tight
06/23 Set rooftop Equipment & hook up
06/23 Elevator Construction Car #1
07/09 CMU infill @ Elevator Openings
07/23 Elevator Construction Car #2
08/06 CMU infill @ Elevator Openings
08/20 Elevator Construction Car #3
09/03 CMU infill @ Elevator Openings
09/18 State Elevator inspection Lead
09/18 Remove Man Lift
09/21 Infill Framing @ Manlift Landings
09/28 Sheathing Lift Leave Out Area
10/05 Finishes @ Infilled Landings
01/28 184 days Building Interior
01/28 Layout & Install Overhead Hangars 1st fl
01/30 Spray Applied Fireproofing - 1st Floor
02/10 Overhead P, M, & E 1st fl

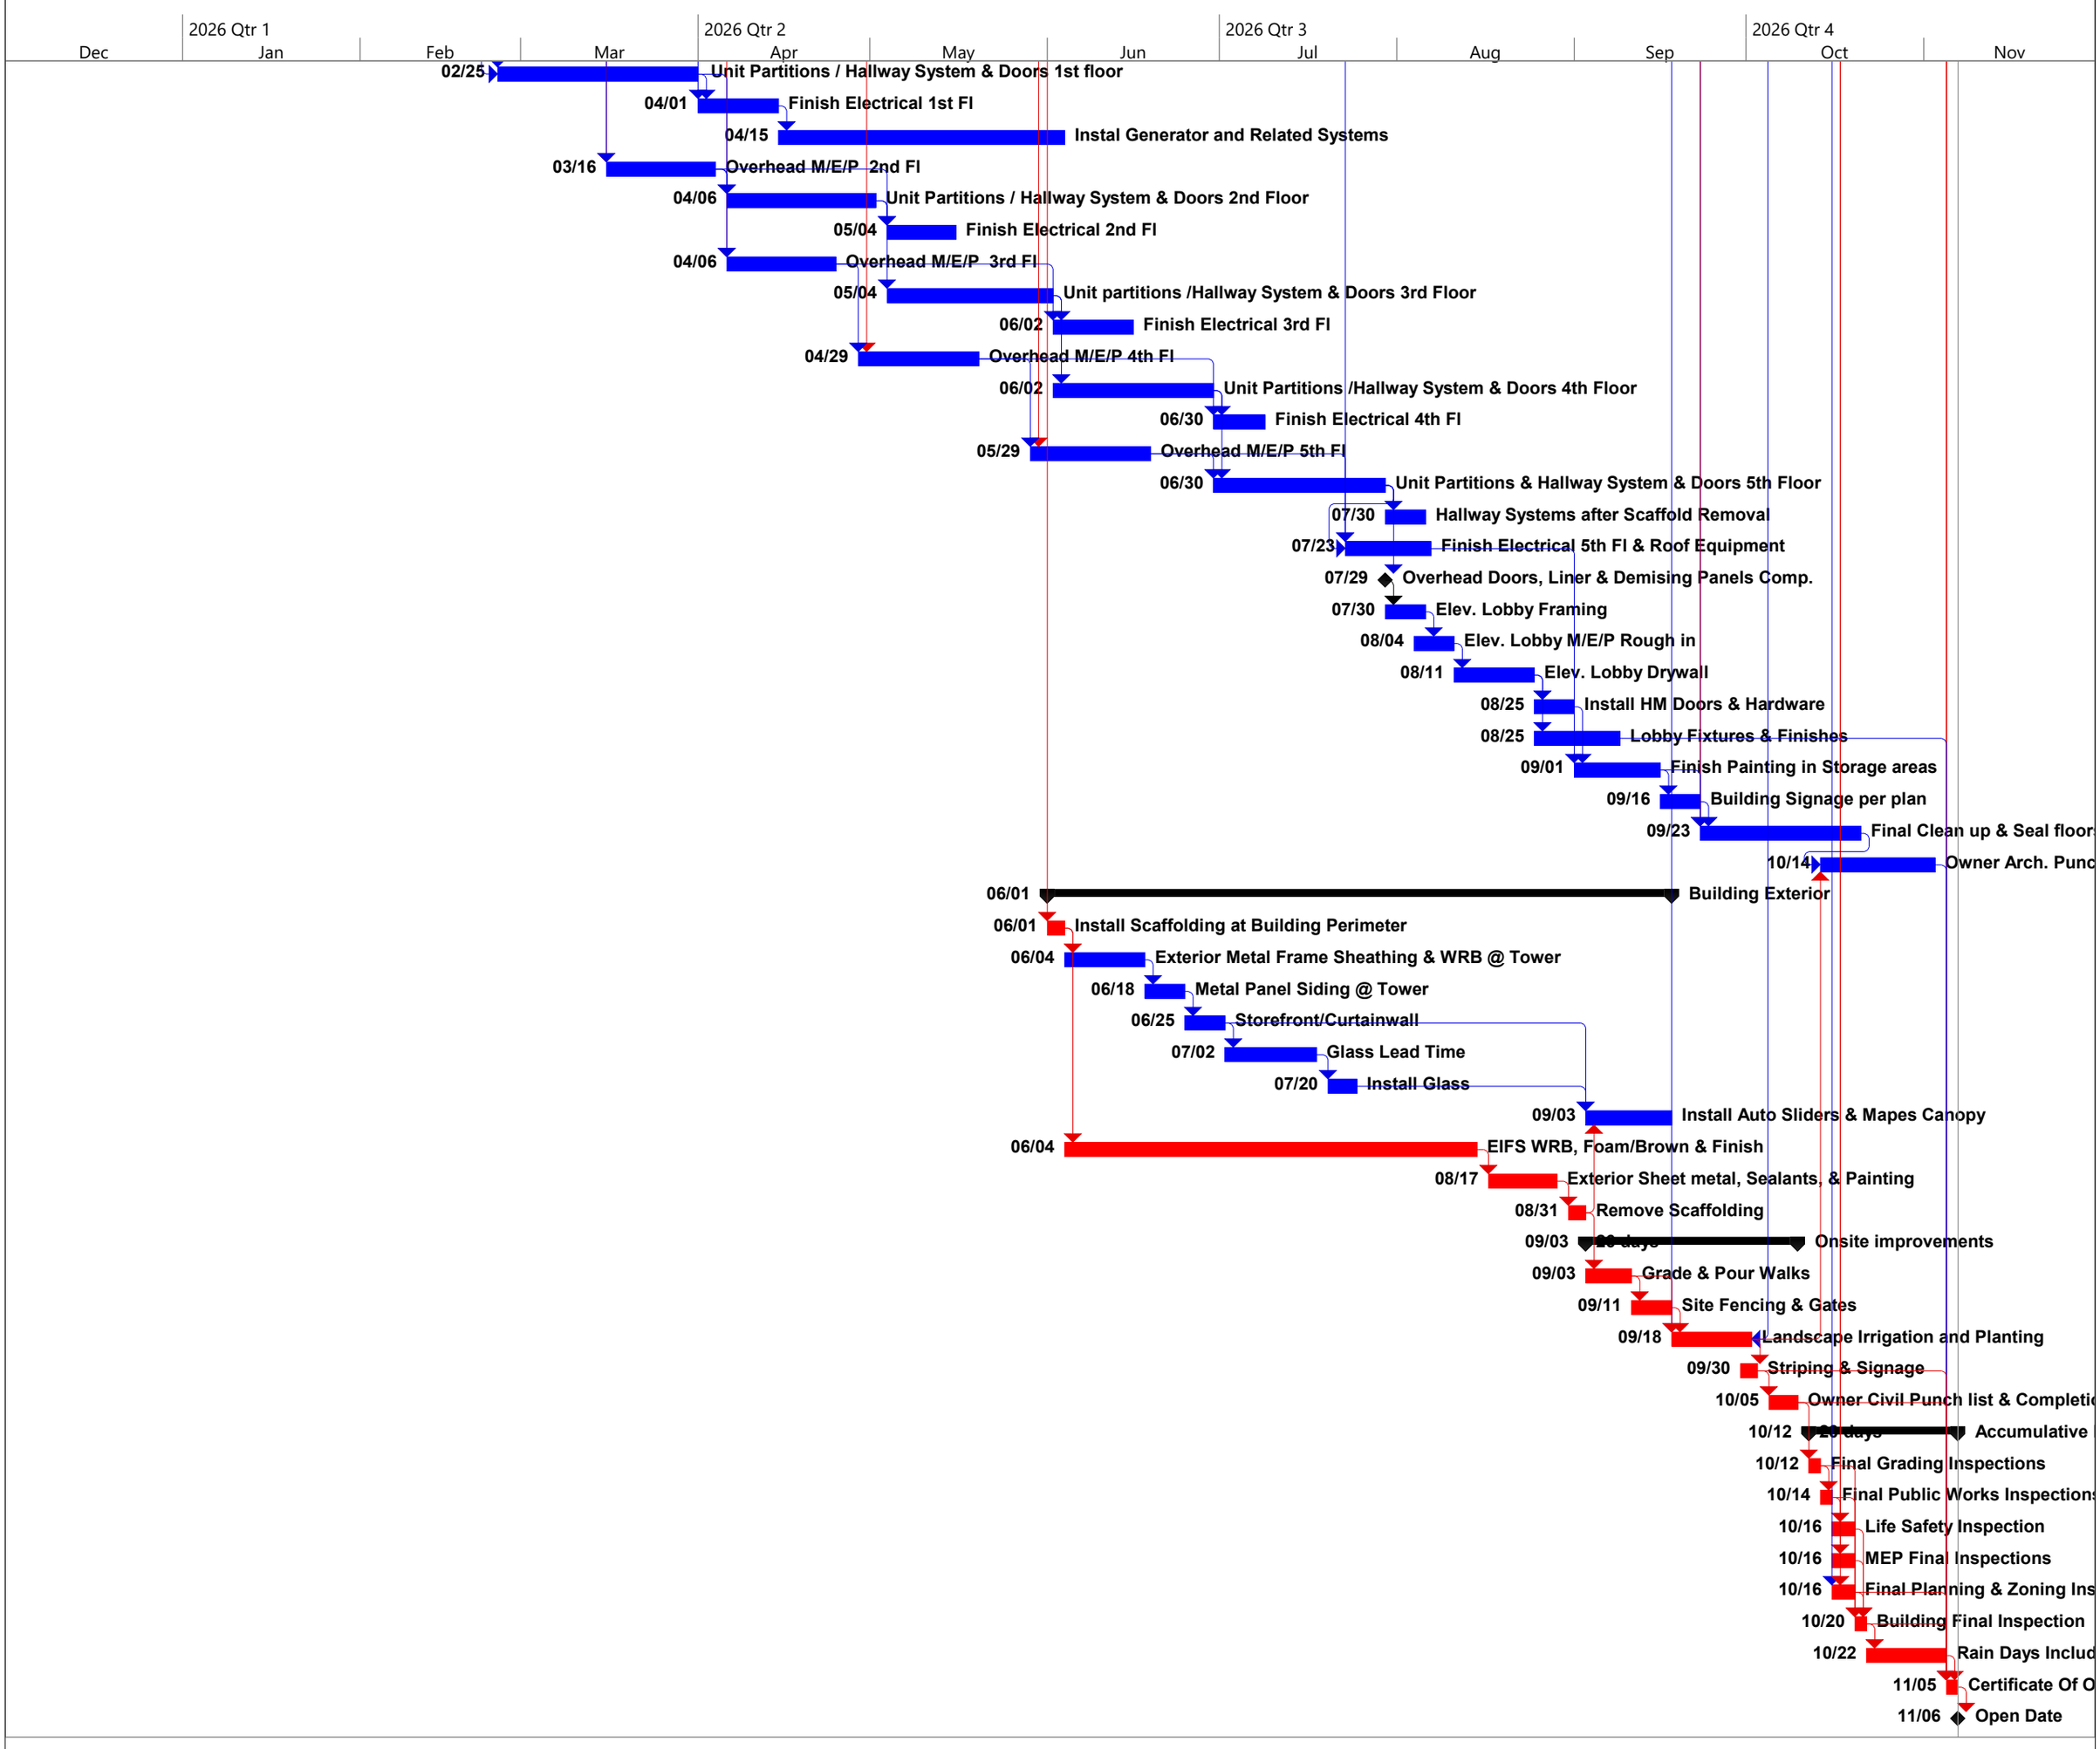
2026 Qtr 1
2026 Qtr 2
2026 Qtr 3
2026 Qtr 4
Dec
Jan
Feb
Mar
Apr
May
Jun
Jul
Aug
Sep
Oct
Nov
02/25 Unit Partitions / Hallway System & Doors 1st floor
04/01 Finish Electrical 1st Fl
04/15 Instal Generator and Related Systems
03/16 Overhead M/E/P 2nd Fl
04/06 Unit Partitions / Hallway System & Doors 2nd Floor
05/04 Finish Electrical 2nd Fl
04/06 Overhead M/E/P 3rd Fl
05/04 Unit partitions /Hallway System & Doors 3rd Floor
06/02 Finish Electrical 3rd Fl
04/29 Overhead M/E/P 4th Fl
06/02 Unit Partitions /Hallway System & Doors 4th Floor
06/30 Finish Electrical 4th Fl
05/29 Overhead M/E/P 5th Fl
06/30 Unit Partitions & Hallway System & Doors 5th Floor
07/30 Hallway Systems after Scaffold Removal
07/23 Finish Electrical 5th Fl & Roof Equipment
07/29 Overhead Doors, Liner & Demising Panels Comp.
07/30 Elev. Lobby Framing
08/04 Elev. Lobby M/E/P Rough in
08/11 Elev. Lobby Drywall
08/25 Install HM Doors & Hardware
08/25 Lobby Fixtures & Finishes
09/01 Finish Painting in Storage areas
09/16 Building Signage per plan
09/23 Final Clean up & Seal floor
10/14 Owner Arch. Punc
06/01 Building Exterior
06/01 Install Scaffolding at Building Perimeter
06/04 Exterior Metal Frame Sheathing & WRB @ Tower
06/18 Metal Panel Siding @ Tower
06/25 Storefront/Curtainwall
07/02 Glass Lead Time
07/20 Install Glass
09/03 Install Auto Sliders & Mapes Canopy
06/04 EIFS WRB, Foam/Brown & Finish
08/17 Exterior Sheet metal, Sealants, & Painting
08/31 Remove Scaffolding
09/03 Onsite improvements
09/03 Grade & Pour Walks
09/11 Site Fencing & Gates
09/18 Landscape Irrigation and Planting
09/30 Striping & Signage
10/05 Owner Civil Punch list & Completi
10/12 Accumulative
10/12 Final Grading Inspections
10/14 Final Public Works Inspection
10/16 Life Safety Inspection
10/16 MEP Final Inspections
10/16 Final Planning & Zoning Ins
10/20 Building Final Inspection
10/22 Rain Days Includ
11/05 Certificate Of O
11/06 Open Date

2027 Qtr 1 | 2027 Qtr 2 | 2027 Qtr 3 | 2027 Qtr 4

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct

Grading & Building Slab Construction

Building Construction

3

ngs

vator inspection Lead Time & Approval

nlift Landings

ave Out Area

nfilled Landings

Building Interior

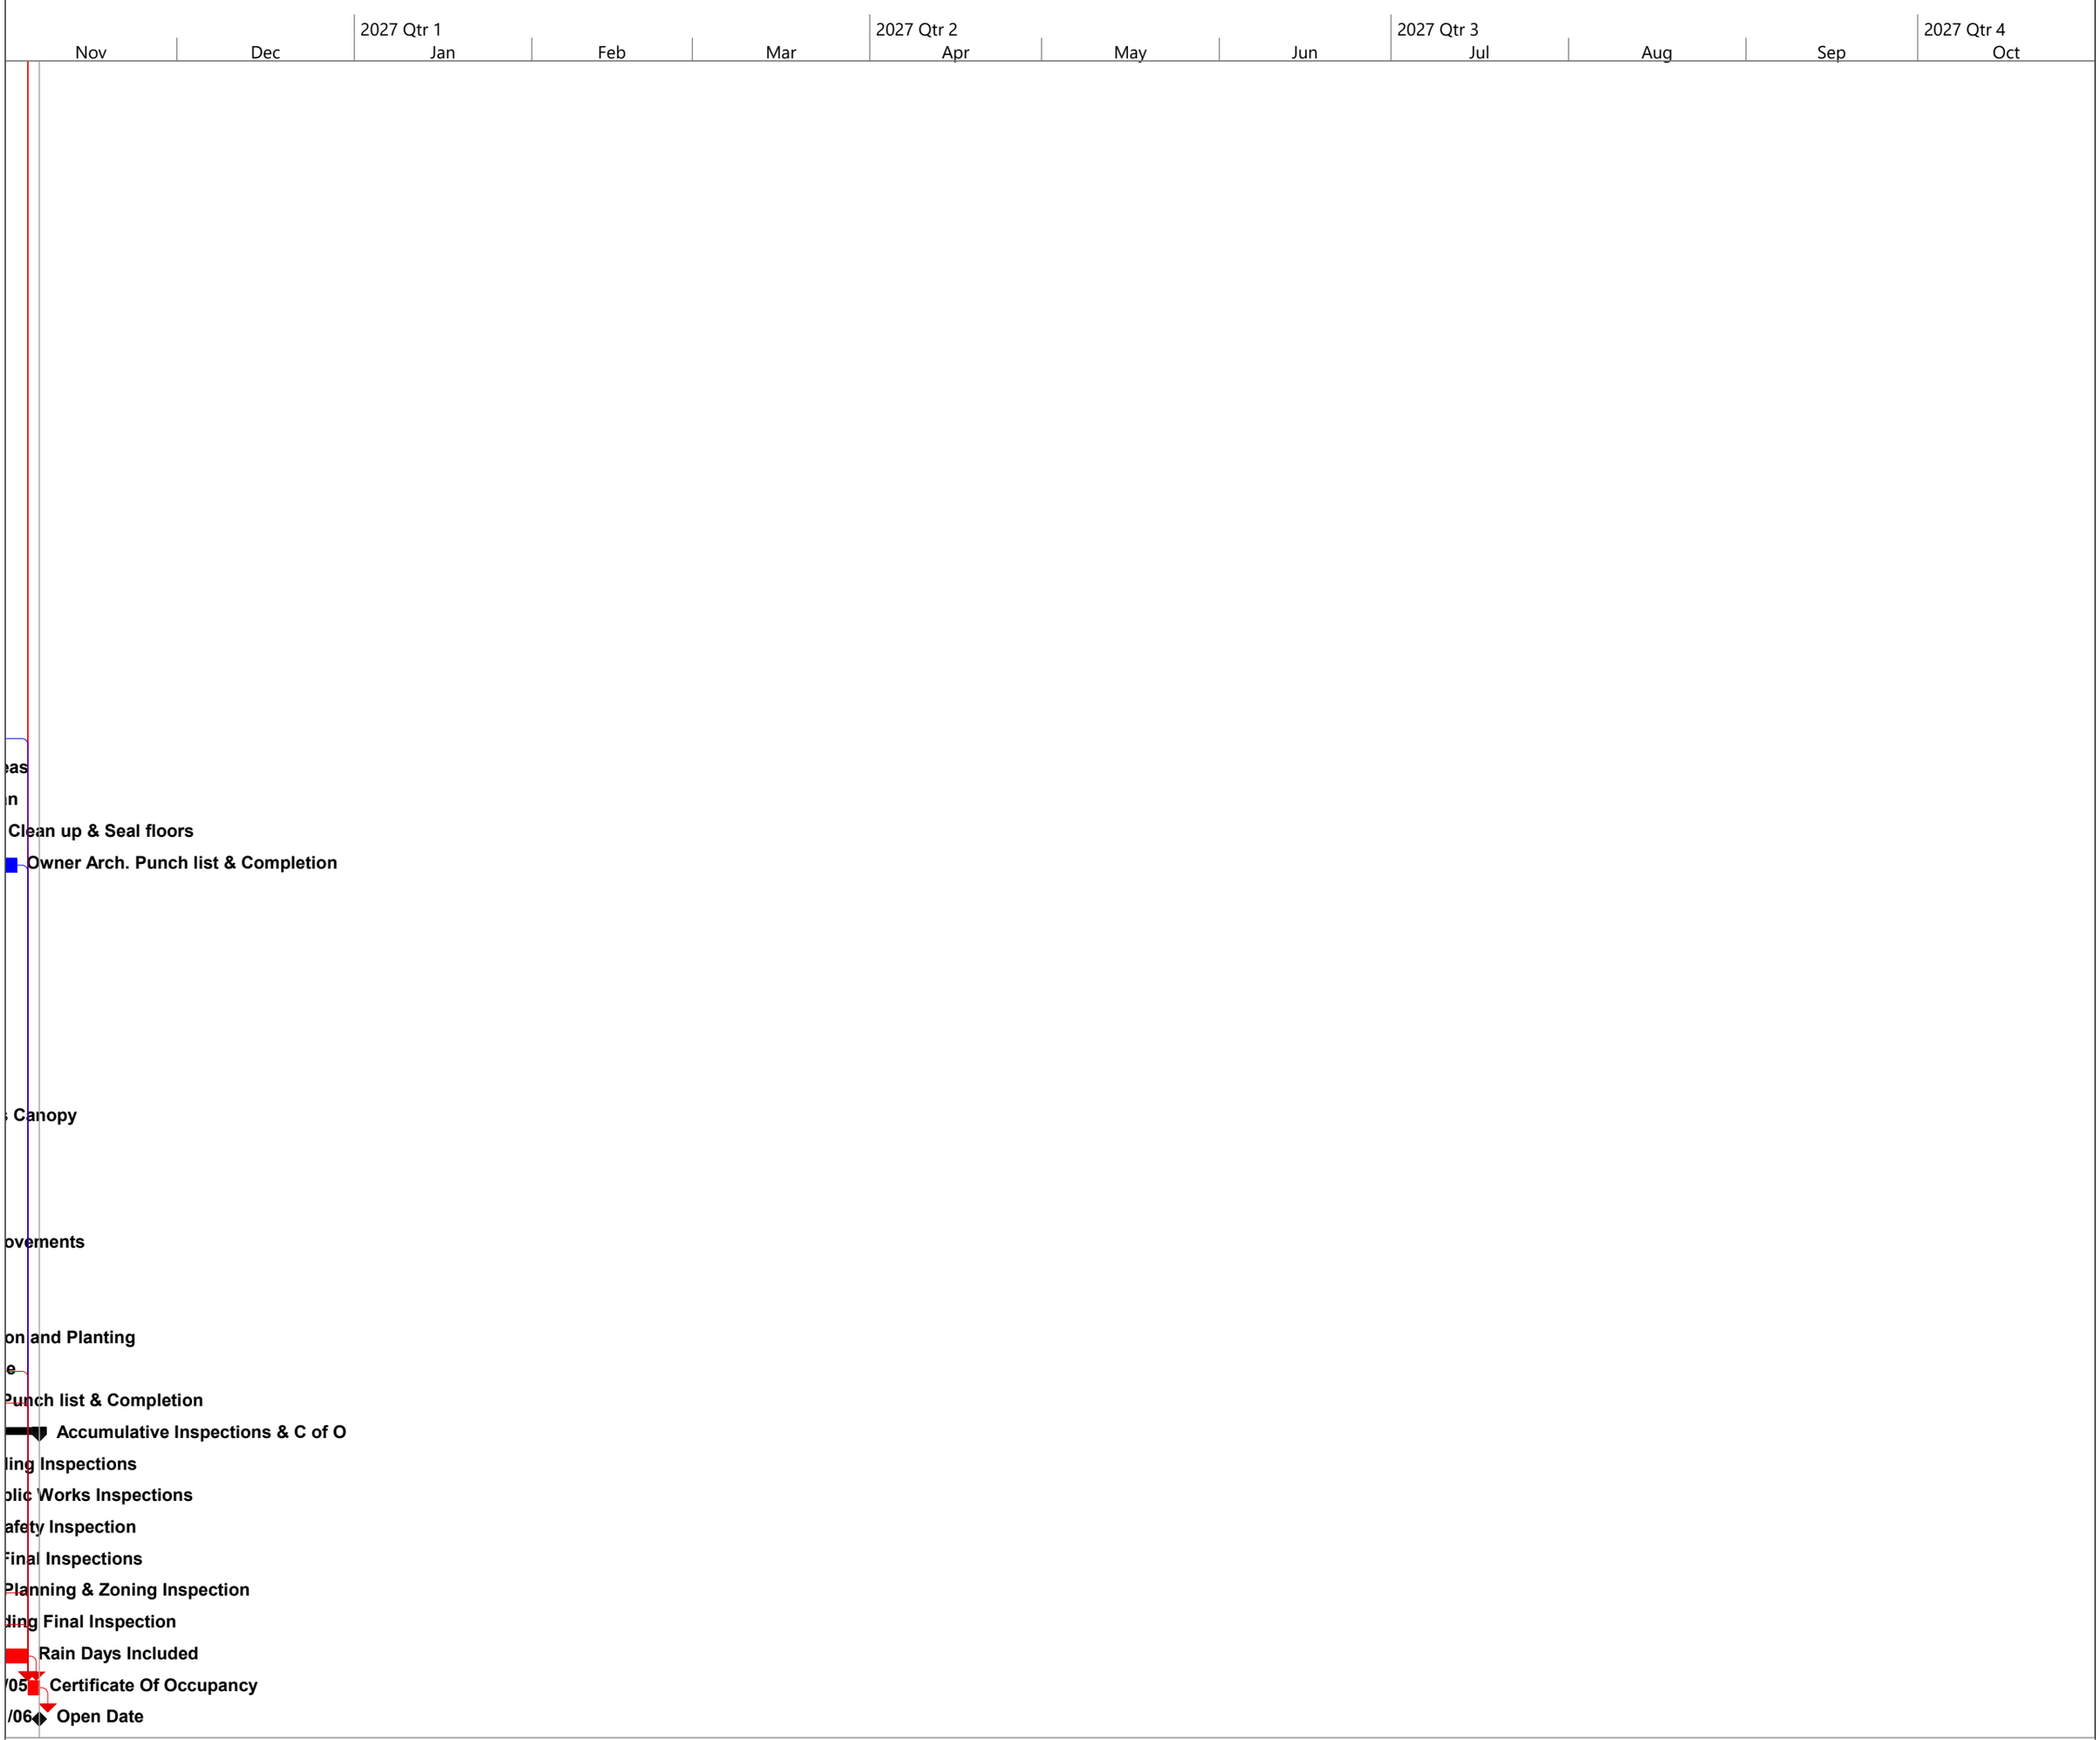
2027 Qtr 1
2027 Qtr 2
2027 Qtr 3
2027 Qtr 4
Nov
Dec
Jan
Feb
Mar
Apr
May
Jun
Jul
Aug
Sep
Oct
eas
n
Clean up & Seal floors
Owner Arch. Punch list & Completion
Canopy
ovements
on and Planting
e
Punch list & Completion
Accumulative Inspections & C of O
ling Inspections
blic Works Inspections
afety Inspection
Final Inspections
Planning & Zoning Inspection
ding Final Inspection
Rain Days Included
/05
Certificate Of Occupancy
/06
Open Date
