	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Grading & Building Slab Construction**	**313 days**	**295 days**	**18d**	**9/8/25**	**9/8/25**	**0d**	**12/4/26**	**11/6/26**	**20d**
2	Commencement Date 9/8/2025	1 day	1 day	0d	9/8/25	9/8/25	0d	9/8/25	9/8/25	0d
3	HBI Mobilization	8 days	8 days	0d	9/9/25	9/9/25	0d	9/18/25	9/18/25	0d
4	Install Temp Fencing & BMP's	3 days	3 days	0d	9/19/25	9/19/25	0d	9/23/25	9/23/25	0d
5	Move Existing Rolling Gate	5 days			9/22/25			9/26/25		
6	Surface Demo Existing Phase II areas	16 days	12 days	4d	9/29/25	10/3/25	-4d	10/20/25	10/20/25	0d
7	AQMD Notification for Transite Fire Water	10 days			10/16/25			10/29/25		
8	Identify & Cap Existing Utilities to Limits	3 days	3 days	0d	10/16/25	9/19/25	19d	10/20/25	9/23/25	19d
9	Abate Fire Water Lines per Change Order #2	5 days			10/30/25			11/5/25		
10	Grading Permit Needed	0 days			10/20/25			10/20/25		
11	Grading Permit Delay - Actual	17 days			10/21/25			11/12/25		
12	Pre-Grade Meeting w/ City	1 day			11/13/25			11/13/25		
13	Rain and Mud Delay - Taken from item 147 below	6 days			11/14/25			11/21/25		
14	O/X & Grading for Bldg pad	8 days	12 days	-4d	11/24/25	10/21/25	24d	12/5/25	11/5/25	22d
15	Certify Pad / Pad Delivery Date	2 days	2 days	0d	12/8/25	11/6/25	22d	12/9/25	11/7/25	22d
16	Building Permit required	0 days	0 days	0d	12/9/25	11/7/25	22d	12/9/25	11/7/25	22d
17	Install Fire line Modifications	7 days	7 days	0d	12/10/25	9/24/25	55d	12/18/25	10/2/25	55d
18	Underslab Electrical & Plumbing	6 days	6 days	0d	12/10/25	11/10/25	22d	12/17/25	11/17/25	22d
19	Building Foundations & Pre-lim CMU/Forms	10 days	10 days	0d	12/10/25	11/10/25	22d	12/23/25	11/21/25	22d
20	Elevator Pit Form & Pour	10 days	10 days	0d	12/10/25	11/10/25	22d	12/23/25	11/21/25	22d
21	Slab Base Material Import & Grading	5 days	5 days	0d	12/24/25	11/24/25	22d	1/2/26	12/2/25	23d
22	Slab Vapor Barrier & Reinforcing	10 days	10 days	0d	12/31/25	12/1/25	22d	1/14/26	12/12/25	23d
23	Slab on Grade Pour North	4 days	4 days	0d	1/9/26	12/9/25	23d	1/14/26	12/12/25	23d
24	Slab on Grade Pour South	4 days	4 days	0d	1/15/26	12/15/25	23d	1/20/26	12/18/25	23d
25	**Site Wet Utilities**	**21 days**	**21 days**	**0d**	**12/10/25**	**11/10/25**	**22d**	**1/12/26**	**12/10/25**	**23d**
26	Storm Drain Piping & Catch Basins from Phase 1 Stubs	6 days	6 days	0d	12/10/25	11/10/25	22d	12/17/25	11/17/25	22d
27	Extend Sewer Laterals to building	5 days	5 days	0d	12/18/25	11/18/25	22d	12/24/25	11/24/25	22d
28	Extend Fire / Domestic Water Service to Building	10 days	10 days	0d	12/29/25	11/25/25	24d	1/12/26	12/10/25	23d
29	Domestic & Fire Water Services Completion	0 days	0 days	0d	1/12/26	12/10/25	23d	1/12/26	12/10/25	23d
30	**Site Dry Utilities**	**8 days**	**8 days**	**0d**	**12/18/25**	**11/18/25**	**22d**	**12/31/25**	**12/1/25**	**22d**
31	Extend Power & Lov Voltage conduits to Bldg from Stubs	5 days	5 days	0d	12/18/25	11/18/25	22d	12/24/25	11/24/25	22d
32	Install Generac & Site lighting Conduits	3 days	3 days	0d	12/29/25	11/25/25	24d	12/31/25	12/1/25	22d
33	**Onsite improvements For Early Base Pave**	**22 days**	**22 days**	**0d**	**1/13/26**	**12/11/25**	**23d**	**2/11/26**	**1/14/26**	**20d**
34	Grade for Curb & Gutter	4 days	4 days	0d	1/13/26	12/11/25	23d	1/16/26	12/16/25	23d
35	Install Irrigation Sleeves	1 day	1 day	0d	1/19/26	12/17/25	23d	1/19/26	12/17/25	23d
36	Place Curb & Gutter	4 days	4 days	0d	1/20/26	12/18/25	23d	1/23/26	12/23/25	23d
37	Grade & Pour Walks	5 days	5 days	0d	1/22/26	12/22/25	23d	1/28/26	12/30/25	21d
38	Agg Base Import & AC Base Paving	10 days	10 days	0d	1/29/26	12/31/25	21d	2/11/26	1/14/26	20d
39	**Vertical Building Construction**	**215 days**	**211 days**	**4d**	**1/15/26**	**12/15/25**	**23d**	**11/18/26**	**10/15/26**	**24d**
40	CMU Walls to 14'-8" North	15 days	15 days	0d	1/15/26	12/15/25	23d	2/4/26	1/7/26	20d
41	CMU Walls to 14'-8" South	15 days	15 days	0d	2/5/26	1/8/26	20d	2/26/26	1/28/26	21d

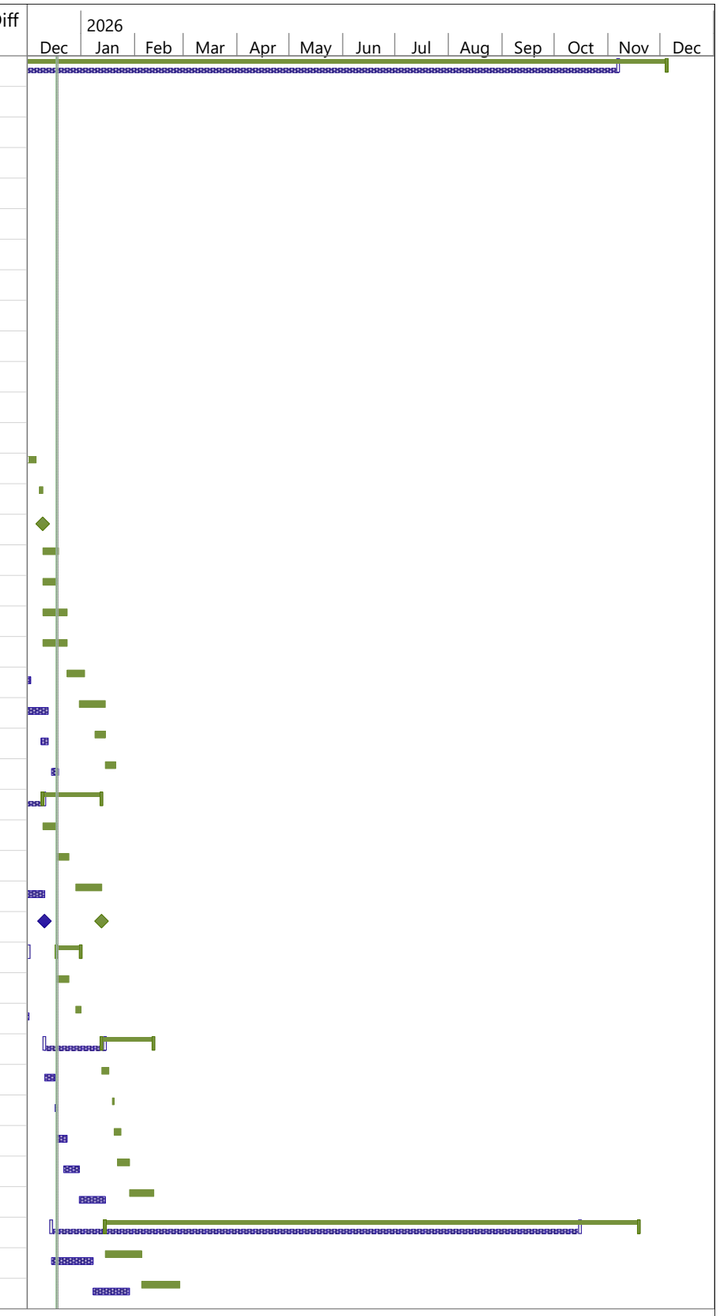

Project: Project1
Date: 12/18/25

Task: Previous
Task: Current
Milestone: Previous
Milestone: Current
Summary: Previous
Summary: Current
Placeholder Duration: Previous
Placeholder Duration: Current
Placeholder Start: Previous
Placeholder Start: Current
Placeholder Finish: Previous
Placeholder Finish: Current
Inactive Task: Previous
Inactive Task: Current
Inactive Milestone: Previous
Inactive Milestone: Current
Inactive Summary: Previous
Inactive Summary: Current

		Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
42		Structural Steel Framing & Metal Deck to 2nd floor N.	7 days	7 days	0d	2/5/26	1/8/26	20d	2/13/26	1/16/26	20d
43		Structural Steel Framing & Metal Deck to 2nd floor S.	7 days	7 days	0d	2/23/26	1/23/26	21d	3/3/26	2/2/26	21d
44		Rebar, Hangars & Deck2 Pour North	7 days	7 days	0d	2/17/26	1/19/26	21d	2/25/26	1/27/26	21d
45		Rebar, Hangars & Deck2 Pour South	7 days	7 days	0d	3/4/26	2/3/26	21d	3/12/26	2/11/26	21d
46		CMU Walls to 25'-4" North	12 days	10 days	2d	2/27/26	1/29/26	21d	3/16/26	2/11/26	23d
47		CMU Walls to 25'-4" South	12 days	10 days	2d	3/17/26	2/12/26	23d	4/1/26	2/26/26	24d
48		2nd floor Shear walls North @ 15k/week	12 days	12 days	0d	2/27/26	1/29/26	21d	3/16/26	2/13/26	21d
49		3rd Floor Decking North @ 5k/day	7 days	7 days	0d	3/11/26	2/10/26	21d	3/19/26	2/19/26	20d
50		Rebar, Hangars & Deck Pour3 North	5 days	5 days	0d	3/20/26	2/20/26	20d	3/26/26	2/26/26	20d
51		2nd floor Shear walls South @ 15k/week	12 days	12 days	0d	3/17/26	2/12/26	23d	4/1/26	3/2/26	22d
52		3rd Floor Decking South@ 5k/day	7 days	7 days	0d	3/30/26	2/26/26	22d	4/7/26	3/6/26	22d
53		Rebar, Hangars & Deck3 Pour South	5 days	5 days	0d	4/8/26	3/9/26	22d	4/14/26	3/13/26	22d
54		CMU Walls to 36' North	10 days	10 days	0d	4/2/26	2/27/26	24d	4/15/26	3/12/26	24d
55		CMU Walls to 36' South	10 days	10 days	0d	4/16/26	3/16/26	23d	4/29/26	3/27/26	23d
56		3rd floor Shear walls North @ 15k/week	12 days	12 days	0d	4/2/26	2/27/26	24d	4/17/26	3/16/26	24d
57		4th Floor Decking North @ 5k/day	7 days	7 days	0d	4/16/26	3/13/26	24d	4/24/26	3/23/26	24d
58		Rebar, Hangars & Deck Pour4 North	5 days	5 days	0d	4/27/26	3/24/26	24d	5/1/26	3/30/26	24d
59		3rd floor Shear walls South @ 15k/week	12 days	12 days	0d	4/16/26	3/16/26	23d	5/1/26	3/31/26	23d
60		4th Floor Decking South@ 5k/day	7 days	7 days	0d	4/29/26	3/27/26	23d	5/7/26	4/6/26	23d
61		Rebar, Hangars & Deck4 Pour South	5 days	5 days	0d	5/8/26	4/7/26	23d	5/14/26	4/13/26	23d
62		CMU Walls to 46'-8" North	10 days	10 days	0d	5/4/26	3/31/26	24d	5/15/26	4/13/26	24d
63		CMU Walls to 46'-8" South	10 days	10 days	0d	5/18/26	4/14/26	24d	6/1/26	4/27/26	25d
64		4th floor Shear walls North @ 15k/week	12 days	12 days	0d	5/4/26	3/31/26	24d	5/19/26	4/15/26	24d
65		5th Floor Decking North @ 5k/day	7 days	7 days	0d	5/15/26	4/13/26	24d	5/26/26	4/21/26	25d
66		Rebar, Hangars & Deck Pour5 North	5 days	5 days	0d	5/27/26	4/22/26	25d	6/2/26	4/28/26	25d
67		4th floor Shear walls South @ 15k/week	12 days	12 days	0d	5/18/26	4/14/26	24d	6/3/26	4/29/26	25d
68		5th Floor Decking South@ 5k/day	7 days	7 days	0d	6/1/26	4/27/26	25d	6/9/26	5/5/26	25d
69		Rebar, Hangars & Deck5 Pour South	7 days	7 days	0d	6/10/26	5/6/26	25d	6/18/26	5/14/26	25d
70		CMU Walls to 57'-4" North	10 days	10 days	0d	6/3/26	4/29/26	25d	6/16/26	5/12/26	25d
71		CMU Walls to 57'-4" South	10 days	10 days	0d	6/19/26	5/15/26	25d	7/2/26	5/29/26	24d
72		5th floor Shear walls North @ 15k/week	14 days	14 days	0d	6/3/26	4/29/26	25d	6/22/26	5/18/26	25d
73		Roof Equipment Structural	3 days	3 days	0d	6/18/26	5/14/26	25d	6/22/26	5/18/26	25d
74		Roof Decking North @ 5k/day	7 days	7 days	0d	6/23/26	5/19/26	25d	7/1/26	5/28/26	24d
75		Roof Drains, Screens & Curbs	10 days	10 days	0d	7/2/26	5/29/26	24d	7/17/26	6/11/26	26d
76		5th floor Shear walls South @ 15k/week	12 days	12 days	0d	6/19/26	5/15/26	25d	7/8/26	6/2/26	26d
77		Roof Equipment Structural	3 days	3 days	0d	7/2/26	5/29/26	24d	7/8/26	6/2/26	26d
78		Roof Decking South@ 5k/day	7 days	7 days	0d	7/9/26	6/3/26	26d	7/17/26	6/11/26	26d
79		Roof insulation Crickets & TPO	7 days	7 days	0d	7/20/26	6/12/26	26d	7/28/26	6/22/26	26d
80		Building Temporarily Water Tight	0 days	0 days	0d	7/28/26	6/22/26	26d	7/28/26	6/22/26	26d
81		Set rooftop Equipment & hook up	3 days	3 days	0d	7/29/26	6/23/26	26d	7/31/26	6/25/26	26d
82		Elevator Construction Car #1	20 days	20 days	0d	7/29/26	6/23/26	26d	8/25/26	7/22/26	24d

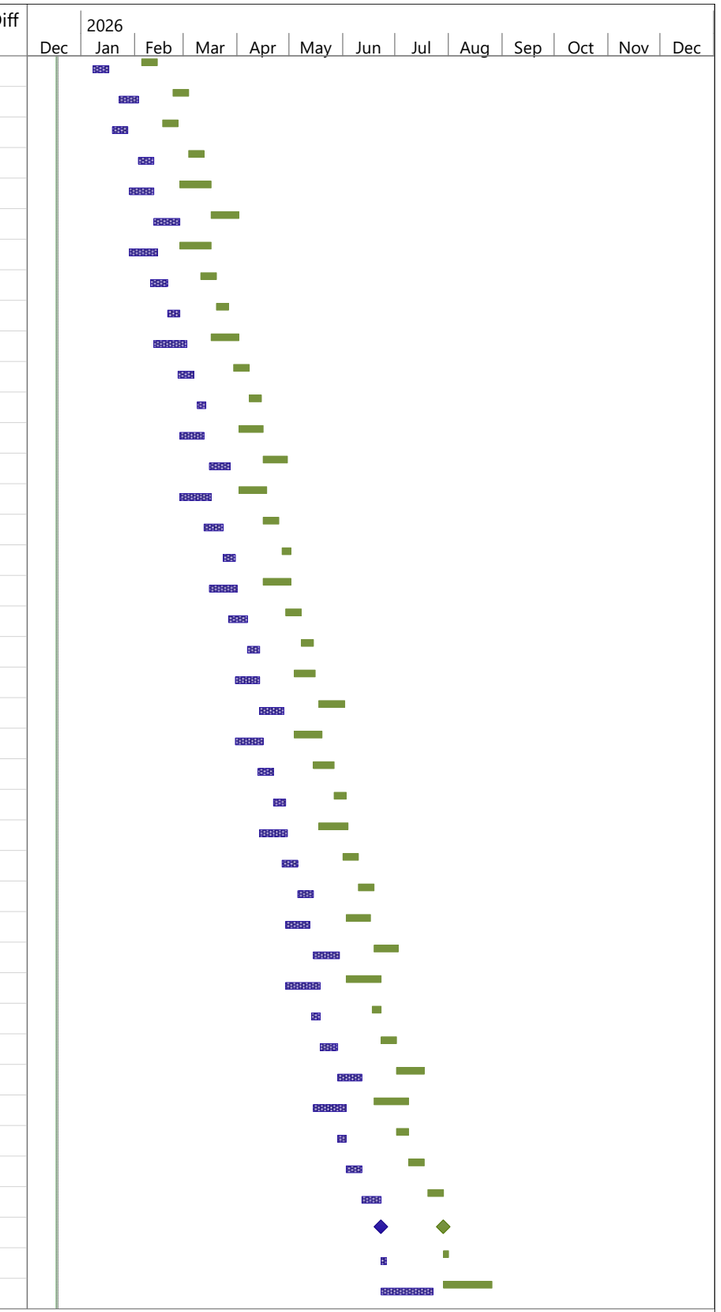

Project: Project1
Date: 12/18/25

Task: Previous
Task: Current
Milestone: Previous
Milestone: Current
Summary: Previous
Summary: Current
Placeholder Duration: Previous
Placeholder Duration: Current
Placeholder Start: Previous
Placeholder Start: Current
Placeholder Finish: Previous
Placeholder Finish: Current
Inactive Task: Previous
Inactive Task: Current
Inactive Milestone: Previous
Inactive Milestone: Current
Inactive Summary: Previous
Inactive Summary: Current

		Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
83		CMU infill @ Elevator Openings	10 days	10 days	0d	8/12/26	7/9/26	24d	8/25/26	7/22/26	24d
84		Elevator Construction Car #2	20 days	20 days	0d	8/26/26	7/23/26	24d	9/23/26	8/19/26	25d
85		CMU infill @ Elevator Openings	10 days	10 days	0d	9/10/26	8/6/26	25d	9/23/26	8/19/26	25d
86		Elevator Construction Car #3	20 days	20 days	0d	9/24/26	8/20/26	25d	10/21/26	9/17/26	24d
87		CMU infill @ Elevator Openings	10 days	10 days	0d	10/8/26	9/3/26	25d	10/21/26	9/17/26	24d
88		State Elevator inspection Lead Time & Approval	20 days	20 days	0d	10/22/26	9/18/26	24d	11/18/26	10/15/26	24d
89		Remove Man Lift	2 days	2 days	0d	10/22/26	9/18/26	24d	10/23/26	9/21/26	24d
90		Infill Framing @ Manlift Landings	7 days	7 days	0d	10/23/26	9/21/26	24d	11/2/26	9/29/26	24d
91		Sheathing Lift Leave Out Area	5 days	5 days	0d	10/30/26	9/28/26	24d	11/5/26	10/2/26	24d
92		Finishes @ Infilled Landings	5 days	5 days	0d	11/6/26	10/5/26	24d	11/12/26	10/9/26	24d
93		**Building Interior**	**186 days**	**194 days**	**-8d**	**2/26/26**	**1/28/26**	**21d**	**11/18/26**	**11/2/26**	**12d**
94		Layout & Install Overhead Hangars 1st fl	2 days	2 days	0d	2/26/26	1/28/26	21d	2/27/26	1/29/26	21d
95		Spray Applied Fireproofing - 1st Floor	10 days	10 days	0d	3/2/26	1/30/26	21d	3/13/26	2/12/26	21d
96		Overhead P, M, & E 1st fl	15 days	15 days	0d	3/11/26	2/10/26	21d	3/31/26	3/3/26	20d
97		Unit Partitions / Hallway System & Doors 1st floor	25 days	25 days	0d	3/25/26	2/25/26	20d	4/28/26	3/31/26	20d
98		Finish Electrical 1st Fl	10 days	10 days	0d	4/29/26	4/1/26	20d	5/12/26	4/14/26	20d
99		Instal Generator and Related Systems	35 days	35 days	0d	5/13/26	4/15/26	20d	7/1/26	6/3/26	20d
100		Overhead M/E/P 2nd Fl	15 days	15 days	0d	4/15/26	3/16/26	22d	5/5/26	4/3/26	22d
101		Unit Partitions / Hallway System & Doors 2nd Floor	20 days	20 days	0d	5/6/26	4/6/26	22d	6/3/26	5/1/26	23d
102		Finish Electrical 2nd Fl	10 days	10 days	0d	6/4/26	5/4/26	23d	6/17/26	5/15/26	23d
103		Overhead M/E/P 3rd Fl	15 days	15 days	0d	5/6/26	4/6/26	22d	5/27/26	4/24/26	23d
104		Unit partitions /Hallway System & Doors 3rd Floor	20 days	20 days	0d	6/4/26	5/4/26	23d	7/1/26	6/1/26	22d
105		Finish Electrical 3rd Fl	10 days	10 days	0d	7/2/26	6/2/26	22d	7/17/26	6/15/26	24d
106		Overhead M/E/P 4th Fl	15 days	15 days	0d	6/3/26	4/29/26	25d	6/23/26	5/19/26	25d
107		Unit Partitions /Hallway System & Doors 4th Floor	20 days	20 days	0d	7/2/26	6/2/26	22d	7/31/26	6/29/26	24d
108		Finish Electrical 4th Fl	5 days	5 days	0d	8/3/26	6/30/26	24d	8/7/26	7/8/26	22d
109		Overhead M/E/P 5th Fl	15 days	15 days	0d	7/2/26	5/29/26	24d	7/24/26	6/18/26	26d
110		Unit Partitions & Hallway System & Doors 5th Floor	20 days	20 days	0d	8/3/26	6/30/26	24d	8/28/26	7/29/26	22d
111		Hallway Systems after Scaffold Removal	5 days	5 days	0d	8/31/26	7/30/26	22d	9/4/26	8/5/26	22d
112		Finish Electrical 5th Fl & Roof Equipment	11 days	11 days	0d	8/24/26	7/23/26	22d	9/8/26	8/6/26	23d
113		Overhead Doors, Liner & Demising Panels Comp.	0 days	0 days	0d	8/28/26	7/29/26	22d	8/28/26	7/29/26	22d
114		Elev. Lobby Framing	5 days	5 days	0d	4/1/26	7/30/26	-86d	4/7/26	8/5/26	-86d
115		Elev. Lobby M/E/P Rough in	5 days	5 days	0d	4/6/26	8/4/26	-86d	4/10/26	8/10/26	-86d
116		Elev. Lobby Drywall	10 days	10 days	0d	4/13/26	8/11/26	-86d	4/24/26	8/24/26	-86d
117		Install HM Doors & Hardware	5 days	5 days	0d	4/29/26	8/25/26	-84d	5/5/26	8/31/26	-84d
118		Lobby Fixtures & Finishes	10 days	10 days	0d	4/27/26	8/25/26	-86d	5/8/26	9/8/26	-87d
119		Finish Painting in Storage areas	10 days	10 days	0d	9/9/26	9/1/26	6d	9/22/26	9/15/26	5d
120		Building Signage per plan	5 days	5 days	0d	9/23/26	9/16/26	5d	9/29/26	9/22/26	5d
121		Final Clean up & Seal floors	20 days	20 days	0d	10/1/26	9/23/26	6d	10/28/26	10/20/26	6d
122		Owner Arch. Punch list & Completion	10 days	14 days	-4d	11/5/26	10/14/26	16d	11/18/26	11/2/26	12d
123		**Building Exterior**	**76 days**	**76 days**	**0d**	**7/7/26**	**6/1/26**	**26d**	**10/21/26**	**9/17/26**	**24d**

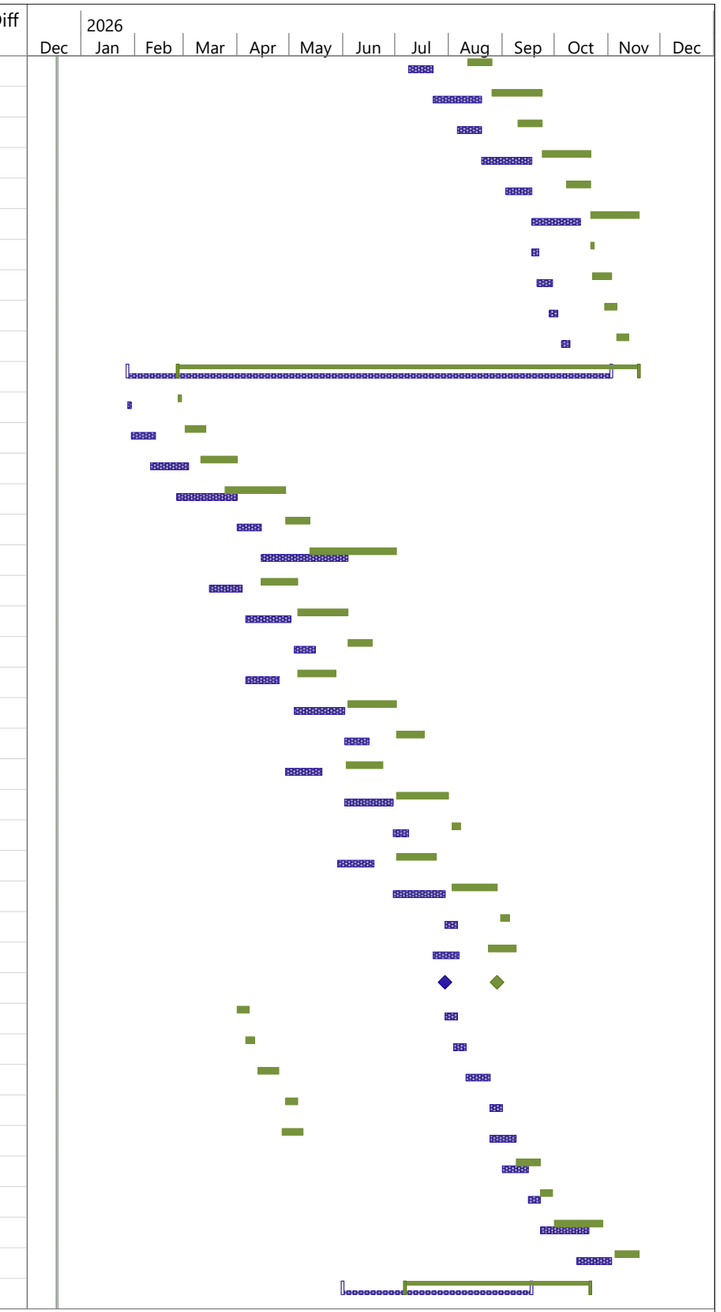

Project: Project1
Date: 12/18/25

Task: Previous
Task: Current
Milestone: Previous
Milestone: Current
Summary: Previous
Summary: Current
Placeholder Duration: Previous
Placeholder Duration: Current
Placeholder Start: Previous
Placeholder Start: Current
Placeholder Finish: Previous
Placeholder Finish: Current
Inactive Task: Previous
Inactive Task: Current
Inactive Milestone: Previous
Inactive Milestone: Current
Inactive Summary: Previous
Inactive Summary: Current

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
124	Install Scaffolding at Building Perimeter	3 days	3 days	0d	7/7/26	6/1/26	26d	7/9/26	6/3/26	26d
125	Exterior Metal Frame Sheathing & WRB @ Tower	10 days	10 days	0d	7/10/26	6/4/26	26d	7/23/26	6/17/26	26d
126	Metal Panel Siding @ Tower	5 days	5 days	0d	7/24/26	6/18/26	26d	7/30/26	6/24/26	26d
127	Storefront/Curtainwall	5 days	5 days	0d	7/31/26	6/25/26	26d	8/6/26	7/1/26	26d
128	Glass Lead Time	10 days	10 days	0d	8/7/26	7/2/26	26d	8/20/26	7/17/26	24d
129	Install Glass	5 days	5 days	0d	8/21/26	7/20/26	24d	8/27/26	7/24/26	24d
130	Install Auto Sliders & Mapes Canopy	10 days	10 days	0d	10/8/26	9/3/26	25d	10/21/26	9/17/26	24d
131	**EIFS WRB, Foam/Brown & Finish**	**50 days**	**50 days**	**0d**	**7/10/26**	**6/4/26**	**26d**	**9/18/26**	**8/14/26**	**25d**
132	Waterproof Membrane	10 days			7/10/26			7/23/26		
133	EIFS Foam	15 days			7/24/26			8/13/26		
134	EIFS Mesh Coat	15 days			8/14/26			9/3/26		
135	EIFS Top Coat	10 days			9/4/26			9/18/26		
136	Exterior Sheet metal, Sealants, & Painting	10 days	10 days	0d	9/21/26	8/17/26	25d	10/2/26	8/28/26	25d
137	Remove Scaffolding	3 days	3 days	0d	10/5/26	8/31/26	25d	10/7/26	9/2/26	25d
138	**Onsite improvements**	**26 days**	**26 days**	**0d**	**10/8/26**	**9/3/26**	**25d**	**11/12/26**	**10/9/26**	**24d**
139	Grade & Pour Walks	5 days	5 days	Equal	10/8/26	9/3/26	Different	10/14/26	9/10/26	Different
140	Site Fencing & Gates	5 days	5 days	0d	10/15/26	9/11/26	24d	10/21/26	9/17/26	24d
141	Landscape Irrigation and Planting	10 days	10 days	Equal	10/22/26	9/18/26	Different	11/4/26	10/1/26	Different
142	Striping & Signage	3 days	3 days	Equal	11/3/26	9/30/26	Different	11/5/26	10/2/26	Different
143	Owner Civil Punch list & Completion	5 days	5 days	0d	11/6/26	10/5/26	24d	11/12/26	10/9/26	24d
144	**Accumulative Inspections & C of O**	**19 days**	**20 days**	**Different**	**11/6/26**	**10/12/26**	**Different**	**12/4/26**	**11/6/26**	**Different**
145	Final Grading Inspections	2 days	2 days	0d	11/13/26	10/12/26	24d	11/16/26	10/13/26	24d
146	Final Public Works Inspections	2 days	2 days	0d	11/17/26	10/14/26	24d	11/18/26	10/15/26	24d
147	Life Safety Inspection	2 days	2 days	0d	11/19/26	10/16/26	24d	11/20/26	10/19/26	24d
148	MEP Final Inspections	2 days	2 days	0d	11/19/26	10/16/26	24d	11/20/26	10/19/26	24d
149	Final Planning & Zoning Inspection	2 days	2 days	0d	11/19/26	10/16/26	24d	11/20/26	10/19/26	24d
150	Building Final Inspection	2 days	2 days	0d	11/23/26	10/20/26	24d	11/24/26	10/21/26	24d
151	Rain Days Included	4 days	10 days	-6d	11/25/26	10/22/26	24d	12/2/26	11/4/26	20d
152	Certificate Of Occupancy	2 days	2 days	0d	12/3/26	11/5/26	20d	12/4/26	11/6/26	20d
153	Open Date	0 days	0 days	0d	12/4/26	11/6/26	20d	12/4/26	11/6/26	20d
154	Original Contracted Open Date	0 days			11/6/26			11/6/26		

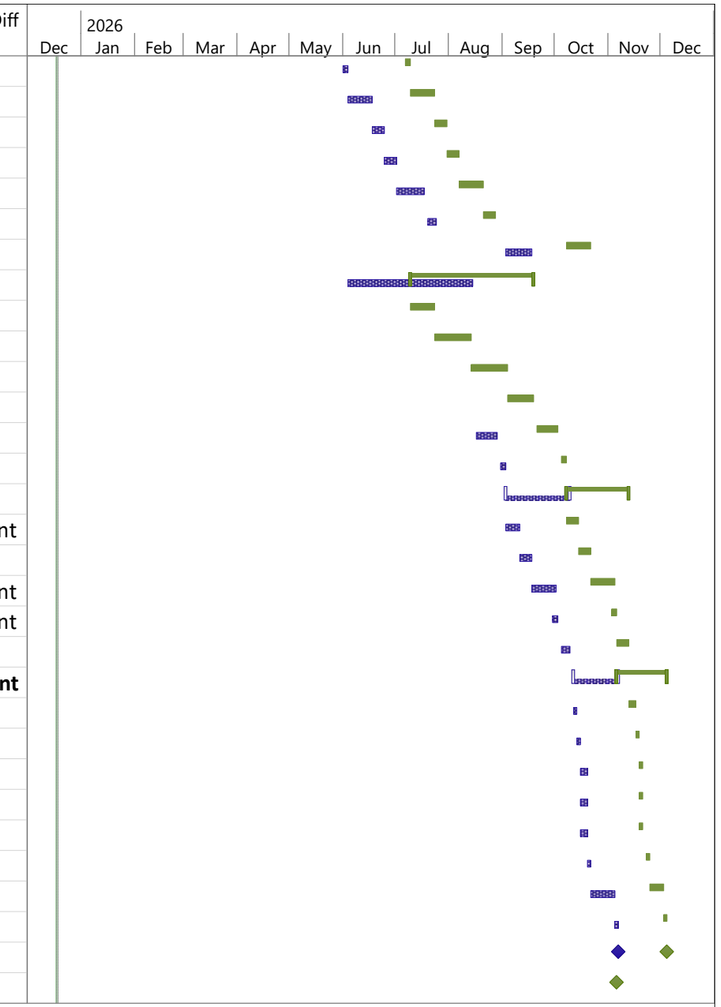

Project: Project1
Date: 12/18/25

Task: Previous
Task: Current
Milestone: Previous
Milestone: Current
Summary: Previous
Summary: Current
Placeholder Duration: Previous
Placeholder Duration: Current
Placeholder Start: Previous
Placeholder Start: Current
Placeholder Finish: Previous
Placeholder Finish: Current
Inactive Task: Previous
Inactive Task: Current
Inactive Milestone: Previous
Inactive Milestone: Current
Inactive Summary: Previous
Inactive Summary: Current
