Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
CA17097 - Anaheim - La Palma Phase 2 (exp) - 27261 - 2025.12.08 - UP(		314	0%	08-Sep-25A	02-Dec-26	0	08-Sep-25	02-Dec-26	0
Grading & Building Slab Construction		314	0%	08-Sep-25A	02-Dec-26	0	08-Sep-25	02-Dec-26	0
2	Commencement Date 9/8/2025	0	0%	08-Sep-25A	08-Sep-25A		08-Sep-25	08-Sep-25	0
3	HBI Mobilization	0	0%	09-Sep-25A	18-Sep-25A		09-Sep-25	18-Sep-25	0
4	Install Temp Fencing & BMP's	0	0%	19-Sep-25A	23-Sep-25A		19-Sep-25	23-Sep-25	0
5	Move Existing Rolling Gate	0	0%	22-Sep-25A	26-Sep-25A		22-Sep-25	26-Sep-25	0
6	Surface Demo Existing Phase II areas	0	0%	29-Sep-25A	20-Oct-25A		29-Sep-25	20-Oct-25	0
8	Identify & Cap Existing Utilities to Limits	0	0%	16-Oct-25A	20-Oct-25A		16-Oct-25	20-Oct-25	0
7	AQMD Notification for Transite Fire Water	0	0%	16-Oct-25A	29-Oct-25A		16-Oct-25	29-Oct-25	0
10	Grading Permit Needed	0	0%	20-Oct-25A	20-Oct-25A		20-Oct-25	20-Oct-25	0
11	Grading Permit Delay - Actual	0	0%	21-Oct-25A	12-Nov-25A		21-Oct-25	12-Nov-25	0
9	Abate Fire Water Lines per Change Order #2	0	0%	30-Oct-25A	05-Nov-25A		30-Oct-25	05-Nov-25	0
12	Pre-Grade Meeting w/ City	0	0%	13-Nov-25A	13-Nov-25A		13-Nov-25	13-Nov-25	0
13	Rain and Mud Delay - Taken from item 147 below	0	0%	14-Nov-25A	21-Nov-25A		14-Nov-25	21-Nov-25	0
14	O/X & Grading for Bldg pad	0	0%	24-Nov-25A	05-Dec-25A		24-Nov-25	04-Dec-25	-1
15	Certify Pad / Pad Delivery Date	2	0%	08-Dec-25	09-Dec-25	0	08-Dec-25	09-Dec-25	0
18	Underslab Electrical & Plumbing	6	0%	10-Dec-25	17-Dec-25	0	10-Dec-25	17-Dec-25	0
17	Install Fire line Modifications	7	0%	10-Dec-25	18-Dec-25	12	10-Dec-25	18-Dec-25	0
20	Elevator Pit Form & Pour	10	0%	10-Dec-25	23-Dec-25	3	10-Dec-25	23-Dec-25	0
16	Building Permit required	0	0%	10-Dec-25	10-Dec-25	12	10-Dec-25	10-Dec-25	0
19	Building Foundations & Pre-lim CMU/Forms	10	0%	10-Dec-25	23-Dec-25	0	10-Dec-25	23-Dec-25	0
21	Slab Base Material Import & Grading	5	0%	24-Dec-25	31-Dec-25	0	24-Dec-25	31-Dec-25	0
22	Slab Vapor Barrier & Reinforcing	10	0%	30-Dec-25	13-Jan-26	0	30-Dec-25	13-Jan-26	0
23	Slab on Grade Pour North	4	0%	08-Jan-26	13-Jan-26	0	08-Jan-26	13-Jan-26	0
24	Slab on Grade Pour South	4	0%	14-Jan-26	19-Jan-26	11	14-Jan-26	19-Jan-26	0
Building Exterior		76	0%	02-Jul-26	19-Oct-26	30	02-Jul-26	19-Oct-26	0
124	Install Scaffolding at Building Perimeter	3	0%	02-Jul-26	07-Jul-26	0	02-Jul-26	07-Jul-26	0
125	Exterior Metal Frame Sheathing & WRB @ Tower	10	0%	08-Jul-26	21-Jul-26	58	08-Jul-26	21-Jul-26	0
126	Metal Panel Siding @ Tower	5	0%	22-Jul-26	28-Jul-26	58	22-Jul-26	28-Jul-26	0
127	Storefront/Curtainwall	5	0%	29-Jul-26	04-Aug-26	58	29-Jul-26	04-Aug-26	0
128	Glass Lead Time	10	0%	05-Aug-26	18-Aug-26	58	05-Aug-26	18-Aug-26	0
129	Install Glass	5	0%	19-Aug-26	25-Aug-26	58	19-Aug-26	25-Aug-26	0
136	Exterior Sheet metal, Sealants, & Painting	10	0%	17-Sep-26	30-Sep-26	0	17-Sep-26	30-Sep-26	0
137	Remove Scaffolding	3	0%	01-Oct-26	05-Oct-26	0	01-Oct-26	05-Oct-26	0
130	Install Auto Sliders & Mapes Canopy	10	0%	06-Oct-26	19-Oct-26	30	06-Oct-26	19-Oct-26	0
EIFS WRB, Foam/Brown & Finish		50	0%	08-Jul-26	16-Sep-26	0	08-Jul-26	16-Sep-26	0
132	Waterproof Membrane	10	0%	08-Jul-26	21-Jul-26	0	08-Jul-26	21-Jul-26	0
133	EIFS Foam	15	0%	22-Jul-26	11-Aug-26	0	22-Jul-26	11-Aug-26	0
134	EIFS Mesh Coat	15	0%	12-Aug-26	01-Sep-26	0	12-Aug-26	01-Sep-26	0
135	EIFS Top Coat	10	0%	02-Sep-26	16-Sep-26	0	02-Sep-26	16-Sep-26	0
Site Wet Utilities		21	0%	10-Dec-25	12-Jan-26	185	10-Dec-25	12-Jan-26	0
26	Storm Drain Piping & Catch Basins from Phase 1 Stubs	6	0%	10-Dec-25	17-Dec-25	185	10-Dec-25	17-Dec-25	0
27	Extend Sewer Laterals to building	5	0%	18-Dec-25	24-Dec-25	185	18-Dec-25	24-Dec-25	0
28	Extend Fire / Domestic Water Service to Building	10	0%	26-Dec-25	09-Jan-26	185	26-Dec-25	09-Jan-26	0
29	Domestic & Fire Water Services Completion	0	0%	12-Jan-26	12-Jan-26	185	12-Jan-26	12-Jan-26	0
Onsite Improvements		26	0%	06-Oct-26	10-Nov-26	0	06-Oct-26	10-Nov-26	0
139	Grade & Pour Walks	5	0%	06-Oct-26	12-Oct-26	0	06-Oct-26	12-Oct-26	0
140	Site Fencing & Gates	5	0%	13-Oct-26	19-Oct-26	0	13-Oct-26	19-Oct-26	0
141	Landscape Irrigation and Planting	10	0%	20-Oct-26	02-Nov-26	0	20-Oct-26	02-Nov-26	0
142	Striping & Signage	3	0%	30-Oct-26	03-Nov-26	0	30-Oct-26	03-Nov-26	0
143	Owner Civil Punch list & Completion	5	0%	04-Nov-26	10-Nov-26	0	04-Nov-26	10-Nov-26	0
Site Dry Utilities		8	0%	18-Dec-25	30-Dec-25	234	18-Dec-25	30-Dec-25	0
31	Extend Power & Lov Voltage conduits to Bldg from Stubs	5	0%	18-Dec-25	24-Dec-25	234	18-Dec-25	24-Dec-25	0
32	Install Generac & Site lighting Conduits	3	0%	26-Dec-25	30-Dec-25	234	26-Dec-25	30-Dec-25	0
Onsite Improvements For Early Base Pave		22	0%	12-Jan-26	10-Feb-26	185	12-Jan-26	10-Feb-26	0
34	Grade for Curb & Gutter	4	0%	12-Jan-26	15-Jan-26	185	12-Jan-26	15-Jan-26	0
35	Install Irrigation Sleeves	1	0%	16-Jan-26	16-Jan-26	185	16-Jan-26	16-Jan-26	0
36	Place Curb & Gutter	4	0%	19-Jan-26	22-Jan-26	185	19-Jan-26	22-Jan-26	0
37	Grade & Pour Walks	5	0%	21-Jan-26	27-Jan-26	185	21-Jan-26	27-Jan-26	0
38	Agg Base Import & AC Base Paving	10	0%	28-Jan-26	10-Feb-26	185	28-Jan-26	10-Feb-26	0
Accumulative Inspections & C of O		314	0%	08-Sep-25	02-Dec-26	0	08-Sep-25	02-Dec-26	0
154	Original Contracted Open Date	0	100%	08-Sep-25	08-Sep-25	314	08-Sep-25	08-Sep-25	0
145	Final Grading Inspections	2	0%	11-Nov-26	12-Nov-26	0	11-Nov-26	12-Nov-26	0
146	Final Public Works Inspections	2	0%	13-Nov-26	16-Nov-26	0	13-Nov-26	16-Nov-26	0
148	MEP Final Inspections	2	0%	17-Nov-26	18-Nov-26	0	17-Nov-26	18-Nov-26	0
149	Final Planning & Zoning Inspection	2	0%	17-Nov-26	18-Nov-26	0	17-Nov-26	18-Nov-26	0
147	Life Safety Inspection	2	0%	17-Nov-26	18-Nov-26	0	17-Nov-26	18-Nov-26	0
150	Building Final Inspection	2	0%	19-Nov-26	20-Nov-26	0	19-Nov-26	20-Nov-26	0
151	Rain Days Included	4	0%	23-Nov-26	27-Nov-26	0	23-Nov-26	27-Nov-26	0
152	Certificate Of Occupancy	2	0%	30-Nov-26	01-Dec-26	0	30-Nov-26	01-Dec-26	0

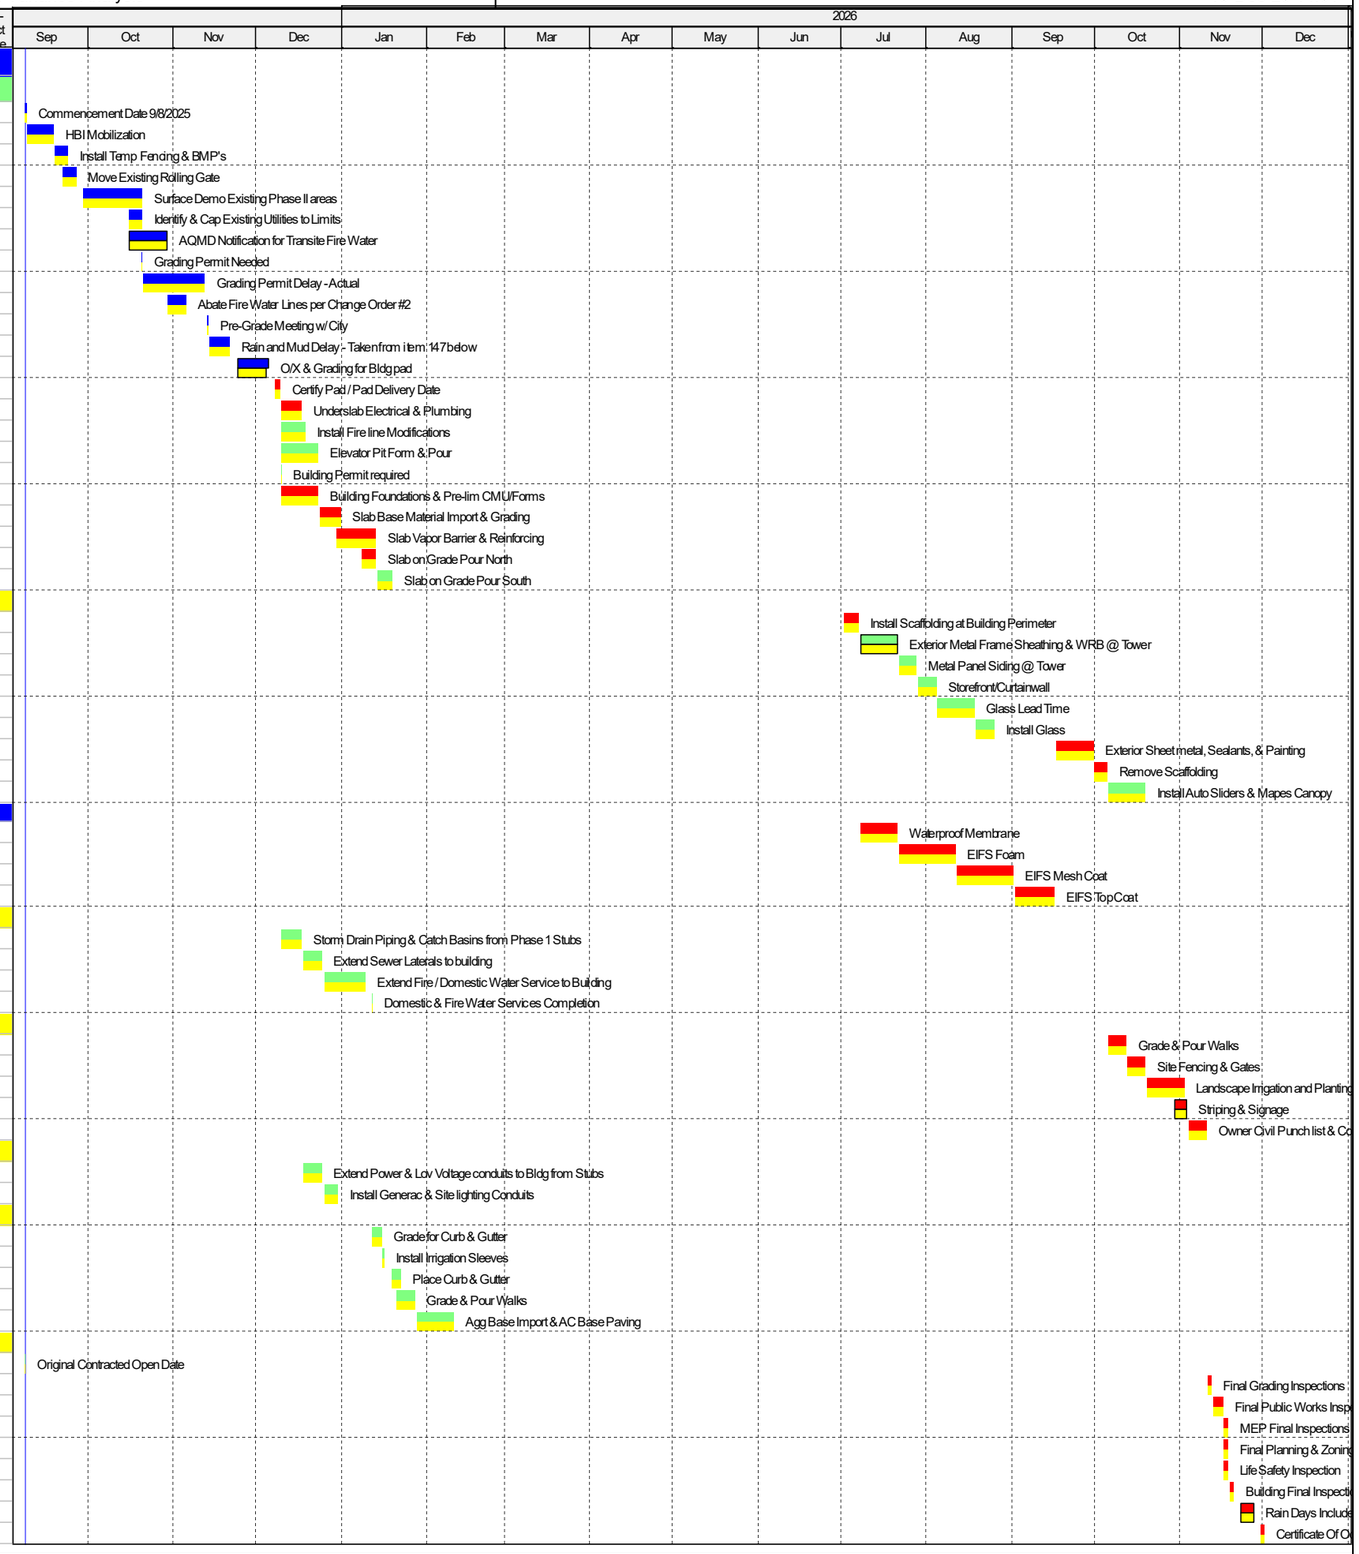

Project Baseline Bar | Remaining Work | ◇ Baseline Milestone
Actual Work | Critical Remaining Work | ◆ Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
153	Open Date	0	0%	02-Dec-26*	02-Dec-26	0	02-Dec-26	02-Dec-26	0
Building Interior		186	0%	25-Feb-26	16-Nov-26	10	25-Feb-26	16-Nov-26	0
94	Layout & Install Overhead Hangars 1st fl	2	0%	25-Feb-26	26-Feb-26	24	25-Feb-26	26-Feb-26	0
95	Spray Applied Fireproofing - 1st Floor	10	0%	27-Feb-26	12-Mar-26	24	27-Feb-26	12-Mar-26	0
96	Overhead P,M, & E 1st f	15	0%	10-Mar-26	30-Mar-26	24	10-Mar-26	30-Mar-26	0
97	Unit Partitions / Hallway System & Doors 1st floor	25	0%	24-Mar-26	27-Apr-26	24	24-Mar-26	27-Apr-26	0
114	Elev. Lobby Framing	5	0%	31-Mar-26	06-Apr-26	107	31-Mar-26	06-Apr-26	0
115	Elev. Lobby M/E/P Rough in	5	0%	03-Apr-26	09-Apr-26	107	03-Apr-26	09-Apr-26	0
116	Elev. Lobby Drywall	10	0%	10-Apr-26	23-Apr-26	107	10-Apr-26	23-Apr-26	0
100	Overhead M/E/P 2nd Fl	15	0%	14-Apr-26	04-May-26	19	14-Apr-26	04-May-26	0
118	Lobby Fixtures & Finishes	10	0%	24-Apr-26	07-May-26	142	24-Apr-26	07-May-26	0
98	Finish Electrical 1st Fl	10	0%	28-Apr-26	11-May-26	64	28-Apr-26	11-May-26	0
117	Install HM Doors & Hardware	5	0%	28-Apr-26	04-May-26	105	28-Apr-26	04-May-26	0
101	Unit Partitions / Hallway System & Doors 2nd Floor	20	0%	05-May-26	02-Jun-26	19	05-May-26	02-Jun-26	0
103	Overhead M/E/P 3rd Fl	15	0%	05-May-26	26-May-26	34	05-May-26	26-May-26	0
99	Instal Generator and Related Systems	35	0%	12-May-26	30-Jun-26	107	12-May-26	30-Jun-26	0
106	Overhead M/E/P 4th Fl	15	0%	02-Jun-26	22-Jun-26	30	02-Jun-26	22-Jun-26	0
102	Finish Electrical 2nd Fl	10	0%	03-Jun-26	16-Jun-26	49	03-Jun-26	16-Jun-26	0
104	Unit partitions /Hallway System & Doors 3rd Floor	20	0%	03-Jun-26	30-Jun-26	19	03-Jun-26	30-Jun-26	0
109	Overhead M/E/P 5th Fl	15	0%	01-Jul-26	22-Jul-26	24	01-Jul-26	22-Jul-26	0
105	Finish Electrical 3rd Fl	10	0%	01-Jul-26	15-Jul-26	39	01-Jul-26	15-Jul-26	0
107	Unit Partitions /Hallway System & Doors 4th Floor	20	0%	01-Jul-26	29-Jul-26	19	01-Jul-26	29-Jul-26	0
110	Unit Partitions & Hallway System & Doors 5th Floor	20	0%	30-Jul-26	26-Aug-26	19	30-Jul-26	26-Aug-26	0
108	Finish Electrical 4th Fl	5	0%	30-Jul-26	05-Aug-26	29	30-Jul-26	05-Aug-26	0
112	Finish Electrical 5th Fl & Roof Equipment	11	0%	20-Aug-26	03-Sep-26	19	20-Aug-26	03-Sep-26	0
111	Hallway Systems after Scaffold Removal	5	0%	27-Aug-26	02-Sep-26	62	27-Aug-26	02-Sep-26	0
113	Overhead Doors, Liner & Demising Panels Comp.	0	0%	27-Aug-26	27-Aug-26	67	27-Aug-26	27-Aug-26	0
119	Finish Painting in Storage areas	10	0%	04-Sep-26	18-Sep-26	19	04-Sep-26	18-Sep-26	0
120	Building Signage per plan	5	0%	21-Sep-26	25-Sep-26	19	21-Sep-26	25-Sep-26	0
121	Final Clean up & Seal floors	20	0%	29-Sep-26	26-Oct-26	18	29-Sep-26	26-Oct-26	0
122	Owner Arch. Punch list & Completion	10	0%	03-Nov-26	16-Nov-26	8	03-Nov-26	16-Nov-26	0
Vertical Building Construction		215	0%	14-Jan-26	16-Nov-26	0	14-Jan-26	16-Nov-26	0
40	CMU Walls to 14'-8" North	15	0%	14-Jan-26	03-Feb-26	0	14-Jan-26	03-Feb-26	0
41	CMU Walls to 14'-8" South	15	0%	04-Feb-26	25-Feb-26	0	04-Feb-26	25-Feb-26	0
42	Structural Steel Framing & Metal Deck to 2nd floor N.	7	0%	04-Feb-26	12-Feb-26	1	04-Feb-26	12-Feb-26	0
44	Rebar, Hangars & Deck2 Pour North	7	0%	13-Feb-26	24-Feb-26	1	13-Feb-26	24-Feb-26	0
43	Structural Steel Framing & Metal Deck to 2nd floor S.	7	0%	20-Feb-26	02-Mar-26	2	20-Feb-26	02-Mar-26	0
48	2nd floor Shear walls North @ 15k/week	12	0%	26-Feb-26	13-Mar-26	4	26-Feb-26	13-Mar-26	0
46	CMU Walls to 25-4" North	12	0%	26-Feb-26	13-Mar-26	0	26-Feb-26	13-Mar-26	0
45	Rebar, Hangars & Deck2 Pour South	7	0%	03-Mar-26	11-Mar-26	2	03-Mar-26	11-Mar-26	0
49	3rd Floor Decking North @ 5k/day	7	0%	10-Mar-26	18-Mar-26	4	10-Mar-26	18-Mar-26	0
51	2nd floor Shear walls South @ 15k/week	12	0%	16-Mar-26	31-Mar-26	2	16-Mar-26	31-Mar-26	0
47	CMU Walls to 25-4" South	12	0%	16-Mar-26	31-Mar-26	0	16-Mar-26	31-Mar-26	0
50	Rebar, Hangars & Deck Pour3 North	5	0%	19-Mar-26	25-Mar-26	4	19-Mar-26	25-Mar-26	0
52	3rd Floor Decking South@ 5k/day	7	0%	27-Mar-26	06-Apr-26	2	27-Mar-26	06-Apr-26	0
54	CMU Walls to 36' North	10	0%	01-Apr-26	14-Apr-26	0	01-Apr-26	14-Apr-26	0
56	3rd floor Shear walls North @ 15k/week	12	0%	01-Apr-26	16-Apr-26	1	01-Apr-26	16-Apr-26	0
53	Rebar, Hangars & Deck3 Pour South	5	0%	07-Apr-26	13-Apr-26	2	07-Apr-26	13-Apr-26	0
55	CMU Walls to 36' South	10	0%	15-Apr-26	28-Apr-26	1	15-Apr-26	28-Apr-26	0
57	4th Floor Decking North @ 5k/day	7	0%	15-Apr-26	23-Apr-26	0	15-Apr-26	23-Apr-26	0
59	3rd floor Shear walls South @ 15k/week	12	0%	15-Apr-26	30-Apr-26	1	15-Apr-26	30-Apr-26	0
58	Rebar, Hangars & Deck Pour4 North	5	0%	24-Apr-26	30-Apr-26	0	24-Apr-26	30-Apr-26	0
60	4th Floor Decking South@ 5k/day	7	0%	28-Apr-26	06-May-26	1	28-Apr-26	06-May-26	0
62	CMU Walls to 46'-8" North	10	0%	01-May-26	14-May-26	0	01-May-26	14-May-26	0
64	4th floor Shear walls North @ 15k/week	12	0%	01-May-26	18-May-26	0	01-May-26	18-May-26	0
61	Rebar, Hangars & Deck4 Pour South	5	0%	07-May-26	13-May-26	1	07-May-26	13-May-26	0
65	5th Floor Decking North @ 5k/day	7	0%	14-May-26	22-May-26	0	14-May-26	22-May-26	0
63	CMU Walls to 46'-8" South	10	0%	15-May-26	29-May-26	0	15-May-26	29-May-26	0
67	4th floor Shear walls South @ 15k/week	12	0%	15-May-26	02-Jun-26	0	15-May-26	02-Jun-26	0
66	Rebar, Hangars & Deck Pour5 North	5	0%	26-May-26	01-Jun-26	0	26-May-26	01-Jun-26	0
68	5th Floor Decking South@ 5k/day	7	0%	29-May-26	08-Jun-26	0	29-May-26	08-Jun-26	0
70	CMU Walls to 57'-4" North	10	0%	02-Jun-26	15-Jun-26	0	02-Jun-26	15-Jun-26	0
72	5th floor Shear walls North @ 15k/week	14	0%	02-Jun-26	19-Jun-26	0	02-Jun-26	19-Jun-26	0
69	Rebar, Hangars & Deck5 Pour South	7	0%	09-Jun-26	17-Jun-26	0	09-Jun-26	17-Jun-26	0
73	Roof Equipment Structural	3	0%	17-Jun-26	19-Jun-26	0	17-Jun-26	19-Jun-26	0
71	CMU Walls to 57'-4" South	10	0%	18-Jun-26	01-Jul-26	0	18-Jun-26	01-Jul-26	0
76	5th floor Shear walls South @ 15k/week	12	0%	18-Jun-26	06-Jul-26	0	18-Jun-26	06-Jul-26	0
74	Roof Decking North @ 5k/day	7	0%	22-Jun-26	30-Jun-26	0	22-Jun-26	30-Jun-26	0
75	Roof Drains, Screens & Curbs	10	0%	01-Jul-26	15-Jul-26	0	01-Jul-26	15-Jul-26	0
77	Roof Equipment Structural	3	0%	01-Jul-26	06-Jul-26	0	01-Jul-26	06-Jul-26	0

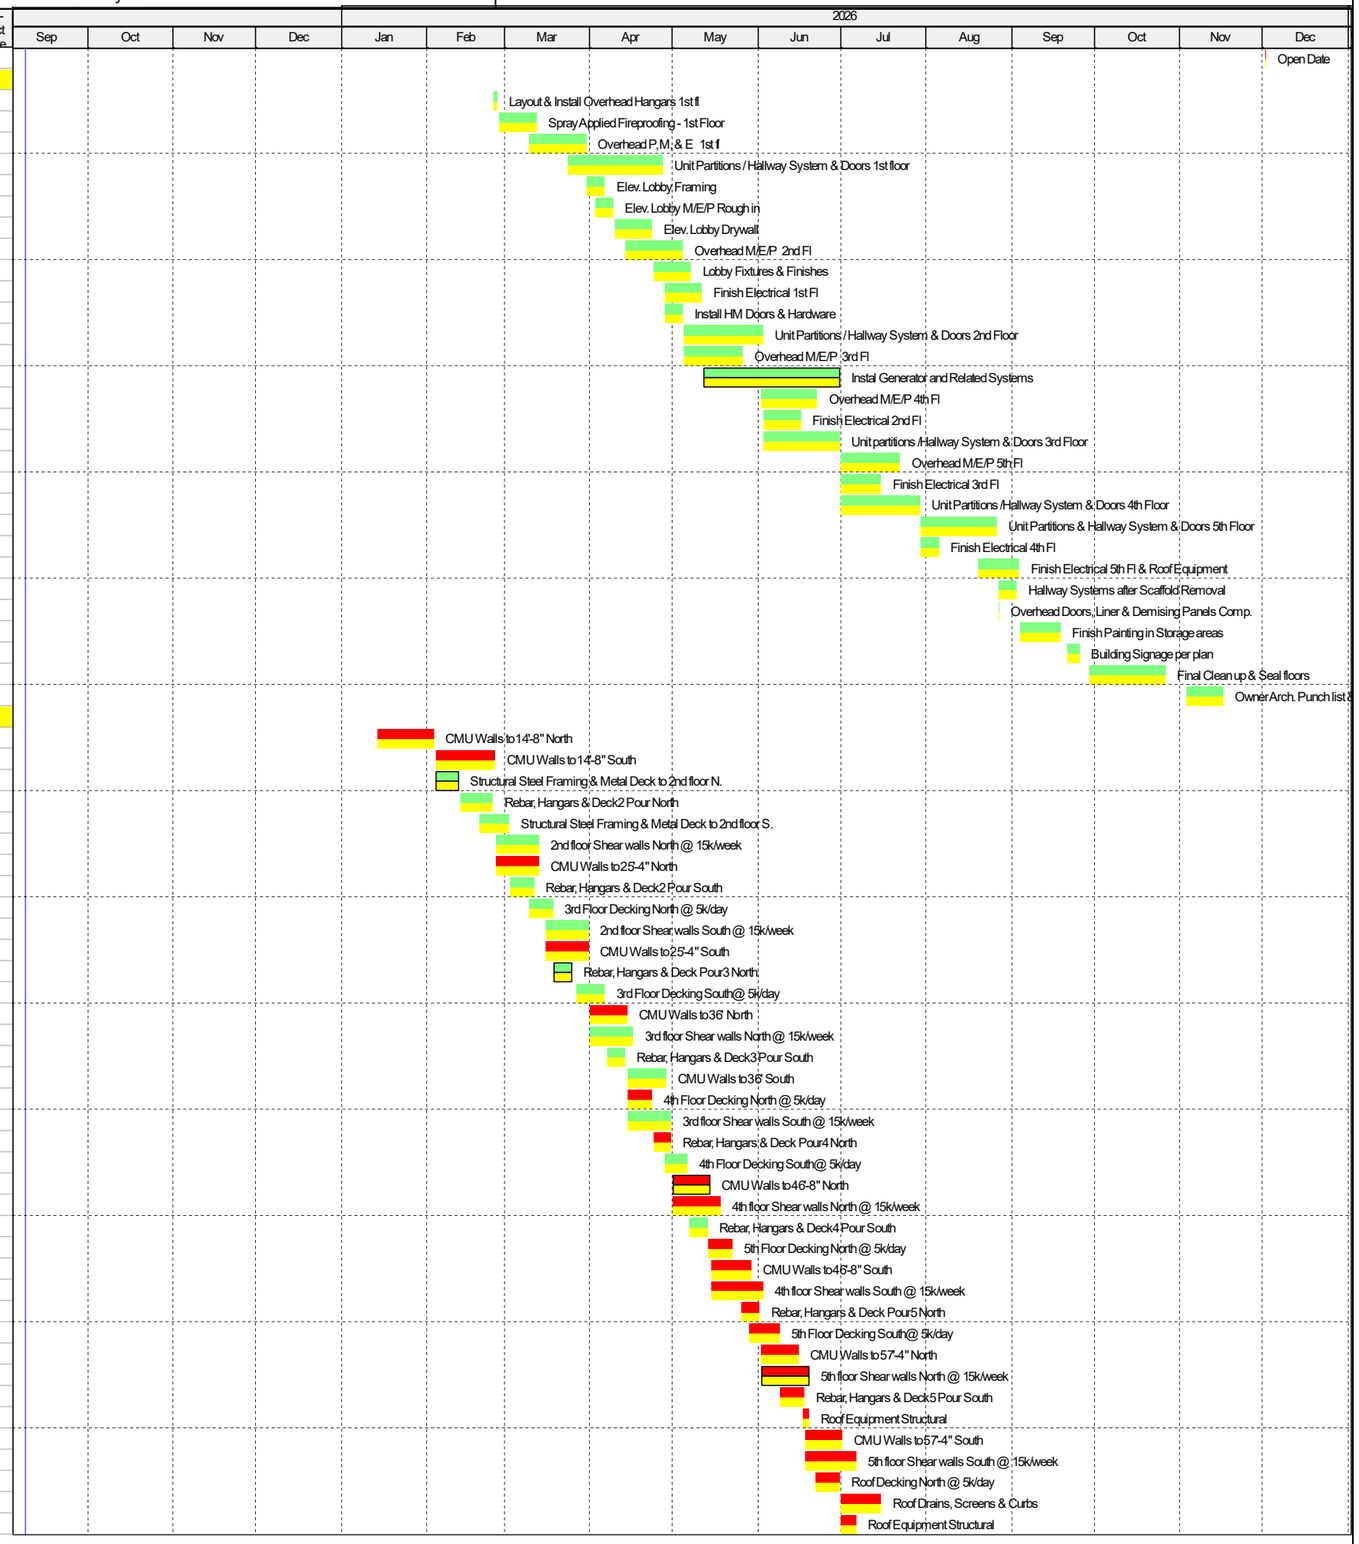

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	BL Project Start	BL Project Finish	Variance - BL Project Finish Date
78	Roof Decking South@ 5k/day	7	0%	07-Jul-26	15-Jul-26	0	07-Jul-26	15-Jul-26	0
79	Roof insulation Crickets & TPO	7	0%	16-Jul-26	24-Jul-26	0	16-Jul-26	24-Jul-26	0
81	Set rooftop Equipment & hook up	3	0%	27-Jul-26	29-Jul-26	34	27-Jul-26	29-Jul-26	0
82	Elevator Construction Car #1	20	0%	27-Jul-26	21-Aug-26	0	27-Jul-26	21-Aug-26	0
80	Building Temporarily Water Tight	0	0%	27-Jul-26	27-Jul-26	0	27-Jul-26	27-Jul-26	0
83	CMU infill @ Elevator Openings	10	0%	10-Aug-26	21-Aug-26	58	10-Aug-26	21-Aug-26	0
84	Elevator Construction Car #2	20	0%	24-Aug-26	21-Sep-26	0	24-Aug-26	21-Sep-26	0
85	CMU infill @ Elevator Openings	10	0%	08-Sep-26	21-Sep-26	38	08-Sep-26	21-Sep-26	0
86	Elevator Construction Car #3	20	0%	22-Sep-26	19-Oct-26	0	22-Sep-26	19-Oct-26	0
87	CMU infill @ Elevator Openings	10	0%	06-Oct-26	19-Oct-26	0	06-Oct-26	19-Oct-26	0
89	Remove Man Lift	2	0%	20-Oct-26	21-Oct-26	4	20-Oct-26	21-Oct-26	0
88	State Elevator inspection Lead Time & Approval	20	0%	20-Oct-26	16-Nov-26	0	20-Oct-26	16-Nov-26	0
90	Infill Framing @ Manlift Landings	7	0%	21-Oct-26	29-Oct-26	4	21-Oct-26	29-Oct-26	0
91	Sheathing Lift Leave OutArea	5	0%	28-Oct-26	03-Nov-26	4	28-Oct-26	03-Nov-26	0
92	Finishes @ Infilled Landings	5	0%	04-Nov-26	10-Nov-26	4	04-Nov-26	10-Nov-26	0

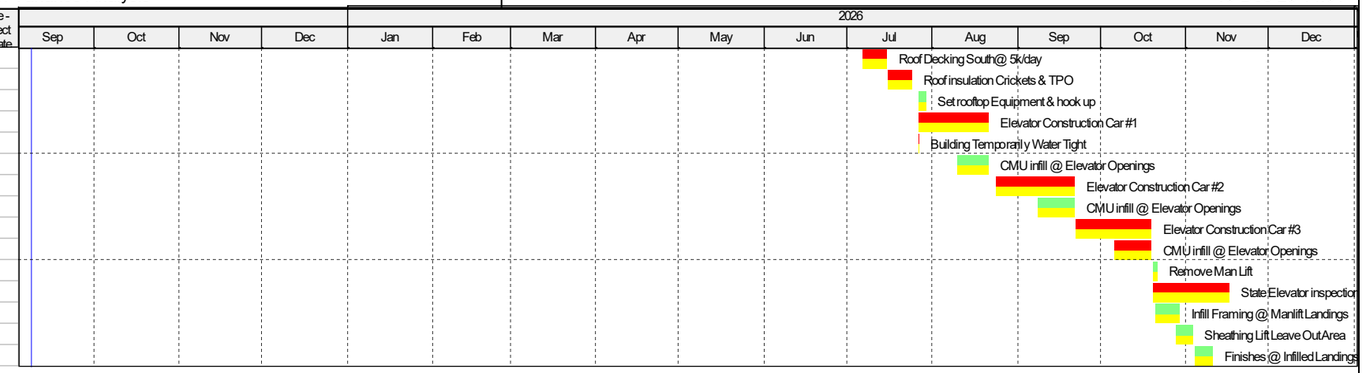

Project Baseline Bar | Remaining Work | Baseline Milestone
Actual Work | Critical Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation
