Public Storage Anaheim Contract Schedule Update

ID		Task Name	Duration	Start	Finish	Predecessors	Actual Finish
1		**Grading & Building Slab Construction**	**313 days**	**Mon 25/09/08**	**Fri 26/12/04**		**NA**
2	✓	Commencement Date 9/8/2025	1 day	Mon 25/09/08	Mon 25/09/08		Mon 25/09...
3	✓	HBI Mobilization	8 days	Tue 25/09/09	Thu 25/09/18	2	Thu 25/09/...
4	✓	Install Temp Fencing & BMP's	3 days	Fri 25/09/19	Tue 25/09/23	3	Tue 25/09/...
5	✓	Move Existing Rolling Gate	5 days	Mon 25/09/22	Fri 25/09/26	4FS-2 days	Fri 25/09/26
6	✓	Surface Demo Existing Phase II areas	16 days	Mon 25/09/29	Mon 25/10/20	5	Mon 25/10...
7	✓	AQMD Notification for Transite Fire Water	10 days	Thu 25/10/16	Wed 25/10/29		Wed 25/10...
8	✓	Identify & Cap Existing Utilities to Limits	3 days	Thu 25/10/16	Mon 25/10/20	6FS-3 days	Mon 25/10...
9	✓	Abate Fire Water Lines per Change Order #2	5 days	Thu 25/10/30	Wed 25/11/05	7	Wed 25/11...
10	✓	**Grading Permit Needed**	**0 days**	Mon 25/10/20	Mon 25/10/20	6	Mon 25/10...
11	✓	**Grading Permit Delay - Actual**	17 days	Tue 25/10/21	Wed 25/11/12	10	Wed 25/11...
12	✓	**Pre-Grade Meeting w/ City**	**1 day**	Thu 25/11/13	Thu 25/11/13	10;11	Thu 25/11/...
13	✓	**Rain and Mud Delay - Taken from item 147 below**	**6 days**	**Fri 25/11/14**	**Fri 25/11/21**	12	Fri 25/11/21
14	✓	O/X & Grading for Bldg pad	8 days	Mon 25/11/24	Fri 25/12/05	3;6;9;12;13	Fri 25/12/05
15		**Certify Pad / Pad Delivery Date**	2 days	Mon 25/12/08	Tue 25/12/09	14	NA
16		Building Permit required	0 days	Tue 25/12/09	Tue 25/12/09	15	NA
17		Install Fire line Modifications	7 days	Wed 25/12/10	Thu 25/12/18	8;9;16	NA
18		Underslab Electrical & Plumbing	6 days	Wed 25/12/10	Wed 25/12/17	15	NA
19		Building Foundations & Pre-lim CMU/Forms	10 days	Wed 25/12/10	Tue 25/12/23	18SS	NA
20		Elevator Pit Form & Pour	10 days	Wed 25/12/10	Tue 25/12/23	15	NA
21		Slab Base Material Import & Grading	5 days	Wed 25/12/24	Fri 26/01/02	19;20FS-3 days	NA
22		Slab Vapor Barrier & Reinforcing	10 days	Wed 25/12/31	Wed 26/01/14	21FS-2 days	NA
23		Slab on Grade Pour North	4 days	Fri 26/01/09	Wed 26/01/14	22FS-4 days;17	NA
24		Slab on Grade Pour South	4 days	Thu 26/01/15	Tue 26/01/20	22;23	NA
25		**Site Wet Utilities**	**21 days**	**Wed 25/12/10**	**Mon 26/01/12**		**NA**
26		Storm Drain Piping & Catch Basins from Phase 1 Stubs	6 days	Wed 25/12/10	Wed 25/12/17	15	NA
27		Extend Sewer Laterals to building	5 days	Thu 25/12/18	Wed 25/12/24	26	NA
28		Extend Fire / Domestic Water Service to Building	10 days	Mon 25/12/29	Mon 26/01/12	27	NA
29		**Domestic & Fire Water Services Completion**	0 days	Mon 26/01/12	Mon 26/01/12	28	NA
30		**Site Dry Utilities**	**8 days**	**Thu 25/12/18**	**Wed 25/12/31**		**NA**
31		Extend Power & Lov Voltage conduits to Bldg from Stul	5 days	Thu 25/12/18	Wed 25/12/24	26	NA
32		Install Generac & Site lighting Conduits	3 days	Mon 25/12/29	Wed 25/12/31	31	NA
33		**Onsite improvements For Early Base Pave**	**22 days**	**Tue 26/01/13**	**Wed 26/02/11**		**NA**
34		Grade for Curb & Gutter	4 days	Tue 26/01/13	Fri 26/01/16	29	NA
35		Install Irrigation Sleeves	1 day	Mon 26/01/19	Mon 26/01/19	34	NA
36		Place Curb & Gutter	4 days	Tue 26/01/20	Fri 26/01/23	34;35	NA
37		Grade & Pour Walks	5 days	Thu 26/01/22	Wed 26/01/28	36FS-2 days	NA
38		Agg Base Import & AC Base Paving	10 days	Thu 26/01/29	Wed 26/02/11	37	NA
39		**Vertical Building Construction**	**215 days**	**Thu 26/01/15**	**Wed 26/11/18**		**NA**
40		CMU Walls to 14'-8" North	15 days	Thu 26/01/15	Wed 26/02/04	23	NA
41		CMU Walls to 14'-8" South	15 days	Thu 26/02/05	Thu 26/02/26	24;40	NA
42		Structural Steel Framing & Metal Deck to 2nd floor N.	7 days	Thu 26/02/05	Fri 26/02/13	40	NA
43		Structural Steel Framing & Metal Deck to 2nd floor S.	7 days	Mon 26/02/23	Tue 26/03/03	42;41FS-4 days	NA
44		Rebar, Hangars & Deck2 Pour North	7 days	Tue 26/02/17	Wed 26/02/25	42	NA

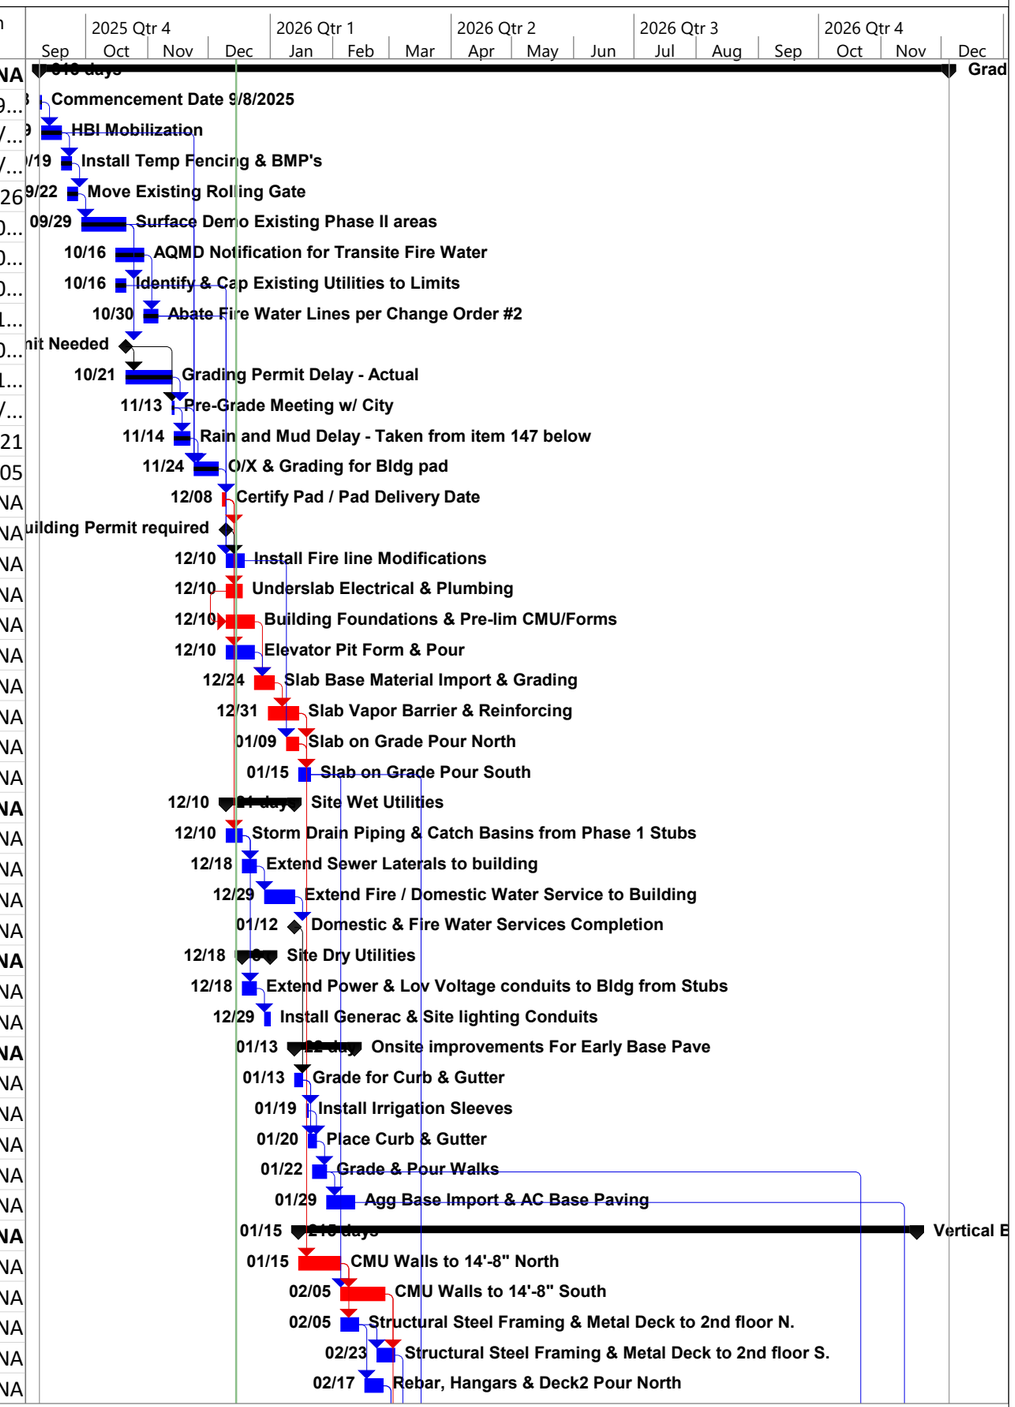

Public Storage Anaheim Contract Schedule Update

ID	Task Name	Duration	Start	Finish	Predecessors	Actual Finish
45	Rebar, Hangars & Deck2 Pour South	7 days	Wed 26/03/04	Thu 26/03/12	43	NA
46	CMU Walls to 25'-4" North	12 days	Fri 26/02/27	Mon 26/03/16	44;41	NA
47	CMU Walls to 25'-4" South	12 days	Tue 26/03/17	Wed 26/04/01	46;24;45	NA
48	2nd floor Shear walls North @ 15k/week	12 days	Fri 26/02/27	Mon 26/03/16	46SS	NA
49	3rd Floor Decking North @ 5k/day	7 days	Wed 26/03/11	Thu 26/03/19	48FS-4 days	NA
50	Rebar, Hangars & Deck Pour3 North	5 days	Fri 26/03/20	Thu 26/03/26	49	NA
51	2nd floor Shear walls South @ 15k/week	12 days	Tue 26/03/17	Wed 26/04/01	47SS	NA
52	3rd Floor Decking South@ 5k/day	7 days	Mon 26/03/30	Tue 26/04/07	51FS-3 days	NA
53	Rebar, Hangars & Deck3 Pour South	5 days	Wed 26/04/08	Tue 26/04/14	52	NA
54	CMU Walls to 36' North	10 days	Thu 26/04/02	Wed 26/04/15	50;47	NA
55	CMU Walls to 36' South	10 days	Thu 26/04/16	Wed 26/04/29	54;53	NA
56	3rd floor Shear walls North @ 15k/week	12 days	Thu 26/04/02	Fri 26/04/17	54SS	NA
57	4th Floor Decking North @ 5k/day	7 days	Thu 26/04/16	Fri 26/04/24	56FS-3 days;54	NA
58	Rebar, Hangars & Deck Pour4 North	5 days	Mon 26/04/27	Fri 26/05/01	57	NA
59	3rd floor Shear walls South @ 15k/week	12 days	Thu 26/04/16	Fri 26/05/01	55SS	NA
60	4th Floor Decking South@ 5k/day	7 days	Wed 26/04/29	Thu 26/05/07	59FS-3 days	NA
61	Rebar, Hangars & Deck4 Pour South	5 days	Fri 26/05/08	Thu 26/05/14	60	NA
62	CMU Walls to 46'-8" North	10 days	Mon 26/05/04	Fri 26/05/15	58;55	NA
63	CMU Walls to 46'-8" South	10 days	Mon 26/05/18	Mon 26/06/01	62;61	NA
64	4th floor Shear walls North @ 15k/week	12 days	Mon 26/05/04	Tue 26/05/19	62SS	NA
65	5th Floor Decking North @ 5k/day	7 days	Fri 26/05/15	Tue 26/05/26	64FS-3 days	NA
66	Rebar, Hangars & Deck Pour5 North	5 days	Wed 26/05/27	Tue 26/06/02	65	NA
67	4th floor Shear walls South @ 15k/week	12 days	Mon 26/05/18	Wed 26/06/03	63SS	NA
68	5th Floor Decking South@ 5k/day	7 days	Mon 26/06/01	Tue 26/06/09	67FS-3 days	NA
69	Rebar, Hangars & Deck5 Pour South	7 days	Wed 26/06/10	Thu 26/06/18	68	NA
70	CMU Walls to 57'-4" North	10 days	Wed 26/06/03	Tue 26/06/16	58;66;63	NA
71	CMU Walls to 57'-4" South	10 days	Fri 26/06/19	Thu 26/07/02	70;61;69	NA
72	5th floor Shear walls North @ 15k/week	14 days	Wed 26/06/03	Mon 26/06/22	70SS	NA
73	Roof Equipment Structural	3 days	Thu 26/06/18	Mon 26/06/22	72FF	NA
74	Roof Decking North @ 5k/day	7 days	Tue 26/06/23	Wed 26/07/01	72FS-3 days;73	NA
75	Roof Drains, Screens & Curbs	10 days	Thu 26/07/02	Fri 26/07/17	74	NA
76	5th floor Shear walls South @ 15k/week	12 days	Fri 26/06/19	Wed 26/07/08	71SS	NA
77	Roof Equipment Structural	3 days	Thu 26/07/02	Wed 26/07/08	76FF	NA
78	Roof Decking South@ 5k/day	7 days	Thu 26/07/09	Fri 26/07/17	76FS-3 days;77	NA
79	Roof insulation Crickets & TPO	7 days	Mon 26/07/20	Tue 26/07/28	78;75	NA
80	**Building Temporarily Water Tight**	0 days	Tue 26/07/28	Tue 26/07/28	79	NA
81	Set rooftop Equipment & hook up	3 days	Wed 26/07/29	Fri 26/07/31	79	NA
82	Elevator Construction Car #1	20 days	Wed 26/07/29	Tue 26/08/25	80	NA
83	CMU infill @ Elevator Openings	10 days	Wed 26/08/12	Tue 26/08/25	82FS-10 days	NA
84	Elevator Construction Car #2	20 days	Wed 26/08/26	Wed 26/09/23	82	NA
85	CMU infill @ Elevator Openings	10 days	Thu 26/09/10	Wed 26/09/23	84FS-10 days	NA
86	Elevator Construction Car #3	20 days	Thu 26/09/24	Wed 26/10/21	84	NA
87	CMU infill @ Elevator Openings	10 days	Thu 26/10/08	Wed 26/10/21	86FS-10 days	NA
88	State Elevator inspection Lead Time & Approval	20 days	Thu 26/10/22	Wed 26/11/18	87	NA

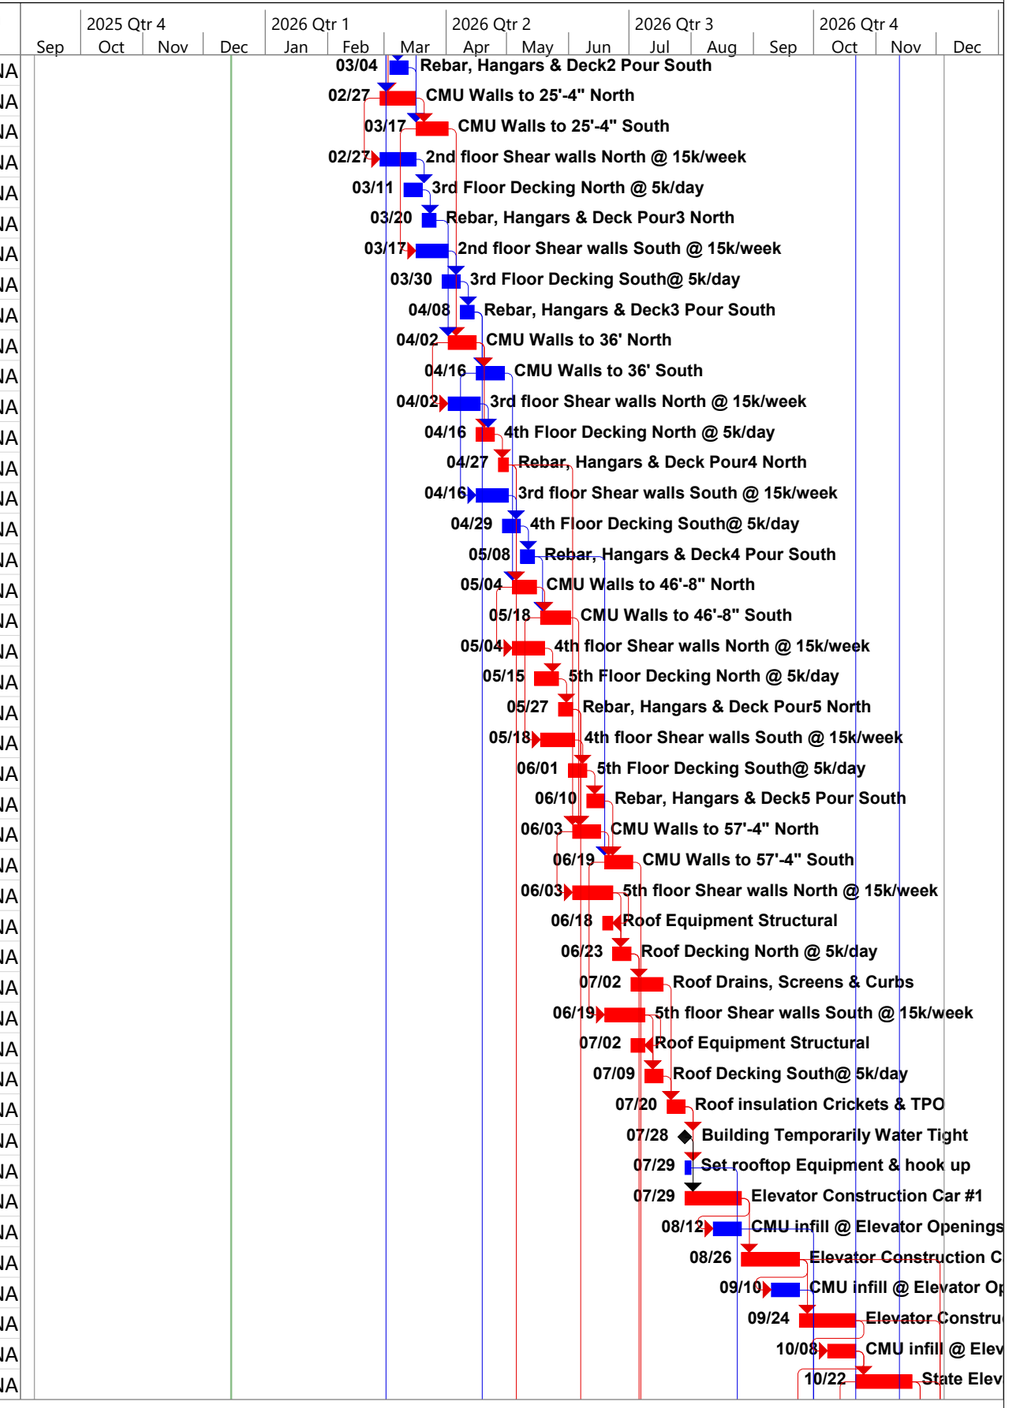

Public Storage Anaheim Contract Schedule Update

ID	Task Name	Duration	Start	Finish	Predecessors	Actual Finish
89	Remove Man Lift	2 days	Thu 26/10/22	Fri 26/10/23	88SS	NA
90	Infill Framing @ Manlift Landings	7 days	Fri 26/10/23	Mon 26/11/02	89FS-1 day	NA
91	Sheathing Lift Leave Out Area	5 days	Fri 26/10/30	Thu 26/11/05	90FS-2 days	NA
92	Finishes @ Infilled Landings	5 days	Fri 26/11/06	Thu 26/11/12	91	NA
93	**Building Interior**	**186 days**	**Thu 26/02/26**	**Wed 26/11/18**		**NA**
94	Layout & Install Overhead Hangars 1st fl	2 days	Thu 26/02/26	Fri 26/02/27	44	NA
95	Spray Applied Fireproofing - 1st Floor	10 days	Mon 26/03/02	Fri 26/03/13	94	NA
96	Overhead P, M, & E 1st fl	15 days	Wed 26/03/11	Tue 26/03/31	94;95FS-3 days	NA
97	Unit Partitions / Hallway System & Doors 1st floor	25 days	Wed 26/03/25	Tue 26/04/28	95;96FS-5 days	NA
98	Finish Electrical 1st Fl	10 days	Wed 26/04/29	Tue 26/05/12	97;96	NA
99	Instal Generator and Related Systems	35 days	Wed 26/05/13	Wed 26/07/01	98	NA
100	Overhead M/E/P 2nd Fl	15 days	Wed 26/04/15	Tue 26/05/05	96;53	NA
101	Unit Partitions / Hallway System & Doors 2nd Floor	20 days	Wed 26/05/06	Wed 26/06/03	97;100	NA
102	Finish Electrical 2nd Fl	10 days	Thu 26/06/04	Wed 26/06/17	101;100;98	NA
103	Overhead M/E/P 3rd Fl	15 days	Wed 26/05/06	Wed 26/05/27	58;100	NA
104	Unit partitions /Hallway System & Doors 3rd Floor	20 days	Thu 26/06/04	Wed 26/07/01	101	NA
105	Finish Electrical 3rd Fl	10 days	Thu 26/07/02	Fri 26/07/17	104;103;102	NA
106	Overhead M/E/P 4th Fl	15 days	Wed 26/06/03	Tue 26/06/23	66;103	NA
107	Unit Partitions /Hallway System & Doors 4th Floor	20 days	Thu 26/07/02	Fri 26/07/31	104	NA
108	Finish Electrical 4th Fl	5 days	Mon 26/08/03	Fri 26/08/07	107;106;105	NA
109	Overhead M/E/P 5th Fl	15 days	Thu 26/07/02	Fri 26/07/24	74;106	NA
110	Unit Partitions & Hallway System & Doors 5th Floor	20 days	Mon 26/08/03	Fri 26/08/28	109;107	NA
111	Hallway Systems after Scaffold Removal	5 days	Mon 26/08/31	Fri 26/09/04	110	NA
112	Finish Electrical 5th Fl & Roof Equipment	11 days	Mon 26/08/24	Tue 26/09/08	110FS-5 days;81;1(	NA
113	**Overhead Doors, Liner & Demising Panels Comp.**	0 days	Fri 26/08/28	Fri 26/08/28	110	NA
114	Elev. Lobby Framing	5 days	Wed 26/04/01	Tue 26/04/07	96	NA
115	Elev. Lobby M/E/P Rough in	5 days	Mon 26/04/06	Fri 26/04/10	114FS-2 days	NA
116	Elev. Lobby Drywall	10 days	Mon 26/04/13	Fri 26/04/24	115	NA
117	Install HM Doors & Hardware	5 days	Wed 26/04/29	Tue 26/05/05	116;97	NA
118	Lobby Fixtures & Finishes	10 days	Mon 26/04/27	Fri 26/05/08	116	NA
119	Finish Painting in Storage areas	10 days	Wed 26/09/09	Tue 26/09/22	112;117	NA
120	Building Signage per plan	5 days	Wed 26/09/23	Tue 26/09/29	119	NA
121	Final Clean up & Seal floors	20 days	Thu 26/10/01	Wed 26/10/28	119;120;87FS-15 d	NA
122	Owner Arch. Punch list & Completion	10 days	Thu 26/11/05	Wed 26/11/18	121FS-5 days;141	NA
123	**Building Exterior**	**76 days**	**Tue 26/07/07**	**Wed 26/10/21**		**NA**
124	Install Scaffolding at Building Perimeter	3 days	Tue 26/07/07	Thu 26/07/09	71	NA
125	Exterior Metal Frame Sheathing & WRB @ Tower	10 days	Fri 26/07/10	Thu 26/07/23	124	NA
126	Metal Panel Siding @ Tower	5 days	Fri 26/07/24	Thu 26/07/30	125	NA
127	Storefront/Curtainwall	5 days	Fri 26/07/31	Thu 26/08/06	126	NA
128	Glass Lead Time	10 days	Fri 26/08/07	Thu 26/08/20	127	NA
129	Install Glass	5 days	Fri 26/08/21	Thu 26/08/27	128	NA
130	Install Auto Sliders & Mapes Canopy	10 days	Thu 26/10/08	Wed 26/10/21	127;137;129	NA
131	**EIFS WRB, Foam/Brown & Finish**	**50 days**	**Fri 26/07/10**	**Fri 26/09/18**	**124**	**NA**
132	Waterproof Membrane	10 days	Fri 26/07/10	Thu 26/07/23	124	NA

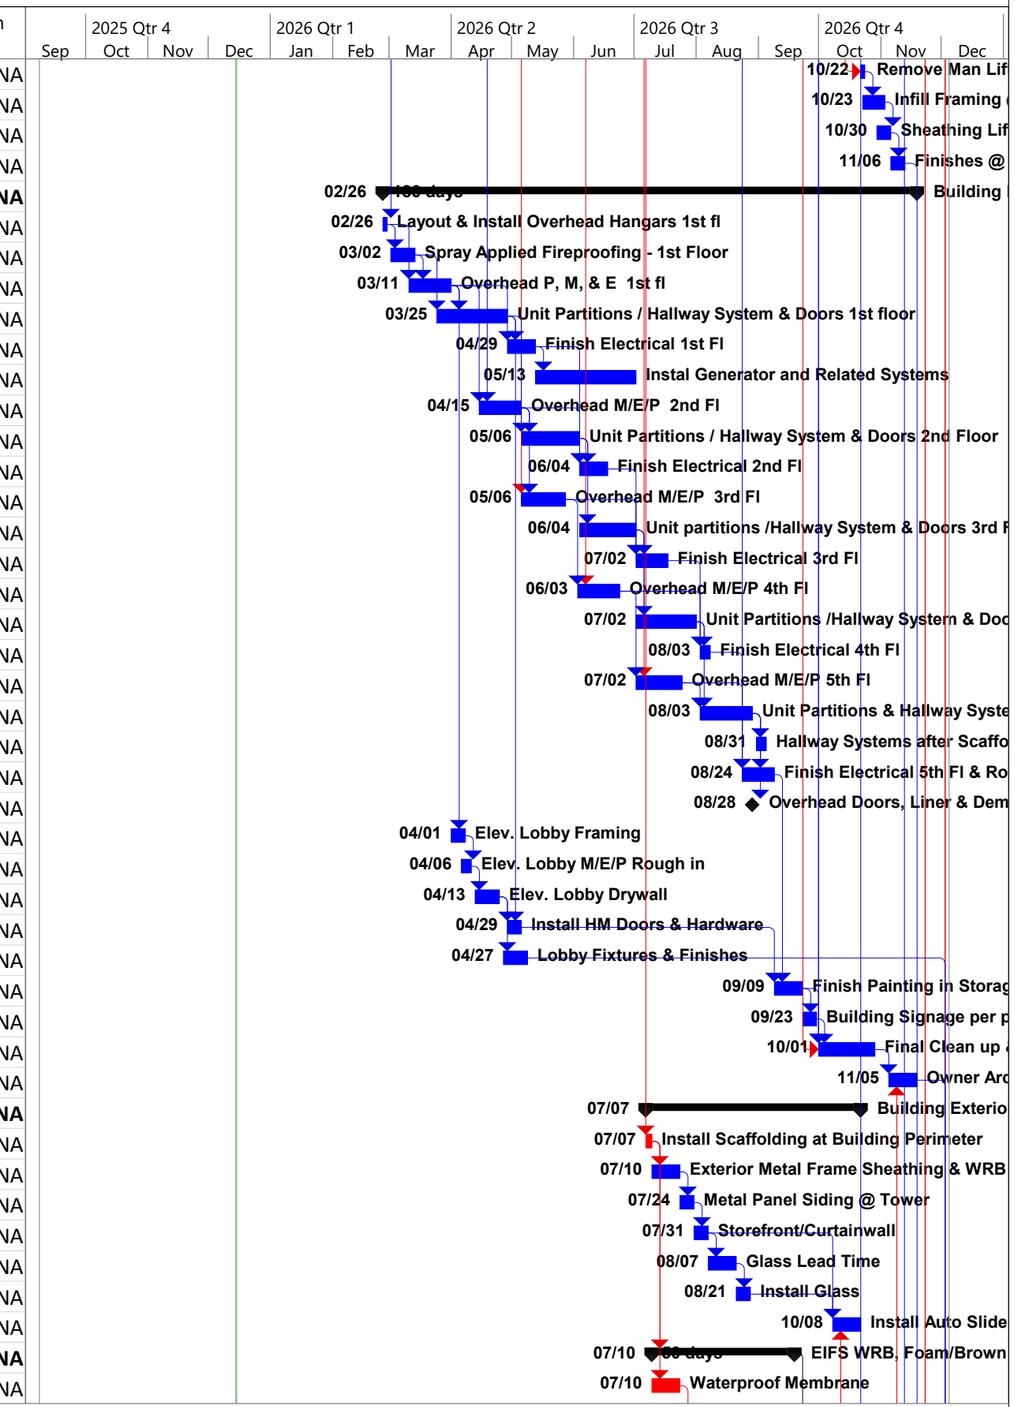

Public Storage Anaheim Contract Schedule Update
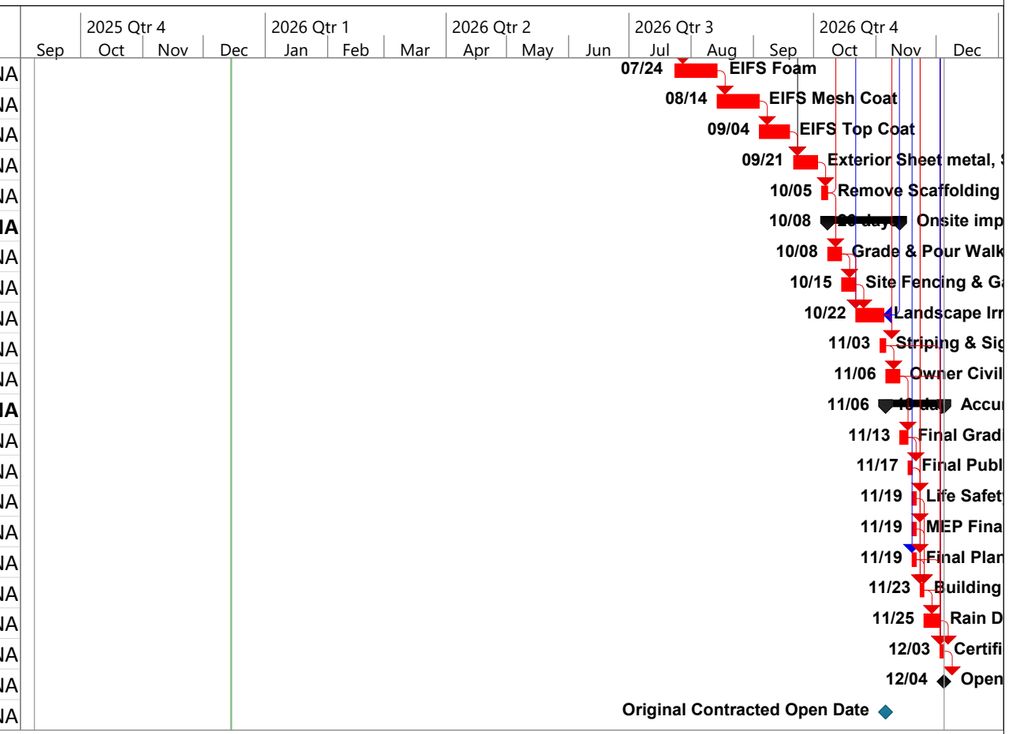
ID		Task Name	Duration	Start	Finish	Predecessors	Actual Finish
133		EIFS Foam	15 days	Fri 26/07/24	Thu 26/08/13	132	NA
134		EIFS Mesh Coat	15 days	Fri 26/08/14	Thu 26/09/03	133	NA
135		EIFS Top Coat	10 days	Fri 26/09/04	Fri 26/09/18	134	NA
136		Exterior Sheet metal, Sealants, & Painting	10 days	Mon 26/09/21	Fri 26/10/02	131;135	NA
137		Remove Scaffolding	3 days	Mon 26/10/05	Wed 26/10/07	136	NA
138		**Onsite improvements**	**26 days**	**Thu 26/10/08**	**Thu 26/11/12**		**NA**
139		Grade & Pour Walks	5 days	Thu 26/10/08	Wed 26/10/14	137	NA
140		Site Fencing & Gates	5 days	Thu 26/10/15	Wed 26/10/21	139	NA
141		Landscape Irrigation and Planting	10 days	Thu 26/10/22	Wed 26/11/04	139;37;38FF;140	NA
142		Striping & Signage	3 days	Tue 26/11/03	Thu 26/11/05	141FS-2 days	NA
143		Owner Civil Punch list & Completion	5 days	Fri 26/11/06	Thu 26/11/12	142	NA
144		**Accumulative Inspections & C of O**	**19 days**	**Fri 26/11/06**	**Fri 26/12/04**		**NA**
145		Final Grading Inspections	2 days	Fri 26/11/13	Mon 26/11/16	143	NA
146		Final Public Works Inspections	2 days	Tue 26/11/17	Wed 26/11/18	145	NA
147		Life Safety Inspection	2 days	Thu 26/11/19	Fri 26/11/20	88	NA
148		MEP Final Inspections	2 days	Thu 26/11/19	Fri 26/11/20	88	NA
149		Final Planning & Zoning Inspection	2 days	Thu 26/11/19	Fri 26/11/20	92;146	NA
150		Building Final Inspection	2 days	Mon 26/11/23	Tue 26/11/24	147;148;145;146;1	NA
151		Rain Days Included	4 days	Wed 26/11/25	Wed 26/12/02	150	NA
152		Certificate Of Occupancy	2 days	Thu 26/12/03	Fri 26/12/04	**142;118;84;88;150**	NA
153		**Open Date**	0 days	Fri 26/12/04	Fri 26/12/04	152	NA
154		Original Contracted Open Date	0 days	Fri 26/11/06	Fri 26/11/06		NA
