	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Grading & Building Slab Construction**	**336 days**	**313 days**	**23d**	**Mon 25/09/08**	**Mon 25/09/08**	**0d**	**Mon 27/01/11**	**Fri 26/12/04**	**26d**
2	Commencement Date 9/8/2025	1 day	1 day	0d	Mon 25/09/08	Mon 25/09/08	0d	Mon 25/09/08	Mon 25/09/08	0d
3	HBI Mobilization	8 days	8 days	0d	Tue 25/09/09	Tue 25/09/09	0d	Thu 25/09/18	Thu 25/09/18	0d
4	Install Temp Fencing & BMP's	3 days	3 days	0d	Fri 25/09/19	Fri 25/09/19	0d	Tue 25/09/23	Tue 25/09/23	0d
5	Move Existing Rolling Gate	5 days	5 days	0d	Mon 25/09/22	Mon 25/09/22	0d	Fri 25/09/26	Fri 25/09/26	0d
6	Surface Demo Existing Phase II areas	16 days	16 days	0d	Mon 25/09/29	Mon 25/09/29	0d	Mon 25/10/20	Mon 25/10/20	0d
7	AQMD Notification for Transite Fire Water	10 days	10 days	0d	Thu 25/10/16	Thu 25/10/16	0d	Wed 25/10/29	Wed 25/10/29	0d
8	Identify & Cap Existing Utilities to Limits	3 days	3 days	0d	Thu 25/10/16	Thu 25/10/16	0d	Mon 25/10/20	Mon 25/10/20	0d
9	Abate Fire Water Lines per Change Order #2	5 days	5 days	0d	Thu 25/10/30	Thu 25/10/30	0d	Wed 25/11/05	Wed 25/11/05	0d
10	Grading Permit Needed	0 days	0 days	0d	Mon 25/10/20	Mon 25/10/20	0d	Mon 25/10/20	Mon 25/10/20	0d
11	Grading Permit Delay - Actual	17 days	17 days	0d	Tue 25/10/21	Tue 25/10/21	0d	Wed 25/11/12	Wed 25/11/12	0d
12	Pre-Grade Meeting w/ City	1 day	1 day	0d	Thu 25/11/13	Thu 25/11/13	0d	Thu 25/11/13	Thu 25/11/13	0d
13	Rain and Mud Delay - Taken from item 147 below	6 days	6 days	0d	Fri 25/11/14	Fri 25/11/14	0d	Fri 25/11/21	Fri 25/11/21	0d
14	O/X & Grading for Bldg pad	8 days	8 days	0d	Mon 25/11/24	Mon 25/11/24	0d	Fri 25/12/05	Fri 25/12/05	0d
15	Certify Pad / Pad Delivery Date	2 days	2 days	0d	Mon 25/12/08	Mon 25/12/08	0d	Tue 25/12/09	Tue 25/12/09	0d
16	Building Permit required	0 days	0 days	0d	Tue 25/12/09	Tue 25/12/09	0d	Tue 25/12/09	Tue 25/12/09	0d
17	Building Permit Delay	13 days			Wed 25/12/10			Tue 25/12/30		
18	Building Permit Received 12.30.25	0 days			Tue 25/12/30			Tue 25/12/30		
19	Rain Delay 1/2-1.9/9 Inc. Pad Dry Out - Part from task 147	6 days			Fri 26/01/02			Fri 26/01/09		
20	Install Fire line Modifications	7 days	7 days	0d	Mon 26/01/12	Wed 25/12/10	23d	Tue 26/01/20	Thu 25/12/18	23d
21	Underslab Electrical & Plumbing	6 days	6 days	0d	Mon 26/01/12	Wed 25/12/10	23d	Mon 26/01/19	Wed 25/12/17	23d
22	Building Foundations & Pre-lim CMU/Forms	10 days	10 days	0d	Mon 26/01/12	Wed 25/12/10	23d	Fri 26/01/23	Tue 25/12/23	23d
23	Elevator Pit Form & Pour	10 days	10 days	0d	Mon 26/01/26	Wed 25/12/10	33d	Fri 26/02/06	Tue 25/12/23	33d
24	Slab Base Material Import & Grading	5 days	5 days	0d	Wed 26/02/04	Wed 25/12/24	30d	Tue 26/02/10	Fri 26/01/02	27d
25	Slab Vapor Barrier & Reinforcing	10 days	10 days	0d	Mon 26/02/09	Wed 25/12/31	28d	Mon 26/02/23	Wed 26/01/14	28d
26	Slab on Grade Pour North	4 days	4 days	0d	Wed 26/02/18	Fri 26/01/09	28d	Mon 26/02/23	Wed 26/01/14	28d
27	Slab on Grade Pour South	4 days	4 days	0d	Tue 26/02/24	Thu 26/01/15	28d	Fri 26/02/27	Tue 26/01/20	28d
28	**Site Wet Utilities**	**21 days**	**21 days**	**0d**	**Wed 26/01/21**	**Wed 25/12/10**	**30d**	**Thu 26/02/19**	**Mon 26/01/12**	**28d**
29	Storm Drain Piping & Catch Basins from Phase 1 Stubs	6 days	6 days	0d	Wed 26/01/21	Wed 25/12/10	30d	Wed 26/01/28	Wed 25/12/17	30d
30	Extend Sewer Laterals to building	5 days	5 days	0d	Thu 26/01/29	Thu 25/12/18	30d	Wed 26/02/04	Wed 25/12/24	30d
31	Extend Fire / Domestic Water Service to Building	10 days	10 days	0d	Thu 26/02/05	Mon 25/12/29	28d	Thu 26/02/19	Mon 26/01/12	28d
32	Domestic & Fire Water Services Completion	0 days	0 days	0d	Thu 26/02/19	Mon 26/01/12	28d	Thu 26/02/19	Mon 26/01/12	28d
33	**Site Dry Utilities**	**8 days**	**8 days**	**0d**	**Thu 26/01/29**	**Thu 25/12/18**	**30d**	**Mon 26/02/09**	**Wed 25/12/31**	**28d**
34	Extend Power & Lov Voltage conduits to Bldg from Stubs	5 days	5 days	0d	Thu 26/01/29	Thu 25/12/18	30d	Wed 26/02/04	Wed 25/12/24	30d
35	Install Generac & Site lighting Conduits	3 days	3 days	0d	Thu 26/02/05	Mon 25/12/29	28d	Mon 26/02/09	Wed 25/12/31	28d
36	**Onsite improvements For Early Base Pave**	**22 days**	**22 days**	**0d**	**Fri 26/02/20**	**Tue 26/01/13**	**28d**	**Mon 26/03/23**	**Wed 26/02/11**	**28d**
37	Grade for Curb & Gutter	4 days	4 days	0d	Fri 26/02/20	Tue 26/01/13	28d	Wed 26/02/25	Fri 26/01/16	28d
38	Install Irrigation Sleeves	1 day	1 day	0d	Thu 26/02/26	Mon 26/01/19	28d	Thu 26/02/26	Mon 26/01/19	28d
39	Place Curb & Gutter	4 days	4 days	0d	Fri 26/02/27	Tue 26/01/20	28d	Wed 26/03/04	Fri 26/01/23	28d
40	Grade & Pour Walks	5 days	5 days	0d	Tue 26/03/03	Thu 26/01/22	28d	Mon 26/03/09	Wed 26/01/28	28d
41	Agg Base Import & AC Base Paving	10 days	10 days	0d	Tue 26/03/10	Thu 26/01/29	28d	Mon 26/03/23	Wed 26/02/11	28d
42	**Vertical Building Construction**	**215 days**	**215 days**	**0d**	**Tue 26/02/24**	**Thu 26/01/15**	**28d**	**Thu 26/12/31**	**Wed 26/11/18**	**31d**
43	CMU Walls to 14'-8" North	15 days	15 days	0d	Tue 26/02/24	Thu 26/01/15	28d	Mon 26/03/16	Wed 26/02/04	28d
44	CMU Walls to 14'-8" South	15 days	15 days	0d	Tue 26/03/17	Thu 26/02/05	28d	Mon 26/04/06	Thu 26/02/26	27d
45	Structural Steel Framing & Metal Deck to 2nd floor N.	7 days	7 days	0d	Tue 26/03/17	Thu 26/02/05	28d	Wed 26/03/25	Fri 26/02/13	28d
46	Structural Steel Framing & Metal Deck to 2nd floor S.	7 days	7 days	0d	Wed 26/04/01	Mon 26/02/23	27d	Thu 26/04/09	Tue 26/03/03	27d
47	Rebar, Hangars & Deck2 Pour North	7 days	7 days	0d	Thu 26/03/26	Tue 26/02/17	27d	Fri 26/04/03	Wed 26/02/25	27d
48	Rebar, Hangars & Deck2 Pour South	7 days	7 days	0d	Fri 26/04/10	Wed 26/03/04	27d	Mon 26/04/20	Thu 26/03/12	27d
49	CMU Walls to 25'-4" North	12 days	12 days	0d	Tue 26/04/07	Fri 26/02/27	27d	Wed 26/04/22	Mon 26/03/16	27d
50	CMU Walls to 25'-4" South	12 days	12 days	0d	Thu 26/04/23	Tue 26/03/17	27d	Fri 26/05/08	Wed 26/04/01	27d
51	2nd floor Shear walls North @ 15k/week	12 days	12 days	0d	Tue 26/04/07	Fri 26/02/27	27d	Wed 26/04/22	Mon 26/03/16	27d
52	3rd Floor Decking North @ 5k/day	7 days	7 days	0d	Fri 26/04/17	Wed 26/03/11	27d	Mon 26/04/27	Thu 26/03/19	27d
53	Rebar, Hangars & Deck Pour3 North	5 days	5 days	0d	Tue 26/04/28	Fri 26/03/20	27d	Mon 26/05/04	Thu 26/03/26	27d

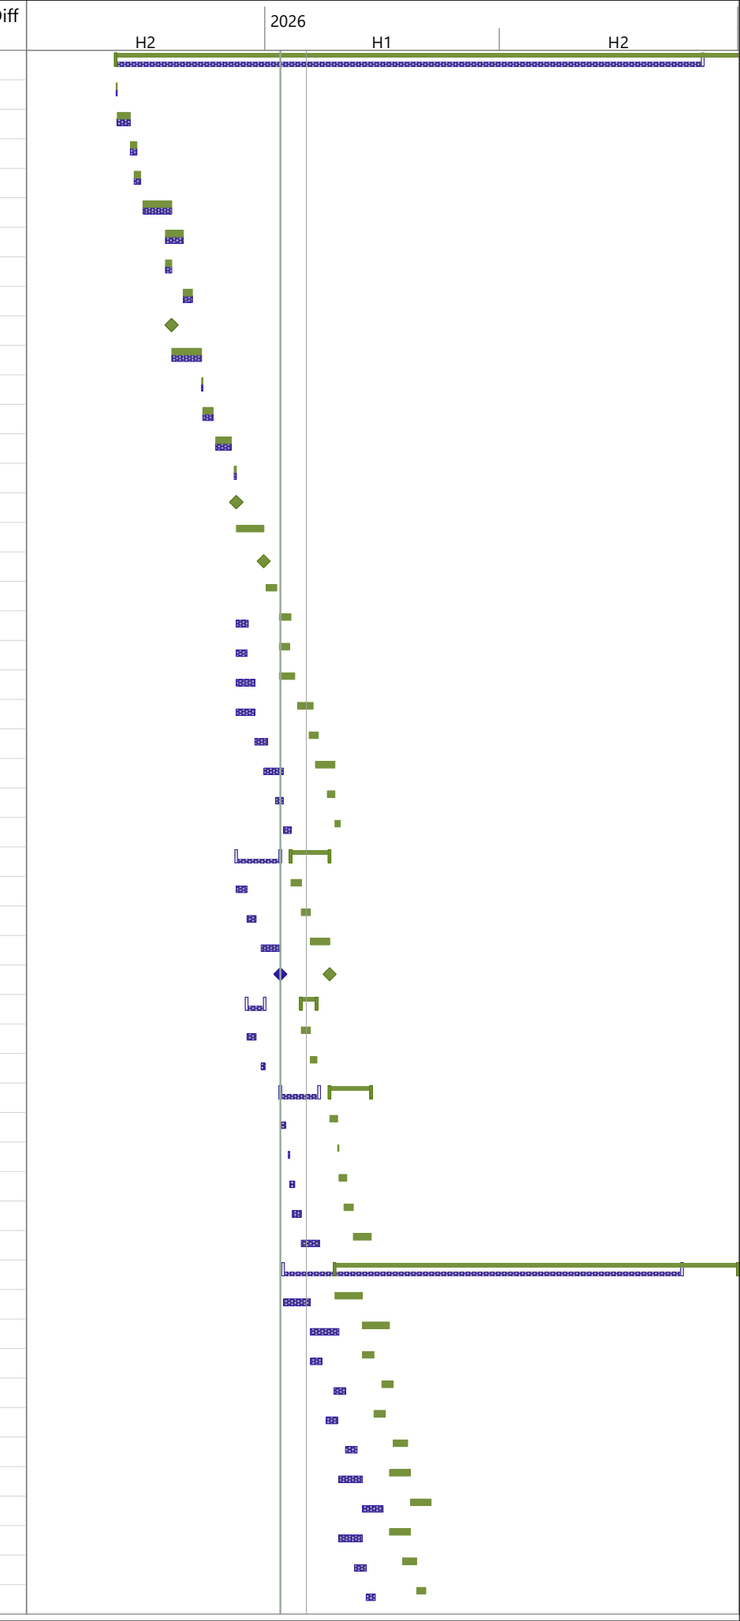

	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
54	2nd floor Shear walls South @ 15k/week	12 days	12 days	0d	Thu 26/04/23	Tue 26/03/17	27d	Fri 26/05/08	Wed 26/04/01	27d
55	3rd Floor Decking South@ 5k/day	7 days	7 days	0d	Wed 26/05/06	Mon 26/03/30	27d	Thu 26/05/14	Tue 26/04/07	27d
56	Rebar, Hangars & Deck3 Pour South	5 days	5 days	0d	Fri 26/05/15	Wed 26/04/08	27d	Thu 26/05/21	Tue 26/04/14	27d
57	CMU Walls to 36' North	10 days	10 days	0d	Mon 26/05/11	Thu 26/04/02	27d	Fri 26/05/22	Wed 26/04/15	27d
58	CMU Walls to 36' South	10 days	10 days	0d	Tue 26/05/26	Thu 26/04/16	28d	Mon 26/06/08	Wed 26/04/29	28d
59	3rd floor Shear walls North @ 15k/week	12 days	12 days	0d	Mon 26/05/11	Thu 26/04/02	27d	Wed 26/05/27	Fri 26/04/17	28d
60	4th Floor Decking North @ 5k/day	7 days	7 days	0d	Tue 26/05/26	Thu 26/04/16	28d	Wed 26/06/03	Fri 26/04/24	28d
61	Rebar, Hangars & Deck Pour4 North	5 days	5 days	0d	Thu 26/06/04	Mon 26/04/27	28d	Wed 26/06/10	Fri 26/05/01	28d
62	3rd floor Shear walls South @ 15k/week	12 days	12 days	0d	Tue 26/05/26	Thu 26/04/16	28d	Wed 26/06/10	Fri 26/05/01	28d
63	4th Floor Decking South@ 5k/day	7 days	7 days	0d	Mon 26/06/08	Wed 26/04/29	28d	Tue 26/06/16	Thu 26/05/07	28d
64	Rebar, Hangars & Deck4 Pour South	5 days	5 days	0d	Wed 26/06/17	Fri 26/05/08	28d	Tue 26/06/23	Thu 26/05/14	28d
65	CMU Walls to 46'-8" North	10 days	10 days	0d	Thu 26/06/11	Mon 26/05/04	28d	Wed 26/06/24	Fri 26/05/15	28d
66	CMU Walls to 46'-8" South	10 days	10 days	0d	Thu 26/06/25	Mon 26/05/18	28d	Fri 26/07/10	Mon 26/06/01	29d
67	4th floor Shear walls North @ 15k/week	12 days	12 days	0d	Thu 26/06/11	Mon 26/05/04	28d	Fri 26/06/26	Tue 26/05/19	28d
68	5th Floor Decking North @ 5k/day	7 days	7 days	0d	Wed 26/06/24	Fri 26/05/15	28d	Thu 26/07/02	Tue 26/05/26	27d
69	Rebar, Hangars & Deck Pour5 North	5 days	5 days	0d	Tue 26/07/07	Wed 26/05/27	29d	Mon 26/07/13	Tue 26/06/02	29d
70	4th floor Shear walls South @ 15k/week	12 days	12 days	0d	Thu 26/06/25	Mon 26/05/18	28d	Tue 26/07/14	Wed 26/06/03	29d
71	5th Floor Decking South@ 5k/day	7 days	7 days	0d	Fri 26/07/10	Mon 26/06/01	29d	Mon 26/07/20	Tue 26/06/09	29d
72	Rebar, Hangars & Deck5 Pour South	7 days	7 days	0d	Tue 26/07/21	Wed 26/06/10	29d	Wed 26/07/29	Thu 26/06/18	29d
73	CMU Walls to 57'-4" North	10 days	10 days	0d	Tue 26/07/14	Wed 26/06/03	29d	Mon 26/07/27	Tue 26/06/16	29d
74	CMU Walls to 57'-4" South	10 days	10 days	0d	Thu 26/07/30	Fri 26/06/19	29d	Wed 26/08/12	Thu 26/07/02	29d
75	5th floor Shear walls North @ 15k/week	14 days	14 days	0d	Tue 26/07/14	Wed 26/06/03	29d	Fri 26/07/31	Mon 26/06/22	29d
76	Roof Equipment Structural	3 days	3 days	0d	Wed 26/07/29	Thu 26/06/18	29d	Fri 26/07/31	Mon 26/06/22	29d
77	Roof Decking North @ 5k/day	7 days	7 days	0d	Mon 26/08/03	Tue 26/06/23	29d	Tue 26/08/11	Wed 26/07/01	29d
78	Roof Drains, Screens & Curbs	10 days	10 days	0d	Wed 26/08/12	Thu 26/07/02	29d	Tue 26/08/25	Fri 26/07/17	27d
79	5th floor Shear walls South @ 15k/week	12 days	12 days	0d	Thu 26/07/30	Fri 26/06/19	29d	Fri 26/08/14	Wed 26/07/08	27d
80	Roof Equipment Structural	3 days	3 days	0d	Wed 26/08/12	Thu 26/07/02	29d	Fri 26/08/14	Wed 26/07/08	27d
81	Roof Decking South@ 5k/day	7 days	7 days	0d	Mon 26/08/17	Thu 26/07/09	27d	Tue 26/08/25	Fri 26/07/17	27d
82	Roof insulation Crickets & TPO	7 days	7 days	0d	Wed 26/08/26	Mon 26/07/20	27d	Thu 26/09/03	Tue 26/07/28	27d
83	Building Temporarily Water Tight	0 days	0 days	0d	Thu 26/09/03	Tue 26/07/28	27d	Thu 26/09/03	Tue 26/07/28	27d
84	Set rooftop Equipment & hook up	3 days	3 days	0d	Fri 26/09/04	Wed 26/07/29	27d	Wed 26/09/09	Fri 26/07/31	28d
85	Elevator Construction Car #1	20 days	20 days	0d	Fri 26/09/04	Wed 26/07/29	27d	Fri 26/10/02	Tue 26/08/25	28d
86	CMU infill @ Elevator Openings	10 days	10 days	0d	Mon 26/09/21	Wed 26/08/12	28d	Fri 26/10/02	Tue 26/08/25	28d
87	Elevator Construction Car #2	20 days	20 days	0d	Mon 26/10/05	Wed 26/08/26	28d	Fri 26/10/30	Wed 26/09/23	27d
88	CMU infill @ Elevator Openings	10 days	10 days	0d	Mon 26/10/19	Thu 26/09/10	27d	Fri 26/10/30	Wed 26/09/23	27d
89	Elevator Construction Car #3	20 days	20 days	0d	Mon 26/11/02	Thu 26/09/24	27d	Tue 26/12/01	Wed 26/10/21	29d
90	CMU infill @ Elevator Openings	10 days	10 days	0d	Mon 26/11/16	Thu 26/10/08	27d	Tue 26/12/01	Wed 26/10/21	29d
91	State Elevator inspection Lead Time & Approval	20 days	20 days	0d	Wed 26/12/02	Thu 26/10/22	29d	Thu 26/12/31	Wed 26/11/18	31d
92	Remove Man Lift	2 days	2 days	0d	Wed 26/12/02	Thu 26/10/22	29d	Thu 26/12/03	Fri 26/10/23	29d
93	Infill Framing @ Manlift Landings	7 days	7 days	0d	Thu 26/12/03	Fri 26/10/23	29d	Fri 26/12/11	Mon 26/11/02	29d
94	Sheathing Lift Leave Out Area	5 days	5 days	0d	Thu 26/12/10	Fri 26/10/30	29d	Wed 26/12/16	Thu 26/11/05	29d
95	Finishes @ Infilled Landings	5 days	5 days	0d	Thu 26/12/17	Fri 26/11/06	29d	Wed 26/12/23	Thu 26/11/12	29d
96	**Building Interior**	**186 days**	**186 days**	**0d**	**Mon 26/04/06**	**Thu 26/02/26**	**27d**	**Thu 26/12/31**	**Wed 26/11/18**	**31d**
97	Layout & Install Overhead Hangars 1st fl	2 days	2 days	0d	Mon 26/04/06	Thu 26/02/26	27d	Tue 26/04/07	Fri 26/02/27	27d
98	Spray Applied Fireproofing - 1st Floor	10 days	10 days	0d	Wed 26/04/08	Mon 26/03/02	27d	Tue 26/04/21	Fri 26/03/13	27d
99	Overhead P, M, & E 1st fl	15 days	15 days	0d	Fri 26/04/17	Wed 26/03/11	27d	Thu 26/05/07	Tue 26/03/31	27d
100	Unit Partitions / Hallway System & Doors 1st floor	25 days	25 days	0d	Fri 26/05/01	Wed 26/03/25	27d	Fri 26/06/05	Tue 26/04/28	28d
101	Finish Electrical 1st Fl	10 days	10 days	0d	Mon 26/06/08	Wed 26/04/29	28d	Fri 26/06/19	Tue 26/05/12	28d
102	Instal Generator and Related Systems	35 days	35 days	0d	Mon 26/06/22	Wed 26/05/13	28d	Tue 26/08/11	Wed 26/07/01	29d
103	Overhead M/E/P 2nd Fl	15 days	15 days	0d	Fri 26/05/22	Wed 26/04/15	27d	Fri 26/06/12	Tue 26/05/05	28d
104	Unit Partitions / Hallway System & Doors 2nd Floor	20 days	20 days	0d	Mon 26/06/15	Wed 26/05/06	28d	Tue 26/07/14	Wed 26/06/03	29d
105	Finish Electrical 2nd Fl	10 days	10 days	0d	Wed 26/07/15	Thu 26/06/04	29d	Tue 26/07/28	Wed 26/06/17	29d
106	Overhead M/E/P 3rd Fl	15 days	15 days	0d	Mon 26/06/15	Wed 26/05/06	28d	Tue 26/07/07	Wed 26/05/27	29d

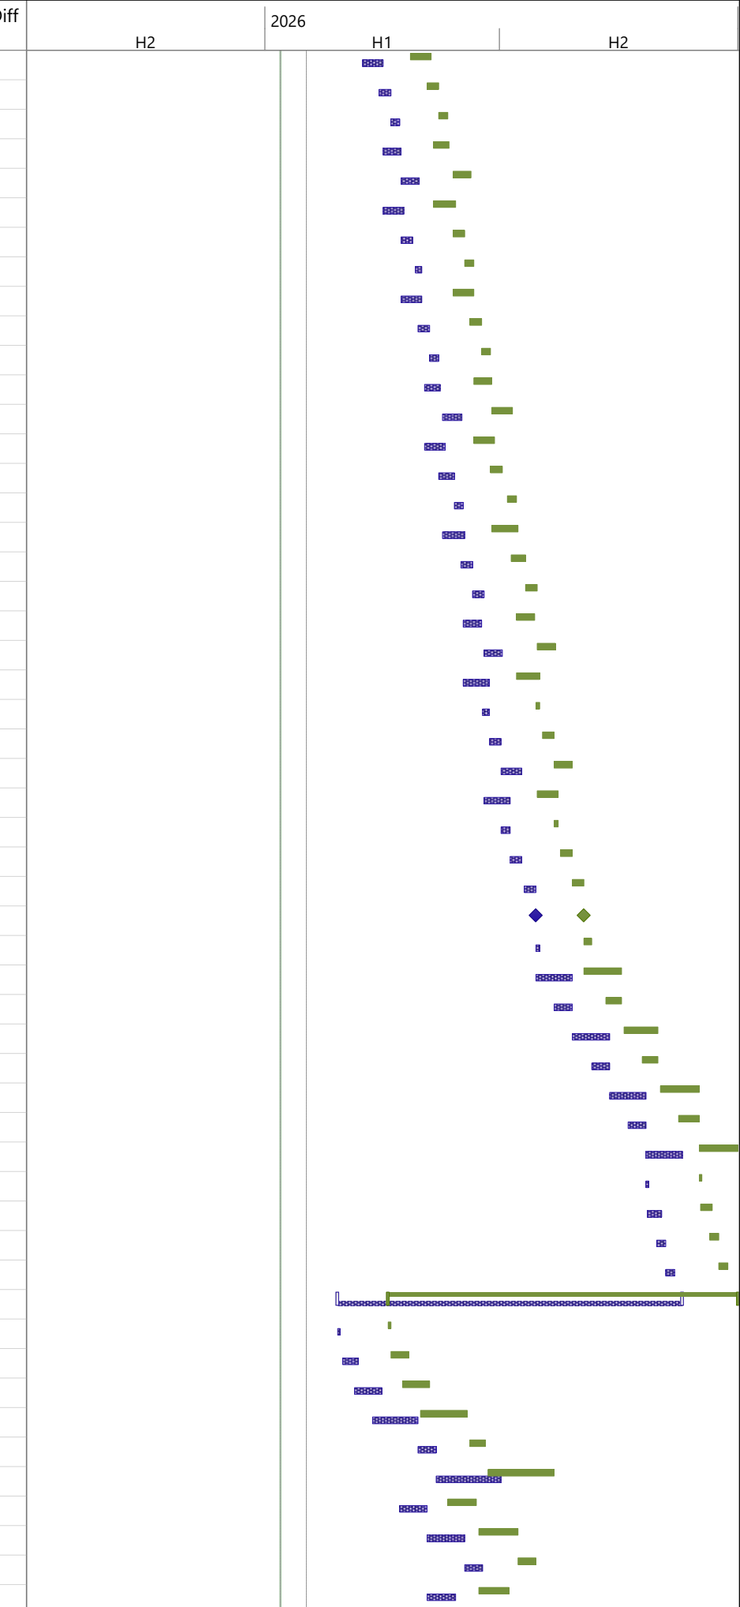
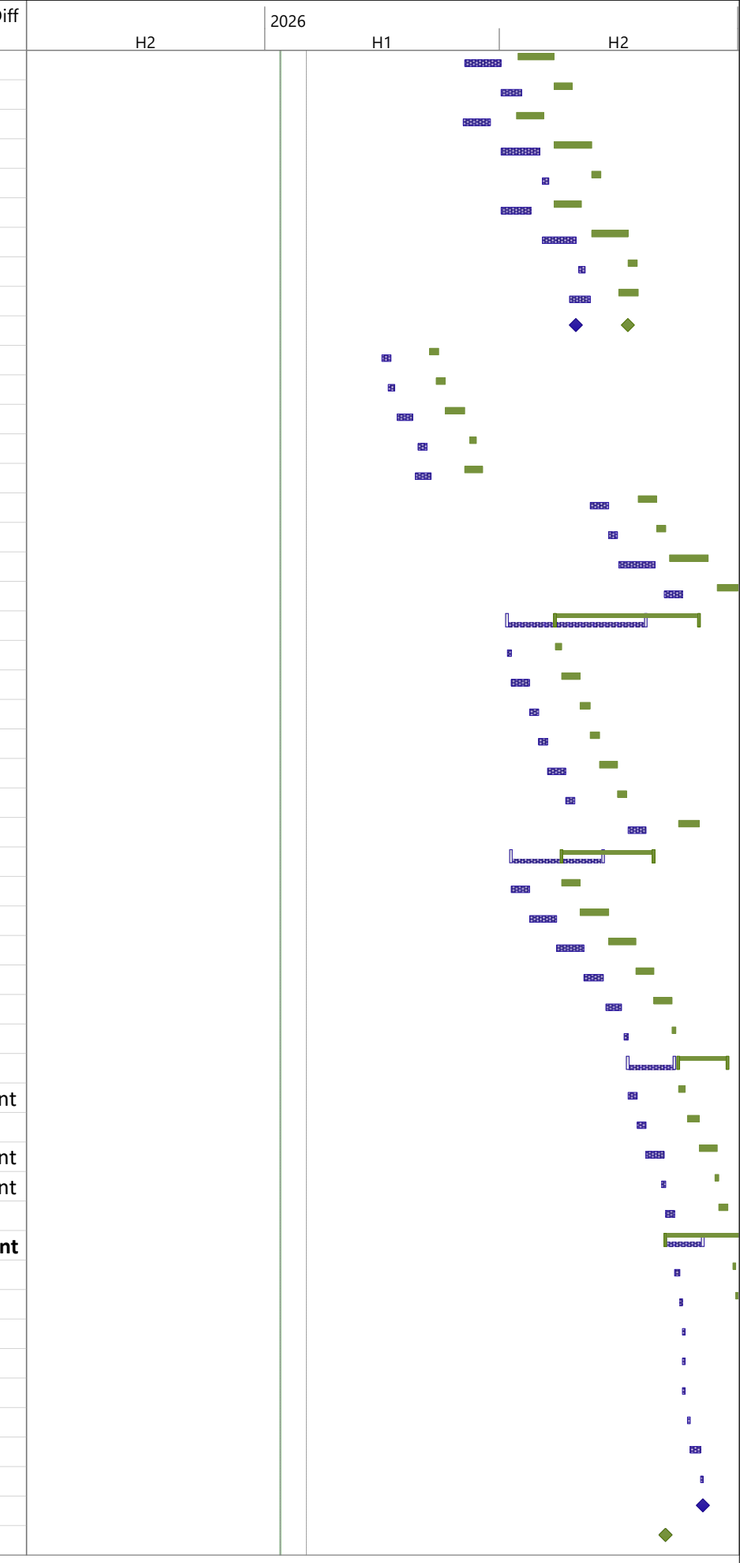
	Name	Duration: Current	Duration: Previous	Duration: Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
107	Unit partitions /Hallway System & Doors 3rd Floor	20 days	20 days	0d	Wed 26/07/15	Thu 26/06/04	29d	Tue 26/08/11	Wed 26/07/01	29d
108	Finish Electrical 3rd Fl	10 days	10 days	0d	Wed 26/08/12	Thu 26/07/02	29d	Tue 26/08/25	Fri 26/07/17	27d
109	Overhead M/E/P 4th Fl	15 days	15 days	0d	Tue 26/07/14	Wed 26/06/03	29d	Mon 26/08/03	Tue 26/06/23	29d
110	Unit Partitions /Hallway System & Doors 4th Floor	20 days	20 days	0d	Wed 26/08/12	Thu 26/07/02	29d	Wed 26/09/09	Fri 26/07/31	28d
111	Finish Electrical 4th Fl	5 days	5 days	0d	Thu 26/09/10	Mon 26/08/03	28d	Wed 26/09/16	Fri 26/08/07	28d
112	Overhead M/E/P 5th Fl	15 days	15 days	0d	Wed 26/08/12	Thu 26/07/02	29d	Tue 26/09/01	Fri 26/07/24	27d
113	Unit Partitions & Hallway System & Doors 5th Floor	20 days	20 days	0d	Thu 26/09/10	Mon 26/08/03	28d	Wed 26/10/07	Fri 26/08/28	28d
114	Hallway Systems after Scaffold Removal	5 days	5 days	0d	Thu 26/10/08	Mon 26/08/31	28d	Wed 26/10/14	Fri 26/09/04	28d
115	Finish Electrical 5th Fl & Roof Equipment	11 days	11 days	0d	Thu 26/10/01	Mon 26/08/24	28d	Thu 26/10/15	Tue 26/09/08	27d
116	Overhead Doors, Liner & Demising Panels Comp.	0 days	0 days	0d	Wed 26/10/07	Fri 26/08/28	28d	Wed 26/10/07	Fri 26/08/28	28d
117	Elev. Lobby Framing	5 days	5 days	0d	Fri 26/05/08	Wed 26/04/01	27d	Thu 26/05/14	Tue 26/04/07	27d
118	Elev. Lobby M/E/P Rough in	5 days	5 days	0d	Wed 26/05/13	Mon 26/04/06	27d	Tue 26/05/19	Fri 26/04/10	27d
119	Elev. Lobby Drywall	10 days	10 days	0d	Wed 26/05/20	Mon 26/04/13	27d	Wed 26/06/03	Fri 26/04/24	28d
120	Install HM Doors & Hardware	5 days	5 days	0d	Mon 26/06/08	Wed 26/04/29	28d	Fri 26/06/12	Tue 26/05/05	28d
121	Lobby Fixtures & Finishes	10 days	10 days	0d	Thu 26/06/04	Mon 26/04/27	28d	Wed 26/06/17	Fri 26/05/08	28d
122	Finish Painting in Storage areas	10 days	10 days	0d	Fri 26/10/16	Wed 26/09/09	27d	Thu 26/10/29	Tue 26/09/22	27d
123	Building Signage per plan	5 days	5 days	0d	Fri 26/10/30	Wed 26/09/23	27d	Thu 26/11/05	Tue 26/09/29	27d
124	Final Clean up & Seal floors	20 days	20 days	0d	Mon 26/11/09	Thu 26/10/01	27d	Tue 26/12/08	Wed 26/10/28	29d
125	Owner Arch. Punch list & Completion	10 days	10 days	0d	Wed 26/12/16	Thu 26/11/05	29d	Thu 26/12/31	Wed 26/11/18	31d
126	**Building Exterior**	**76 days**	**76 days**	**0d**	**Thu 26/08/13**	**Tue 26/07/07**	**27d**	**Tue 26/12/01**	**Wed 26/10/21**	**29d**
127	Install Scaffolding at Building Perimeter	3 days	3 days	0d	Thu 26/08/13	Tue 26/07/07	27d	Mon 26/08/17	Thu 26/07/09	27d
128	Exterior Metal Frame Sheathing & WRB @ Tower	10 days	10 days	0d	Tue 26/08/18	Fri 26/07/10	27d	Mon 26/08/31	Thu 26/07/23	27d
129	Metal Panel Siding @ Tower	5 days	5 days	0d	Tue 26/09/01	Fri 26/07/24	27d	Tue 26/09/08	Thu 26/07/30	28d
130	Storefront/Curtainwall	5 days	5 days	0d	Wed 26/09/09	Fri 26/07/31	28d	Tue 26/09/15	Thu 26/08/06	28d
131	Glass Lead Time	10 days	10 days	0d	Wed 26/09/16	Fri 26/08/07	28d	Tue 26/09/29	Thu 26/08/20	28d
132	Install Glass	5 days	5 days	0d	Wed 26/09/30	Fri 26/08/21	28d	Tue 26/10/06	Thu 26/08/27	28d
133	Install Auto Sliders & Mapes Canopy	10 days	10 days	0d	Mon 26/11/16	Thu 26/10/08	27d	Tue 26/12/01	Wed 26/10/21	29d
134	**EIFS WRB, Foam/Brown & Finish**	**50 days**	**50 days**	**0d**	**Tue 26/08/18**	**Fri 26/07/10**	**27d**	**Tue 26/10/27**	**Fri 26/09/18**	**27d**
135	Waterproof Membrane	10 days	10 days	0d	Tue 26/08/18	Fri 26/07/10	27d	Mon 26/08/31	Thu 26/07/23	27d
136	EIFS Foam	15 days	15 days	0d	Tue 26/09/01	Fri 26/07/24	27d	Tue 26/09/22	Thu 26/08/13	28d
137	EIFS Mesh Coat	15 days	15 days	0d	Wed 26/09/23	Fri 26/08/14	28d	Tue 26/10/13	Thu 26/09/03	28d
138	EIFS Top Coat	10 days	10 days	0d	Wed 26/10/14	Fri 26/09/04	28d	Tue 26/10/27	Fri 26/09/18	27d
139	Exterior Sheet metal, Sealants, & Painting	10 days	10 days	0d	Wed 26/10/28	Mon 26/09/21	27d	Tue 26/11/10	Fri 26/10/02	27d
140	Remove Scaffolding	3 days	3 days	0d	Wed 26/11/11	Mon 26/10/05	27d	Fri 26/11/13	Wed 26/10/07	27d
141	**Onsite improvements**	**26 days**	**26 days**	**0d**	**Mon 26/11/16**	**Thu 26/10/08**	**27d**	**Wed 26/12/23**	**Thu 26/11/12**	**29d**
142	Grade & Pour Walks	5 days	5 days	Equal	Mon 26/11/16	Thu 26/10/08	Different	Fri 26/11/20	Wed 26/10/14	Different
143	Site Fencing & Gates	5 days	5 days	0d	Mon 26/11/23	Thu 26/10/15	27d	Tue 26/12/01	Wed 26/10/21	29d
144	Landscape Irrigation and Planting	10 days	10 days	Equal	Wed 26/12/02	Thu 26/10/22	Different	Tue 26/12/15	Wed 26/11/04	Different
145	Striping & Signage	3 days	3 days	Equal	Mon 26/12/14	Tue 26/11/03	Different	Wed 26/12/16	Thu 26/11/05	Different
146	Owner Civil Punch list & Completion	5 days	5 days	0d	Thu 26/12/17	Fri 26/11/06	29d	Wed 26/12/23	Thu 26/11/12	29d
147	**Accumulative Inspections & C of O**	**42 days**	**19 days**	**Different**	**Fri 26/11/06**	**Fri 26/11/06**	**Equal**	**Mon 27/01/11**	**Fri 26/12/04**	**Different**
148	Final Grading Inspections	2 days	2 days	0d	Mon 26/12/28	Fri 26/11/13	31d	Tue 26/12/29	Mon 26/11/16	31d
149	Final Public Works Inspections	2 days	2 days	0d	Wed 26/12/30	Tue 26/11/17	31d	Thu 26/12/31	Wed 26/11/18	31d
150	Life Safety Inspection	2 days	2 days	0d	Mon 27/01/04	Thu 26/11/19	32d	Tue 27/01/05	Fri 26/11/20	32d
151	MEP Final Inspections	2 days	2 days	0d	Mon 27/01/04	Thu 26/11/19	32d	Tue 27/01/05	Fri 26/11/20	32d
152	Final Planning & Zoning Inspection	2 days	2 days	0d	Mon 27/01/04	Thu 26/11/19	32d	Tue 27/01/05	Fri 26/11/20	32d
153	Building Final Inspection	2 days	2 days	0d	Wed 27/01/06	Mon 26/11/23	32d	Thu 27/01/07	Tue 26/11/24	32d
154	Rain Days Included - Used as of 1/6/26	0 days	4 days	-4d	Thu 27/01/07	Wed 26/11/25	32d	Thu 27/01/07	Wed 26/12/02	26d
155	Certificate Of Occupancy	2 days	2 days	0d	Fri 27/01/08	Thu 26/12/03	26d	Mon 27/01/11	Fri 26/12/04	26d
156	Open Date	0 days	0 days	0d	Mon 27/01/11	Fri 26/12/04	26d	Mon 27/01/11	Fri 26/12/04	26d
157	Original Contracted Open Date	0 days	0 days	0d	Fri 26/11/06	Fri 26/11/06	0d	Fri 26/11/06	Fri 26/11/06	0d
