Public Storage Anaheim Contract Schedule Update

ID	Task Name	% Comple	Duration	Start	Finish
1	**Grading & Building Slab Construction**	**17%**	**327 days**	**Mon 9/8/25**	**Mon 12/28/26**
17	**Building Permit Delay - Finish after 2026 holidays, added Cal. Days**	0%	**13 days**	**Wed 12/10/25**	**Tue 12/30/25**
29	**Site Wet Utilities**	**90%**	**21 days**	**Wed 1/28/26**	**Thu 2/26/26**
30	Storm Drain Piping & Catch Basins from Phase 1 Stubs	90%	6 days	Wed 1/28/26	Wed 2/4/26
31	Extend Sewer Laterals to building	90%	5 days	Thu 2/5/26	Wed 2/11/26
32	Extend Fire / Domestic Water Service to Building	90%	10 days	Thu 2/12/26	Thu 2/26/26
33	**Domestic & Fire Water Services Completion**	0%	0 days	Thu 2/26/26	Thu 2/26/26
34	**Site Dry Utilities**	**78%**	**8 days**	**Thu 2/5/26**	**Tue 2/17/26**
35	Extend Power & Lov Voltage conduits to Bldg from Stubs	95%	5 days	Thu 2/5/26	Wed 2/11/26
36	Install Generac & Site lighting Conduits	50%	3 days	Thu 2/12/26	Tue 2/17/26
37	**Onsite improvements For Early Base Pave**	**0%**	**22 days**	**Fri 2/27/26**	**Mon 3/30/26**
38	Grade for Curb & Gutter	0%	4 days	Fri 2/27/26	Wed 3/4/26
39	Install Irrigation Sleeves	0%	1 day	Thu 3/5/26	Thu 3/5/26
40	Place Curb & Gutter	0%	4 days	Fri 3/6/26	Wed 3/11/26
41	Grade & Pour Walks	0%	5 days	Tue 3/10/26	Mon 3/16/26
42	Agg Base Import & AC Base Paving	0%	10 days	Tue 3/17/26	Mon 3/30/26
43	**Vertical Building Construction**	**7%**	**210 days**	**Tue 2/17/26**	**Tue 12/15/26**
44	CMU Walls to 14'-8" North	85%	15 days	Tue 2/17/26	Mon 3/9/26
45	CMU Walls to 14'-8" South	85%	15 days	Tue 3/3/26	Mon 3/23/26
46	Structural Steel Framing & Metal Deck to 2nd floor N.	90%	7 days	Tue 3/3/26	Wed 3/11/26
47	Structural Steel Framing & Metal Deck to 2nd floor S.	0%	7 days	Wed 3/18/26	Thu 3/26/26
48	Rebar, Hangars & Deck2 Pour North	0%	7 days	Thu 3/12/26	Fri 3/20/26
49	Rebar, Hangars & Deck2 Pour South	0%	7 days	Fri 3/27/26	Mon 4/6/26
50	CMU Walls to 25'-4" North	0%	12 days	Tue 3/24/26	Wed 4/8/26
51	CMU Walls to 25'-4" South	0%	12 days	Thu 4/9/26	Fri 4/24/26
52	2nd floor Shear walls North @ 15k/week	0%	12 days	Tue 3/24/26	Wed 4/8/26
53	3rd Floor Decking North @ 5k/day	0%	7 days	Fri 4/3/26	Mon 4/13/26
54	Rebar, Hangars & Deck Pour3 North	0%	5 days	Tue 4/14/26	Mon 4/20/26
55	2nd floor Shear walls South @ 15k/week	0%	12 days	Thu 4/9/26	Fri 4/24/26
56	3rd Floor Decking South@ 5k/day	0%	7 days	Wed 4/22/26	Thu 4/30/26
57	Rebar, Hangars & Deck3 Pour South	0%	5 days	Fri 5/1/26	Thu 5/7/26
58	CMU Walls to 36' North	0%	10 days	Mon 4/27/26	Fri 5/8/26
59	CMU Walls to 36' South	0%	10 days	Mon 5/11/26	Fri 5/22/26
60	3rd floor Shear walls North @ 15k/week	0%	12 days	Mon 4/27/26	Tue 5/12/26
61	4th Floor Decking North @ 5k/day	0%	7 days	Mon 5/11/26	Tue 5/19/26
62	Rebar, Hangars & Deck Pour4 North	0%	5 days	Wed 5/20/26	Wed 5/27/26
63	3rd floor Shear walls South @ 15k/week	0%	12 days	Mon 5/11/26	Wed 5/27/26
64	4th Floor Decking South@ 5k/day	0%	7 days	Fri 5/22/26	Tue 6/2/26
65	Rebar, Hangars & Deck4 Pour South	0%	5 days	Wed 6/3/26	Tue 6/9/26
66	CMU Walls to 46'-8" North	0%	10 days	Thu 5/28/26	Wed 6/10/26
67	CMU Walls to 46'-8" South	0%	10 days	Thu 6/11/26	Wed 6/24/26
68	4th floor Shear walls North @ 15k/week	0%	12 days	Thu 5/28/26	Fri 6/12/26
69	5th Floor Decking North @ 5k/day	0%	7 days	Wed 6/10/26	Thu 6/18/26
70	Rebar, Hangars & Deck Pour5 North	0%	5 days	Fri 6/19/26	Thu 6/25/26

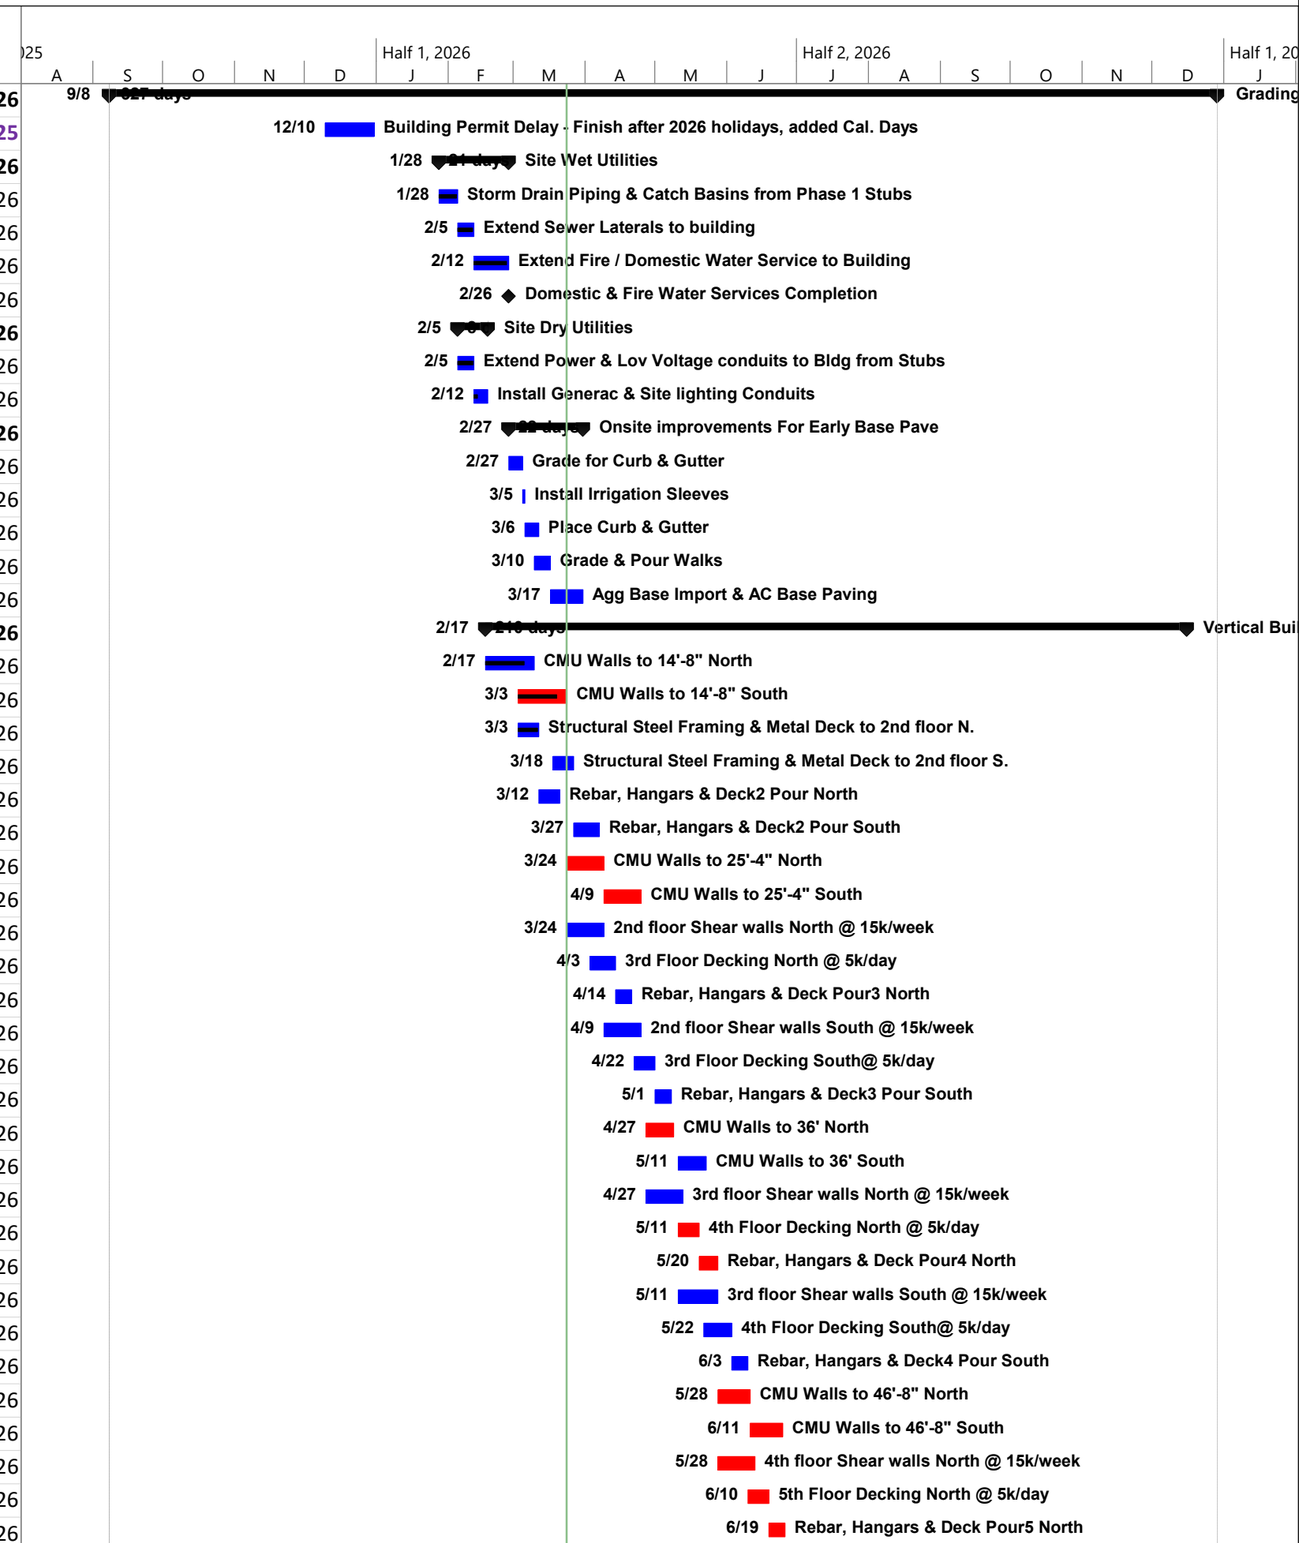

ID	Task Name	% Comple	Duration	Start	Finish
71	4th floor Shear walls South @ 15k/week	0%	12 days	Thu 6/11/26	Fri 6/26/26
72	5th Floor Decking South@ 5k/day	0%	7 days	Wed 6/24/26	Thu 7/2/26
73	Rebar, Hangars & Deck5 Pour South	0%	7 days	Tue 7/7/26	Wed 7/15/26
74	CMU Walls to 57'-4" North	0%	10 days	Fri 6/26/26	Mon 7/13/26
75	CMU Walls to 57'-4" South	0%	10 days	Thu 7/16/26	Wed 7/29/26
76	5th floor Shear walls North @ 15k/week	0%	14 days	Fri 6/26/26	Fri 7/17/26
77	Roof Equipment Structural	0%	3 days	Wed 7/15/26	Fri 7/17/26
78	Roof Decking North @ 5k/day	0%	7 days	Mon 7/20/26	Tue 7/28/26
79	Roof Drains, Screens & Curbs	0%	10 days	Wed 7/29/26	Tue 8/11/26
80	5th floor Shear walls South @ 15k/week	0%	12 days	Thu 7/16/26	Fri 7/31/26
81	Roof Equipment Structural	0%	3 days	Wed 7/29/26	Fri 7/31/26
82	Roof Decking South@ 5k/day	0%	7 days	Mon 8/3/26	Tue 8/11/26
83	Roof insulation Crickets & TPO	0%	7 days	Wed 8/12/26	Thu 8/20/26
84	**Building Temporarily Water Tight**	0%	0 days	Thu 8/20/26	Thu 8/20/26
85	Set rooftop Equipment & hook up	0%	3 days	Fri 8/21/26	Tue 8/25/26
86	Elevator Construction Car #1	0%	20 days	Fri 8/21/26	Fri 9/18/26
87	CMU infill @ Elevator Openings	0%	10 days	Fri 9/4/26	Fri 9/18/26
88	Elevator Construction Car #2	0%	20 days	Mon 9/21/26	Fri 10/16/26
89	CMU infill @ Elevator Openings	0%	10 days	Mon 10/5/26	Fri 10/16/26
90	Elevator Construction Car #3	0%	20 days	Mon 10/19/26	Fri 11/13/26
91	CMU infill @ Elevator Openings	0%	10 days	Mon 11/2/26	Fri 11/13/26
92	State Elevator inspection Lead Time & Approval	0%	20 days	Mon 11/16/26	Tue 12/15/26
93	Remove Man Lift	0%	2 days	Mon 11/16/26	Tue 11/17/26
94	Infill Framing @ Manlift Landings	0%	7 days	Tue 11/17/26	Wed 11/25/26
95	Sheathing Lift Leave Out Area	0%	5 days	Tue 11/24/26	Wed 12/2/26
96	Finishes @ Infilled Landings	0%	5 days	Thu 12/3/26	Wed 12/9/26
97	**Building Interior**	**0%**	**186 days**	**Mon 3/23/26**	**Tue 12/15/26**
98	Layout & Install Overhead Hangars 1st fl	0%	2 days	Mon 3/23/26	Tue 3/24/26
99	Spray Applied Fireproofing - 1st Floor	0%	10 days	Wed 3/25/26	Tue 4/7/26
100	Overhead P, M, & E 1st fl	0%	15 days	Fri 4/3/26	Thu 4/23/26
101	Unit Partitions / Hallway System & Doors 1st floor	0%	25 days	Fri 4/17/26	Thu 5/21/26
102	Finish Electrical 1st Fl	0%	10 days	Fri 5/22/26	Fri 6/5/26
103	Instal Generator and Related Systems	0%	35 days	Mon 6/8/26	Tue 7/28/26
104	Overhead M/E/P 2nd Fl	0%	15 days	Fri 5/8/26	Fri 5/29/26
105	Unit Partitions / Hallway System & Doors 2nd Floor	0%	20 days	Mon 6/1/26	Fri 6/26/26
106	Finish Electrical 2nd Fl	0%	10 days	Mon 6/29/26	Tue 7/14/26
107	Overhead M/E/P 3rd Fl	0%	15 days	Mon 6/1/26	Fri 6/19/26
108	Unit partitions /Hallway System & Doors 3rd Floor	0%	20 days	Mon 6/29/26	Tue 7/28/26
109	Finish Electrical 3rd Fl	0%	10 days	Wed 7/29/26	Tue 8/11/26
110	Overhead M/E/P 4th Fl	0%	15 days	Fri 6/26/26	Mon 7/20/26
111	Unit Partitions /Hallway System & Doors 4th Floor	0%	20 days	Wed 7/29/26	Tue 8/25/26
112	Finish Electrical 4th Fl	0%	5 days	Wed 8/26/26	Tue 9/1/26
113	Overhead M/E/P 5th Fl	0%	15 days	Wed 7/29/26	Tue 8/18/26
114	Unit Partitions & Hallway System & Doors 5th Floor	0%	20 days	Wed 8/26/26	Wed 9/23/26

Public Storage Anaheim Contract Schedule Update
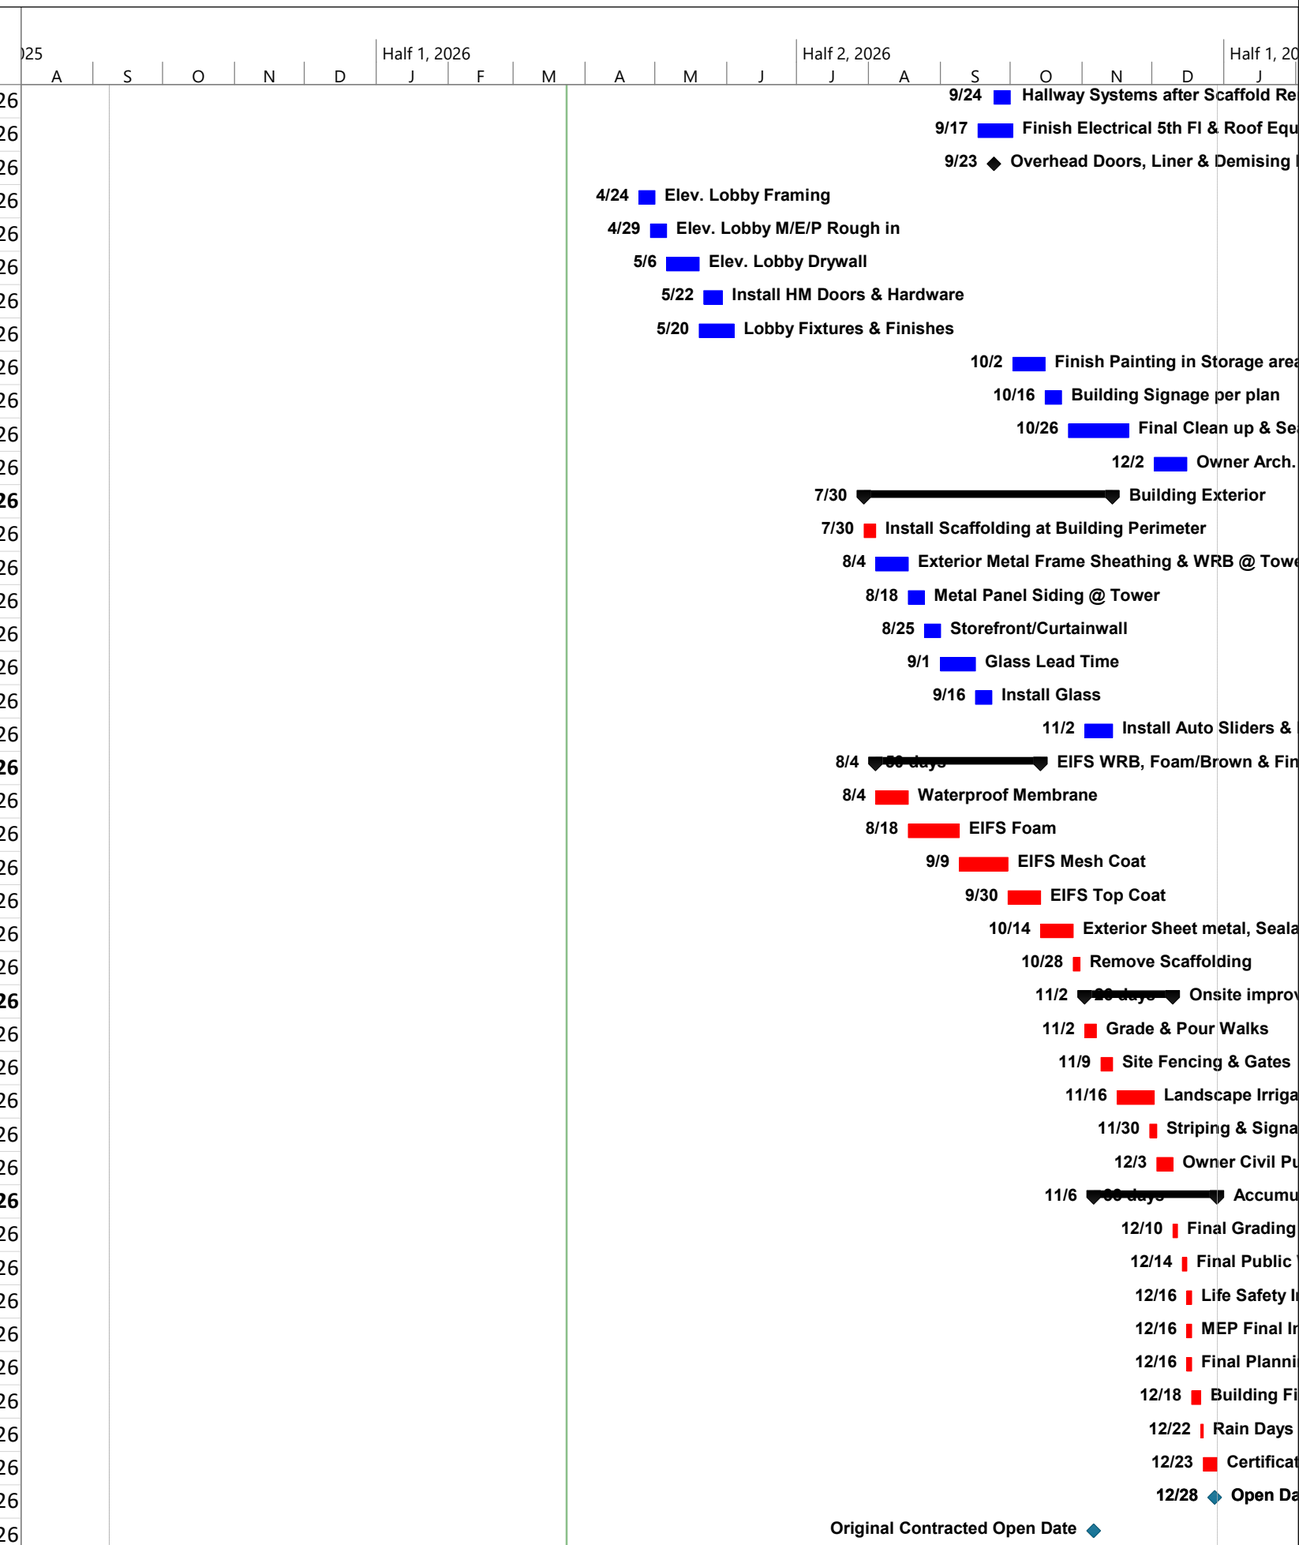
ID	Task Name	% Comple	Duration	Start	Finish
115	Hallway Systems after Scaffold Removal	0%	5 days	Thu 9/24/26	Wed 9/30/26
116	Finish Electrical 5th Fl & Roof Equipment	0%	11 days	Thu 9/17/26	Thu 10/1/26
117	**Overhead Doors, Liner & Demising Panels Comp.**	0%	0 days	Wed 9/23/26	Wed 9/23/26
118	Elev. Lobby Framing	0%	5 days	Fri 4/24/26	Thu 4/30/26
119	Elev. Lobby M/E/P Rough in	0%	5 days	Wed 4/29/26	Tue 5/5/26
120	Elev. Lobby Drywall	0%	10 days	Wed 5/6/26	Tue 5/19/26
121	Install HM Doors & Hardware	0%	5 days	Fri 5/22/26	Fri 5/29/26
122	Lobby Fixtures & Finishes	0%	10 days	Wed 5/20/26	Wed 6/3/26
123	Finish Painting in Storage areas	0%	10 days	Fri 10/2/26	Thu 10/15/26
124	Building Signage per plan	0%	5 days	Fri 10/16/26	Thu 10/22/26
125	Final Clean up & Seal floors	0%	20 days	Mon 10/26/26	Fri 11/20/26
126	Owner Arch. Punch list & Completion	0%	10 days	Wed 12/2/26	Tue 12/15/26
127	**Building Exterior**	**0%**	**76 days**	**Thu 7/30/26**	**Fri 11/13/26**
128	Install Scaffolding at Building Perimeter	0%	3 days	Thu 7/30/26	Mon 8/3/26
129	Exterior Metal Frame Sheathing & WRB @ Tower	0%	10 days	Tue 8/4/26	Mon 8/17/26
130	Metal Panel Siding @ Tower	0%	5 days	Tue 8/18/26	Mon 8/24/26
131	Storefront/Curtainwall	0%	5 days	Tue 8/25/26	Mon 8/31/26
132	Glass Lead Time	0%	10 days	Tue 9/1/26	Tue 9/15/26
133	Install Glass	0%	5 days	Wed 9/16/26	Tue 9/22/26
134	Install Auto Sliders & Mapes Canopy	0%	10 days	Mon 11/2/26	Fri 11/13/26
135	**EIFS WRB, Foam/Brown & Finish**	**0%**	**50 days**	**Tue 8/4/26**	**Tue 10/13/26**
136	Waterproof Membrane	0%	10 days	Tue 8/4/26	Mon 8/17/26
137	EIFS Foam	0%	15 days	Tue 8/18/26	Tue 9/8/26
138	EIFS Mesh Coat	0%	15 days	Wed 9/9/26	Tue 9/29/26
139	EIFS Top Coat	0%	10 days	Wed 9/30/26	Tue 10/13/26
140	Exterior Sheet metal, Sealants, & Painting	0%	10 days	Wed 10/14/26	Tue 10/27/26
141	Remove Scaffolding	0%	3 days	Wed 10/28/26	Fri 10/30/26
142	**Onsite improvements**	**0%**	**26 days**	**Mon 11/2/26**	**Wed 12/9/26**
143	Grade & Pour Walks	0%	5 days	Mon 11/2/26	Fri 11/6/26
144	Site Fencing & Gates	0%	5 days	Mon 11/9/26	Fri 11/13/26
145	Landscape Irrigation and Planting	0%	10 days	Mon 11/16/26	Tue 12/1/26
146	Striping & Signage	0%	3 days	Mon 11/30/26	Wed 12/2/26
147	Owner Civil Punch list & Completion	0%	5 days	Thu 12/3/26	Wed 12/9/26
148	**Accumulative Inspections & C of O**	**0%**	**33 days**	**Fri 11/6/26**	**Mon 12/28/26**
149	Final Grading Inspections	0%	2 days	Thu 12/10/26	Fri 12/11/26
150	Final Public Works Inspections	0%	2 days	Mon 12/14/26	Tue 12/15/26
151	Life Safety Inspection	0%	2 days	Wed 12/16/26	Thu 12/17/26
152	MEP Final Inspections	0%	2 days	Wed 12/16/26	Thu 12/17/26
153	Final Planning & Zoning Inspection	0%	2 days	Wed 12/16/26	Thu 12/17/26
154	Building Final Inspection	0%	2 days	Fri 12/18/26	Mon 12/21/26
155	**Rain Days Included - Used as of 1/6/26**	0%	1 day	Tue 12/22/26	Tue 12/22/26
156	Certificate Of Occupancy	0%	2 days	Wed 12/23/26	Mon 12/28/26
157	**Open Date - Approved with Delay #2**	0%	0 days	Mon 12/28/26	Mon 12/28/26
158	Original Contracted Open Date	0%	0 days	Fri 11/6/26	Fri 11/6/26
