	Name	Duration Current	Duration Previous	Dur Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Grading & Building Slab Construction**	**327 day**	**336 day**	**-9d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Mon 12/28/26**	**Mon 1/11/27**	**-10d**
17	Building Permit Delay - Finish after 2026 holidays, added Cal. Days	13 days	13 days	0d	Wed 12/10/25	Wed 12/10/25	0d	Tue 12/30/25	Tue 12/30/25	0d
29	**Site Wet Utilities**	**21 days**	**21 days**	**0d**	**Wed 1/28/26**	**Wed 1/21/26**	**5d**	**Thu 2/26/26**	**Thu 2/19/26**	**5d**
30	Storm Drain Piping & Catch Basins from Phase 1 Stubs	6 days	6 days	0d	Wed 1/28/26	Wed 1/21/26	5d	Wed 2/4/26	Wed 1/28/26	5d
31	Extend Sewer Laterals to building	5 days	5 days	0d	Thu 2/5/26	Thu 1/29/26	5d	Wed 2/11/26	Wed 2/4/26	5d
32	Extend Fire / Domestic Water Service to Building	10 days	10 days	0d	Thu 2/12/26	Thu 2/5/26	5d	Thu 2/26/26	Thu 2/19/26	5d
33	Domestic & Fire Water Services Completion	0 days	0 days	0d	Thu 2/26/26	Thu 2/19/26	5d	Thu 2/26/26	Thu 2/19/26	5d
34	**Site Dry Utilities**	**8 days**	**8 days**	**0d**	**Thu 2/5/26**	**Thu 1/29/26**	**5d**	**Tue 2/17/26**	**Mon 2/9/26**	**6d**
35	Extend Power & Lov Voltage conduits to Bldg from Stubs	5 days	5 days	0d	Thu 2/5/26	Thu 1/29/26	5d	Wed 2/11/26	Wed 2/4/26	5d
36	Install Generac & Site lighting Conduits	3 days	3 days	0d	Thu 2/12/26	Thu 2/5/26	5d	Tue 2/17/26	Mon 2/9/26	6d
37	**Onsite improvements For Early Base Pave**	**22 days**	**22 days**	**0d**	**Fri 2/27/26**	**Fri 2/20/26**	**5d**	**Mon 3/30/26**	**Mon 3/23/26**	**5d**
38	Grade for Curb & Gutter	4 days	4 days	0d	Fri 2/27/26	Fri 2/20/26	5d	Wed 3/4/26	Wed 2/25/26	5d
39	Install Irrigation Sleeves	1 day	1 day	0d	Thu 3/5/26	Thu 2/26/26	5d	Thu 3/5/26	Thu 2/26/26	5d
40	Place Curb & Gutter	4 days	4 days	0d	Fri 3/6/26	Fri 2/27/26	5d	Wed 3/11/26	Wed 3/4/26	5d
41	Grade & Pour Walks	5 days	5 days	0d	Tue 3/10/26	Tue 3/3/26	5d	Mon 3/16/26	Mon 3/9/26	5d
42	Agg Base Import & AC Base Paving	10 days	10 days	0d	Tue 3/17/26	Tue 3/10/26	5d	Mon 3/30/26	Mon 3/23/26	5d
43	**Vertical Building Construction**	**210 day**	**215 day**	**-5d**	**Tue 2/17/26**	**Tue 2/24/26**	**-5d**	**Tue 12/15/26**	**Thu 12/31/26**	**-12d**
44	CMU Walls to 14'-8" North	15 days	15 days	0d	Tue 2/17/26	Tue 2/24/26	-5d	Mon 3/9/26	Mon 3/16/26	-5d
45	CMU Walls to 14'-8" South	15 days	15 days	0d	Tue 3/3/26	Tue 3/17/26	-10d	Mon 3/23/26	Mon 4/6/26	-10d
46	Structural Steel Framing & Metal Deck to 2nd floor N.	7 days	7 days	0d	Tue 3/3/26	Tue 3/17/26	-10d	Wed 3/11/26	Wed 3/25/26	-10d
47	Structural Steel Framing & Metal Deck to 2nd floor S.	7 days	7 days	0d	Wed 3/18/26	Wed 4/1/26	-10d	Thu 3/26/26	Thu 4/9/26	-10d
48	Rebar, Hangars & Deck2 Pour North	7 days	7 days	0d	Thu 3/12/26	Thu 3/26/26	-10d	Fri 3/20/26	Fri 4/3/26	-10d
49	Rebar, Hangars & Deck2 Pour South	7 days	7 days	0d	Fri 3/27/26	Fri 4/10/26	-10d	Mon 4/6/26	Mon 4/20/26	-10d
50	CMU Walls to 25'-4" North	12 days	12 days	0d	Tue 3/24/26	Tue 4/7/26	-10d	Wed 4/8/26	Wed 4/22/26	-10d
51	CMU Walls to 25'-4" South	12 days	12 days	0d	Thu 4/9/26	Thu 4/23/26	-10d	Fri 4/24/26	Fri 5/8/26	-10d
52	2nd floor Shear walls North @ 15k/week	12 days	12 days	0d	Tue 3/24/26	Tue 4/7/26	-10d	Wed 4/8/26	Wed 4/22/26	-10d
53	3rd Floor Decking North @ 5k/day	7 days	7 days	0d	Fri 4/3/26	Fri 4/17/26	-10d	Mon 4/13/26	Mon 4/27/26	-10d
54	Rebar, Hangars & Deck Pour3 North	5 days	5 days	0d	Tue 4/14/26	Tue 4/28/26	-10d	Mon 4/20/26	Mon 5/4/26	-10d
55	2nd floor Shear walls South @ 15k/week	12 days	12 days	0d	Thu 4/9/26	Thu 4/23/26	-10d	Fri 4/24/26	Fri 5/8/26	-10d
56	3rd Floor Decking South@ 5k/day	7 days	7 days	0d	Wed 4/22/26	Wed 5/6/26	-10d	Thu 4/30/26	Thu 5/14/26	-10d
57	Rebar, Hangars & Deck3 Pour South	5 days	5 days	0d	Fri 5/1/26	Fri 5/15/26	-10d	Thu 5/7/26	Thu 5/21/26	-10d
58	CMU Walls to 36' North	10 days	10 days	0d	Mon 4/27/26	Mon 5/11/26	-10d	Fri 5/8/26	Fri 5/22/26	-10d
59	CMU Walls to 36' South	10 days	10 days	0d	Mon 5/11/26	Tue 5/26/26	-11d	Fri 5/22/26	Mon 6/8/26	-11d
60	3rd floor Shear walls North @ 15k/week	12 days	12 days	0d	Mon 4/27/26	Mon 5/11/26	-10d	Tue 5/12/26	Wed 5/27/26	-11d
61	4th Floor Decking North @ 5k/day	7 days	7 days	0d	Mon 5/11/26	Tue 5/26/26	-11d	Tue 5/19/26	Wed 6/3/26	-11d
62	Rebar, Hangars & Deck Pour4 North	5 days	5 days	0d	Wed 5/20/26	Thu 6/4/26	-11d	Wed 5/27/26	Wed 6/10/26	-10d
63	3rd floor Shear walls South @ 15k/week	12 days	12 days	0d	Mon 5/11/26	Tue 5/26/26	-11d	Wed 5/27/26	Wed 6/10/26	-10d
64	4th Floor Decking South@ 5k/day	7 days	7 days	0d	Fri 5/22/26	Mon 6/8/26	-11d	Tue 6/2/26	Tue 6/16/26	-10d
65	Rebar, Hangars & Deck4 Pour South	5 days	5 days	0d	Wed 6/3/26	Wed 6/17/26	-10d	Tue 6/9/26	Tue 6/23/26	-10d
66	CMU Walls to 46'-8" North	10 days	10 days	0d	Thu 5/28/26	Thu 6/11/26	-10d	Wed 6/10/26	Wed 6/24/26	-10d
67	CMU Walls to 46'-8" South	10 days	10 days	0d	Thu 6/11/26	Thu 6/25/26	-10d	Wed 6/24/26	Fri 7/10/26	-12d
68	4th floor Shear walls North @ 15k/week	12 days	12 days	0d	Thu 5/28/26	Thu 6/11/26	-10d	Fri 6/12/26	Fri 6/26/26	-10d
69	5th Floor Decking North @ 5k/day	7 days	7 days	0d	Wed 6/10/26	Wed 6/24/26	-10d	Thu 6/18/26	Thu 7/2/26	-10d
70	Rebar, Hangars & Deck Pour5 North	5 days	5 days	0d	Fri 6/19/26	Tue 7/7/26	-12d	Thu 6/25/26	Mon 7/13/26	-12d

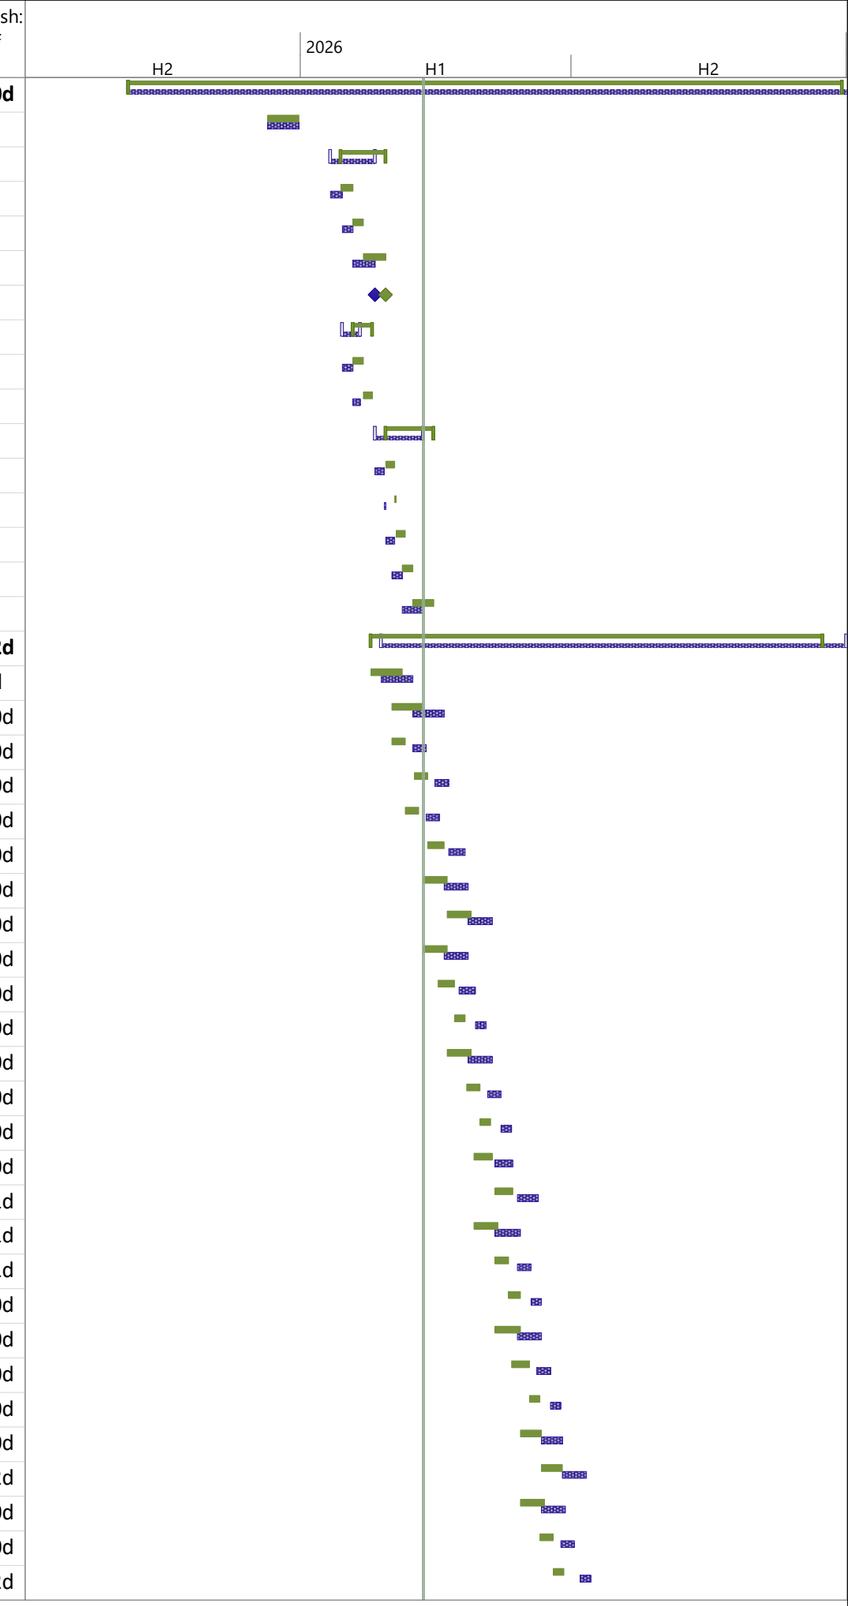

	Name	Duration Current	Duration Previous	Dur Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
71	4th floor Shear walls South @ 15k/week	12 days	12 days	0d	Thu 6/11/26	Thu 6/25/26	-10d	Fri 6/26/26	Tue 7/14/26	-12d
72	5th Floor Decking South@ 5k/day	7 days	7 days	0d	Wed 6/24/26	Fri 7/10/26	-12d	Thu 7/2/26	Mon 7/20/26	-12d
73	Rebar, Hangars & Deck5 Pour South	7 days	7 days	0d	Tue 7/7/26	Tue 7/21/26	-10d	Wed 7/15/26	Wed 7/29/26	-10d
74	CMU Walls to 57'-4" North	10 days	10 days	0d	Fri 6/26/26	Tue 7/14/26	-12d	Mon 7/13/26	Mon 7/27/26	-10d
75	CMU Walls to 57'-4" South	10 days	10 days	0d	Thu 7/16/26	Thu 7/30/26	-10d	Wed 7/29/26	Wed 8/12/26	-10d
76	5th floor Shear walls North @ 15k/week	14 days	14 days	0d	Fri 6/26/26	Tue 7/14/26	-12d	Fri 7/17/26	Fri 7/31/26	-10d
77	Roof Equipment Structural	3 days	3 days	0d	Wed 7/15/26	Wed 7/29/26	-10d	Fri 7/17/26	Fri 7/31/26	-10d
78	Roof Decking North @ 5k/day	7 days	7 days	0d	Mon 7/20/26	Mon 8/3/26	-10d	Tue 7/28/26	Tue 8/11/26	-10d
79	Roof Drains, Screens & Curbs	10 days	10 days	0d	Wed 7/29/26	Wed 8/12/26	-10d	Tue 8/11/26	Tue 8/25/26	-10d
80	5th floor Shear walls South @ 15k/week	12 days	12 days	0d	Thu 7/16/26	Thu 7/30/26	-10d	Fri 7/31/26	Fri 8/14/26	-10d
81	Roof Equipment Structural	3 days	3 days	0d	Wed 7/29/26	Wed 8/12/26	-10d	Fri 7/31/26	Fri 8/14/26	-10d
82	Roof Decking South@ 5k/day	7 days	7 days	0d	Mon 8/3/26	Mon 8/17/26	-10d	Tue 8/11/26	Tue 8/25/26	-10d
83	Roof insulation Crickets & TPO	7 days	7 days	0d	Wed 8/12/26	Wed 8/26/26	-10d	Thu 8/20/26	Thu 9/3/26	-10d
84	Building Temporarily Water Tight	0 days	0 days	0d	Thu 8/20/26	Thu 9/3/26	-10d	Thu 8/20/26	Thu 9/3/26	-10d
85	Set rooftop Equipment & hook up	3 days	3 days	0d	Fri 8/21/26	Fri 9/4/26	-10d	Tue 8/25/26	Wed 9/9/26	-11d
86	Elevator Construction Car #1	20 days	20 days	0d	Fri 8/21/26	Fri 9/4/26	-10d	Fri 9/18/26	Fri 10/2/26	-10d
87	CMU infill @ Elevator Openings	10 days	10 days	0d	Fri 9/4/26	Mon 9/21/26	-11d	Fri 9/18/26	Fri 10/2/26	-10d
88	Elevator Construction Car #2	20 days	20 days	0d	Mon 9/21/26	Mon 10/5/26	-10d	Fri 10/16/26	Fri 10/30/26	-10d
89	CMU infill @ Elevator Openings	10 days	10 days	0d	Mon 10/5/26	Mon 10/19/26	-10d	Fri 10/16/26	Fri 10/30/26	-10d
90	Elevator Construction Car #3	20 days	20 days	0d	Mon 10/19/26	Mon 11/2/26	-10d	Fri 11/13/26	Tue 12/1/26	-12d
91	CMU infill @ Elevator Openings	10 days	10 days	0d	Mon 11/2/26	Mon 11/16/26	-10d	Fri 11/13/26	Tue 12/1/26	-12d
92	State Elevator inspection Lead Time & Approval	20 days	20 days	0d	Mon 11/16/26	Wed 12/2/26	-12d	Tue 12/15/26	Thu 12/31/26	-12d
93	Remove Man Lift	2 days	2 days	0d	Mon 11/16/26	Wed 12/2/26	-12d	Tue 11/17/26	Thu 12/3/26	-12d
94	Infill Framing @ Manlift Landings	7 days	7 days	0d	Tue 11/17/26	Thu 12/3/26	-12d	Wed 11/25/26	Fri 12/11/26	-12d
95	Sheathing Lift Leave Out Area	5 days	5 days	0d	Tue 11/24/26	Thu 12/10/26	-12d	Wed 12/2/26	Wed 12/16/26	-10d
96	Finishes @ Infilled Landings	5 days	5 days	0d	Thu 12/3/26	Thu 12/17/26	-10d	Wed 12/9/26	Wed 12/23/26	-10d
97	**Building Interior**	**186 day**	**186 day**	**0d**	**Mon 3/23/26**	**Mon 4/6/26**	**-10d**	**Tue 12/15/26**	**Thu 12/31/26**	**-12d**
98	Layout & Install Overhead Hangars 1st fl	2 days	2 days	0d	Mon 3/23/26	Mon 4/6/26	-10d	Tue 3/24/26	Tue 4/7/26	-10d
99	Spray Applied Fireproofing - 1st Floor	10 days	10 days	0d	Wed 3/25/26	Wed 4/8/26	-10d	Tue 4/7/26	Tue 4/21/26	-10d
100	Overhead P, M, & E 1st fl	15 days	15 days	0d	Fri 4/3/26	Fri 4/17/26	-10d	Thu 4/23/26	Thu 5/7/26	-10d
101	Unit Partitions / Hallway System & Doors 1st floor	25 days	25 days	0d	Fri 4/17/26	Fri 5/1/26	-10d	Thu 5/21/26	Fri 6/5/26	-11d
102	Finish Electrical 1st Fl	10 days	10 days	0d	Fri 5/22/26	Mon 6/8/26	-11d	Fri 6/5/26	Fri 6/19/26	-10d
103	Instal Generator and Related Systems	35 days	35 days	0d	Mon 6/8/26	Mon 6/22/26	-10d	Tue 7/28/26	Tue 8/11/26	-10d
104	Overhead M/E/P 2nd Fl	15 days	15 days	0d	Fri 5/8/26	Fri 5/22/26	-10d	Fri 5/29/26	Fri 6/12/26	-10d
105	Unit Partitions / Hallway System & Doors 2nd Floor	20 days	20 days	0d	Mon 6/1/26	Mon 6/15/26	-10d	Fri 6/26/26	Tue 7/14/26	-12d
106	Finish Electrical 2nd Fl	10 days	10 days	0d	Mon 6/29/26	Wed 7/15/26	-12d	Tue 7/14/26	Tue 7/28/26	-10d
107	Overhead M/E/P 3rd Fl	15 days	15 days	0d	Mon 6/1/26	Mon 6/15/26	-10d	Fri 6/19/26	Tue 7/7/26	-12d
108	Unit partitions /Hallway System & Doors 3rd Floor	20 days	20 days	0d	Mon 6/29/26	Wed 7/15/26	-12d	Tue 7/28/26	Tue 8/11/26	-10d
109	Finish Electrical 3rd Fl	10 days	10 days	0d	Wed 7/29/26	Wed 8/12/26	-10d	Tue 8/11/26	Tue 8/25/26	-10d
110	Overhead M/E/P 4th Fl	15 days	15 days	0d	Fri 6/26/26	Tue 7/14/26	-12d	Mon 7/20/26	Mon 8/3/26	-10d
111	Unit Partitions /Hallway System & Doors 4th Floor	20 days	20 days	0d	Wed 7/29/26	Wed 8/12/26	-10d	Tue 8/25/26	Wed 9/9/26	-11d
112	Finish Electrical 4th Fl	5 days	5 days	0d	Wed 8/26/26	Thu 9/10/26	-11d	Tue 9/1/26	Wed 9/16/26	-11d
113	Overhead M/E/P 5th Fl	15 days	15 days	0d	Wed 7/29/26	Wed 8/12/26	-10d	Tue 8/18/26	Tue 9/1/26	-10d
114	Unit Partitions & Hallway System & Doors 5th Floor	20 days	20 days	0d	Wed 8/26/26	Thu 9/10/26	-11d	Wed 9/23/26	Wed 10/7/26	-10d

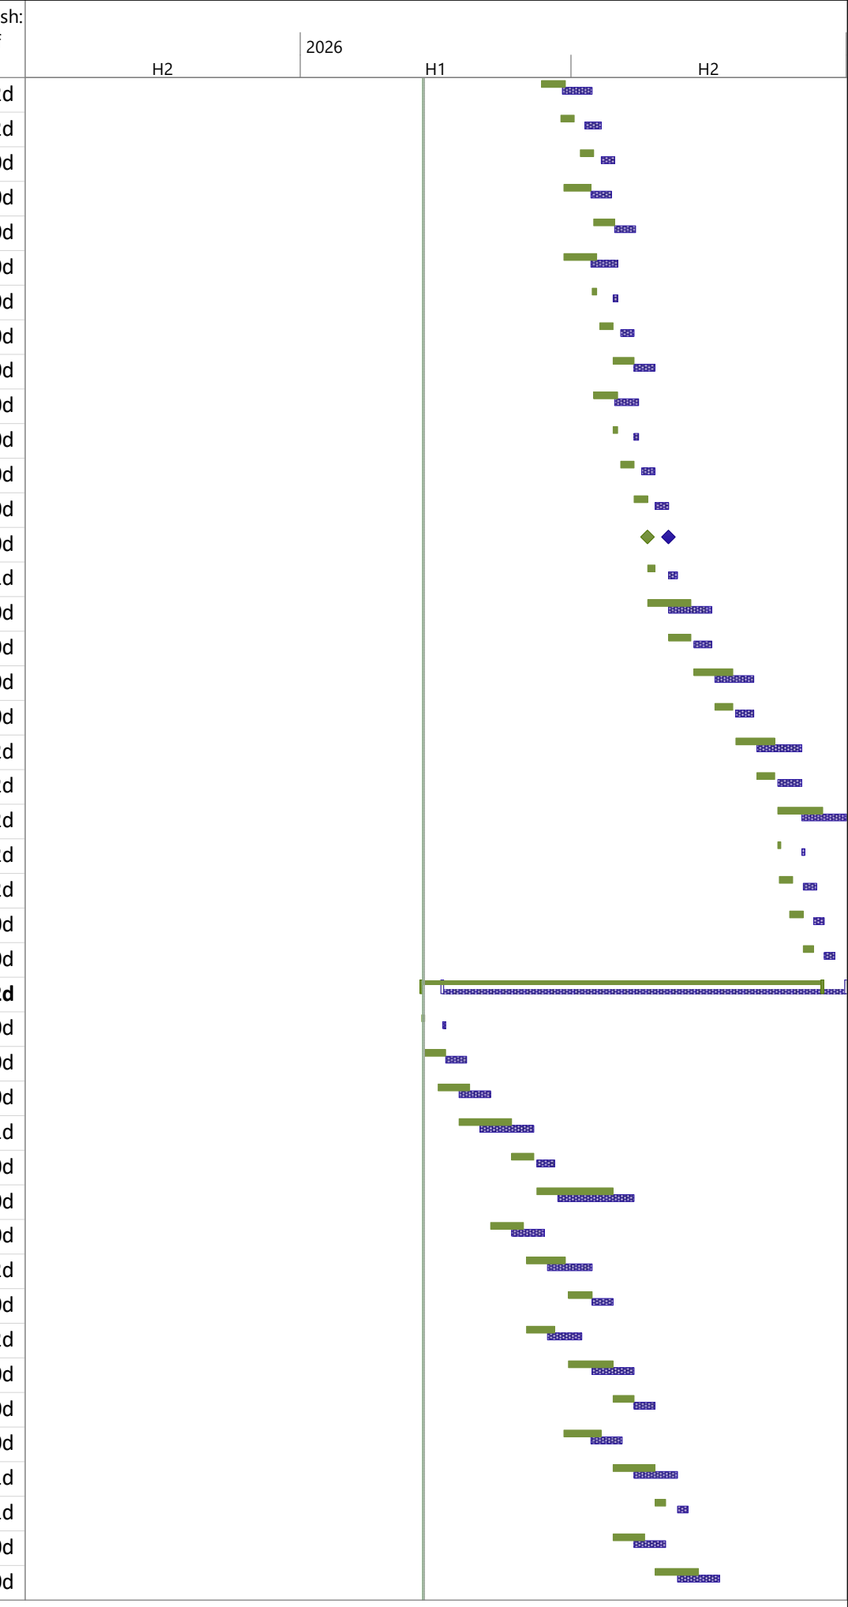
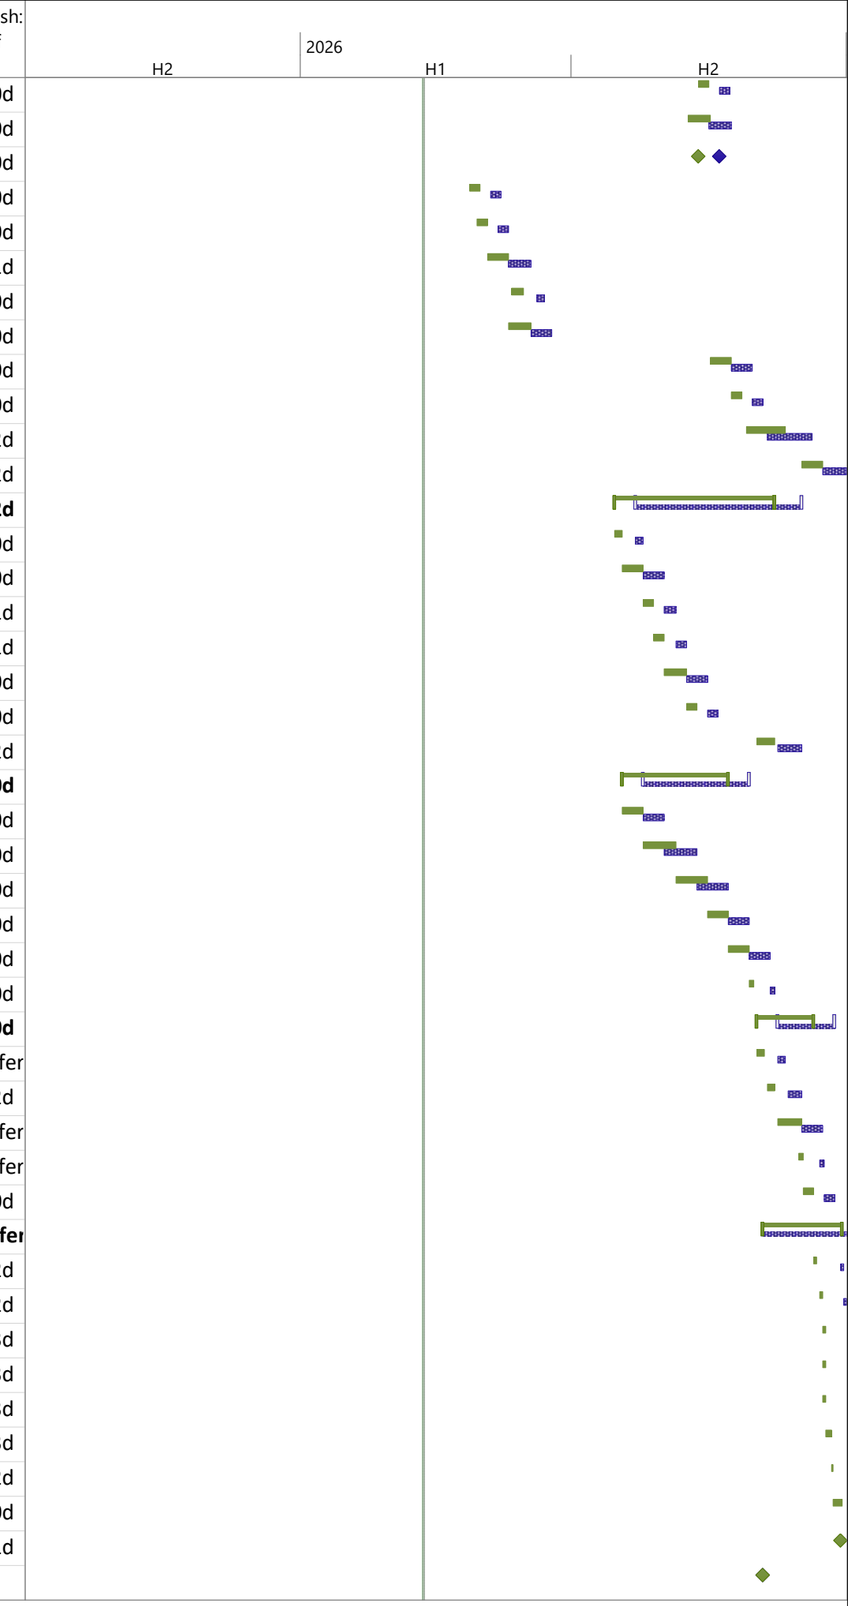
	Name	Duration Current	Duration Previous	Dur Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
115	Hallway Systems after Scaffold Removal	5 days	5 days	0d	Thu 9/24/26	Thu 10/8/26	-10d	Wed 9/30/26	Wed 10/14/26	-10d
116	Finish Electrical 5th Fl & Roof Equipment	11 days	11 days	0d	Thu 9/17/26	Thu 10/1/26	-10d	Thu 10/1/26	Thu 10/15/26	-10d
117	Overhead Doors, Liner & Demising Panels Comp.	0 days	0 days	0d	Wed 9/23/26	Wed 10/7/26	-10d	Wed 9/23/26	Wed 10/7/26	-10d
118	Elev. Lobby Framing	5 days	5 days	0d	Fri 4/24/26	Fri 5/8/26	-10d	Thu 4/30/26	Thu 5/14/26	-10d
119	Elev. Lobby M/E/P Rough in	5 days	5 days	0d	Wed 4/29/26	Wed 5/13/26	-10d	Tue 5/5/26	Tue 5/19/26	-10d
120	Elev. Lobby Drywall	10 days	10 days	0d	Wed 5/6/26	Wed 5/20/26	-10d	Tue 5/19/26	Wed 6/3/26	-11d
121	Install HM Doors & Hardware	5 days	5 days	0d	Fri 5/22/26	Mon 6/8/26	-11d	Fri 5/29/26	Fri 6/12/26	-10d
122	Lobby Fixtures & Finishes	10 days	10 days	0d	Wed 5/20/26	Thu 6/4/26	-11d	Wed 6/3/26	Wed 6/17/26	-10d
123	Finish Painting in Storage areas	10 days	10 days	0d	Fri 10/2/26	Fri 10/16/26	-10d	Thu 10/15/26	Thu 10/29/26	-10d
124	Building Signage per plan	5 days	5 days	0d	Fri 10/16/26	Fri 10/30/26	-10d	Thu 10/22/26	Thu 11/5/26	-10d
125	Final Clean up & Seal floors	20 days	20 days	0d	Mon 10/26/26	Mon 11/9/26	-10d	Fri 11/20/26	Tue 12/8/26	-12d
126	Owner Arch. Punch list & Completion	10 days	10 days	0d	Wed 12/2/26	Wed 12/16/26	-10d	Tue 12/15/26	Thu 12/31/26	-12d
127	**Building Exterior**	**76 days**	**76 days**	**0d**	**Thu 7/30/26**	**Thu 8/13/26**	**-10d**	**Fri 11/13/26**	**Tue 12/1/26**	**-12d**
128	Install Scaffolding at Building Perimeter	3 days	3 days	0d	Thu 7/30/26	Thu 8/13/26	-10d	Mon 8/3/26	Mon 8/17/26	-10d
129	Exterior Metal Frame Sheathing & WRB @ Tower	10 days	10 days	0d	Tue 8/4/26	Tue 8/18/26	-10d	Mon 8/17/26	Mon 8/31/26	-10d
130	Metal Panel Siding @ Tower	5 days	5 days	0d	Tue 8/18/26	Tue 9/1/26	-10d	Mon 8/24/26	Tue 9/8/26	-11d
131	Storefront/Curtainwall	5 days	5 days	0d	Tue 8/25/26	Wed 9/9/26	-11d	Mon 8/31/26	Tue 9/15/26	-11d
132	Glass Lead Time	10 days	10 days	0d	Tue 9/1/26	Wed 9/16/26	-11d	Tue 9/15/26	Tue 9/29/26	-10d
133	Install Glass	5 days	5 days	0d	Wed 9/16/26	Wed 9/30/26	-10d	Tue 9/22/26	Tue 10/6/26	-10d
134	Install Auto Sliders & Mapes Canopy	10 days	10 days	0d	Mon 11/2/26	Mon 11/16/26	-10d	Fri 11/13/26	Tue 12/1/26	-12d
135	**EIFS WRB, Foam/Brown & Finish**	**50 days**	**50 days**	**0d**	**Tue 8/4/26**	**Tue 8/18/26**	**-10d**	**Tue 10/13/26**	**Tue 10/27/26**	**-10d**
136	Waterproof Membrane	10 days	10 days	0d	Tue 8/4/26	Tue 8/18/26	-10d	Mon 8/17/26	Mon 8/31/26	-10d
137	EIFS Foam	15 days	15 days	0d	Tue 8/18/26	Tue 9/1/26	-10d	Tue 9/8/26	Tue 9/22/26	-10d
138	EIFS Mesh Coat	15 days	15 days	0d	Wed 9/9/26	Wed 9/23/26	-10d	Tue 9/29/26	Tue 10/13/26	-10d
139	EIFS Top Coat	10 days	10 days	0d	Wed 9/30/26	Wed 10/14/26	-10d	Tue 10/13/26	Tue 10/27/26	-10d
140	Exterior Sheet metal, Sealants, & Painting	10 days	10 days	0d	Wed 10/14/26	Wed 10/28/26	-10d	Tue 10/27/26	Tue 11/10/26	-10d
141	Remove Scaffolding	3 days	3 days	0d	Wed 10/28/26	Wed 11/11/26	-10d	Fri 10/30/26	Fri 11/13/26	-10d
142	**Onsite improvements**	**26 days**	**26 days**	**0d**	**Mon 11/2/26**	**Mon 11/16/26**	**-10d**	**Wed 12/9/26**	**Wed 12/23/26**	**-10d**
143	Grade & Pour Walks	5 days	5 days	Equ	Mon 11/2/26	Mon 11/16/26	Differ	Fri 11/6/26	Fri 11/20/26	Differ
144	Site Fencing & Gates	5 days	5 days	0d	Mon 11/9/26	Mon 11/23/26	-10d	Fri 11/13/26	Tue 12/1/26	-12d
145	Landscape Irrigation and Planting	10 days	10 days	Equ	Mon 11/16/26	Wed 12/2/26	Differ	Tue 12/1/26	Tue 12/15/26	Differ
146	Striping & Signage	3 days	3 days	Equ	Mon 11/30/26	Mon 12/14/26	Differ	Wed 12/2/26	Wed 12/16/26	Differ
147	Owner Civil Punch list & Completion	5 days	5 days	0d	Thu 12/3/26	Thu 12/17/26	-10d	Wed 12/9/26	Wed 12/23/26	-10d
148	**Accumulative Inspections & C of O**	**33 days**	**42 days**	**Dif**	**Fri 11/6/26**	**Fri 11/6/26**	**Equal**	**Mon 12/28/26**	**Mon 1/11/27**	**Differ**
149	Final Grading Inspections	2 days	2 days	0d	Thu 12/10/26	Mon 12/28/26	-12d	Fri 12/11/26	Tue 12/29/26	-12d
150	Final Public Works Inspections	2 days	2 days	0d	Mon 12/14/26	Wed 12/30/26	-12d	Tue 12/15/26	Thu 12/31/26	-12d
151	Life Safety Inspection	2 days	2 days	0d	Wed 12/16/26	Mon 1/4/27	-13d	Thu 12/17/26	Tue 1/5/27	-13d
152	MEP Final Inspections	2 days	2 days	0d	Wed 12/16/26	Mon 1/4/27	-13d	Thu 12/17/26	Tue 1/5/27	-13d
153	Final Planning & Zoning Inspection	2 days	2 days	0d	Wed 12/16/26	Mon 1/4/27	-13d	Thu 12/17/26	Tue 1/5/27	-13d
154	Building Final Inspection	2 days	2 days	0d	Fri 12/18/26	Wed 1/6/27	-13d	Mon 12/21/26	Thu 1/7/27	-13d
155	Rain Days Included - Used as of 1/6/26	1 day	0 days	1d	Tue 12/22/26	Thu 1/7/27	-13d	Tue 12/22/26	Thu 1/7/27	-12d
156	Certificate Of Occupancy	2 days	2 days	0d	Wed 12/23/26	Fri 1/8/27	-12d	Mon 12/28/26	Mon 1/11/27	-10d
157	Open Date - Approved with Delay #2	0 days	0 days	0d	Mon 12/28/26	Mon 1/11/27	-11d	Mon 12/28/26	Mon 1/11/27	-11d
158	Original Contracted Open Date	0 days	0 days	0d	Fri 11/6/26	Fri 11/6/26	0d	Fri 11/6/26	Fri 11/6/26	0d
