ID	Task Mode	Task Name	Duration	Start	Finish
0		**Public Storage HQ**	**187 days**	**Mon 25/09/08**	**Mon 26/06/01**
1		**Construction Documents**	**50 days**	**Mon 25/09/08**	**Fri 25/11/14**
2		CD Kick off and Start	34 days	Mon 25/09/08	Thu 25/10/23
3		65% progress set	1 day	Fri 25/10/24	Fri 25/10/24
4		Owner Drawing review Of 65% set	5 days	Mon 25/10/27	Fri 25/10/31
5		Completon of Bid, Demo and Permit Submital set	10 days	Mon 25/11/03	Fri 25/11/14
6		**Plan Check**	**29 days**	**Mon 25/11/17**	**Mon 25/12/29**
7		**Issue for Interiors Permit (Plan Check)**	**29 days**	**Mon 25/11/17**	**Mon 25/12/29**
8		City Permit Review	15 days	Mon 25/11/17	Fri 25/12/05
9		Drawing Coordination/City Comments	13 days	Mon 25/12/08	Wed 25/12/24
10		Receive interior TI Building Permit	1 day	Mon 25/12/29	Mon 25/12/29
11		**Issue for Demo Permit**	**16 days**	**Mon 25/11/17**	**Mon 25/12/08**
12		Demo Permit Review	15 days	Mon 25/11/17	Fri 25/12/05
13		Receive Demo Permit	1 day	Mon 25/12/08	Mon 25/12/08
14		**Bidding**	**19 days**	**Mon 25/11/17**	**Thu 25/12/11**
15		Bidding for TI GCs	15 days	Mon 25/11/17	Fri 25/12/05
16		Award GC Contract	4 days	Mon 25/12/08	Thu 25/12/11
17		**Contracting**	**16 days**	**Fri 25/12/12**	**Thu 26/01/08**
18		Execute Demo LOA	1 day	Fri 25/12/12	Fri 25/12/12
19		Contract Preparation	5 days	Mon 25/12/15	Fri 25/12/19
20		Contract Negotiation	5 days	Mon 25/12/22	Tue 25/12/30
21		Contract Execution	5 days	Fri 26/01/02	Thu 26/01/08
22		**ARCO Procurement**	**69 days**	**Fri 26/01/09**	**Wed 26/04/15**
23		Submittal Approval	2 wks	Fri 26/01/09	Thu 26/01/22
24		Light Fixtures	8 wks	Fri 26/01/23	Thu 26/03/19
25		Millwork Shop Drawings	2,2 wks	Fri 26/01/23	Fri 26/02/06
26		Millwork Field Measure and Fab	6 wks	Thu 26/03/05	Wed 26/04/15
27		Flooring - Tile and Carpet	6 wks	Fri 26/01/23	Thu 26/03/05
28		Frames	6 wks	Fri 26/01/23	Thu 26/03/05
29		Doors, Hardware	8 wks	Fri 26/01/23	Thu 26/03/19
30		Appliances	8 wks	Fri 26/01/23	Thu 26/03/19
31		Ceiling Baffles	10 wks	Fri 26/01/23	Thu 26/04/02
32		**Procurement Of Direct FBO items**	**136 days**	**Mon 25/09/08**	**Fri 26/03/20**
33		**Furniture**	**97 days**	**Fri 25/10/31**	**Fri 26/03/20**
34		Select Furniture Vendor	1 day	Fri 25/10/31	Fri 25/10/31
35		Review and finalize details for furniture	15 days	Mon 25/11/03	Fri 25/11/21
36		Furniture Order Due	1 day	Mon 25/11/24	Mon 25/11/24
37		Furniture Lead Time	80 days	Tue 25/11/25	Fri 26/03/20
38		**HVAC Equipment**	**71 days**	**Mon 25/10/27**	**Fri 26/02/06**
39		Order Roof Top HVAC equipment	1 day	Mon 25/10/27	Mon 25/10/27
40		HVAC Equipment Lead Time	70 days	Tue 25/10/28	Fri 26/02/06
41		**Elevator Modernization**	**123 days**	**Mon 25/09/08**	**Tue 26/03/03**
42		Contract for Elevator Modernization	1 day	Mon 25/09/08	Mon 25/09/08
43		Elevator Equipment Lead Time	97 days	Tue 25/09/09	Tue 26/01/27
44		Elevator Modernization	25 days	Wed 26/01/28	Tue 26/03/03
45		**Demolition**	**25 days**	**Mon 25/12/15**	**Thu 26/01/22**
46		MEP/F Make Safe	3 wks	Mon 25/12/15	Thu 26/01/08
47		Demolition	5 wks	Mon 25/12/15	Thu 26/01/22
48		Slab Demo and Coring	3 days	Tue 26/01/20	Thu 26/01/22
49		**Construction**	**101 days**	**Fri 26/01/09**	**Fri 26/05/29**
50		Overhead MEP Rough In	30 days	Fri 26/01/09	Thu 26/02/19
51		Low Voltage Bulk Cabling	20 days	Fri 26/01/30	Thu 26/02/26
52		Walls - Studs and Track	15 days	Fri 26/01/23	Thu 26/02/12
53		Underslab MEP	3 days	Fri 26/01/23	Tue 26/01/27
54		MEP Rough-in Walls	15 days	Fri 26/02/06	Thu 26/02/26
55		Single Side Drywall	7 days	Fri 26/02/13	Mon 26/02/23
56		Second Side Drywall	7 days	Tue 26/02/24	Wed 26/03/04
57		Wall Tape and Bed	12 days	Thu 26/03/05	Fri 26/03/20
58		Grid Install Rework	10 days	Mon 26/03/16	Fri 26/03/27

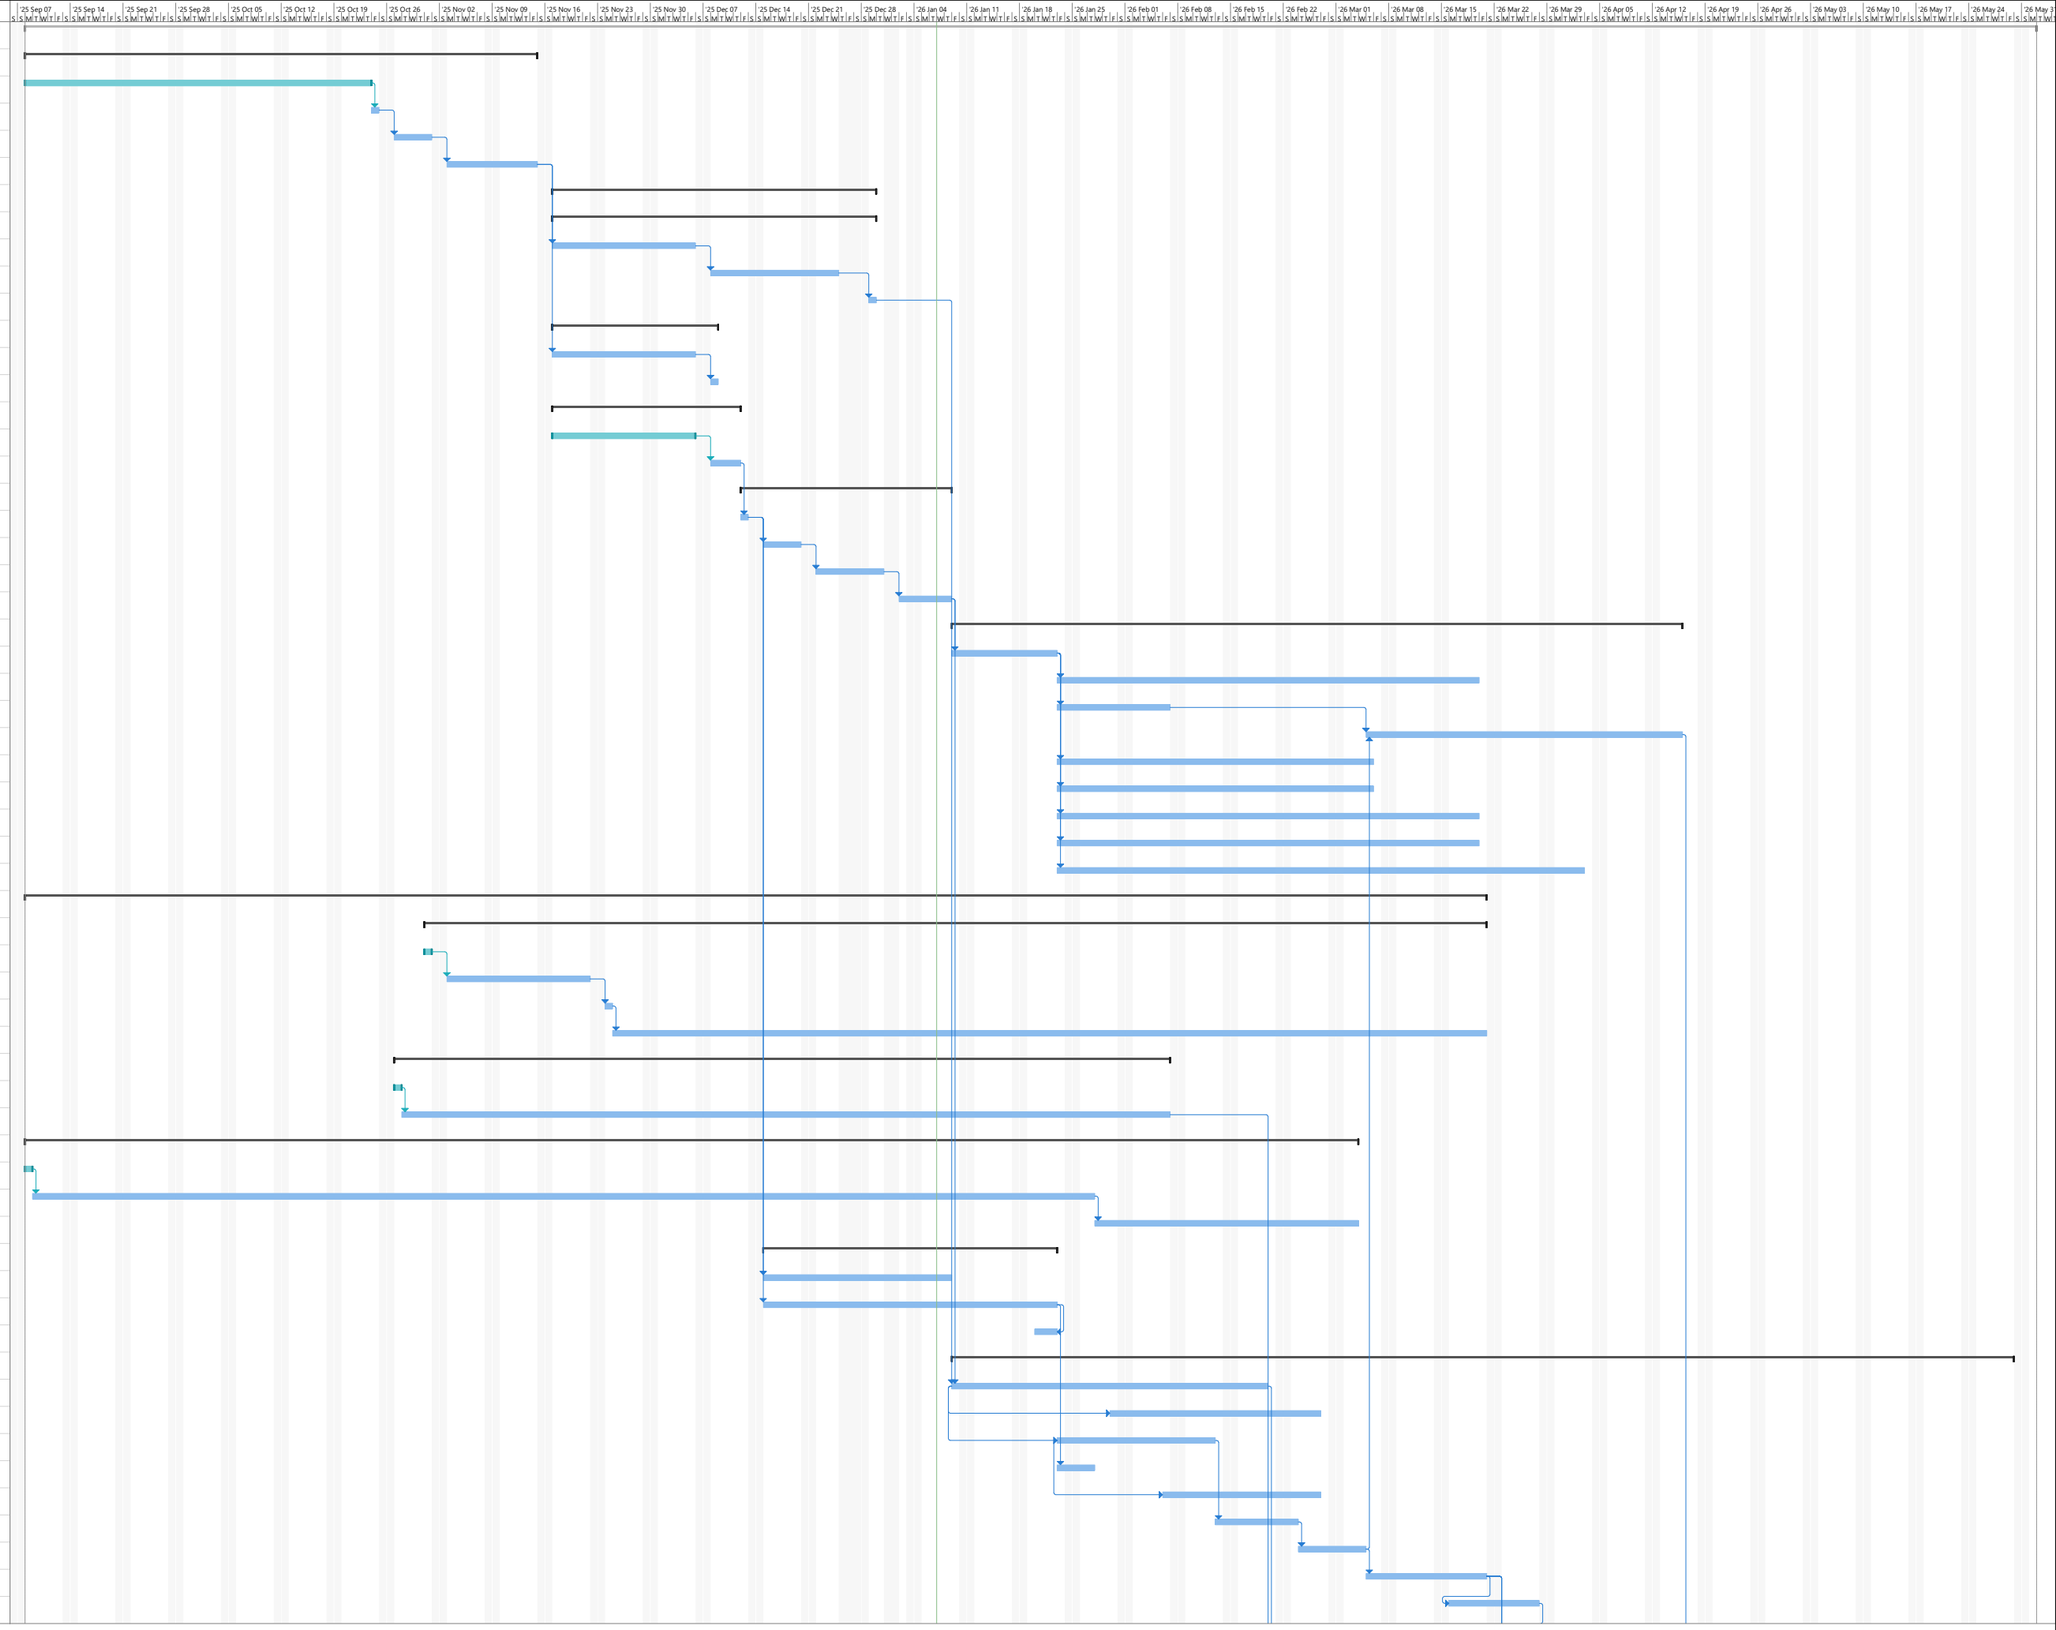
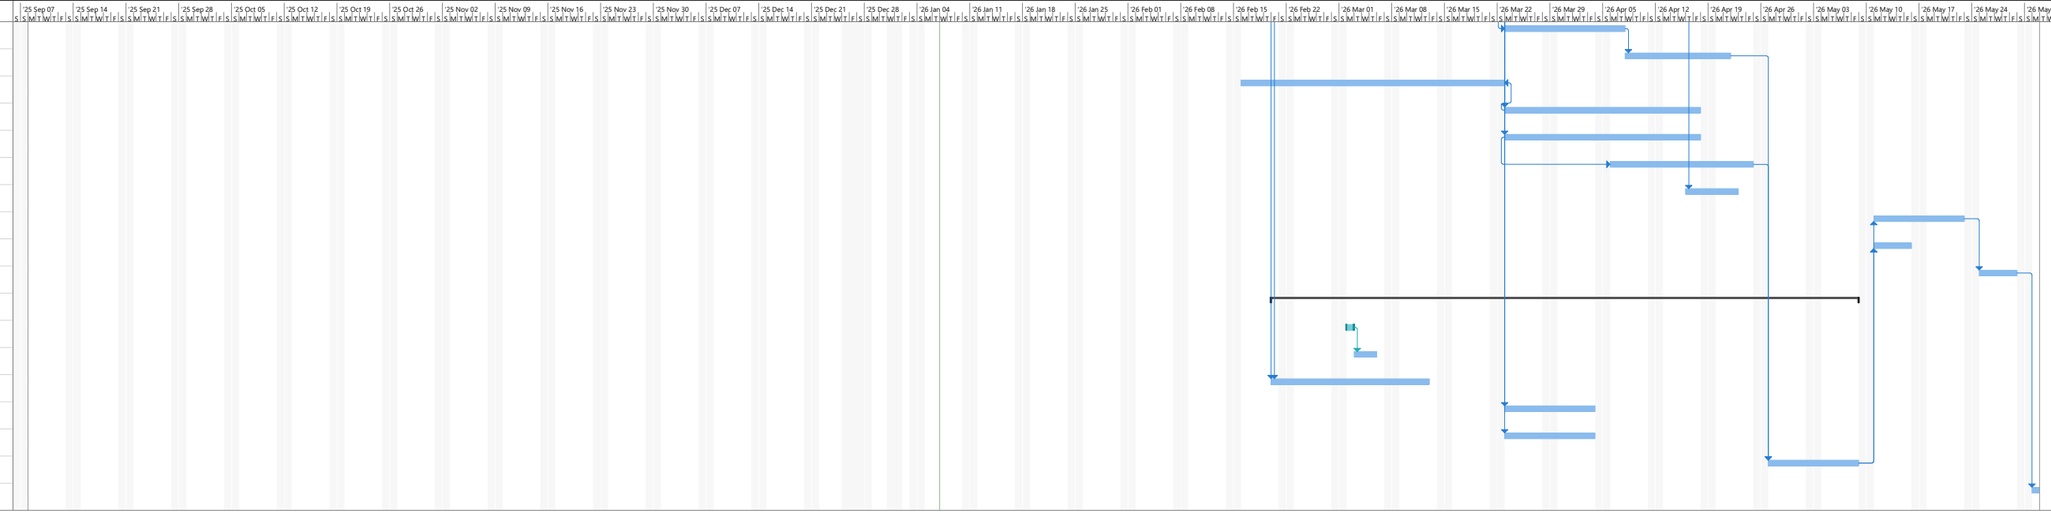
ID	Task Mode	Task Name	Duration	Start	Finish
59		Light Fixture Install and Ceiling MEP Finishes	12 days	Mon 26/03/23	Tue 26/04/07
60		Ceiling Tile Installation	10 days	Wed 26/04/08	Tue 26/04/21
61		Restroom Renovations	25 days	Mon 26/02/16	Mon 26/03/23
62		Carpet and Tile Prep and Install	20 days	Mon 26/03/23	Fri 26/04/17
63		Painting	20 days	Mon 26/03/23	Fri 26/04/17
64		MEP Trimout	15 days	Mon 26/04/06	Fri 26/04/24
65		Millwork Install	5 days	Thu 26/04/16	Wed 26/04/22
66		Inspections and Commissioning	10 days	Mon 26/05/11	Fri 26/05/22
67		Punch Walk and Corrections	5 days	Mon 26/05/11	Fri 26/05/15
68		Final Clean	5 days	Mon 26/05/25	Fri 26/05/29
69		**Install of Owner Provided Equipment/Vendors**	**56 days**	**Fri 26/02/20**	**Fri 26/05/08**
70		Confirm Weather For RTU Replacements	1 day	Mon 26/03/02	Mon 26/03/02
71		RTU Replacement	3 days	Tue 26/03/03	Thu 26/03/05
72		VAV Replacements	15 days	Fri 26/02/20	Thu 26/03/12
73		AV Equipment Installation	10 days	Mon 26/03/23	Fri 26/04/03
74		Security Systems Equipment Installation	10 days	Mon 26/03/23	Fri 26/04/03
75		Furniture Systems Installation	10 days	Mon 26/04/27	Fri 26/05/08
76		Move in	1 day	Mon 26/06/01	Mon 26/06/01
