Public Storage HQ - Project Orange
Preliminary Project Schedule
2811 Internet Blvd
Frisco, TX 75034

ID	Task Name	Duration	Start	Finish	Predecessors	Successors
0	**Public Storage HQ**	**188 da**	**Mon 25/09/**	**Tue 26/06/0**		
1	**Construction Documents**	**50 day**	**Mon 25/09/0**	**Fri 25/11/14**		
2	CD Kick off and Start	34 day	Mon 25/09/0	Thu 25/10/23		3
3	65% progress set	1 day	Fri 25/10/24	Fri 25/10/24	2	4
4	Owner Drawing review Of 65% set	5 days	Mon 25/10/2	Fri 25/10/31	3	5
5	Completon of Bid, Demo and Permit Submital set	10 days	Mon 25/11/03	Fri 25/11/14	4	8;12
6	**Plan Check**	**36 day**	**Mon 25/11/1**	**Fri 26/01/09**		
7	**Issue for Interiors Permit (Plan Check)**	**36 day**	**Mon 25/11/1**	**Fri 26/01/09**		
8	City Permit Review	15 day	Mon 25/11/1	Fri 25/12/05	5	9
9	Drawing Coordination/City Comments	20 day	Mon 25/12/0	Thu 26/01/08	8	10
10	Receive interior TI Building Permit	1 day	Fri 26/01/09	Fri 26/01/09	9	81;104;127;149
11	**Issue for Demo Permit**	**16 day**	**Mon 25/11/1**	**Mon 25/12/0**		
12	Demo Permit Review	15 day	Mon 25/11/1	Fri 25/12/05	5	13
13	Receive Demo Permit	1 day	Mon 25/12/0	Mon 25/12/0	12	
14	**Bidding**	**19 day**	**Mon 25/11/1**	**Thu 25/12/1**		
15	Bidding for TI GCs	15 day	Mon 25/11/1	Fri 25/12/05		16
16	Award GC Contract	4 days	Mon 25/12/0	Thu 25/12/11	15	18
17	**Contracting**	**16 day**	**Fri 25/12/12**	**Thu 26/01/0**		
18	Execute Demo LOA	1 day	Fri 25/12/12	Fri 25/12/12	16	77;19;78
19	Contract Preparation	5 days	Mon 25/12/1	Fri 25/12/19	18	20
20	Contract Negotiation	5 days	Mon 25/12/2	Tue 25/12/30	19	21
21	Contract Execution	5 days	Fri 26/01/02	Thu 26/01/08	20	81;23;104;127;14
22	**ARCO Procurement**	**79 day**	**Fri 26/01/09**	**Wed 26/04/2**		
23	Submittal Approval - MEPs	2 wks	Fri 26/01/09	Thu 26/01/22	21	24;25;58;59;60;61
24	Light Fixtures	9 wks	Fri 26/01/23	Thu 26/03/26	23	95;118;140;162
25	Millwork Shop Drawings	2 wks	Fri 26/01/23	Thu 26/02/05	23	26;27;28;29
26	Millwork Field Measure and Fab - Level 1 So	6 wks	Mon 26/02/1	Fri 26/03/27	92;25	102;125;147;169
27	Millwork Field Measure and Fab - Level 1 Nc	6 wks	Thu 26/03/19	Wed 26/04/2	25;115	125;147;169
28	Millwork Field Measure and Fab - Level 2 So	6 wks	Mon 26/03/0	Fri 26/04/17	25;137	125;147;169
29	Millwork Field Measure and Fab - Level 2 Nc	6 wks	Fri 26/03/13	Thu 26/04/23	25;159	125;147;169
30	Flooring - FC1 Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	44
31	Flooring - FC2 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	45
32	Flooring - FC3 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	46
33	Flooring - FC4 -Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	47
34	Flooring - FC5 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	48
35	Flooring - FC7 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	49
36	Flooring - LVT1 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	50

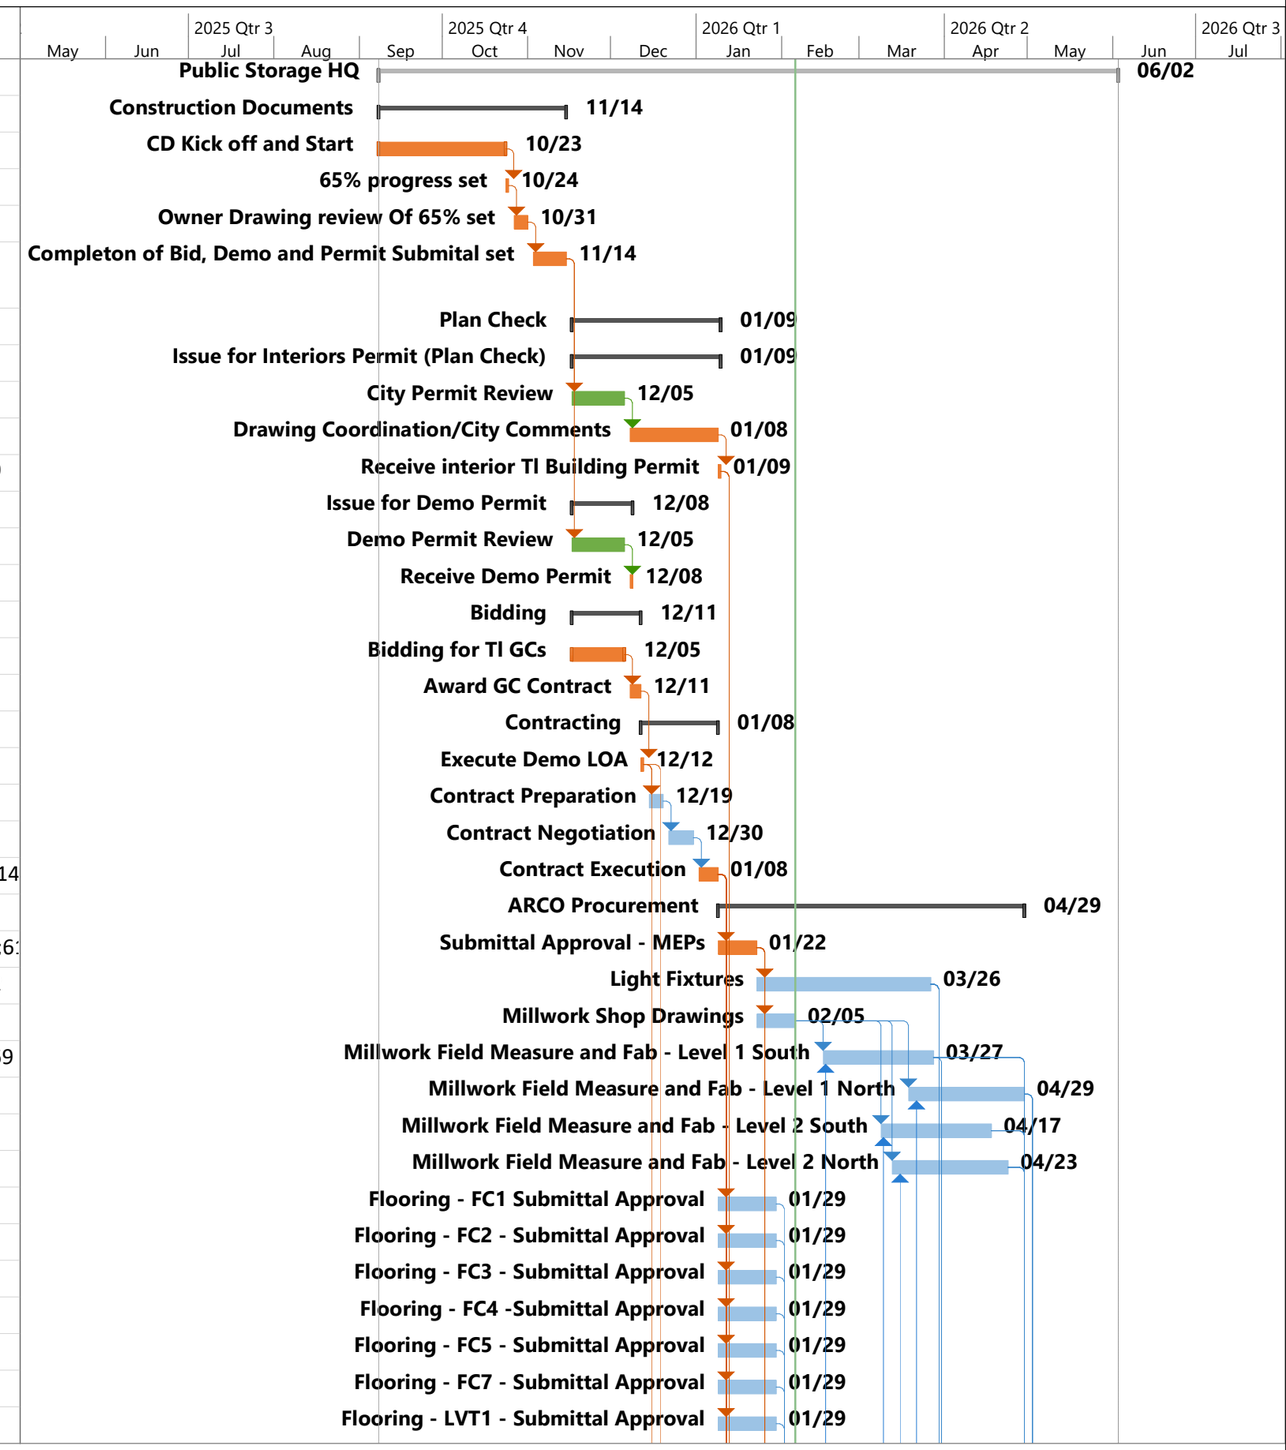

Public Storage HQ - Project Orange
Preliminary Project Schedule
2811 Internet Blvd
Frisco, TX 75034

ID	Task Mode	Task Name	Duratio	Start	Finish	Predecessors	Successors
37		Flooring - VCT1 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	51
38		Flooring - FT1 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	52
39		Flooring - FT2 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	53
40		Wall Tile - WT1 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	54
41		Wall Tile - WT2 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	55
42		Wall Tile - WT3 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	56
43		Wall Tile - WT4 - Submittal Approval	3 wks	Fri 26/01/09	Thu 26/01/29	21	57
44		Flooring - FC1	6 wks	Fri 26/01/30	Thu 26/03/12	30	99;122;144;166
45		Flooring - FC2	6 wks	Fri 26/01/30	Thu 26/03/12	31	99;122;144;166
46		Flooring - FC3	6 wks	Fri 26/01/30	Thu 26/03/12	32	99;122;144;166
47		Flooring - FC4	6 wks	Fri 26/01/30	Thu 26/03/12	33	99;122;144;166
48		Flooring - FC5	6 wks	Fri 26/01/30	Thu 26/03/12	34	99;122;144;166
49		Flooring - FC7	6 wks	Fri 26/01/30	Thu 26/03/12	35	99;122;144;166
50		Flooring - LVT1	6 wks	Fri 26/01/30	Thu 26/03/12	36	99;122;144;166
51		Flooring - VCT1	6 wks	Fri 26/01/30	Thu 26/03/12	37	99;122;144;166
52		Flooring - FT1	3 wks	Fri 26/01/30	Thu 26/02/19	38	99;122;144;166
53		Flooring - FT2	6 wks	Fri 26/01/30	Thu 26/03/12	39	99;122;144;166
54		Wall Tile - WT1	2 wks	Fri 26/01/30	Thu 26/02/12	40	99;122;144;166
55		Wall Tile - WT2	2 wks	Fri 26/01/30	Thu 26/02/12	41	99;122;144;166
56		Wall Tile - WT3	4 wks	Fri 26/01/30	Thu 26/02/26	42	99;98FF;121FF;12
57		Wall Tile - WT4	2 wks	Fri 26/01/30	Thu 26/02/12	43	99;98FF;121FF;12
58		Door Frames	6 wks	Fri 26/01/23	Thu 26/03/05	23	116;138;160
59		Doors, Hardware	8 wks	Fri 26/01/23	Thu 26/03/19	23	170
60		Appliances	8 wks	Fri 26/01/23	Thu 26/03/19	23	170
61		Ceiling Baffles - Breakroom	10 wks	Fri 26/01/23	Thu 26/04/02	23	
62		**Procurement Of Direct FBO items**	**103 da**	**Fri 25/10/31**	**Mon 26/03/3**		
63		**Furniture**	**97 day**	**Fri 25/10/31**	**Fri 26/03/20**		
64		Select Furniture Vendor	1 day	Fri 25/10/31	Fri 25/10/31		65
65		Review and finalize details for furniture	15 day	Mon 25/11/0	Fri 25/11/21	64	66
66		Furniture Order Due	1 day	Mon 25/11/2	Mon 25/11/2	65	67
67		Furniture Lead Time	80 day	Tue 25/11/25	Fri 26/03/20	66	182
68		**HVAC Equipment**	**58 day**	**Mon 25/12/(**	**Tue 26/03/03**		
69		Order Roof Top HVAC equipment	1 day	Mon 25/12/0	Mon 25/12/0		70;71
70		HVAC Equipment Lead Time - RTUs	50 day	Wed 25/12/1	Mon 26/03/0	69	175
71		HVAC Equipment Lead Time - VAVs	57 day	Tue 25/12/09	Tue 26/03/03	69	176;177;179;178
72		**Elevator Modernization**	**56 day**	**Mon 26/01/1**	**Mon 26/03/3**		
73		Contract for Elevator Modernization	1 day	Mon 26/01/1	Mon 26/01/1		74
74		Elevator Equipment Lead Time	30 day	Tue 26/01/13	Mon 26/02/2	73	75

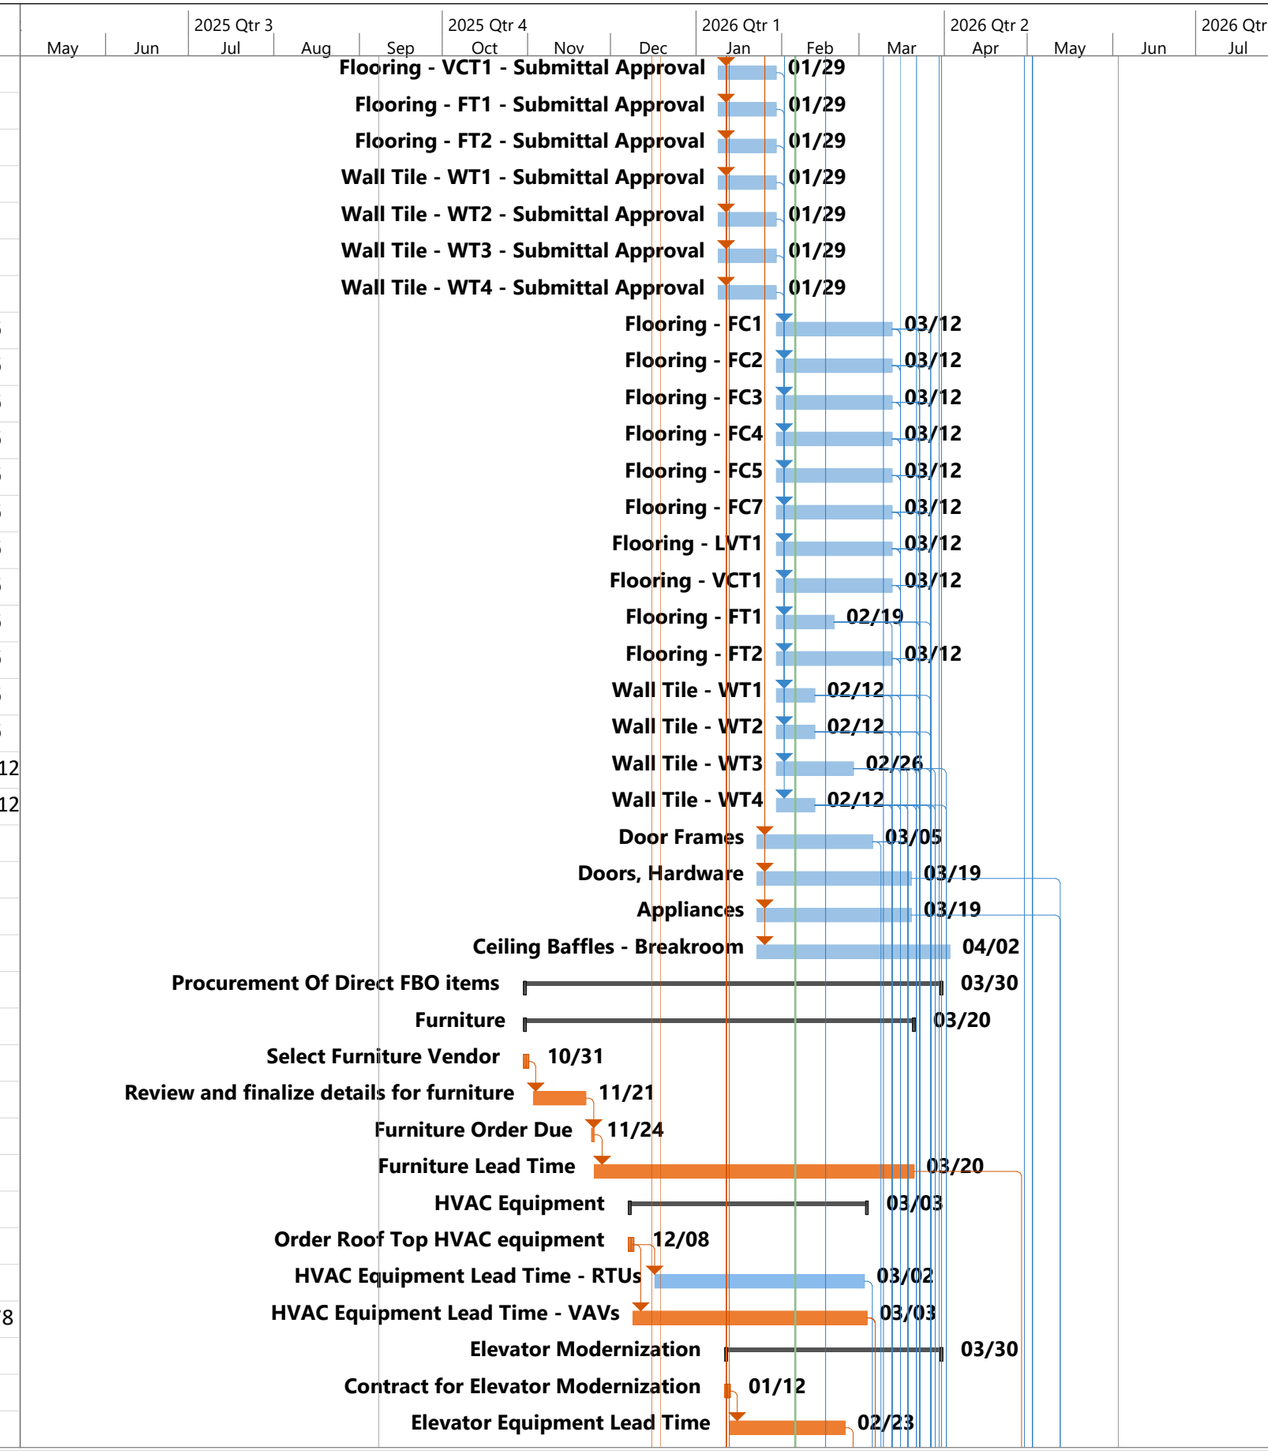

Public Storage HQ - Project Orange
Preliminary Project Schedule
2811 Internet Blvd
Frisco, TX 75034

ID	Task Mode	Task Name	Duratio	Start	Finish	Predecessors	Successors
75		Elevator Modernization	25 day	Tue 26/02/2	Mon 26/03/3	74	170
76		**Demolition**	**29 day**	**Mon 25/12/1**	**Wed 26/01/2**		
77		MEP/F Make Safe	3 wks	Mon 25/12/1	Thu 26/01/08	18	
78		Demolition	5 wks	Fri 25/12/19	Wed 26/01/2	18	83SS
79		**Construction**	**101 da**	**Mon 26/01/1**	**Mon 26/06/0**		
80		**Level 1 South**	**70 day**	**Mon 26/01/1**	**Fri 26/04/17**		
81		Overhead MEP Rough In	30 day	Mon 26/01/1	Fri 26/02/20	21;10	84SS;82SS+3 wks;
82		Low Voltage Bulk Cabling	20 day	Mon 26/02/0	Fri 26/02/27	81SS+3 wks	180;181
83		Slab Demo and Coring	4 days	Tue 26/01/2	Fri 26/01/23	78SS	85;106
84		Walls - Studs and Track	4 days	Thu 26/01/2	Tue 26/01/27	81SS	89SS+1 day;91;13
85		Underslab MEP	6 days	Mon 26/01/2	Mon 26/02/0	83	86
86		Underslab MEP Inspection	1 day	Tue 26/02/0	Tue 26/02/0	85	87
87		Concrete Slab Pourback	2 days	Wed 26/02/0	Thu 26/02/05	86	99
88		Fire Alarm Rough-in	2 days	Wed 26/01/2	Thu 26/01/2	84	170
89		MEP Rough-in Walls	10 day	Fri 26/01/23	Thu 26/02/05	84SS+1 day	92FF;90
90		MEP Rough-in Inspection	1 day	Fri 26/02/06	Fri 26/02/06	89	92
91		Single Side Drywall	5 days	Wed 26/01/2	Tue 26/02/0	84	92
92		Second Side Drywall	5 days	Mon 26/02/0	Fri 26/02/13	91;89FF;90	93SS+2 days;26
93		Wall Tape and Bed	6 days	Wed 26/02/1	Wed 26/02/1	92SS+2 days	180;181;100;99;9
94		Grid Install Rework	6 days	Wed 26/03/1	Wed 26/03/19	93FS-1 wk;176	95FS-1 wk
95		Light Fixture Install and Ceiling MEP Finish	8 days	Fri 26/03/27	Tue 26/04/07	94FS-1 wk;24	96;119;141;163
96		Ceiling Cover Inspection	1 day	Wed 26/04/0	Wed 26/04/0	95	97
97		Ceiling Tile Installation	3 days	Wed 26/04/1	Fri 26/04/17	96;119;141;163	182
98		Restroom Renovations	10 day	Fri 26/02/27	Fri 26/03/13	99SF;56FF;57FF	101
99		Carpet and Tile Prep and Install	8 days	Fri 26/03/13	Tue 26/03/2	93;44;45;46;47;48;4	98SF;182
100		Painting	10 day	Thu 26/02/19	Wed 26/03/0	93	101SS+2 wks
101		MEP Trimout	10 day	Fri 26/03/13	Thu 26/03/26	100SS+2 wks;98	172
102		Millwork Install	5 days	Mon 26/03/3	Fri 26/04/03	26	
103		**Level 1 North**	**83 day**	**Mon 26/01/1**	**Wed 26/05/0**		
104		Overhead MEP Rough In	30 day	Mon 26/01/1	Fri 26/02/20	21;10	105SS+3 wks;177
105		Low Voltage Bulk Cabling	20 day	Mon 26/02/0	Fri 26/02/27	104SS+3 wks	180;181
106		Slab Demo and Coring	3 days	Mon 26/01/2	Wed 26/01/2	83	108;129
107		Walls - Studs and Track	3 days	Mon 26/02/0	Wed 26/02/1	152	112SS+2 wks;114,
108		Underslab MEP	3 days	Thu 26/01/29	Mon 26/02/0	106	109
109		Underslab MEP Inspection	1 day	Tue 26/02/0	Tue 26/02/0	108	110
110		Concrete Slab Pourback	4 days	Wed 26/02/0	Mon 26/02/0	109	122
111		Fire Alarm Rough-in	2 days	Thu 26/02/1	Fri 26/02/13	107	170
112		MEP Rough-in Walls	10 day	Mon 26/02/2	Fri 26/03/06	107SS+2 wks	115FF;113

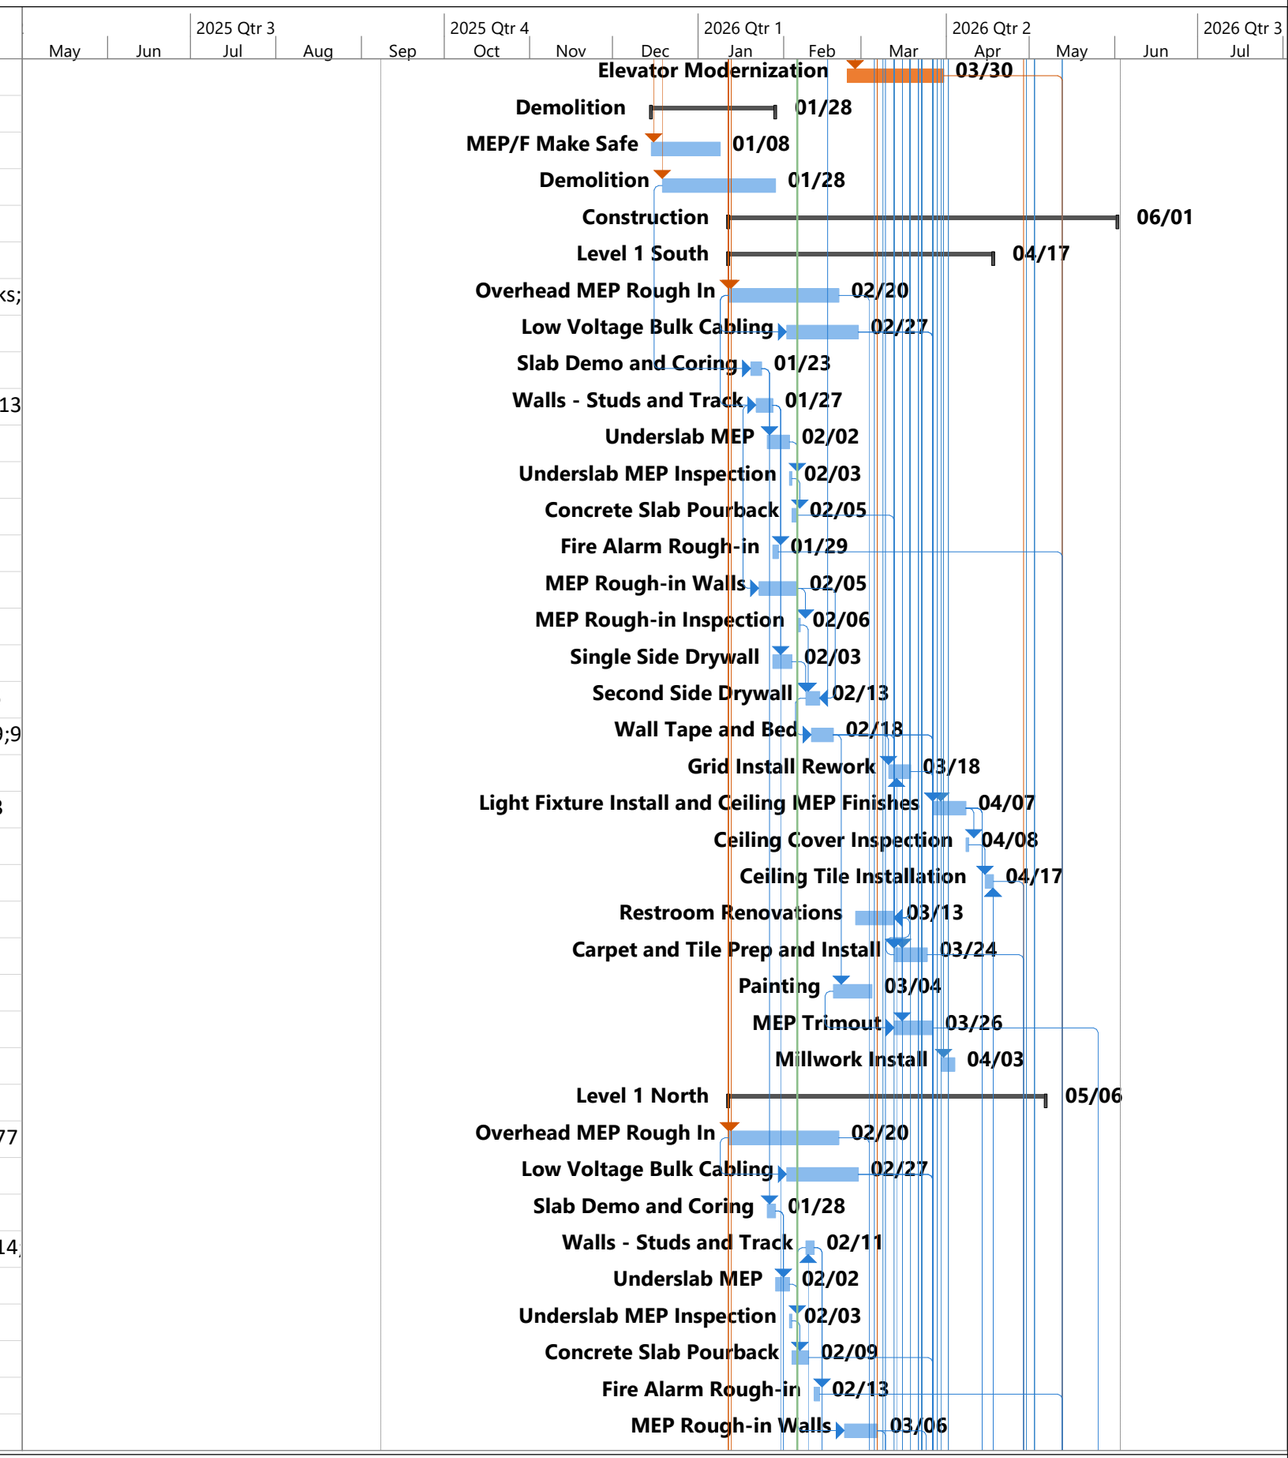

ID	Task Mode	Task Name	Duratio	Start	Finish	Predecessors	Successors
113		MEP Rough-in Inspection	1 day	Mon 26/03/0	Mon 26/03/0	112	115
114		Single Side Drywall	7 days	Thu 26/02/12	Fri 26/02/20	107	115
115		Second Side Drywall	7 days	Tue 26/03/10	Wed 26/03/1	112FF;114;113	116;27
116		Wall Tape and Bed	6 days	Thu 26/03/19	Thu 26/03/26	115;58	180;181;123;122;
117		Grid Install Rework	4 days	Fri 26/03/20	Wed 26/03/2	116FS-1 wk;177	118FS-1 wk
118		Light Fixture Install and Ceiling MEP Finish	12 day	Fri 26/03/27	Mon 26/04/1	117FS-1 wk;24	119
119		Ceiling Cover Inspection	1 day	Tue 26/04/14	Tue 26/04/14	95;118	97;120
120		Ceiling Tile Installation	10 day	Wed 26/04/1	Tue 26/04/28	119	182
121		Restroom Renovations	10 day	Fri 26/03/13	Fri 26/03/27	122SF;56FF;57FF	124
122		Carpet and Tile Prep and Install	8 days	Fri 26/03/27	Tue 26/04/07	116;44;45;46;47;48	121SF;182
123		Painting	10 day	Fri 26/03/27	Thu 26/04/09	116	124SS+2 wks
124		MEP Trimout	10 day	Fri 26/04/10	Thu 26/04/23	121;123SS+2 wks	172
125		Millwork Install	5 days	Thu 26/04/30	Wed 26/05/0	26;27;28;29	170
126		**Level 2 South**	**83 day**	**Mon 26/01/1**	**Wed 26/05/0**		
127		Overhead MEP Rough In	30 day	Mon 26/01/1	Fri 26/02/20	21;10	128SS+3 wks;178
128		Low Voltage Bulk Cabling	20 day	Mon 26/02/0	Fri 26/02/27	127SS+3 wks	180;181
129		Slab Demo and Coring	2 days	Thu 26/01/29	Fri 26/01/30	106	131;151
130		Walls - Studs and Track	4 days	Wed 26/01/2	Mon 26/02/0	84	134SS+2 wks;136
131		Underslab MEP	3 days	Mon 26/02/0	Wed 26/02/0	129	132
132		Underslab MEP Inspection	1 day	Thu 26/02/05	Thu 26/02/05	131	135
133		Fire Alarm Rough-in	2 days	Tue 26/02/03	Wed 26/02/0	130	170
134		MEP Rough-in Walls	10 day	Wed 26/02/1	Tue 26/02/24	130SS+2 wks	137FF;135
135		MEP Rough-in Inspection	1 day	Wed 26/02/2	Wed 26/02/2	134;132	137
136		Single Side Drywall	7 days	Tue 26/02/03	Wed 26/02/1	130	137
137		Second Side Drywall	7 days	Thu 26/02/26	Fri 26/03/06	134FF;136;135	138;28
138		Wall Tape and Bed	5 days	Mon 26/03/0	Fri 26/03/13	137;58	180;181;145;144;
139		Grid Install Rework	5 days	Wed 26/03/1	Tue 26/03/17	138FS-1 wk;178	140FS-1 wk
140		Light Fixture Install and Ceiling MEP Finish	12 day	Fri 26/03/27	Mon 26/04/1	139FS-1 wk;24	141
141		Ceiling Cover Inspection	1 day	Tue 26/04/14	Tue 26/04/14	95;140	97;142
142		Ceiling Tile Installation	10 day	Wed 26/04/1	Tue 26/04/28	141	182
143		Restroom Renovations	10 day	Mon 26/03/0	Mon 26/03/1	144SF;56FF;57FF	146
144		Carpet and Tile Prep and Install	10 day	Mon 26/03/1	Fri 26/03/27	138;44;45;46;47;48	143SF;182
145		Painting	10 day	Mon 26/03/1	Fri 26/03/27	138	146SS+2 wks
146		MEP Trimout	10 day	Mon 26/03/3	Fri 26/04/10	143;145SS+2 wks	172
147		Millwork Install	5 days	Thu 26/04/30	Wed 26/05/0	26;27;28;29	170
148		**Level 2 North**	**83 day**	**Mon 26/01/1**	**Wed 26/05/0**		
149		Overhead MEP Rough In	30 day	Mon 26/01/1	Fri 26/02/20	21;10	150SS+3 wks;179
150		Low Voltage Bulk Cabling	20 day	Mon 26/02/0	Fri 26/02/27	149SS+3 wks	180;181

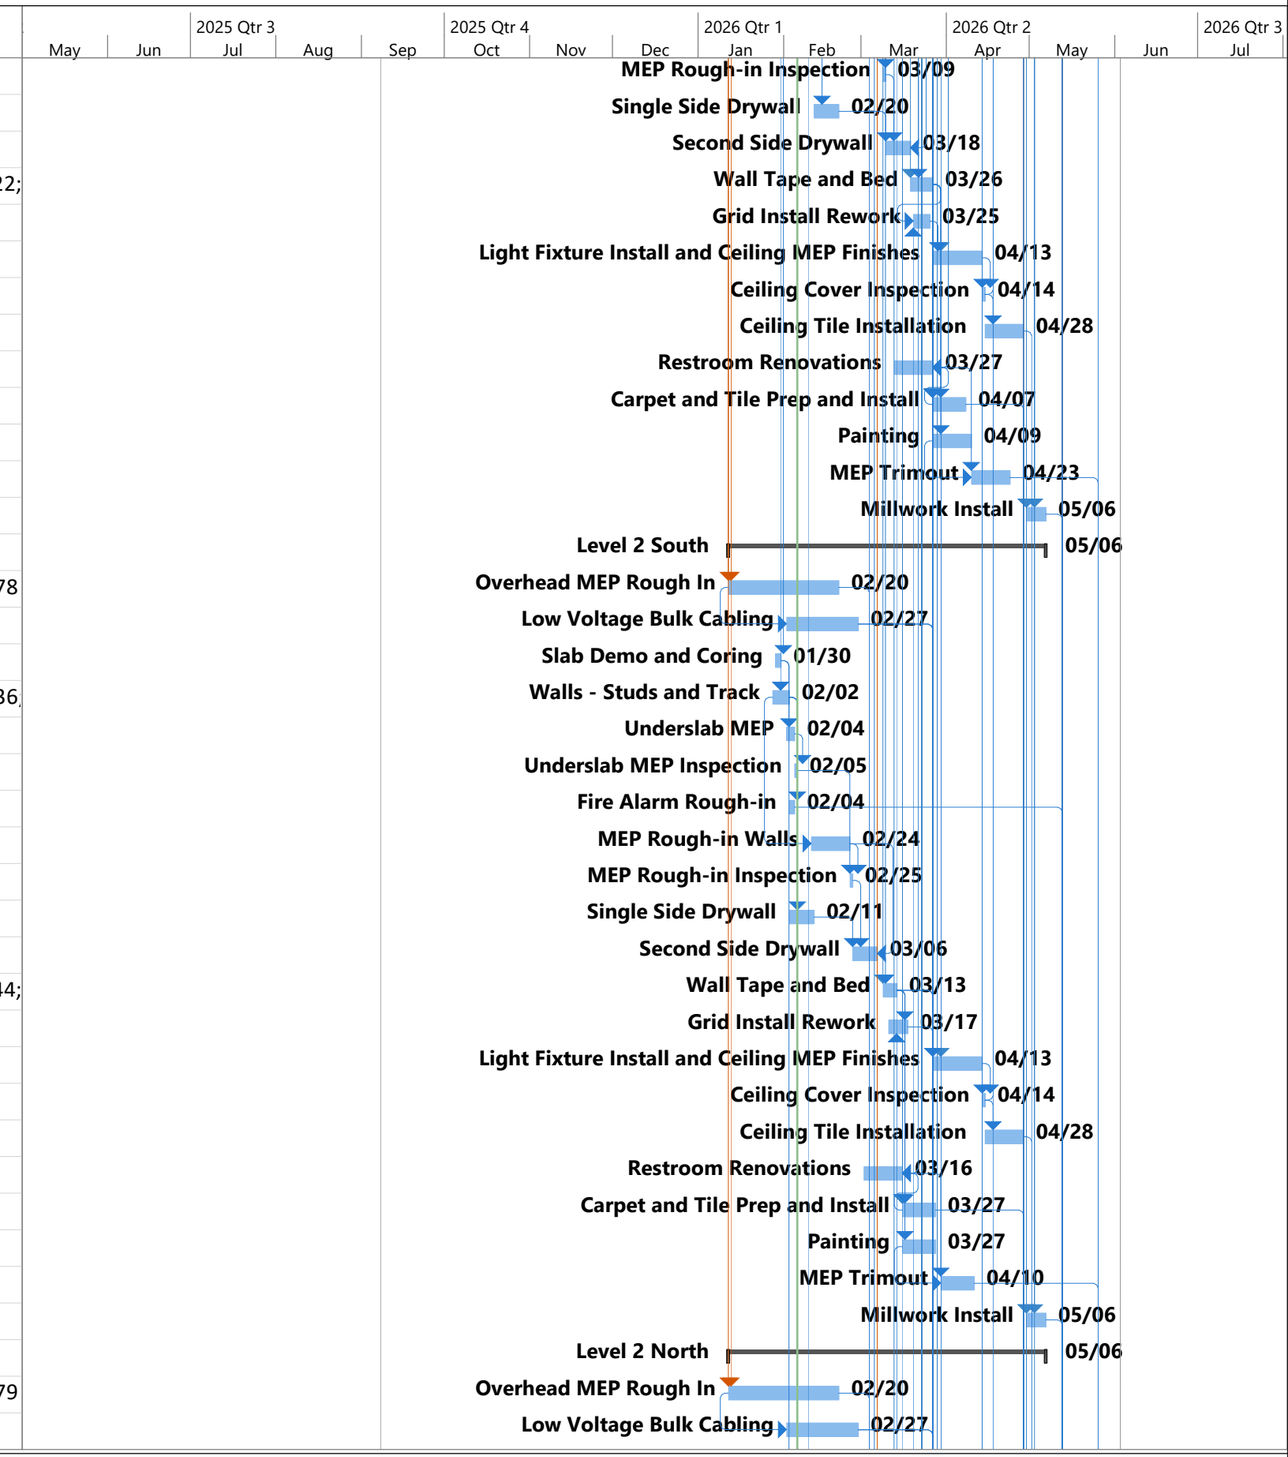

Public Storage HQ - Project Orange
Preliminary Project Schedule
2811 Internet Blvd
Frisco, TX 75034
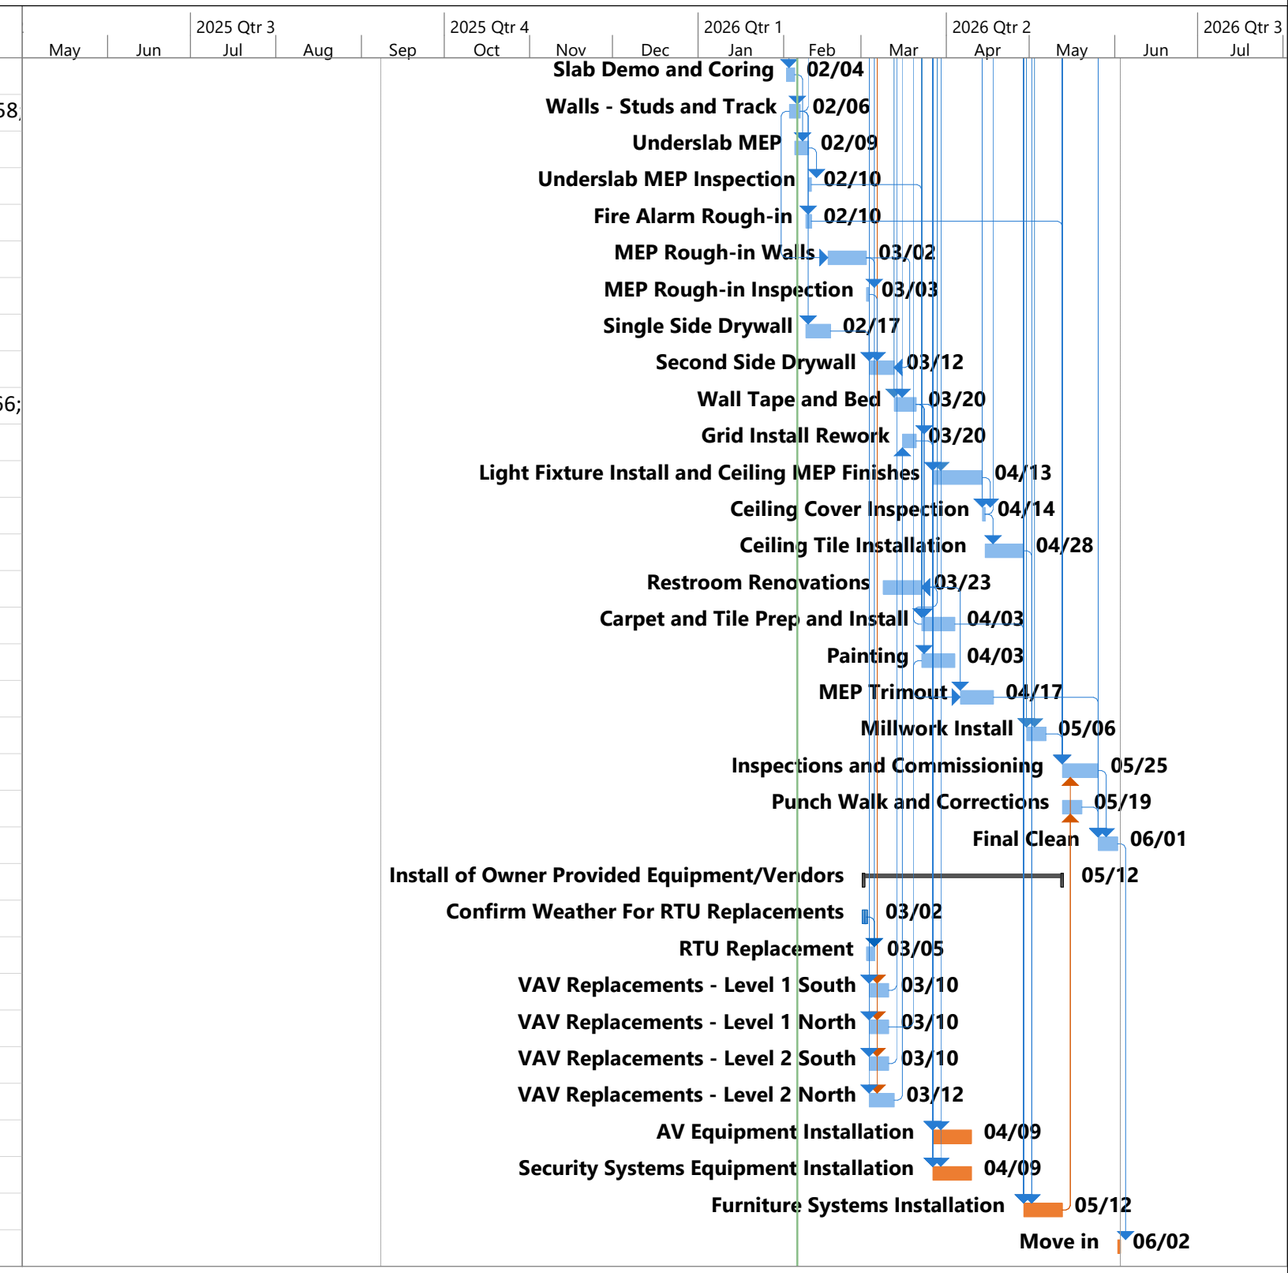
ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors
151		Slab Demo and Coring	3 days	Mon 26/02/0	Wed 26/02/0	129	153
152		Walls - Studs and Track	4 days	Tue 26/02/03	Fri 26/02/06	130	156SS+2 wks;158,
153		Underslab MEP	3 days	Thu 26/02/05	Mon 26/02/0	151	154
154		Underslab MEP Inspection	1 day	Tue 26/02/10	Tue 26/02/10	153	166
155		Fire Alarm Rough-in	2 days	Mon 26/02/0	Tue 26/02/10	152	170
156		MEP Rough-in Walls	10 day	Tue 26/02/17	Mon 26/03/0	152SS+2 wks	159FF;157
157		MEP Rough-in Inspection	1 day	Tue 26/03/03	Tue 26/03/03	156	159
158		Single Side Drywall	7 days	Mon 26/02/0	Tue 26/02/17	152	159
159		Second Side Drywall	7 days	Wed 26/03/0	Thu 26/03/12	156FF;158;157	160;29
160		Wall Tape and Bed	6 days	Fri 26/03/13	Fri 26/03/20	159;58	180;181;167;166;
161		Grid Install Rework	5 days	Mon 26/03/1	Fri 26/03/20	160FS-1 wk;179	162FS-1 wk
162		Light Fixture Install and Ceiling MEP Finish	12 day	Fri 26/03/27	Mon 26/04/1	161FS-1 wk;24	163
163		Ceiling Cover Inspection	1 day	Tue 26/04/14	Tue 26/04/14	95;162	97;164
164		Ceiling Tile Installation	10 day	Wed 26/04/1	Tue 26/04/28	163	182
165		Restroom Renovations	10 day	Mon 26/03/0	Mon 26/03/2	166SF;56FF;57FF	168
166		Carpet and Tile Prep and Install	10 day	Mon 26/03/2	Fri 26/04/03	160;44;45;46;47;48	165SF;182
167		Painting	10 day	Mon 26/03/2	Fri 26/04/03	160	168SS+2 wks
168		MEP Trimout	10 day	Mon 26/04/0	Fri 26/04/17	165;167SS+2 wks	172
169		Millwork Install	5 days	Thu 26/04/30	Wed 26/05/0	26;27;28;29	170
170		Inspections and Commissioning	9 days	Wed 26/05/1	Mon 26/05/2	182;59;60;75;125;1	172
171		Punch Walk and Corrections	5 days	Wed 26/05/1	Tue 26/05/19	182	172
172		Final Clean	5 days	Tue 26/05/26	Mon 26/06/0	170;171;124;101;14	183
173		**Install of Owner Provided Equipment/Vend**	**52 day**	**Mon 26/03/0**	**Tue 26/05/1**		
174		Confirm Weather For RTU Replacements	1 day	Mon 26/03/0	Mon 26/03/0		175
175		RTU Replacement	3 days	Tue 26/03/03	Thu 26/03/05	174;70	
176		VAV Replacements - Level 1 South	5 days	Wed 26/03/0	Tue 26/03/10	71;81	94
177		VAV Replacements - Level 1 North	5 days	Wed 26/03/0	Tue 26/03/10	71;104	117
178		VAV Replacements - Level 2 South	5 days	Wed 26/03/0	Tue 26/03/10	71;127	139
179		VAV Replacements - Level 2 North	7 days	Wed 26/03/0	Thu 26/03/12	71;149	161
180		AV Equipment Installation	10 day	Fri 26/03/27	Thu 26/04/09	93;82;105;116;128;	
181		Security Systems Equipment Installation	10 day	Fri 26/03/27	Thu 26/04/09	93;82;105;116;128;	
182		Furniture Systems Installation	10 day	Wed 26/04/2	Tue 26/05/12	97;67;99;120;122;1	171;170
183		Move in	1 day	Tue 26/06/02	Tue 26/06/02	172
