	Name	Duration: Current	Duration: Previous	Dur Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
1	**Construction Documents**	**50 days**	**50 days**	**0d**	**Mon 25/09/08**	**Mon 25/09/08**	**0d**	**Fri 25/11/14**	**Fri 25/11/14**	**0d**
2	CD Kick off and Start	34 days	34 days	0d	Mon 25/09/08	Mon 25/09/08	0d	Thu 25/10/23	Thu 25/10/23	0d
3	65% progress set	1 day	1 day	0d	Fri 25/10/24	Fri 25/10/24	0d	Fri 25/10/24	Fri 25/10/24	0d
4	Owner Drawing review Of 65% set	5 days	5 days	0d	Mon 25/10/27	Mon 25/10/27	0d	Fri 25/10/31	Fri 25/10/31	0d
5	Completon of Bid, Demo and Permit Submital set	10 days	10 days	0d	Mon 25/11/03	Mon 25/11/03	0d	Fri 25/11/14	Fri 25/11/14	0d
6	**Plan Check**	**36 days**	**29 days**	**7d**	**Mon 25/11/17**	**Mon 25/11/17**	**0d**	**Fri 26/01/09**	**Mon 25/12/29**	**9d**
7	**Issue for Interiors Permit (Plan Check)**	**36 days**	**29 days**	**7d**	**Mon 25/11/17**	**Mon 25/11/17**	**0d**	**Fri 26/01/09**	**Mon 25/12/29**	**9d**
8	City Permit Review	15 days	15 days	0d	Mon 25/11/17	Mon 25/11/17	0d	Fri 25/12/05	Fri 25/12/05	0d
9	Drawing Coordination/City Comments	20 days	13 days	7d	Mon 25/12/08	Mon 25/12/08	0d	Thu 26/01/08	Wed 25/12/24	11d
10	Receive interior Tl Building Permit	1 day	1 day	0d	Fri 26/01/09	Mon 25/12/29	9d	Fri 26/01/09	Mon 25/12/29	9d
11	**Issue for Demo Permit**	**16 days**	**16 days**	**0d**	**Mon 25/11/17**	**Mon 25/11/17**	**0d**	**Mon 25/12/08**	**Mon 25/12/08**	**0d**
12	Demo Permit Review	15 days	15 days	0d	Mon 25/11/17	Mon 25/11/17	0d	Fri 25/12/05	Fri 25/12/05	0d
13	Receive Demo Permit	1 day	1 day	0d	Mon 25/12/08	Mon 25/12/08	0d	Mon 25/12/08	Mon 25/12/08	0d
14	**Bidding**	**19 days**	**19 days**	**0d**	**Mon 25/11/17**	**Mon 25/11/17**	**0d**	**Thu 25/12/11**	**Thu 25/12/11**	**0d**
15	Bidding for Tl GCs	15 days	15 days	0d	Mon 25/11/17	Mon 25/11/17	0d	Fri 25/12/05	Fri 25/12/05	0d
16	Award GC Contract	4 days	4 days	0d	Mon 25/12/08	Mon 25/12/08	0d	Thu 25/12/11	Thu 25/12/11	0d
17	**Contracting**	**16 days**	**16 days**	**0d**	**Fri 25/12/12**	**Fri 25/12/12**	**0d**	**Thu 26/01/08**	**Thu 26/01/08**	**0d**
18	Execute Demo LOA	1 day	1 day	0d	Fri 25/12/12	Fri 25/12/12	0d	Fri 25/12/12	Fri 25/12/12	0d
19	Contract Preparation	5 days	5 days	0d	Mon 25/12/15	Mon 25/12/15	0d	Fri 25/12/19	Fri 25/12/19	0d
20	Contract Negotiation	5 days	5 days	0d	Mon 25/12/22	Mon 25/12/22	0d	Tue 25/12/30	Tue 25/12/30	0d
21	Contract Execution	5 days	5 days	0d	Fri 26/01/02	Fri 26/01/02	0d	Thu 26/01/08	Thu 26/01/08	0d
22	**ARCO Procurement**	**79 days**	**69 days**	**10c**	**Fri 26/01/09**	**Fri 26/01/09**	**0d**	**Wed 26/04/29**	**Wed 26/04/15**	**10d**
23	Submittal Approval - MEPs	2 wks	2 wks	0d	Fri 26/01/09	Fri 26/01/09	0d	Thu 26/01/22	Thu 26/01/22	0d
24	Light Fixtures	9 wks	8 wks	5d	Fri 26/01/23	Fri 26/01/23	0d	Thu 26/03/26	Thu 26/03/19	5d
25	Millwork Shop Drawings	2 wks	2,2 wks	-1d	Fri 26/01/23	Fri 26/01/23	0d	Thu 26/02/05	Fri 26/02/06	-1d
26	Millwork Field Measure and Fab - Level 1 South	6 wks	6 wks	0d	Mon 26/02/16	Thu 26/03/05	-13d	Fri 26/03/27	Wed 26/04/15	-13d
27	Millwork Field Measure and Fab - Level 1 North	6 wks			Thu 26/03/19			Wed 26/04/29		
28	Millwork Field Measure and Fab - Level 2 South	6 wks			Mon 26/03/09			Fri 26/04/17		
29	Millwork Field Measure and Fab - Level 2 North	6 wks			Fri 26/03/13			Thu 26/04/23		
30	Flooring - FC1 Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
31	Flooring - FC2 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
32	Flooring - FC3 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
33	Flooring - FC4 -Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
34	Flooring - FC5 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
35	Flooring - FC7 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
36	Flooring - LVT1 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
37	Flooring - VCT1 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		

	Name	Duration: Current	Duration: Previous	Dur Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
38	Flooring - FT1 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
39	Flooring - FT2 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
40	Wall Tile - WT1 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
41	Wall Tile - WT2 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
42	Wall Tile - WT3 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
43	Wall Tile - WT4 - Submittal Approval	3 wks			Fri 26/01/09			Thu 26/01/29		
44	Flooring - FC1	6 wks	6 wks	0d	Fri 26/01/30	Fri 26/01/23	5d	Thu 26/03/12	Thu 26/03/05	5d
45	Flooring - FC2	6 wks			Fri 26/01/30			Thu 26/03/12		
46	Flooring - FC3	6 wks			Fri 26/01/30			Thu 26/03/12		
47	Flooring - FC4	6 wks			Fri 26/01/30			Thu 26/03/12		
48	Flooring - FC5	6 wks			Fri 26/01/30			Thu 26/03/12		
49	Flooring - FC7	6 wks			Fri 26/01/30			Thu 26/03/12		
50	Flooring - LVT1	6 wks			Fri 26/01/30			Thu 26/03/12		
51	Flooring - VCT1	6 wks			Fri 26/01/30			Thu 26/03/12		
52	Flooring - FT1	3 wks			Fri 26/01/30			Thu 26/02/19		
53	Flooring - FT2	6 wks			Fri 26/01/30			Thu 26/03/12		
54	Wall Tile - WT1	2 wks			Fri 26/01/30			Thu 26/02/12		
55	Wall Tile - WT2	2 wks			Fri 26/01/30			Thu 26/02/12		
56	Wall Tile - WT3	4 wks			Fri 26/01/30			Thu 26/02/26		
57	Wall Tile - WT4	2 wks			Fri 26/01/30			Thu 26/02/12		
58	Door Frames	6 wks	6 wks	0d	Fri 26/01/23	Fri 26/01/23	0d	Thu 26/03/05	Thu 26/03/05	0d
59	Doors, Hardware	8 wks	8 wks	0d	Fri 26/01/23	Fri 26/01/23	0d	Thu 26/03/19	Thu 26/03/19	0d
60	Appliances	8 wks	8 wks	0d	Fri 26/01/23	Fri 26/01/23	0d	Thu 26/03/19	Thu 26/03/19	0d
61	Ceiling Baffles - Breakroom	10 wks	10 wks	0d	Fri 26/01/23	Fri 26/01/23	0d	Thu 26/04/02	Thu 26/04/02	0d
62	**Procurement Of Direct FBO items**	**103 days**	**136 days**	**-33**	**Fri 25/10/31**	**Mon 25/09/08**	**39d**	**Mon 26/03/30**	**Fri 26/03/20**	**6d**
63	**Furniture**	**97 days**	**97 days**	**0d**	**Fri 25/10/31**	**Fri 25/10/31**	**0d**	**Fri 26/03/20**	**Fri 26/03/20**	**0d**
64	Select Furniture Vendor	1 day	1 day	0d	Fri 25/10/31	Fri 25/10/31	0d	Fri 25/10/31	Fri 25/10/31	0d
65	Review and finalize details for furniture	15 days	15 days	0d	Mon 25/11/03	Mon 25/11/03	0d	Fri 25/11/21	Fri 25/11/21	0d
66	Furniture Order Due	1 day	1 day	0d	Mon 25/11/24	Mon 25/11/24	0d	Mon 25/11/24	Mon 25/11/24	0d
67	Furniture Lead Time	80 days	80 days	0d	Tue 25/11/25	Tue 25/11/25	0d	Fri 26/03/20	Fri 26/03/20	0d
68	**HVAC Equipment**	**58 days**	**71 days**	**-13**	**Mon 25/12/08**	**Mon 25/10/27**	**30d**	**Tue 26/03/03**	**Fri 26/02/06**	**17d**
69	Order Roof Top HVAC equipment	1 day	1 day	0d	Mon 25/12/08	Mon 25/10/27	30d	Mon 25/12/08	Mon 25/10/27	30d
70	HVAC Equipment Lead Time - RTUs	50 days			Wed 25/12/17			Mon 26/03/02		
71	HVAC Equipment Lead Time - VAVs	57 days	70 days	-13	Tue 25/12/09	Tue 25/10/28	30d	Tue 26/03/03	Fri 26/02/06	17d
72	**Elevator Modernization**	**56 days**	**123 days**	**-67**	**Mon 26/01/12**	**Mon 25/09/08**	**90d**	**Mon 26/03/30**	**Tue 26/03/03**	**19d**
73	Contract for Elevator Modernization	1 day	1 day	0d	Mon 26/01/12	Mon 25/09/08	90d	Mon 26/01/12	Mon 25/09/08	90d
74	Elevator Equipment Lead Time	30 days	97 days	-67	Tue 26/01/13	Tue 25/09/09	90d	Mon 26/02/23	Tue 26/01/27	19d

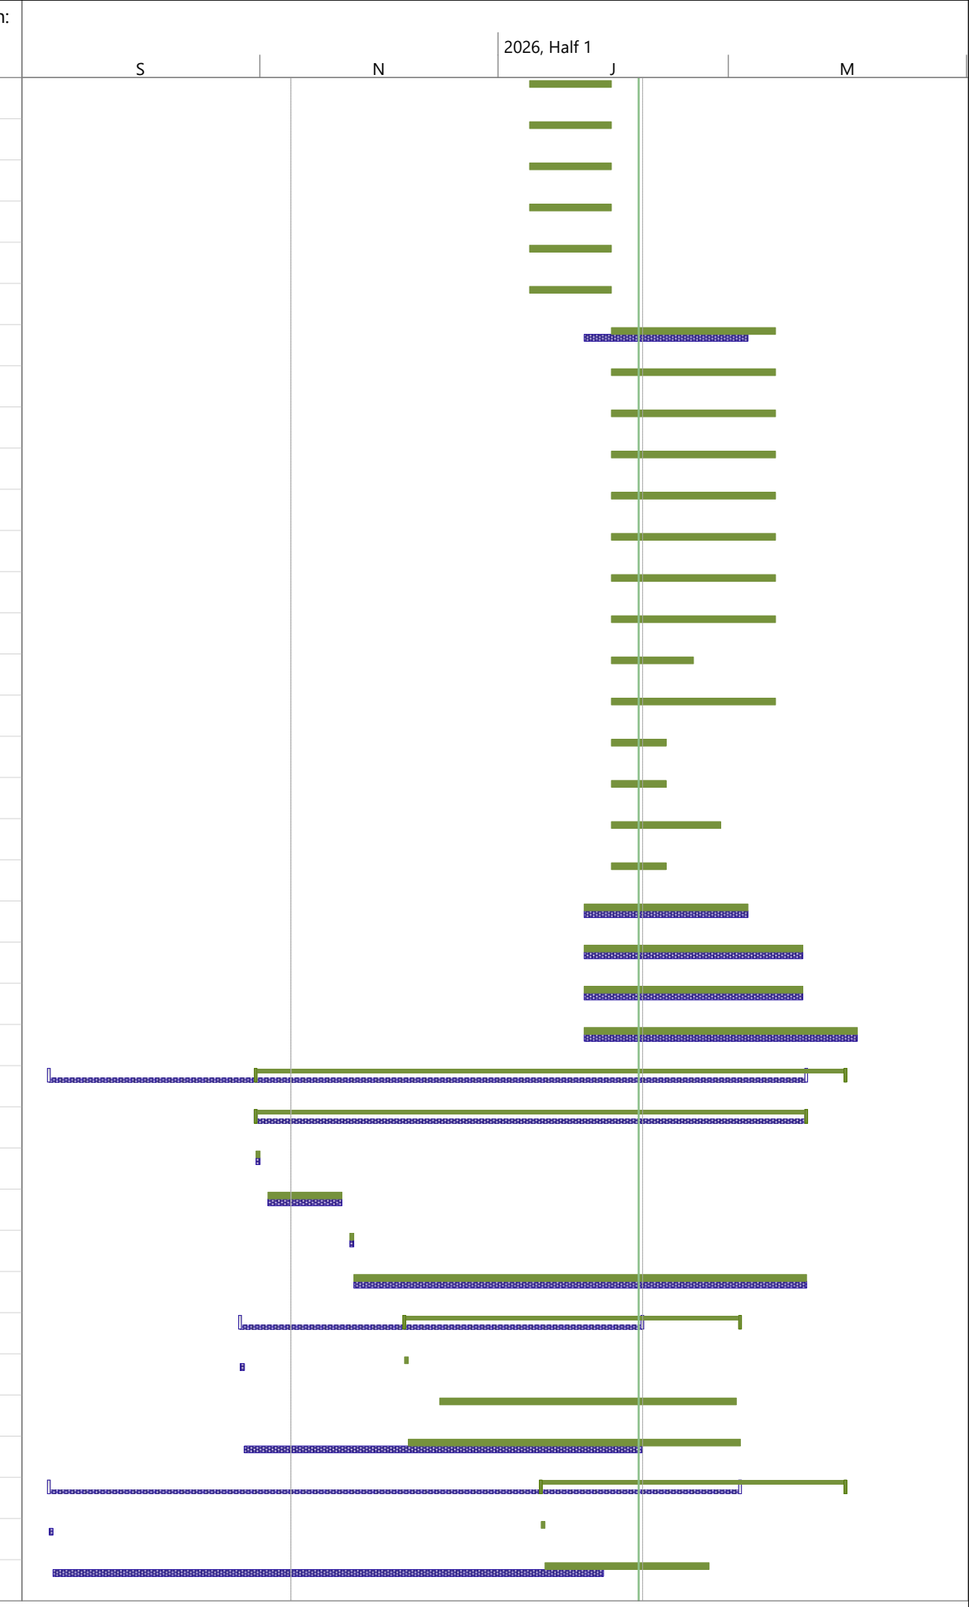

	Name	Duration: Current	Duration: Previous	Dur Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
75	Elevator Modernization	25 days	25 days	0d	Tue 26/02/24	Wed 26/01/28	19d	Mon 26/03/30	Tue 26/03/03	19d
76	**Demolition**	**29 days**	**25 days**	**4d**	**Mon 25/12/15**	**Mon 25/12/15**	**0d**	**Wed 26/01/28**	**Thu 26/01/22**	**4d**
77	MEP/F Make Safe	3 wks	3 wks	0d	Mon 25/12/15	Mon 25/12/15	0d	Thu 26/01/08	Thu 26/01/08	0d
78	Demolition	5 wks	5 wks	0d	Fri 25/12/19	Mon 25/12/15	4d	Wed 26/01/28	Thu 26/01/22	4d
79	Slab Demo and Coring		3 days			Tue 26/01/20			Thu 26/01/22	
80	**Construction**	**101 days**	**101 days**	**0d**	**Mon 26/01/12**	**Fri 26/01/09**	**1d**	**Mon 26/06/01**	**Fri 26/05/29**	**1d**
81	**Level 1 South**	**70 days**			**Mon 26/01/12**			**Fri 26/04/17**		
82	Overhead MEP Rough In	30 days	30 days	0d	Mon 26/01/12	Fri 26/01/09	1d	Fri 26/02/20	Thu 26/02/19	1d
83	Low Voltage Bulk Cabling	20 days	20 days	0d	Mon 26/02/02	Fri 26/01/30	1d	Fri 26/02/27	Thu 26/02/26	1d
84	Slab Demo and Coring	4 days			Tue 26/01/20			Fri 26/01/23		
85	Walls - Studs and Track	4 days	15 days	-11	Thu 26/01/22	Fri 26/01/23	-1d	Tue 26/01/27	Thu 26/02/12	-12d
86	Underslab MEP	6 days	3 days	3d	Mon 26/01/26	Fri 26/01/23	1d	Mon 26/02/02	Tue 26/01/27	4d
87	Underslab MEP Inspection	1 day			Tue 26/02/03			Tue 26/02/03		
88	Concrete Slab Pourback	2 days			Wed 26/02/04			Thu 26/02/05		
89	Fire Alarm Rough-in	2 days			Wed 26/01/28			Thu 26/01/29		
90	MEP Rough-in Walls	10 days	15 days	-5d	Fri 26/01/23	Fri 26/02/06	-10d	Thu 26/02/05	Thu 26/02/26	-15d
91	MEP Rough-in Inspection	1 day			Fri 26/02/06			Fri 26/02/06		
92	Single Side Drywall	5 days	7 days	-2d	Wed 26/01/28	Fri 26/02/13	-12d	Tue 26/02/03	Mon 26/02/23	-14d
93	Second Side Drywall	5 days	7 days	-2d	Mon 26/02/09	Tue 26/02/24	-11d	Fri 26/02/13	Wed 26/03/04	-13d
94	Wall Tape and Bed	6 days	12 days	-6d	Wed 26/02/11	Thu 26/03/05	-16d	Wed 26/02/18	Fri 26/03/20	-22d
95	Grid Install Rework	6 days	10 days	-4d	Wed 26/03/11	Mon 26/03/16	-3d	Wed 26/03/18	Fri 26/03/27	-7d
96	Light Fixture Install and Ceiling MEP Finishes	8 days	12 days	-4d	Fri 26/03/27	Mon 26/03/23	4d	Tue 26/04/07	Tue 26/04/07	0d
97	Ceiling Cover Inspection	1 day			Wed 26/04/08			Wed 26/04/08		
98	Ceiling Tile Installation	3 days	10 days	-7d	Wed 26/04/15	Wed 26/04/08	5d	Fri 26/04/17	Tue 26/04/21	-2d
99	Restroom Renovations	10 days	25 days	-15	Fri 26/02/27	Mon 26/02/16	9d	Fri 26/03/13	Mon 26/03/23	-6d
100	Carpet and Tile Prep and Install	8 days	20 days	-12	Fri 26/03/13	Mon 26/03/23	-6d	Tue 26/03/24	Fri 26/04/17	-18d
101	Painting	10 days	20 days	-10	Thu 26/02/19	Mon 26/03/23	-22d	Wed 26/03/04	Fri 26/04/17	-32d
102	MEP Trimout	10 days	15 days	-5d	Fri 26/03/13	Mon 26/04/06	-16d	Thu 26/03/26	Fri 26/04/24	-21d
103	Millwork Install	5 days	5 days	0d	Mon 26/03/30	Thu 26/04/16	-13d	Fri 26/04/03	Wed 26/04/22	-13d
104	**Level 1 North**	**83 days**			**Mon 26/01/12**			**Wed 26/05/06**		
105	Overhead MEP Rough In	30 days			Mon 26/01/12			Fri 26/02/20		
106	Low Voltage Bulk Cabling	20 days			Mon 26/02/02			Fri 26/02/27		
107	Slab Demo and Coring	3 days			Mon 26/01/26			Wed 26/01/28		
108	Walls - Studs and Track	3 days			Mon 26/02/09			Wed 26/02/11		
109	Underslab MEP	3 days			Thu 26/01/29			Mon 26/02/02		
110	Underslab MEP Inspection	1 day			Tue 26/02/03			Tue 26/02/03		
111	Concrete Slab Pourback	4 days			Wed 26/02/04			Mon 26/02/09		

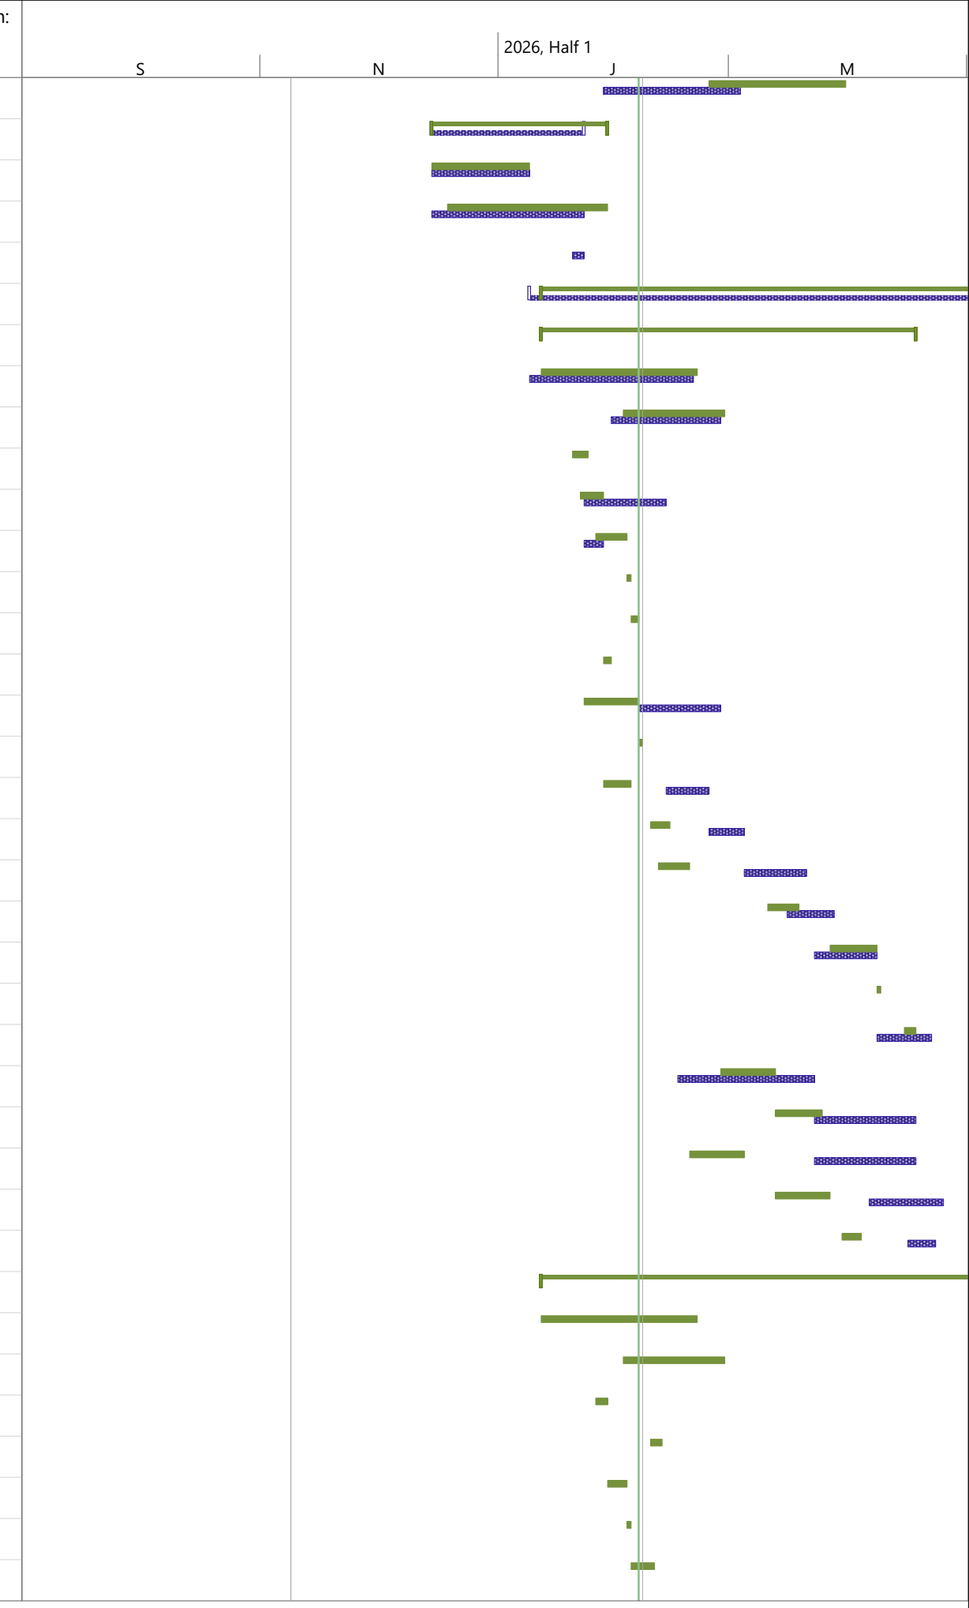

	Name	Duration: Current	Duration: Previous	Dur Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
112	Fire Alarm Rough-in	2 days			Thu 26/02/12			Fri 26/02/13		
113	MEP Rough-in Walls	10 days			Mon 26/02/23			Fri 26/03/06		
114	MEP Rough-in Inspection	1 day			Mon 26/03/09			Mon 26/03/09		
115	Single Side Drywall	7 days			Thu 26/02/12			Fri 26/02/20		
116	Second Side Drywall	7 days			Tue 26/03/10			Wed 26/03/18		
117	Wall Tape and Bed	6 days			Thu 26/03/19			Thu 26/03/26		
118	Grid Install Rework	4 days			Fri 26/03/20			Wed 26/03/25		
119	Light Fixture Install and Ceiling MEP Finishes	12 days			Fri 26/03/27			Mon 26/04/13		
120	Ceiling Cover Inspection	1 day			Tue 26/04/14			Tue 26/04/14		
121	Ceiling Tile Installation	10 days			Wed 26/04/15			Tue 26/04/28		
122	Restroom Renovations	10 days			Fri 26/03/13			Fri 26/03/27		
123	Carpet and Tile Prep and Install	8 days			Fri 26/03/27			Tue 26/04/07		
124	Painting	10 days			Fri 26/03/27			Thu 26/04/09		
125	MEP Trimout	10 days			Fri 26/04/10			Thu 26/04/23		
126	Millwork Install	5 days			Thu 26/04/30			Wed 26/05/06		
127	**Level 2 South**	**83 days**			**Mon 26/01/12**			**Wed 26/05/06**		
128	Overhead MEP Rough In	30 days			Mon 26/01/12			Fri 26/02/20		
129	Low Voltage Bulk Cabling	20 days			Mon 26/02/02			Fri 26/02/27		
130	Slab Demo and Coring	2 days			Thu 26/01/29			Fri 26/01/30		
131	Walls - Studs and Track	4 days			Wed 26/01/28			Mon 26/02/02		
132	Underslab MEP	3 days			Mon 26/02/02			Wed 26/02/04		
133	Underslab MEP Inspection	1 day			Thu 26/02/05			Thu 26/02/05		
134	Fire Alarm Rough-in	2 days			Tue 26/02/03			Wed 26/02/04		
135	MEP Rough-in Walls	10 days			Wed 26/02/11			Tue 26/02/24		
136	MEP Rough-in Inspection	1 day			Wed 26/02/25			Wed 26/02/25		
137	Single Side Drywall	7 days			Tue 26/02/03			Wed 26/02/11		
138	Second Side Drywall	7 days			Thu 26/02/26			Fri 26/03/06		
139	Wall Tape and Bed	5 days			Mon 26/03/09			Fri 26/03/13		
140	Grid Install Rework	5 days			Wed 26/03/11			Tue 26/03/17		
141	Light Fixture Install and Ceiling MEP Finishes	12 days			Fri 26/03/27			Mon 26/04/13		
142	Ceiling Cover Inspection	1 day			Tue 26/04/14			Tue 26/04/14		
143	Ceiling Tile Installation	10 days			Wed 26/04/15			Tue 26/04/28		
144	Restroom Renovations	10 days			Mon 26/03/02			Mon 26/03/16		
145	Carpet and Tile Prep and Install	10 days			Mon 26/03/16			Fri 26/03/27		
146	Painting	10 days			Mon 26/03/16			Fri 26/03/27		
147	MEP Trimout	10 days			Mon 26/03/30			Fri 26/04/10		
148	Millwork Install	5 days			Thu 26/04/30			Wed 26/05/06		

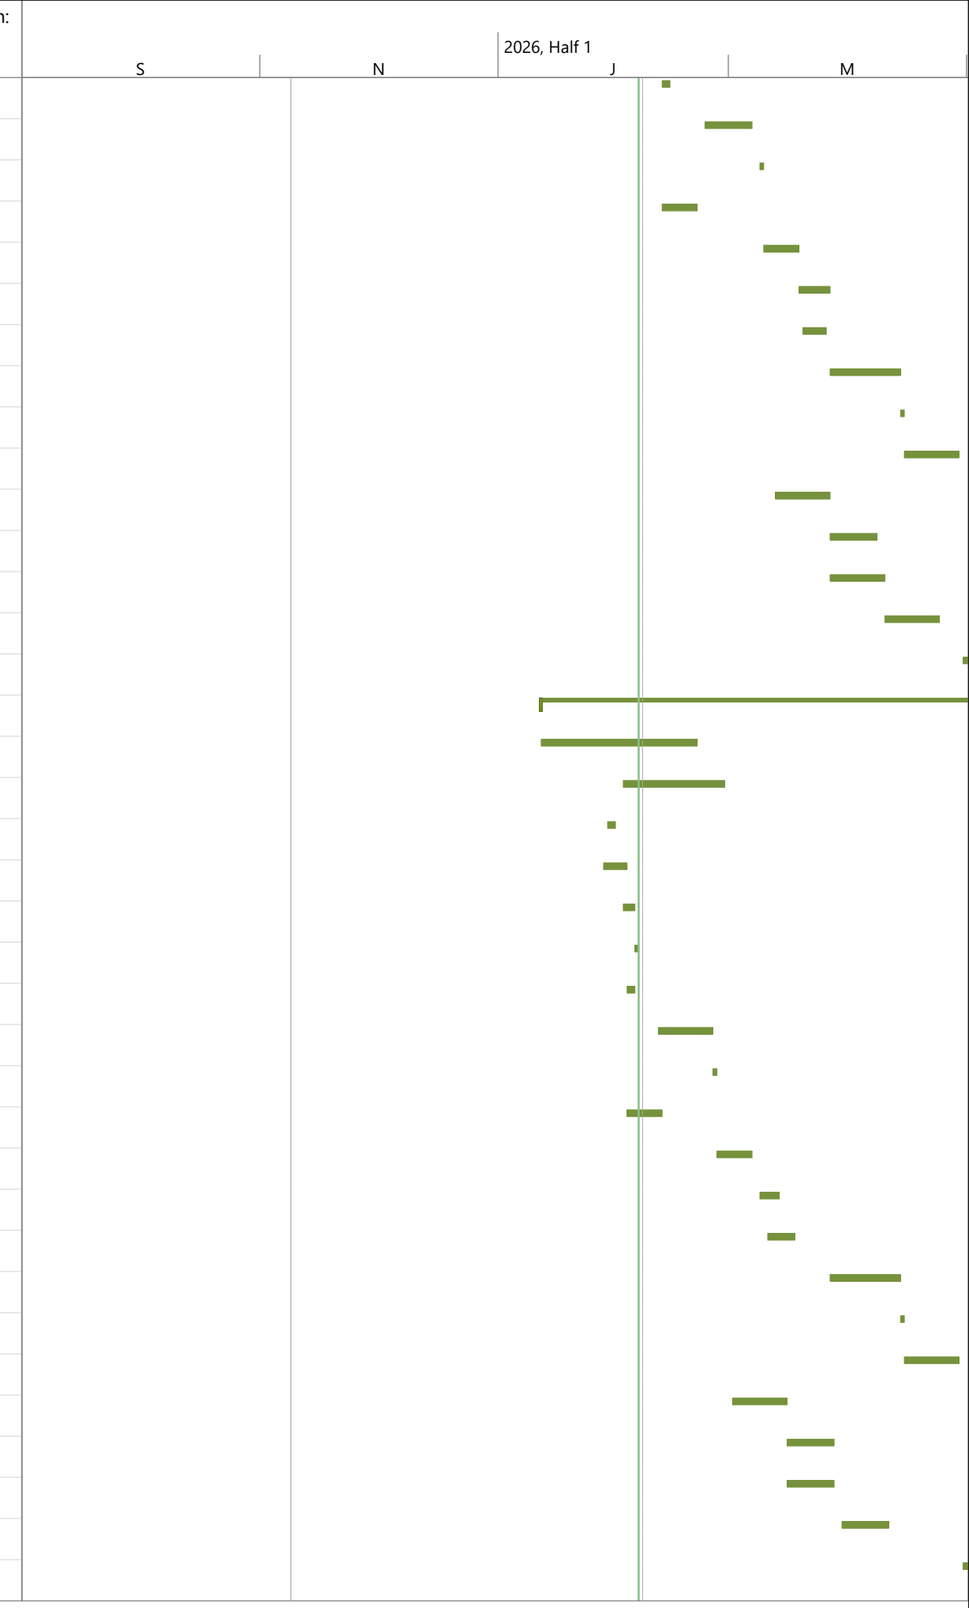
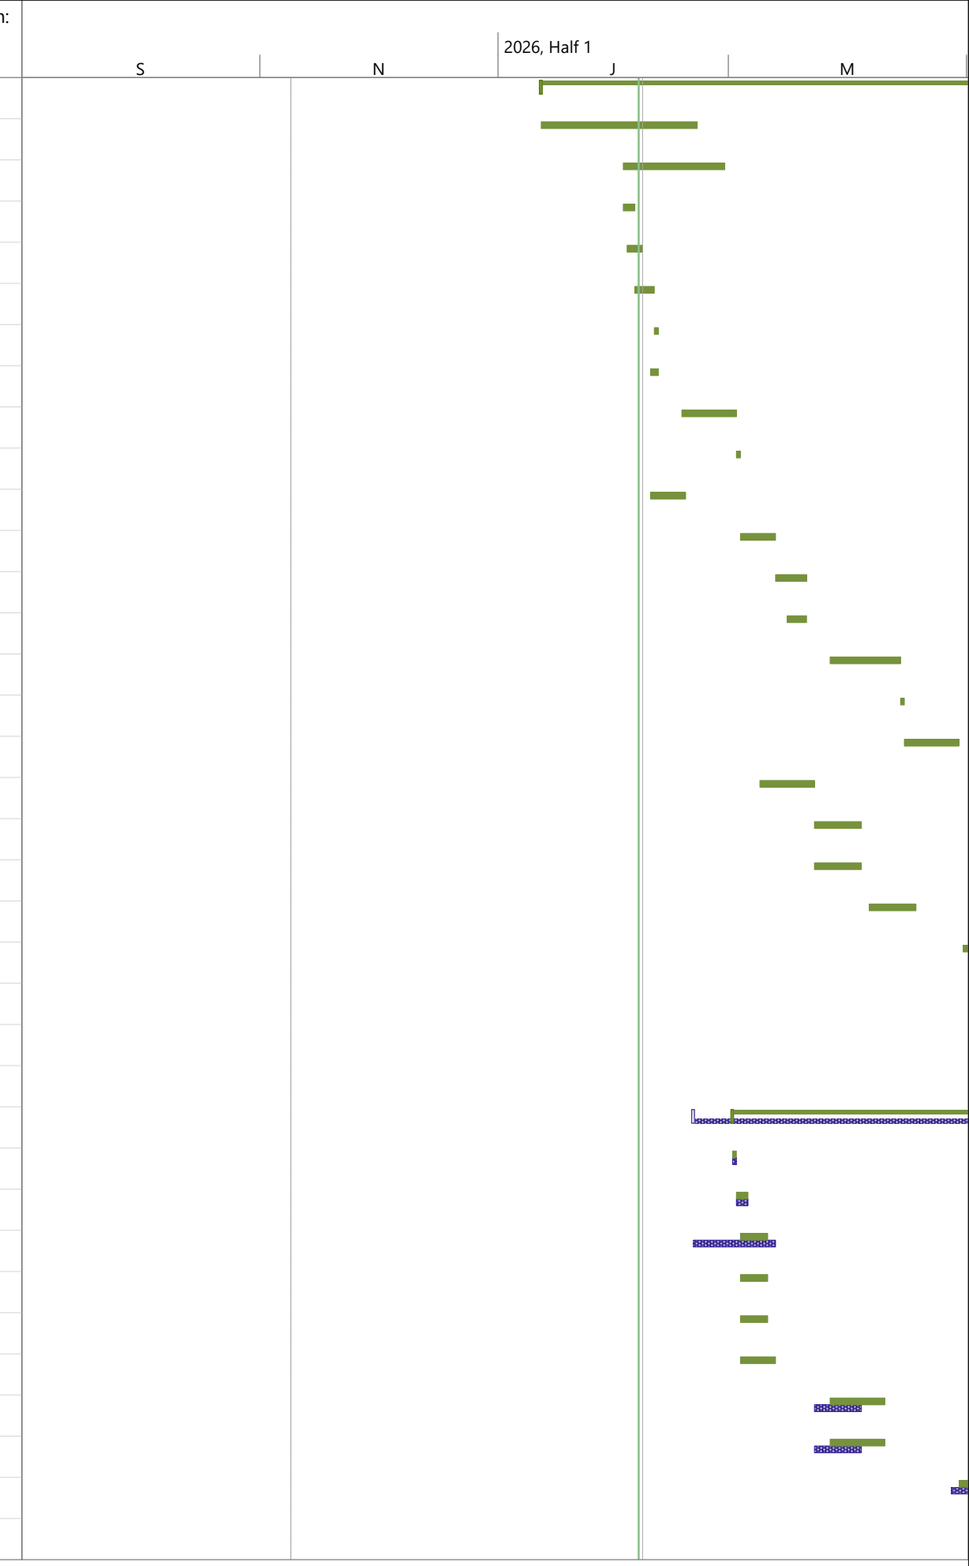
	Name	Duration: Current	Duration: Previous	Dur Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish: Diff
149	**Level 2 North**	**83 days**			**Mon 26/01/12**			**Wed 26/05/06**		
150	Overhead MEP Rough In	30 days			Mon 26/01/12			Fri 26/02/20		
151	Low Voltage Bulk Cabling	20 days			Mon 26/02/02			Fri 26/02/27		
152	Slab Demo and Coring	3 days			Mon 26/02/02			Wed 26/02/04		
153	Walls - Studs and Track	4 days			Tue 26/02/03			Fri 26/02/06		
154	Underslab MEP	3 days			Thu 26/02/05			Mon 26/02/09		
155	Underslab MEP Inspection	1 day			Tue 26/02/10			Tue 26/02/10		
156	Fire Alarm Rough-in	2 days			Mon 26/02/09			Tue 26/02/10		
157	MEP Rough-in Walls	10 days			Tue 26/02/17			Mon 26/03/02		
158	MEP Rough-in Inspection	1 day			Tue 26/03/03			Tue 26/03/03		
159	Single Side Drywall	7 days			Mon 26/02/09			Tue 26/02/17		
160	Second Side Drywall	7 days			Wed 26/03/04			Thu 26/03/12		
161	Wall Tape and Bed	6 days			Fri 26/03/13			Fri 26/03/20		
162	Grid Install Rework	5 days			Mon 26/03/16			Fri 26/03/20		
163	Light Fixture Install and Ceiling MEP Finishes	12 days			Fri 26/03/27			Mon 26/04/13		
164	Ceiling Cover Inspection	1 day			Tue 26/04/14			Tue 26/04/14		
165	Ceiling Tile Installation	10 days			Wed 26/04/15			Tue 26/04/28		
166	Restroom Renovations	10 days			Mon 26/03/09			Mon 26/03/23		
167	Carpet and Tile Prep and Install	10 days			Mon 26/03/23			Fri 26/04/03		
168	Painting	10 days			Mon 26/03/23			Fri 26/04/03		
169	MEP Trimout	10 days			Mon 26/04/06			Fri 26/04/17		
170	Millwork Install	5 days			Thu 26/04/30			Wed 26/05/06		
171	Inspections and Commissioning	9 days	10 days	-1d	Wed 26/05/13	Mon 26/05/11	2d	Mon 26/05/25	Fri 26/05/22	1d
172	Punch Walk and Corrections	5 days	5 days	0d	Wed 26/05/13	Mon 26/05/11	2d	Tue 26/05/19	Fri 26/05/15	2d
173	Final Clean	5 days	5 days	0d	Tue 26/05/26	Mon 26/05/25	1d	Mon 26/06/01	Fri 26/05/29	1d
174	**Install of Owner Provided Equipment/Vendors**	**52 days**	**56 days**	**-4d**	**Mon 26/03/02**	**Fri 26/02/20**	**6d**	**Tue 26/05/12**	**Fri 26/05/08**	**2d**
175	Confirm Weather For RTU Replacements	1 day	1 day	0d	Mon 26/03/02	Mon 26/03/02	0d	Mon 26/03/02	Mon 26/03/02	0d
176	RTU Replacement	3 days	3 days	0d	Tue 26/03/03	Tue 26/03/03	0d	Thu 26/03/05	Thu 26/03/05	0d
177	VAV Replacements - Level 1 South	5 days	15 days	-10	Wed 26/03/04	Fri 26/02/20	8d	Tue 26/03/10	Thu 26/03/12	-2d
178	VAV Replacements - Level 1 North	5 days			Wed 26/03/04			Tue 26/03/10		
179	VAV Replacements - Level 2 South	5 days			Wed 26/03/04			Tue 26/03/10		
180	VAV Replacements - Level 2 North	7 days			Wed 26/03/04			Thu 26/03/12		
181	AV Equipment Installation	10 days	10 days	0d	Fri 26/03/27	Mon 26/03/23	4d	Thu 26/04/09	Fri 26/04/03	4d
182	Security Systems Equipment Installation	10 days	10 days	0d	Fri 26/03/27	Mon 26/03/23	4d	Thu 26/04/09	Fri 26/04/03	4d
183	Furniture Systems Installation	10 days	10 days	0d	Wed 26/04/29	Mon 26/04/27	2d	Tue 26/05/12	Fri 26/05/08	2d
184	Move in	1 day	1 day	0d	Tue 26/06/02	Mon 26/06/01	1d	Tue 26/06/02	Mon 26/06/01	1d
