Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

Public Storage Dashboard

Data Date: 2/18/2026

Type	Project	Region	Responsible
Construction	Frisco, TX	Central	Matthew Hobson

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
6/1/2026	6/3/2026	-2 Baseline -1 Previous	Remaining Work Compression: 23% — ALERT

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	1/8/2026	1/8/2026	1/8/2026	0	0	Contract Execution	On Track – Gaining
Foundation Complete	1/22/2026	2/4/2026	2/4/2026	-13	0	Slab Demo And Coring - Level 2 North	Delayed – Gaining
Weather Tight	3/4/2026	3/12/2026	3/12/2026	-8	0	Second Side Drywall - Level 2 North	Delayed – Gaining
Elevator Complete	3/3/2026	3/30/2026	4/6/2026	-34	-7	Elevator Modernization	Delayed – Slipping
Conditioned Air	3/12/2026	3/12/2026	4/21/2026	-40	-40	Vav Replacements - Level 2 North	Delayed – Slipping
Structure Top Out	4/21/2026	4/28/2026	4/24/2026	-3	4	Ceiling Tile Installation - Level 2 North	Delayed – Gaining
Permanent Power	4/24/2026	4/17/2026	5/4/2026	-10	-17	Mep Trimout - Level 2 North	Delayed – Slipping
Closeout Cleaning	5/29/2026	6/1/2026	6/2/2026	-4	-1	Final Clean	Delayed – Slipping
Contract Completion	6/1/2026	6/2/2026	6/3/2026	-2	-1	Move In	Delayed – Slipping

Baseline Variance

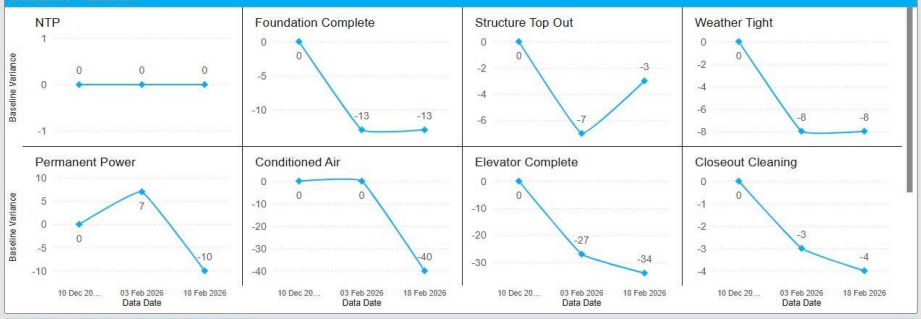

Schedule Performance Summary

Summary

Overall, the schedule is showing acute performance and reliability risks, driven by major deficiencies in schedule quality, excessive changes, ineffective execution, severe critical path delays, and high compression levels. Immediate and coordinated corrective actions are needed to address technical shortcomings, regain schedule stability, and realign the project with baseline objectives.

Critical Path Compression: 12.00% — ALERT
Significant compression applied to the critical path may mask underlying delays but introduces risks related to execution feasibility, resource congestion, and compromised quality. Review of compression strategies is recommended.

Critical Path Variance: 73% — WARNING
The critical path has slipped considerably compared to the baseline, signaling substantial project delays and heightened risk of late completion. Immediate investigation into the causes of this slippage is warranted.

Execution Score: 33% — ALERT
Execution practices are severely lacking, indicating the schedule is not being used effectively for planning or monitoring upcoming work. This increases the likelihood of uncoordinated activity, delays, and reduced schedule reliability.

Finish Variance: 13% — WARNING
The project is currently forecast to finish later than planned by a notable margin, though within the cautionary range. Continued monitoring and mitigation of finish slippage are necessary.

Remaining Work Compression: 23% — ALERT
A high percentage of remaining activities have been shortened, indicating aggressive schedule recovery efforts that may not be realistic. Over-compression can endanger execution quality and increase future delay risk.

Schedule Change Index: 23% — ALERT
Over one-fifth of activities have experienced changes this period, reflecting excessive volatility and poor planning discipline. High instability can undermine confidence in schedule forecasts and project predictability.

Powered By STELIC INSIGHT+ACTION=IMPACT
