Public Storage HQ - Project Orange
Preliminary Project Schedule
2811 Internet Blvd
Frisco, TX 75034

ID	Task Name	Duration	Start	Finish
0	**Public Storage HQ**	**189 days**	**Mon 9/8/25**	**Thu 6/4/26**
1	**Construction Documents**	**50 days**	**Mon 9/8/25**	**Fri 11/14/25**
2	CD Kick off and Start	34 days	Mon 9/8/25	Thu 10/23/25
3	65% progress set	1 day	Fri 10/24/25	Fri 10/24/25
4	Owner Drawing review Of 65% set	5 days	Mon 10/27/25	Fri 10/31/25
5	Completon of Bid, Demo and Permit Submital set	10 days	Mon 11/3/25	Fri 11/14/25
6	**Plan Check**	**36 days**	**Mon 11/17/25**	**Fri 1/9/26**
7	**Issue for Interiors Permit (Plan Check)**	**36 days**	**Mon 11/17/25**	**Fri 1/9/26**
8	City Permit Review	15 days	Mon 11/17/25	Fri 12/5/25
9	Drawing Coordination/City Comments	20 days	Mon 12/8/25	Thu 1/8/26
10	Receive interior TI Building Permit	1 day	Fri 1/9/26	Fri 1/9/26
11	**Issue for Demo Permit**	**16 days**	**Mon 11/17/25**	**Mon 12/8/25**
12	Demo Permit Review	15 days	Mon 11/17/25	Fri 12/5/25
13	Receive Demo Permit	1 day	Mon 12/8/25	Mon 12/8/25
14	**Bidding**	**19 days**	**Mon 11/17/25**	**Thu 12/11/25**
15	Bidding for TI GCs	15 days	Mon 11/17/25	Fri 12/5/25
16	Award GC Contract	4 days	Mon 12/8/25	Thu 12/11/25
17	**Contracting**	**16 days**	**Fri 12/12/25**	**Thu 1/8/26**
18	Execute Demo LOA	1 day	Fri 12/12/25	Fri 12/12/25
19	Contract Preparation	5 days	Mon 12/15/25	Fri 12/19/25
20	Contract Negotiation	5 days	Mon 12/22/25	Tue 12/30/25
21	Contract Execution	5 days	Fri 1/2/26	Thu 1/8/26
22	**ARCO Procurement**	**84 days**	**Fri 1/9/26**	**Wed 5/6/26**
23	Submittal Approval - MEPs	2.2 wks	Fri 1/9/26	Fri 1/23/26
24	Regular Light Fixture Submittal Approval (Architect)	9 days	Wed 1/28/26	Mon 2/9/26
25	Specialty Light Fixture Submittal Approval (Architect)	7 days	Mon 2/9/26	Tue 2/17/26
26	Light Fixtures - Regular Fixtures	8 wks	Tue 2/10/26	Mon 4/6/26
27	Light Fixtures - Specialty Fixtures	9.5 wks	Wed 2/18/26	Fri 4/24/26
28	Millwork Shop Drawings	2 wks	Fri 1/23/26	Thu 2/5/26
29	Millwork Drawing Review Approval	3 days	Fri 2/6/26	Tue 2/10/26
30	Millwork Field Measure and Fab - Level 1 South	5 wks	Thu 3/5/26	Wed 4/8/26
31	Millwork Field Measure and Fab - Level 1 North	5 wks	Tue 3/17/26	Mon 4/20/26
32	Millwork Field Measure and Fab - Level 2 South	5 wks	Mon 3/2/26	Fri 4/3/26
33	Millwork Field Measure and Fab - Level 2 North	5 wks	Fri 3/13/26	Thu 4/16/26
34	Flooring - FC1 Submittal Approval	1.4 wks	Wed 2/4/26	Thu 2/12/26
35	Flooring - FC2 - Submittal Approval	1.4 wks	Wed 2/4/26	Thu 2/12/26
36	Flooring - FC3 - Submittal Approval	1.4 wks	Wed 2/4/26	Thu 2/12/26
37	Flooring - FC4 -Submittal Approval	1.4 wks	Wed 2/4/26	Thu 2/12/26
38	Flooring - LVT1 - Submittal Approval	1.4 wks	Wed 2/4/26	Thu 2/12/26
39	Flooring - VCT1 - Submittal Approval	1.4 wks	Wed 2/4/26	Thu 2/12/26
40	Flooring - FT1 - Submittal Approval	1 wk	Wed 2/4/26	Tue 2/10/26
41	Flooring - FT2 - Submittal Approval	1 wk	Wed 2/4/26	Tue 2/10/26
42	Wall Tile - WT1 - Submittal Approval	1 wk	Wed 2/4/26	Tue 2/10/26
43	Wall Tile - WT2 - Submittal Approval	1 wk	Wed 2/4/26	Tue 2/10/26
44	Wall Tile - WT3 - Submittal Approval	1 wk	Wed 2/4/26	Tue 2/10/26
45	Wall Tile - WT4 - Submittal Approval	1 wk	Wed 2/4/26	Tue 2/10/26
46	Flooring - FC1	7.8 wks	Fri 2/13/26	Wed 4/8/26
47	Flooring - FC2	7.8 wks	Fri 2/13/26	Wed 4/8/26
48	Flooring - FC3	6 wks	Fri 2/13/26	Thu 3/26/26
49	Flooring - FC4	6 wks	Fri 2/13/26	Thu 3/26/26
50	Flooring - LVT1	8.8 wks	Fri 2/13/26	Wed 4/15/26
51	Flooring - VCT1	6 wks	Fri 2/13/26	Thu 3/26/26
52	Flooring - FT1	4.4 wks	Wed 2/11/26	Thu 3/12/26
53	Flooring - FT2	6.6 wks	Wed 2/11/26	Fri 3/27/26
54	Wall Tile - WT1	2 wks	Wed 2/11/26	Tue 2/24/26
55	Wall Tile - WT2	2 wks	Wed 2/11/26	Tue 2/24/26
56	Wall Tile - WT3	7.8 wks	Wed 2/11/26	Mon 4/6/26
57	Wall Tile - WT4	3.6 wks	Wed 2/11/26	Fri 3/6/26
58	Doors, Frames, and Hardware Submittal Review	5 days	Mon 2/16/26	Fri 2/20/26
59	Door Frames	5 wks	Wed 2/25/26	Tue 3/31/26
60	Doors, Hardware	8 wks	Mon 2/23/26	Fri 4/17/26
61	Appliances	8 wks	Mon 1/26/26	Fri 3/20/26
62	Breakroom Ceiling Baffle Product Selection (by others)	6 days	Thu 2/19/26	Thu 2/26/26
63	Ceiling Baffles - Breakroom	10 wks	Thu 2/26/26	Wed 5/6/26

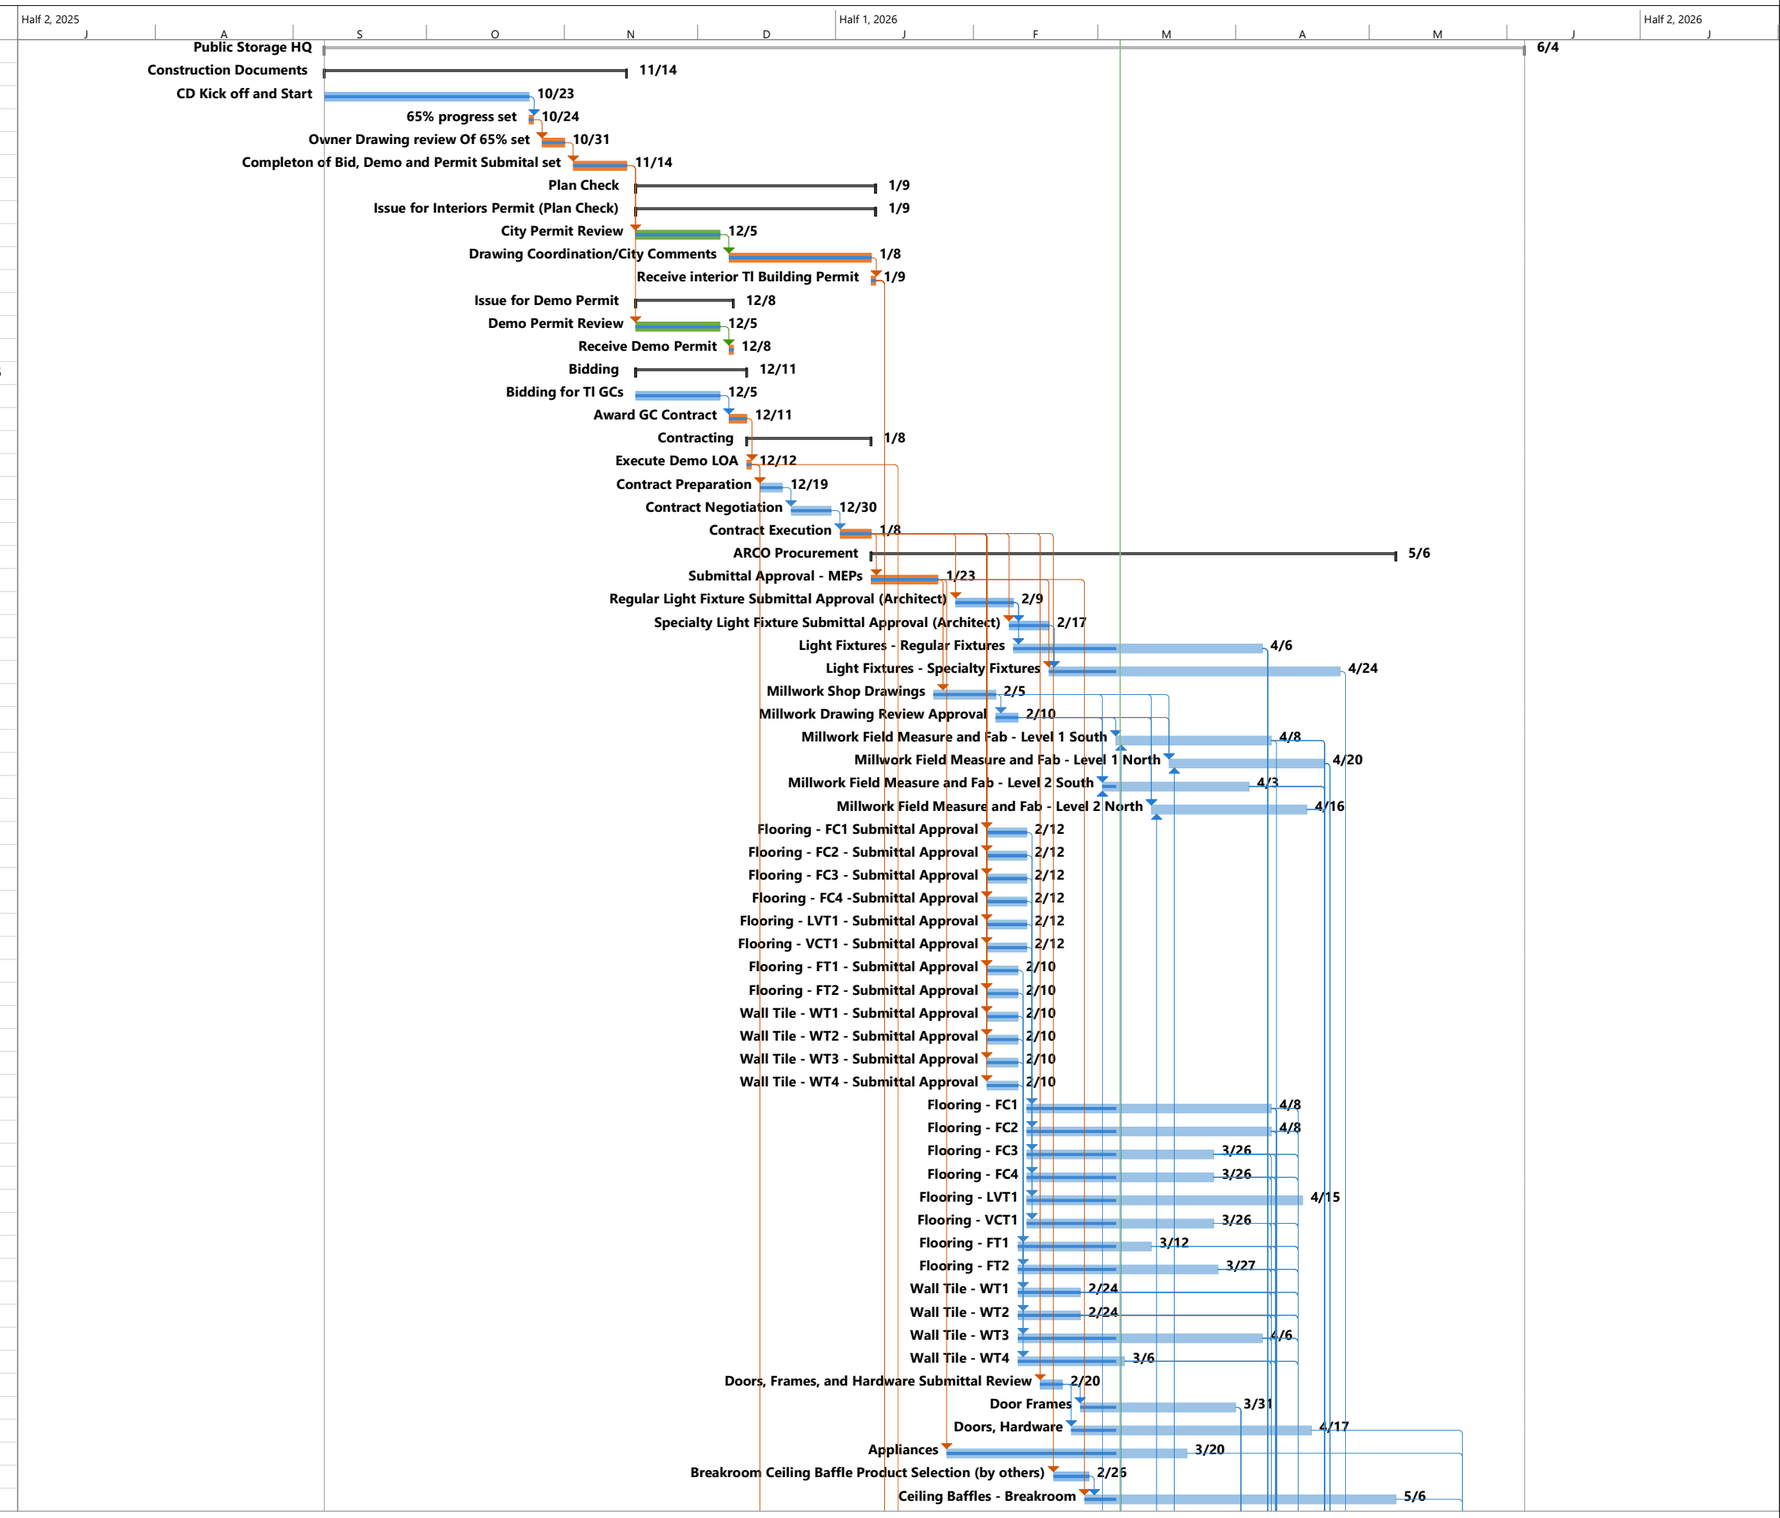

Public Storage HQ - Project Orange
Preliminary Project Schedule
2811 Internet Blvd
Frisco, TX 75034

ID	Task Name	Duration	Start	Finish
64	**Procurement Of Direct FBO items**	**116 days**	**Mon 11/3/25**	**Fri 4/17/26**
65	**Furniture**	**116 days**	**Mon 11/3/25**	**Fri 4/17/26**
66	Select Furniture Vendor	1 day	Thu 2/19/26	Thu 2/19/26
67	Review and finalize details for furniture	15 days	Mon 11/3/25	Fri 11/21/25
68	Furniture Order Due	1 day	Mon 11/24/25	Mon 11/24/25
69	Furniture Lead Time	80 days	Tue 12/23/25	Fri 4/17/26
70	**HVAC Equipment**	**80 days**	**Tue 12/9/25**	**Fri 4/3/26**
71	Order Roof Top HVAC equipment	1 day	Tue 12/9/25	Tue 12/9/25
72	HVAC Equipment Lead Time - RTUs	58 days	Tue 12/9/25	Wed 3/4/26
73	HVAC Equipment Lead Time - VAVs (Round 1)	58 days	Tue 12/9/25	Wed 3/4/26
74	HVAC Equipment Lead Time - VAVs (Round 2)	32 days	Thu 2/19/26	Fri 4/3/26
75	**Elevator Modernization**	**60 days**	**Tue 1/13/26**	**Mon 4/6/26**
76	Contract for Elevator Modernization	1 day	Thu 2/19/26	Thu 2/19/26
77	Elevator Equipment Lead Time	35 days	Tue 1/13/26	Mon 3/2/26
78	Elevator Modernization	25 days	Tue 3/3/26	Mon 4/6/26
79	**Demolition**	**34 days**	**Mon 12/15/25**	**Wed 2/4/26**
80	MEP/F Make Safe	3 wks	Mon 12/15/25	Thu 1/8/26
81	Demolition	3 wks	Thu 1/15/26	Wed 2/4/26
82	**Construction**	**102 days**	**Mon 1/12/26**	**Wed 6/3/26**
83	**Level 1 South**	**82.5 days**	**Mon 1/12/26**	**Wed 5/6/26**
84	Overhead MEP Rough In	20 days	Mon 1/12/26	Fri 2/6/26
85	Low Voltage Bulk Cabling	10 days	Thu 2/19/26	Wed 3/4/26
86	Slab Demo and Coring	4 days	Tue 1/20/26	Fri 1/23/26
87	Walls - Studs and Track	4 days	Thu 1/22/26	Tue 1/27/26
88	Underslab MEP	6 days	Mon 1/26/26	Mon 2/2/26
89	Underslab MEP Inspection	1 day	Thu 2/19/26	Thu 2/19/26
90	Concrete Slab Pourback	2 days	Fri 2/20/26	Mon 2/23/26
91	Fire Alarm Rough-in	2 days	Thu 2/19/26	Fri 2/20/26
92	MEP Rough-in Walls	10 days	Fri 1/23/26	Thu 2/5/26
93	MEP Rough-in Inspection	5 days	Fri 2/6/26	Thu 2/12/26
94	Single Side Drywall	5 days	Thu 2/19/26	Wed 2/25/26
95	Second Side Drywall	5 days	Thu 2/26/26	Wed 3/4/26
96	Wall Tape and Bed	13 days	Tue 2/17/26	Thu 3/5/26
97	Grid Install Rework	5 days	Thu 3/12/26	Wed 3/18/26
98	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	Tue 4/7/26	Thu 4/16/26
99	Light Fixture Install (Specialty)	8 days	Fri 4/24/26	Wed 5/6/26
100	Ceiling Cover Inspection	1 day	Fri 4/17/26	Fri 4/17/26
101	Ceiling Tile Installation	3 days	Fri 4/24/26	Tue 4/28/26
102	Restroom Renovations	10 days	Fri 3/27/26	Fri 4/10/26
103	Carpet and Tile Prep and Install	6 days	Fri 4/10/26	Fri 4/17/26
104	Painting	10 days	Fri 3/6/26	Thu 3/19/26
105	MEP Trimout	8 days	Fri 4/10/26	Tue 4/21/26
106	Millwork Install	5 days	Thu 4/9/26	Wed 4/15/26
107	**Level 1 North**	**81 days**	**Mon 1/12/26**	**Mon 5/4/26**
108	Overhead MEP Rough In	20 days	Mon 1/12/26	Fri 2/6/26
109	Low Voltage Bulk Cabling	10 days	Thu 2/19/26	Wed 3/4/26
110	Slab Demo and Coring	3 days	Mon 1/26/26	Wed 1/28/26
111	Walls - Studs and Track	3 days	Mon 2/9/26	Wed 2/11/26
112	Underslab MEP	3 days	Thu 1/29/26	Mon 2/2/26
113	Underslab MEP Inspection	1 day	Thu 2/19/26	Thu 2/19/26
114	Concrete Slab Pourback	4 days	Fri 2/20/26	Wed 2/25/26
115	Fire Alarm Rough-in	2 days	Thu 2/19/26	Fri 2/20/26
116	MEP Rough-in Walls	10 days	Mon 2/23/26	Fri 3/6/26
117	MEP Rough-in Inspection	1 day	Mon 3/9/26	Mon 3/9/26
118	Single Side Drywall	5 days	Thu 2/19/26	Wed 2/25/26
119	Second Side Drywall	5 days	Tue 3/10/26	Mon 3/16/26
120	Wall Tape and Bed	6 days	Wed 4/1/26	Wed 4/8/26
121	Grid Install Rework	4 days	Thu 4/2/26	Tue 4/7/26
122	Light Fixture Install (Regular) and Ceiling MEP Finishes	12 days	Tue 4/7/26	Wed 4/22/26
123	Ceiling Cover Inspection	1 day	Thu 4/23/26	Thu 4/23/26
124	Ceiling Tile Installation	5 days	Fri 4/24/26	Thu 4/30/26
125	Restroom Renovations	10 days	Thu 3/26/26	Thu 4/9/26
126	Carpet and Tile Prep and Install	7 days	Thu 4/9/26	Fri 4/17/26
127	Painting	10 days	Thu 4/9/26	Wed 4/22/26

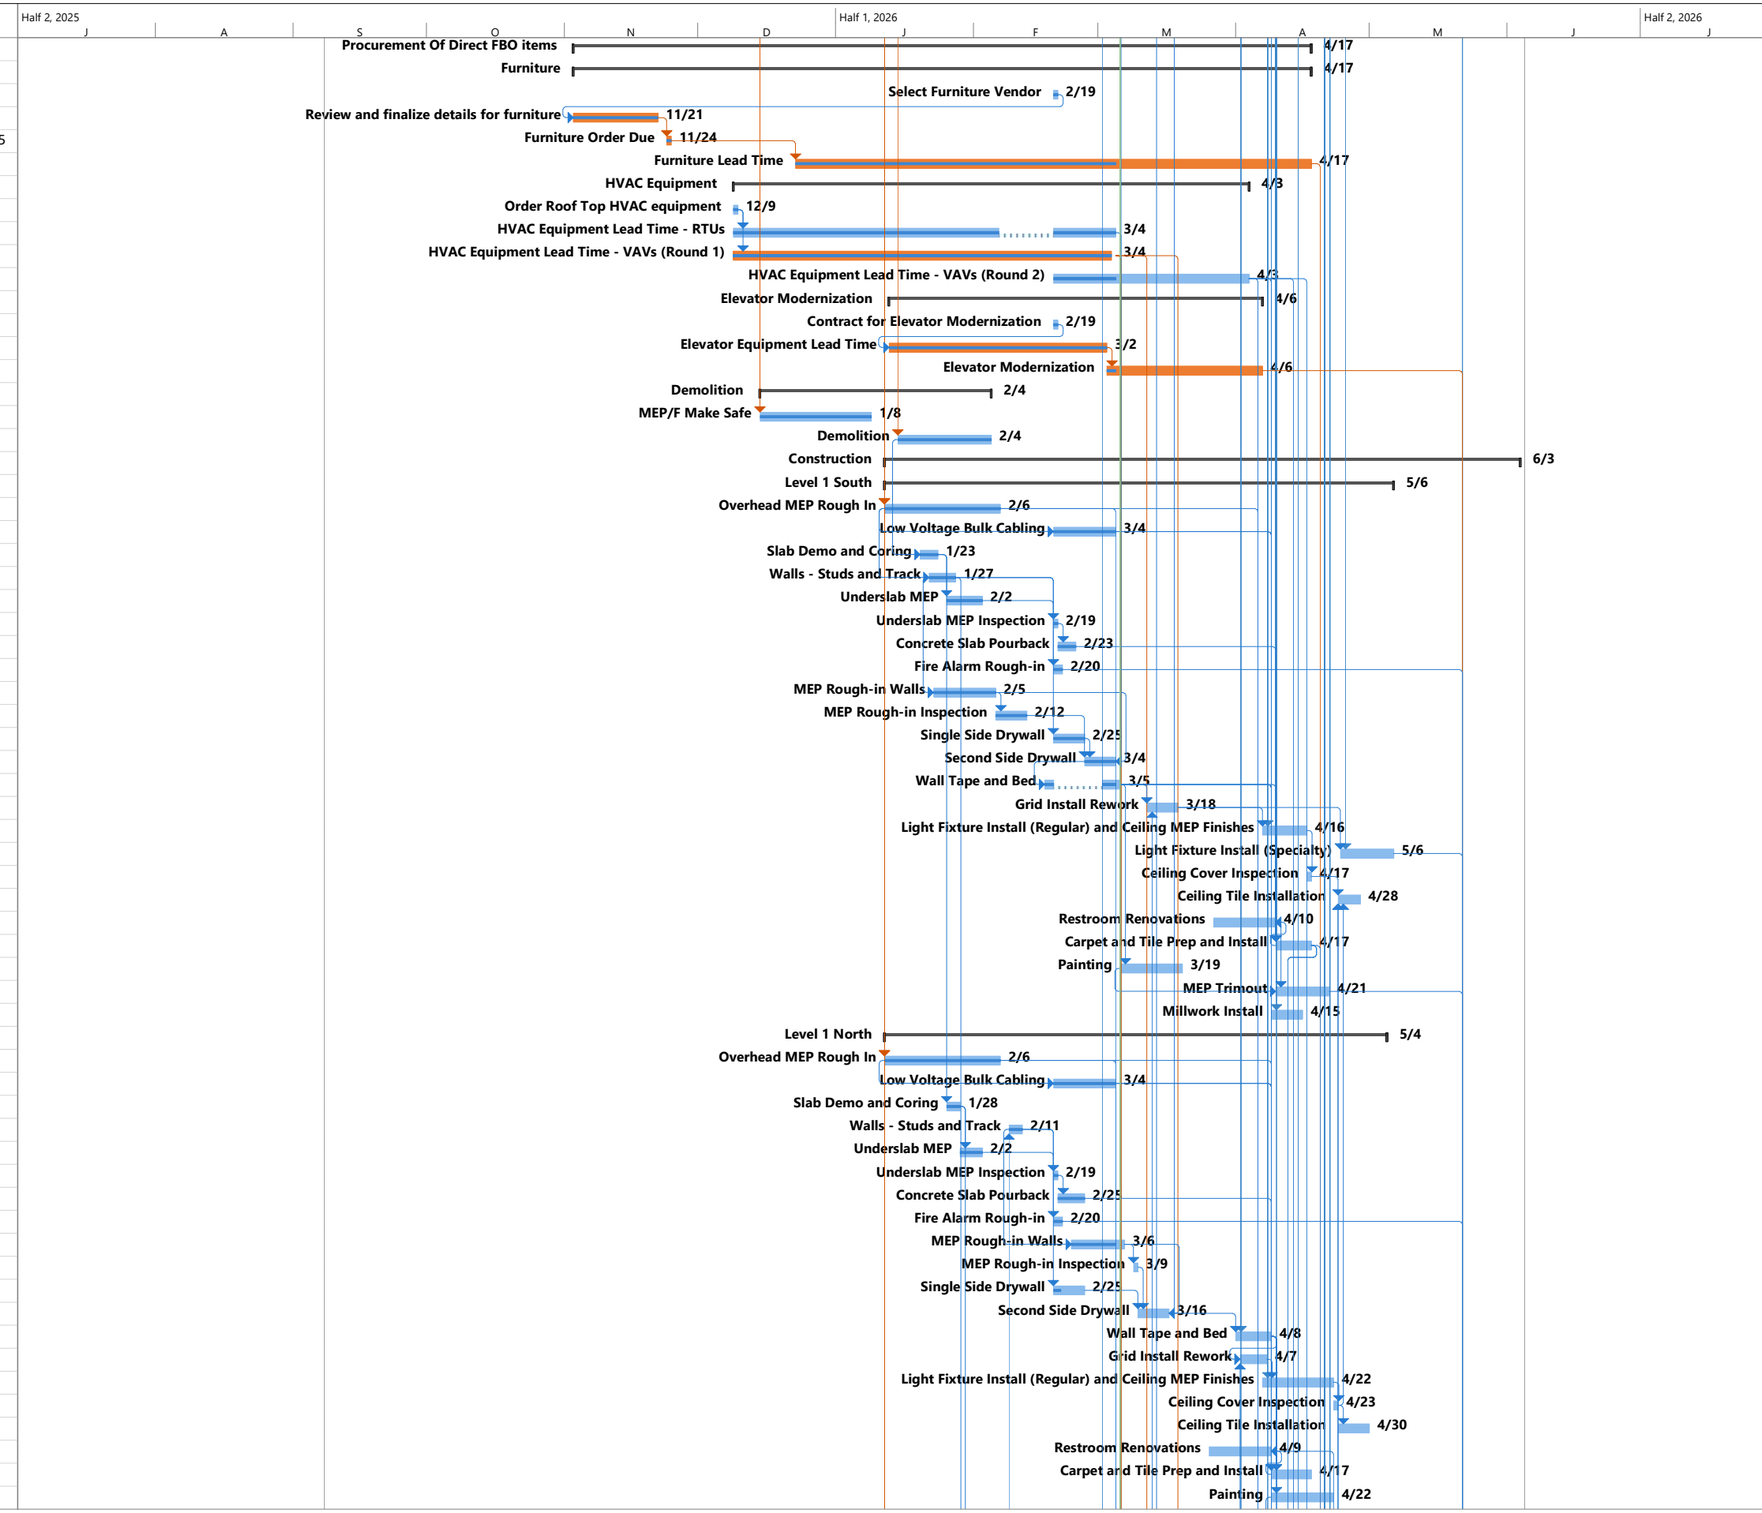

Public Storage HQ - Project Orange
Preliminary Project Schedule
2811 Internet Blvd
Frisco, TX 75034
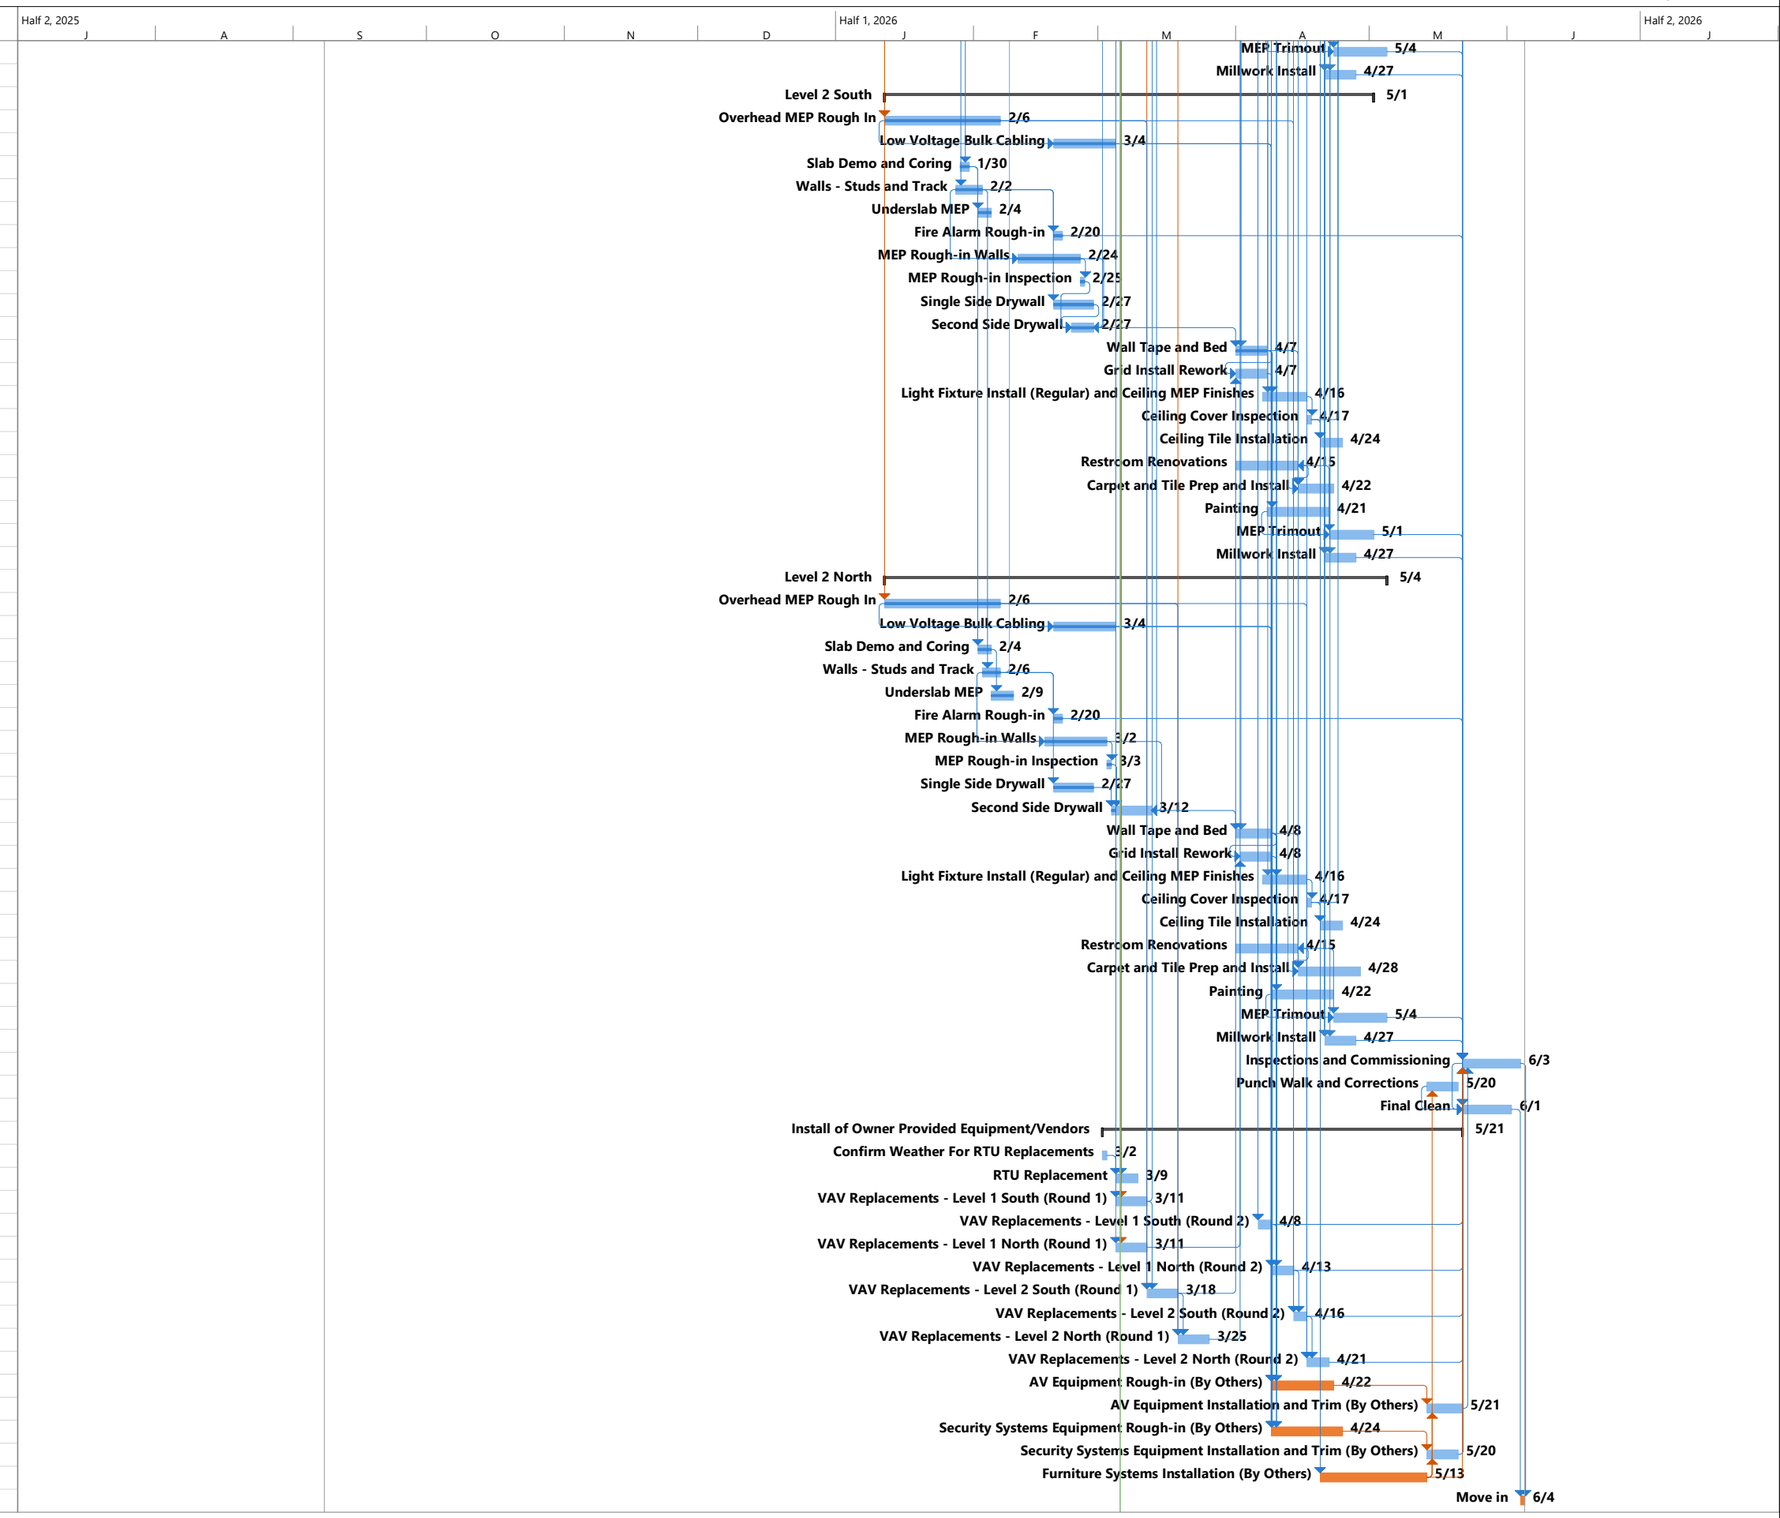
ID	Task Name	Duration	Start	Finish
128	MEP Trimout	8 days	Thu 4/23/26	Mon 5/4/26
129	Millwork Install	5 days	Tue 4/21/26	Mon 4/27/26
130	**Level 2 South**	**80 days**	**Mon 1/12/26**	**Fri 5/1/26**
131	Overhead MEP Rough In	20 days	Mon 1/12/26	Fri 2/6/26
132	Low Voltage Bulk Cabling	10 days	Thu 2/19/26	Wed 3/4/26
133	Slab Demo and Coring	2 days	Thu 1/29/26	Fri 1/30/26
134	Walls - Studs and Track	4 days	Wed 1/28/26	Mon 2/2/26
135	Underslab MEP	3 days	Mon 2/2/26	Wed 2/4/26
136	Fire Alarm Rough-in	2 days	Thu 2/19/26	Fri 2/20/26
137	MEP Rough-in Walls	10 days	Wed 2/11/26	Tue 2/24/26
138	MEP Rough-in Inspection	1 day	Wed 2/25/26	Wed 2/25/26
139	Single Side Drywall	7 days	Thu 2/19/26	Fri 2/27/26
140	Second Side Drywall	5 days	Mon 2/23/26	Fri 2/27/26
141	Wall Tape and Bed	5 days	Wed 4/1/26	Tue 4/7/26
142	Grid Install Rework	5 days	Wed 4/1/26	Tue 4/7/26
143	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	Tue 4/7/26	Thu 4/16/26
144	Ceiling Cover Inspection	1 day	Fri 4/17/26	Fri 4/17/26
145	Ceiling Tile Installation	5 days	Mon 4/20/26	Fri 4/24/26
146	Restroom Renovations	10 days	Wed 4/1/26	Wed 4/15/26
147	Carpet and Tile Prep and Install	6 days	Wed 4/15/26	Wed 4/22/26
148	Painting	10 days	Wed 4/8/26	Tue 4/21/26
149	MEP Trimout	8 days	Wed 4/22/26	Fri 5/1/26
150	Millwork Install	5 days	Tue 4/21/26	Mon 4/27/26
151	**Level 2 North**	**81 days**	**Mon 1/12/26**	**Mon 5/4/26**
152	Overhead MEP Rough In	20 days	Mon 1/12/26	Fri 2/6/26
153	Low Voltage Bulk Cabling	10 days	Thu 2/19/26	Wed 3/4/26
154	Slab Demo and Coring	3 days	Mon 2/2/26	Wed 2/4/26
155	Walls - Studs and Track	4 days	Tue 2/3/26	Fri 2/6/26
156	Underslab MEP	3 days	Thu 2/5/26	Mon 2/9/26
157	Fire Alarm Rough-in	2 days	Thu 2/19/26	Fri 2/20/26
158	MEP Rough-in Walls	10 days	Tue 2/17/26	Mon 3/2/26
159	MEP Rough-in Inspection	1 day	Tue 3/3/26	Tue 3/3/26
160	Single Side Drywall	7 days	Thu 2/19/26	Fri 2/27/26
161	Second Side Drywall	7 days	Wed 3/4/26	Thu 3/12/26
162	Wall Tape and Bed	6 days	Wed 4/1/26	Wed 4/8/26
163	Grid Install Rework	5 days	Thu 4/2/26	Wed 4/8/26
164	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	Tue 4/7/26	Thu 4/16/26
165	Ceiling Cover Inspection	1 day	Fri 4/17/26	Fri 4/17/26
166	Ceiling Tile Installation	5 days	Mon 4/20/26	Fri 4/24/26
167	Restroom Renovations	10 days	Wed 4/1/26	Wed 4/15/26
168	Carpet and Tile Prep and Install	10 days	Wed 4/15/26	Tue 4/28/26
169	Painting	10 days	Thu 4/9/26	Wed 4/22/26
170	MEP Trimout	8 days	Thu 4/23/26	Mon 5/4/26
171	Millwork Install	5 days	Tue 4/21/26	Mon 4/27/26
172	Inspections and Commissioning	8 days	Fri 5/22/26	Wed 6/3/26
173	Punch Walk and Corrections	5 days	Thu 5/14/26	Wed 5/20/26
174	Final Clean	6 days	Fri 5/22/26	Mon 6/1/26
175	**Install of Owner Provided Equipment/Vendors**	**59 days**	**Mon 3/2/26**	**Thu 5/21/26**
176	Confirm Weather For RTU Replacements	1 day	Mon 3/2/26	Mon 3/2/26
177	RTU Replacement	3 days	Thu 3/5/26	Mon 3/9/26
178	VAV Replacements - Level 1 South (Round 1)	5 days	Thu 3/5/26	Wed 3/11/26
179	VAV Replacements - Level 1 South (Round 2)	3 days	Mon 4/6/26	Wed 4/8/26
180	VAV Replacements - Level 1 North (Round 1)	5 days	Thu 3/5/26	Wed 3/11/26
181	VAV Replacements - Level 1 North (Round 2)	3 days	Thu 4/9/26	Mon 4/13/26
182	VAV Replacements - Level 2 South (Round 1)	5 days	Thu 3/12/26	Wed 3/18/26
183	VAV Replacements - Level 2 South (Round 2)	3 days	Tue 4/14/26	Thu 4/16/26
184	VAV Replacements - Level 2 North (Round 1)	5 days	Thu 3/19/26	Wed 3/25/26
185	VAV Replacements - Level 2 North (Round 2)	3 days	Fri 4/17/26	Tue 4/21/26
186	AV Equipment Rough-in (By Others)	10 days	Thu 4/9/26	Wed 4/22/26
187	AV Equipment Installation and Trim (By Others)	6 days	Thu 5/14/26	Thu 5/21/26
188	Security Systems Equipment Rough-in (By Others)	12 days	Thu 4/9/26	Fri 4/24/26
189	Security Systems Equipment Installation and Trim (By Others)	5 days	Thu 5/14/26	Wed 5/20/26
190	Furniture Systems Installation (By Others)	18 days	Mon 4/20/26	Wed 5/13/26
191	Move in	1 day	Thu 6/4/26	Thu 6/4/26
