	Name	Duration: Current	Duration: Previous	Duratı Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish Diff
1	**Construction Documents**	**50 days**	**50 days**	**0d**	**Mon 9/8/25**	**Mon 9/8/25**	**0d**	**Fri 11/14/25**	**Fri 11/14/25**	**0d**
2	CD Kick off and Start	34 days	34 days	0d	Mon 9/8/25	Mon 9/8/25	0d	Thu 10/23/25	Thu 10/23/25	0d
3	65% progress set	1 day	1 day	0d	Fri 10/24/25	Fri 10/24/25	0d	Fri 10/24/25	Fri 10/24/25	0d
4	Owner Drawing review Of 65% set	5 days	5 days	0d	Mon 10/27/25	Mon 10/27/25	0d	Fri 10/31/25	Fri 10/31/25	0d
5	Completon of Bid, Demo and Permit Submital set	10 days	10 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Fri 11/14/25	Fri 11/14/25	0d
6	**Plan Check**	**36 days**	**36 days**	**0d**	**Mon 11/17/25**	**Mon 11/17/25**	**0d**	**Fri 1/9/26**	**Fri 1/9/26**	**0d**
7	**Issue for Interiors Permit (Plan Check)**	**36 days**	**36 days**	**0d**	**Mon 11/17/25**	**Mon 11/17/25**	**0d**	**Fri 1/9/26**	**Fri 1/9/26**	**0d**
8	City Permit Review	15 days	15 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Fri 12/5/25	Fri 12/5/25	0d
9	Drawing Coordination/City Comments	20 days	20 days	0d	Mon 12/8/25	Mon 12/8/25	0d	Thu 1/8/26	Thu 1/8/26	0d
10	Receive interior Tl Building Permit	1 day	1 day	0d	Fri 1/9/26	Fri 1/9/26	0d	Fri 1/9/26	Fri 1/9/26	0d
11	**Issue for Demo Permit**	**16 days**	**16 days**	**0d**	**Mon 11/17/25**	**Mon 11/17/25**	**0d**	**Mon 12/8/25**	**Mon 12/8/25**	**0d**
12	Demo Permit Review	15 days	15 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Fri 12/5/25	Fri 12/5/25	0d
13	Receive Demo Permit	1 day	1 day	0d	Mon 12/8/25	Mon 12/8/25	0d	Mon 12/8/25	Mon 12/8/25	0d
14	**Bidding**	**19 days**	**19 days**	**0d**	**Mon 11/17/25**	**Mon 11/17/25**	**0d**	**Thu 12/11/25**	**Thu 12/11/25**	**0d**
15	Bidding for Tl GCs	15 days	15 days	0d	Mon 11/17/25	Mon 11/17/25	0d	Fri 12/5/25	Fri 12/5/25	0d
16	Award GC Contract	4 days	4 days	0d	Mon 12/8/25	Mon 12/8/25	0d	Thu 12/11/25	Thu 12/11/25	0d
17	**Contracting**	**16 days**	**16 days**	**0d**	**Fri 12/12/25**	**Fri 12/12/25**	**0d**	**Thu 1/8/26**	**Thu 1/8/26**	**0d**
18	Execute Demo LOA	1 day	1 day	0d	Fri 12/12/25	Fri 12/12/25	0d	Fri 12/12/25	Fri 12/12/25	0d
19	Contract Preparation	5 days	5 days	0d	Mon 12/15/25	Mon 12/15/25	0d	Fri 12/19/25	Fri 12/19/25	0d
20	Contract Negotiation	5 days	5 days	0d	Mon 12/22/25	Mon 12/22/25	0d	Tue 12/30/25	Tue 12/30/25	0d
21	Contract Execution	5 days	5 days	0d	Fri 1/2/26	Fri 1/2/26	0d	Thu 1/8/26	Thu 1/8/26	0d
22	**ARCO Procurement**	**84 days**	**84 days**	**0d**	**Fri 1/9/26**	**Fri 1/9/26**	**0d**	**Wed 5/6/26**	**Wed 5/6/26**	**0d**
23	Submittal Approval - MEPs	2.2 wks	2.2 wks	0d	Fri 1/9/26	Fri 1/9/26	0d	Fri 1/23/26	Fri 1/23/26	0d
24	Regular Light Fixture Submittal Approval (Architect)	9 days	9 days	0d	Wed 1/28/26	Wed 1/28/26	0d	Mon 2/9/26	Mon 2/9/26	0d
25	Specialty Light Fixture Submittal Approval (Architect)	7 days	7 days	0d	Mon 2/9/26	Mon 2/9/26	0d	Tue 2/17/26	Tue 2/17/26	0d
26	Light Fixtures - Regular Fixtures	8 wks	8 wks	0d	Tue 2/10/26	Tue 2/10/26	0d	Mon 4/6/26	Mon 4/6/26	0d
27	Light Fixtures - Specialty Fixtures	9.5 wks	9.5 wks	0d	Wed 2/18/26	Wed 2/18/26	0d	Fri 4/24/26	Fri 4/24/26	0d
28	Millwork Shop Drawings	2 wks	2 wks	0d	Fri 1/23/26	Fri 1/23/26	0d	Thu 2/5/26	Thu 2/5/26	0d
29	Millwork Drawing Review Approval	3 days	3 days	0d	Fri 2/6/26	Fri 2/6/26	0d	Tue 2/10/26	Tue 2/10/26	0d
30	Millwork Field Measure and Fab - Level 1 South	5 wks	5 wks	0d	Thu 3/5/26	Thu 3/5/26	0d	Wed 4/8/26	Wed 4/8/26	0d
31	Millwork Field Measure and Fab - Level 1 North	5 wks	5 wks	0d	Tue 3/17/26	Tue 3/17/26	0d	Mon 4/20/26	Mon 4/20/26	0d
32	Millwork Field Measure and Fab - Level 2 South	5 wks	5 wks	0d	Mon 3/2/26	Wed 3/11/26	-7d	Fri 4/3/26	Tue 4/14/26	-7d
33	Millwork Field Measure and Fab - Level 2 North	5 wks	5 wks	0d	Fri 3/13/26	Fri 3/13/26	0d	Thu 4/16/26	Thu 4/16/26	0d
34	Flooring - FC1 Submittal Approval	1.4 wks	1.4 wks	0d	Wed 2/4/26	Wed 2/4/26	0d	Thu 2/12/26	Thu 2/12/26	0d
35	Flooring - FC2 - Submittal Approval	1.4 wks	1.4 wks	0d	Wed 2/4/26	Wed 2/4/26	0d	Thu 2/12/26	Thu 2/12/26	0d
36	Flooring - FC3 - Submittal Approval	1.4 wks	1.4 wks	0d	Wed 2/4/26	Wed 2/4/26	0d	Thu 2/12/26	Thu 2/12/26	0d
37	Flooring - FC4 -Submittal Approval	1.4 wks	1.4 wks	0d	Wed 2/4/26	Wed 2/4/26	0d	Thu 2/12/26	Thu 2/12/26	0d
38	Flooring - LVT1 - Submittal Approval	1.4 wks	1.4 wks	0d	Wed 2/4/26	Wed 2/4/26	0d	Thu 2/12/26	Thu 2/12/26	0d
39	Flooring - VCT1 - Submittal Approval	1.4 wks	1.4 wks	0d	Wed 2/4/26	Wed 2/4/26	0d	Thu 2/12/26	Thu 2/12/26	0d
40	Flooring - FT1 - Submittal Approval	1 wk	1 wk	0d	Wed 2/4/26	Wed 2/4/26	0d	Tue 2/10/26	Tue 2/10/26	0d
41	Flooring - FT2 - Submittal Approval	1 wk	1 wk	0d	Wed 2/4/26	Wed 2/4/26	0d	Tue 2/10/26	Tue 2/10/26	0d
42	Wall Tile - WT1 - Submittal Approval	1 wk	1 wk	0d	Wed 2/4/26	Wed 2/4/26	0d	Tue 2/10/26	Tue 2/10/26	0d
43	Wall Tile - WT2 - Submittal Approval	1 wk	1 wk	0d	Wed 2/4/26	Wed 2/4/26	0d	Tue 2/10/26	Tue 2/10/26	0d
44	Wall Tile - WT3 - Submittal Approval	1 wk	1 wk	0d	Wed 2/4/26	Wed 2/4/26	0d	Tue 2/10/26	Tue 2/10/26	0d
45	Wall Tile - WT4 - Submittal Approval	1 wk	1 wk	0d	Wed 2/4/26	Wed 2/4/26	0d	Tue 2/10/26	Tue 2/10/26	0d
46	Flooring - FC1	7.8 wks	6 wks	9d	Fri 2/13/26	Fri 2/13/26	0d	Wed 4/8/26	Thu 3/26/26	9d
47	Flooring - FC2	7.8 wks	6 wks	9d	Fri 2/13/26	Fri 2/13/26	0d	Wed 4/8/26	Thu 3/26/26	9d
48	Flooring - FC3	6 wks	6 wks	0d	Fri 2/13/26	Fri 2/13/26	0d	Thu 3/26/26	Thu 3/26/26	0d
49	Flooring - FC4	6 wks	6 wks	0d	Fri 2/13/26	Fri 2/13/26	0d	Thu 3/26/26	Thu 3/26/26	0d
50	Flooring - LVT1	8.8 wks	6 wks	14d	Fri 2/13/26	Fri 2/13/26	0d	Wed 4/15/26	Thu 3/26/26	14d
51	Flooring - VCT1	6 wks	6 wks	0d	Fri 2/13/26	Fri 2/13/26	0d	Thu 3/26/26	Thu 3/26/26	0d
52	Flooring - FT1	4.4 wks	3 wks	7d	Wed 2/11/26	Wed 2/11/26	0d	Thu 3/12/26	Tue 3/3/26	7d
53	Flooring - FT2	6.6 wks	6 wks	3d	Wed 2/11/26	Wed 2/11/26	0d	Fri 3/27/26	Tue 3/24/26	3d
54	Wall Tile - WT1	2 wks	2 wks	0d	Wed 2/11/26	Wed 2/11/26	0d	Tue 2/24/26	Tue 2/24/26	0d
55	Wall Tile - WT2	2 wks	2 wks	0d	Wed 2/11/26	Wed 2/11/26	0d	Tue 2/24/26	Tue 2/24/26	0d
56	Wall Tile - WT3	7.8 wks	4 wks	19d	Wed 2/11/26	Wed 2/11/26	0d	Mon 4/6/26	Tue 3/10/26	19d
57	Wall Tile - WT4	3.6 wks	2 wks	8d	Wed 2/11/26	Wed 2/11/26	0d	Fri 3/6/26	Tue 2/24/26	8d
58	Doors, Frames, and Hardware Submittal Review	5 days	5 days	0d	Mon 2/16/26	Mon 2/16/26	0d	Fri 2/20/26	Fri 2/20/26	0d
59	Door Frames	5 wks	5 wks	0d	Wed 2/25/26	Wed 2/25/26	0d	Tue 3/31/26	Tue 3/31/26	0d
60	Doors, Hardware	8 wks	8 wks	0d	Mon 2/23/26	Mon 2/23/26	0d	Fri 4/17/26	Fri 4/17/26	0d
61	Appliances	8 wks	8 wks	0d	Mon 1/26/26	Mon 1/26/26	0d	Fri 3/20/26	Fri 3/20/26	0d
62	Breakroom Ceiling Baffle Product Selection (by others)	6 days	6 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Thu 2/26/26	Thu 2/26/26	0d
63	Ceiling Baffles - Breakroom	10 wks	10 wks	0d	Thu 2/26/26	Thu 2/26/26	0d	Wed 5/6/26	Wed 5/6/26	0d
64	**Procurement Of Direct FBO items**	**116 days**	**116 days**	**0d**	**Mon 11/3/25**	**Mon 11/3/25**	**0d**	**Fri 4/17/26**	**Fri 4/17/26**	**0d**

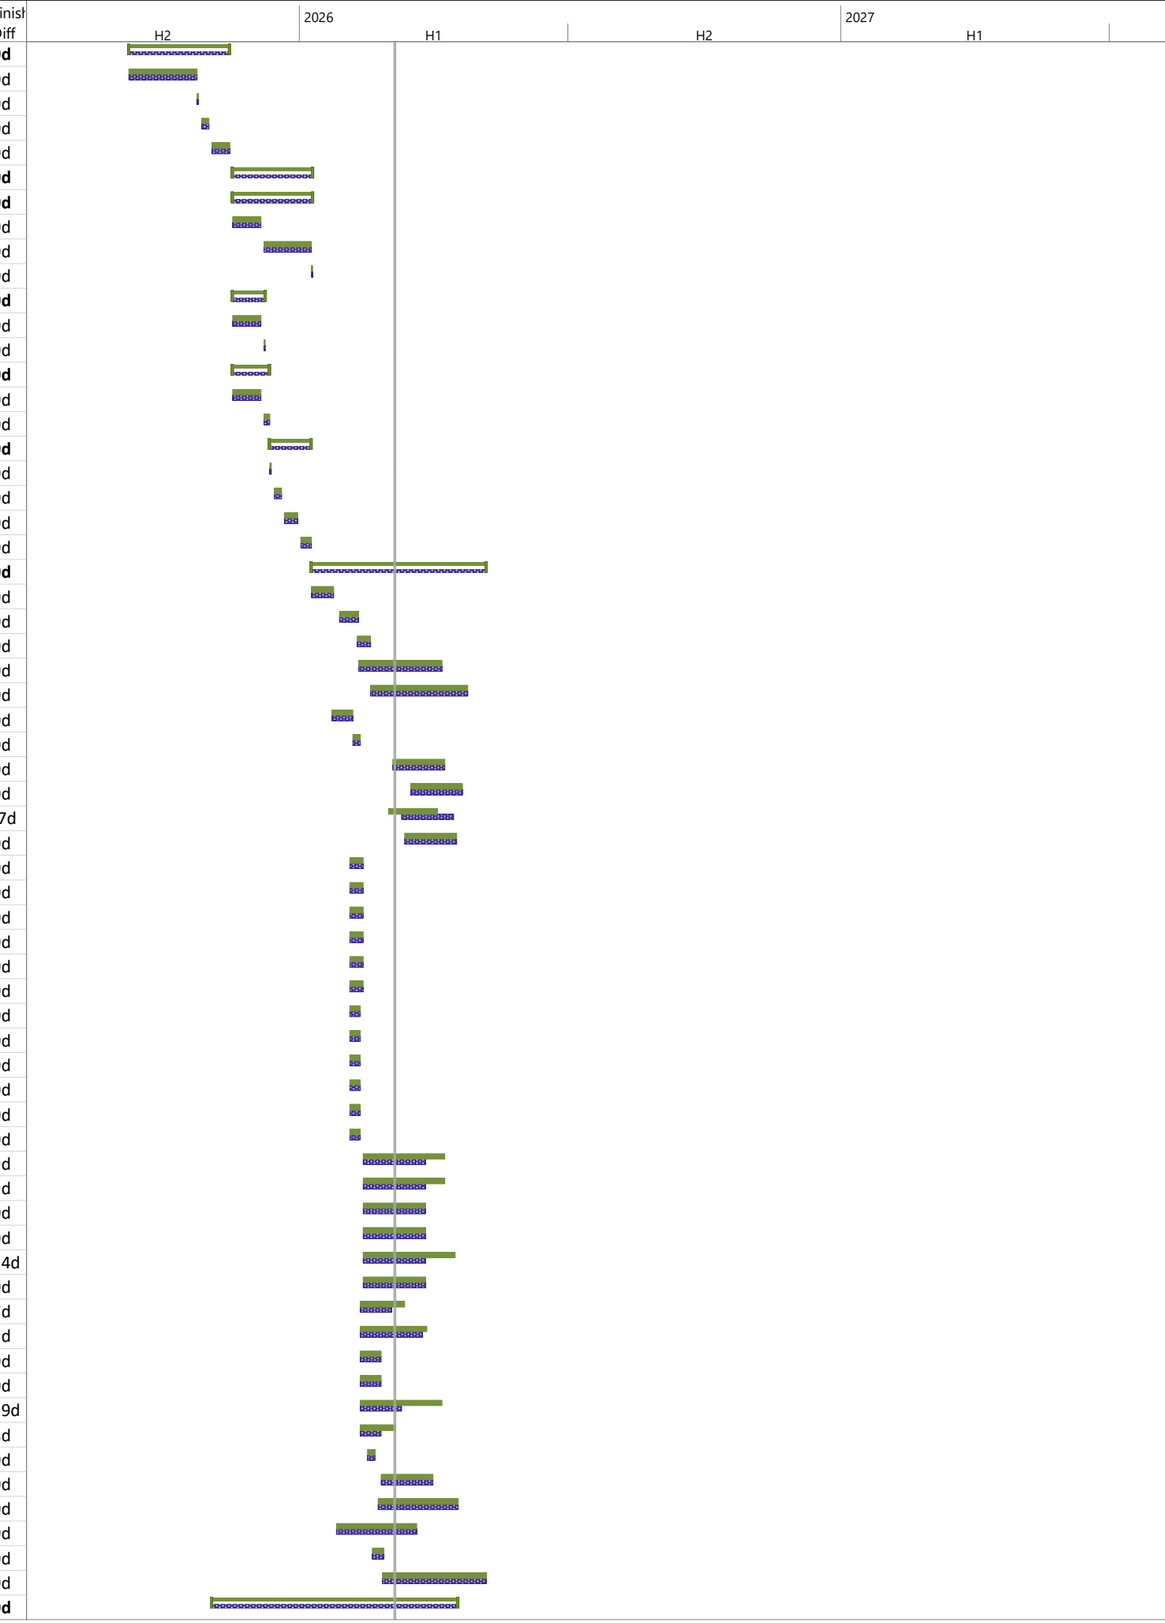

	Name	Duration: Current	Duration: Previous	Duratı Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish Diff
65	**Furniture**	**116 days**	**116 days**	**0d**	**Mon 11/3/25**	**Mon 11/3/25**	**0d**	**Fri 4/17/26**	**Fri 4/17/26**	**0d**
66	Select Furniture Vendor	1 day	1 day	0d	Thu 2/19/26	Thu 2/19/26	0d	Thu 2/19/26	Thu 2/19/26	0d
67	Review and finalize details for furniture	15 days	15 days	0d	Mon 11/3/25	Mon 11/3/25	0d	Fri 11/21/25	Fri 11/21/25	0d
68	Furniture Order Due	1 day	1 day	0d	Mon 11/24/25	Mon 11/24/25	0d	Mon 11/24/25	Mon 11/24/25	0d
69	Furniture Lead Time	80 days	80 days	0d	Tue 12/23/25	Tue 12/23/25	0d	Fri 4/17/26	Fri 4/17/26	0d
70	**HVAC Equipment**	**80 days**	**80 days**	**0d**	**Tue 12/9/25**	**Tue 12/9/25**	**0d**	**Fri 4/3/26**	**Fri 4/3/26**	**0d**
71	Order Roof Top HVAC equipment	1 day	1 day	0d	Tue 12/9/25	Tue 12/9/25	0d	Tue 12/9/25	Tue 12/9/25	0d
72	HVAC Equipment Lead Time - RTUs	58 days	58 days	0d	Tue 12/9/25	Tue 12/9/25	0d	Wed 3/4/26	Wed 3/4/26	0d
73	HVAC Equipment Lead Time - VAVs (Round 1)	58 days	58 days	0d	Tue 12/9/25	Tue 12/9/25	0d	Wed 3/4/26	Wed 3/4/26	0d
74	HVAC Equipment Lead Time - VAVs (Round 2)	32 days	32 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Fri 4/3/26	Fri 4/3/26	0d
75	**Elevator Modernization**	**60 days**	**60 days**	**0d**	**Tue 1/13/26**	**Tue 1/13/26**	**0d**	**Mon 4/6/26**	**Mon 4/6/26**	**0d**
76	Contract for Elevator Modernization	1 day	1 day	0d	Thu 2/19/26	Thu 2/19/26	0d	Thu 2/19/26	Thu 2/19/26	0d
77	Elevator Equipment Lead Time	35 days	35 days	0d	Tue 1/13/26	Tue 1/13/26	0d	Mon 3/2/26	Mon 3/2/26	0d
78	Elevator Modernization	25 days	25 days	0d	Tue 3/3/26	Tue 3/3/26	0d	Mon 4/6/26	Mon 4/6/26	0d
79	**Demolition**	**34 days**	**34 days**	**0d**	**Mon 12/15/25**	**Mon 12/15/25**	**0d**	**Wed 2/4/26**	**Wed 2/4/26**	**0d**
80	MEP/F Make Safe	3 wks	3 wks	0d	Mon 12/15/25	Mon 12/15/25	0d	Thu 1/8/26	Thu 1/8/26	0d
81	Demolition	3 wks	3 wks	0d	Thu 1/15/26	Thu 1/15/26	0d	Wed 2/4/26	Wed 2/4/26	0d
82	**Construction**	**102 days**	**103 days**	**-1d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Wed 6/3/26**	**Thu 6/4/26**	**-1d**
83	**Level 1 South**	**82.5 days**	**82.5 days**	**0d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Wed 5/6/26**	**Wed 5/6/26**	**0d**
84	Overhead MEP Rough In	20 days	20 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Fri 2/6/26	Fri 2/6/26	0d
85	Low Voltage Bulk Cabling	10 days	10 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Wed 3/4/26	Wed 3/4/26	0d
86	Slab Demo and Coring	4 days	4 days	0d	Tue 1/20/26	Tue 1/20/26	0d	Fri 1/23/26	Fri 1/23/26	0d
87	Walls - Studs and Track	4 days	4 days	0d	Thu 1/22/26	Thu 1/22/26	0d	Tue 1/27/26	Tue 1/27/26	0d
88	Underslab MEP	6 days	6 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Mon 2/2/26	Mon 2/2/26	0d
89	Underslab MEP Inspection	1 day	1 day	0d	Thu 2/19/26	Thu 2/19/26	0d	Thu 2/19/26	Thu 2/19/26	0d
90	Concrete Slab Pourback	2 days	2 days	0d	Fri 2/20/26	Fri 2/20/26	0d	Mon 2/23/26	Mon 2/23/26	0d
91	Fire Alarm Rough-in	2 days	2 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Fri 2/20/26	Fri 2/20/26	0d
92	MEP Rough-in Walls	10 days	10 days	0d	Fri 1/23/26	Fri 1/23/26	0d	Thu 2/5/26	Thu 2/5/26	0d
93	MEP Rough-in Inspection	5 days	5 days	0d	Fri 2/6/26	Fri 2/6/26	0d	Thu 2/12/26	Thu 2/12/26	0d
94	Single Side Drywall	5 days	5 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Wed 2/25/26	Wed 2/25/26	0d
95	Second Side Drywall	5 days	5 days	0d	Thu 2/26/26	Thu 2/26/26	0d	Wed 3/4/26	Wed 3/4/26	0d
96	Wall Tape and Bed	13 days	13 days	0d	Tue 2/17/26	Tue 2/17/26	0d	Thu 3/5/26	Thu 3/5/26	0d
97	Grid Install Rework	5 days	5 days	0d	Thu 3/12/26	Thu 3/12/26	0d	Wed 3/18/26	Wed 3/18/26	0d
98	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	8 days	0d	Tue 4/7/26	Tue 4/7/26	0d	Thu 4/16/26	Thu 4/16/26	0d
99	Light Fixture Install (Specialty)	8 days	8 days	0d	Fri 4/24/26	Fri 4/24/26	0d	Wed 5/6/26	Wed 5/6/26	0d
100	Ceiling Cover Inspection	1 day	1 day	0d	Fri 4/17/26	Fri 4/17/26	0d	Fri 4/17/26	Fri 4/17/26	0d
101	Ceiling Tile Installation	3 days	3 days	0d	Fri 4/24/26	Fri 4/24/26	0d	Tue 4/28/26	Tue 4/28/26	0d
102	Restroom Renovations	10 days	10 days	0d	Fri 3/27/26	Fri 3/13/26	10d	Fri 4/10/26	Fri 3/27/26	10d
103	Carpet and Tile Prep and Install	6 days	8 days	-2d	Fri 4/10/26	Fri 3/27/26	10d	Fri 4/17/26	Tue 4/7/26	8d
104	Painting	10 days	10 days	0d	Fri 3/6/26	Fri 3/6/26	0d	Thu 3/19/26	Thu 3/19/26	0d
105	MEP Trimout	8 days	8 days	0d	Fri 4/10/26	Fri 3/27/26	10d	Tue 4/21/26	Tue 4/7/26	10d
106	Millwork Install	5 days	5 days	0d	Thu 4/9/26	Thu 4/9/26	0d	Wed 4/15/26	Wed 4/15/26	0d
107	**Level 1 North**	**81 days**	**81 days**	**0d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Mon 5/4/26**	**Mon 5/4/26**	**0d**
108	Overhead MEP Rough In	20 days	20 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Fri 2/6/26	Fri 2/6/26	0d
109	Low Voltage Bulk Cabling	10 days	10 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Wed 3/4/26	Wed 3/4/26	0d
110	Slab Demo and Coring	3 days	3 days	0d	Mon 1/26/26	Mon 1/26/26	0d	Wed 1/28/26	Wed 1/28/26	0d
111	Walls - Studs and Track	3 days	3 days	0d	Mon 2/9/26	Mon 2/9/26	0d	Wed 2/11/26	Wed 2/11/26	0d
112	Underslab MEP	3 days	3 days	0d	Thu 1/29/26	Thu 1/29/26	0d	Mon 2/2/26	Mon 2/2/26	0d
113	Underslab MEP Inspection	1 day	1 day	0d	Thu 2/19/26	Thu 2/19/26	0d	Thu 2/19/26	Thu 2/19/26	0d
114	Concrete Slab Pourback	4 days	4 days	0d	Fri 2/20/26	Fri 2/20/26	0d	Wed 2/25/26	Wed 2/25/26	0d
115	Fire Alarm Rough-in	2 days	2 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Fri 2/20/26	Fri 2/20/26	0d
116	MEP Rough-in Walls	10 days	10 days	0d	Mon 2/23/26	Mon 2/23/26	0d	Fri 3/6/26	Fri 3/6/26	0d
117	MEP Rough-in Inspection	1 day	1 day	0d	Mon 3/9/26	Mon 3/9/26	0d	Mon 3/9/26	Mon 3/9/26	0d
118	Single Side Drywall	5 days	5 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Wed 2/25/26	Wed 2/25/26	0d
119	Second Side Drywall	5 days	5 days	0d	Tue 3/10/26	Tue 3/10/26	0d	Mon 3/16/26	Mon 3/16/26	0d
120	Wall Tape and Bed	6 days	6 days	0d	Wed 4/1/26	Wed 4/1/26	0d	Wed 4/8/26	Wed 4/8/26	0d
121	Grid Install Rework	4 days	4 days	0d	Thu 4/2/26	Thu 4/2/26	0d	Tue 4/7/26	Tue 4/7/26	0d
122	Light Fixture Install (Regular) and Ceiling MEP Finishes	12 days	12 days	0d	Tue 4/7/26	Tue 4/7/26	0d	Wed 4/22/26	Wed 4/22/26	0d
123	Ceiling Cover Inspection	1 day	1 day	0d	Thu 4/23/26	Thu 4/23/26	0d	Thu 4/23/26	Thu 4/23/26	0d
124	Ceiling Tile Installation	5 days	5 days	0d	Fri 4/24/26	Fri 4/24/26	0d	Thu 4/30/26	Thu 4/30/26	0d
125	Restroom Renovations	10 days	10 days	0d	Thu 3/26/26	Thu 3/26/26	0d	Thu 4/9/26	Thu 4/9/26	0d
126	Carpet and Tile Prep and Install	7 days	8 days	-1d	Thu 4/9/26	Thu 4/9/26	0d	Fri 4/17/26	Mon 4/20/26	-1d
127	Painting	10 days	10 days	0d	Thu 4/9/26	Thu 4/9/26	0d	Wed 4/22/26	Wed 4/22/26	0d
128	MEP Trimout	8 days	8 days	0d	Thu 4/23/26	Thu 4/23/26	0d	Mon 5/4/26	Mon 5/4/26	0d

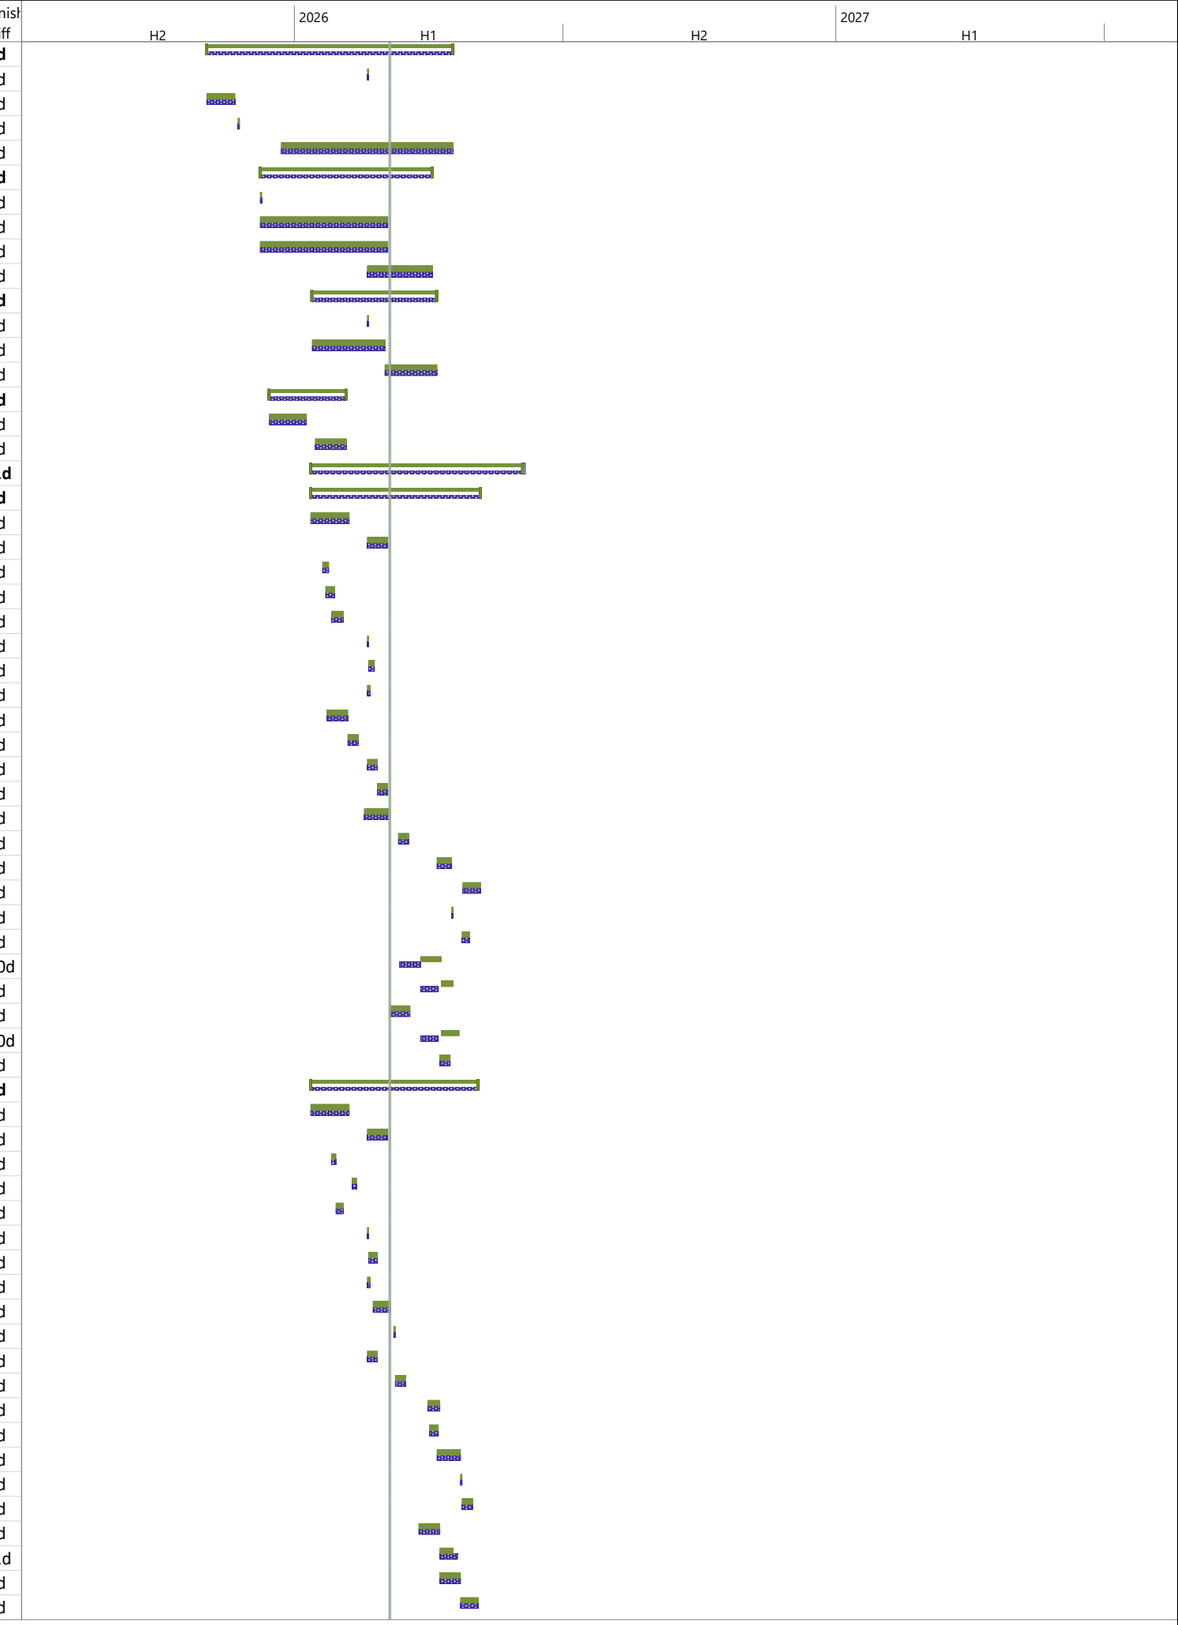
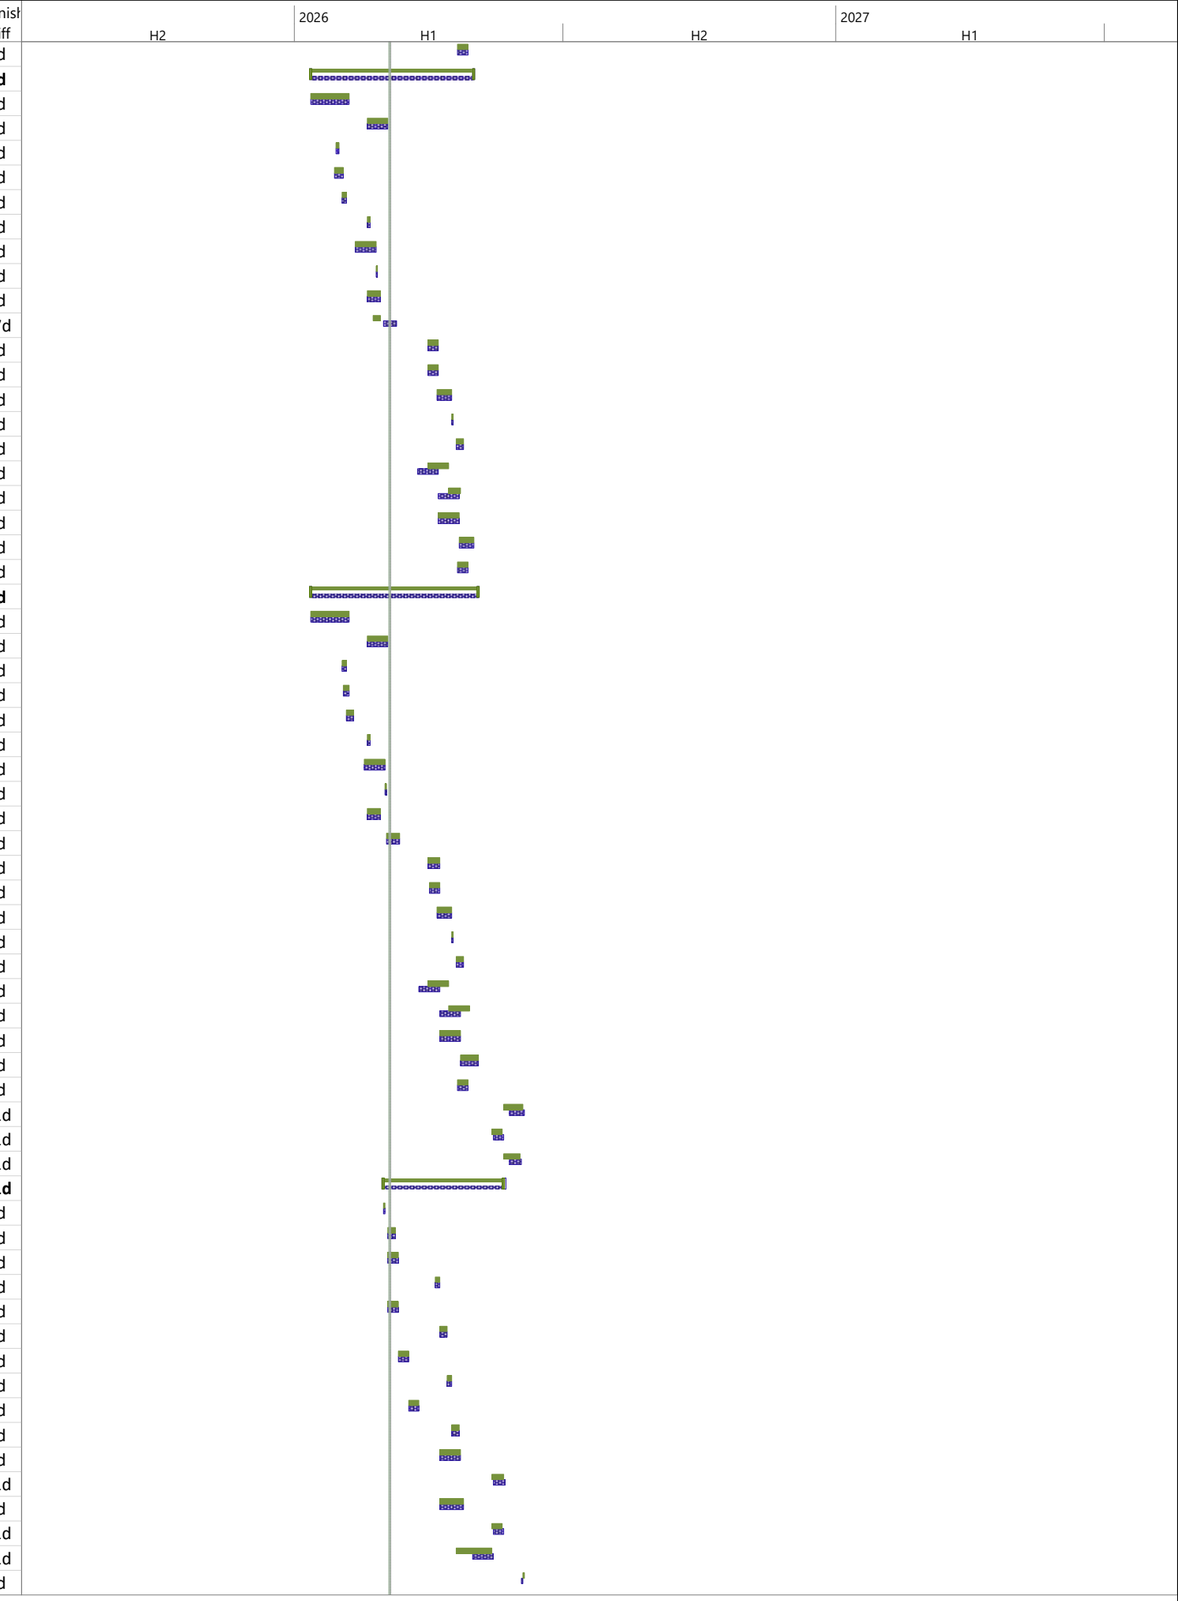
	Name	Duration: Current	Duration: Previous	Duratı Diff	Start: Current	Start: Previous	Start: Diff	Finish: Current	Finish: Previous	Finish Diff
129	Millwork Install	5 days	5 days	0d	Tue 4/21/26	Tue 4/21/26	0d	Mon 4/27/26	Mon 4/27/26	0d
130	**Level 2 South**	**80 days**	**80 days**	**0d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Fri 5/1/26**	**Fri 5/1/26**	**0d**
131	Overhead MEP Rough In	20 days	20 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Fri 2/6/26	Fri 2/6/26	0d
132	Low Voltage Bulk Cabling	10 days	10 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Wed 3/4/26	Wed 3/4/26	0d
133	Slab Demo and Coring	2 days	2 days	0d	Thu 1/29/26	Thu 1/29/26	0d	Fri 1/30/26	Fri 1/30/26	0d
134	Walls - Studs and Track	4 days	4 days	0d	Wed 1/28/26	Wed 1/28/26	0d	Mon 2/2/26	Mon 2/2/26	0d
135	Underslab MEP	3 days	3 days	0d	Mon 2/2/26	Mon 2/2/26	0d	Wed 2/4/26	Wed 2/4/26	0d
136	Fire Alarm Rough-in	2 days	2 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Fri 2/20/26	Fri 2/20/26	0d
137	MEP Rough-in Walls	10 days	10 days	0d	Wed 2/11/26	Wed 2/11/26	0d	Tue 2/24/26	Tue 2/24/26	0d
138	MEP Rough-in Inspection	1 day	1 day	0d	Wed 2/25/26	Wed 2/25/26	0d	Wed 2/25/26	Wed 2/25/26	0d
139	Single Side Drywall	7 days	7 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Fri 2/27/26	Fri 2/27/26	0d
140	Second Side Drywall	5 days	7 days	-2d	Mon 2/23/26	Mon 3/2/26	-5d	Fri 2/27/26	Tue 3/10/26	-7d
141	Wall Tape and Bed	5 days	5 days	0d	Wed 4/1/26	Wed 4/1/26	0d	Tue 4/7/26	Tue 4/7/26	0d
142	Grid Install Rework	5 days	5 days	0d	Wed 4/1/26	Wed 4/1/26	0d	Tue 4/7/26	Tue 4/7/26	0d
143	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	8 days	0d	Tue 4/7/26	Tue 4/7/26	0d	Thu 4/16/26	Thu 4/16/26	0d
144	Ceiling Cover Inspection	1 day	1 day	0d	Fri 4/17/26	Fri 4/17/26	0d	Fri 4/17/26	Fri 4/17/26	0d
145	Ceiling Tile Installation	5 days	5 days	0d	Mon 4/20/26	Mon 4/20/26	0d	Fri 4/24/26	Fri 4/24/26	0d
146	Restroom Renovations	10 days	10 days	0d	Wed 4/1/26	Wed 3/25/26	5d	Wed 4/15/26	Wed 4/8/26	5d
147	Carpet and Tile Prep and Install	6 days	10 days	-4d	Wed 4/15/26	Wed 4/8/26	5d	Wed 4/22/26	Tue 4/21/26	1d
148	Painting	10 days	10 days	0d	Wed 4/8/26	Wed 4/8/26	0d	Tue 4/21/26	Tue 4/21/26	0d
149	MEP Trimout	8 days	8 days	0d	Wed 4/22/26	Wed 4/22/26	0d	Fri 5/1/26	Fri 5/1/26	0d
150	Millwork Install	5 days	5 days	0d	Tue 4/21/26	Tue 4/21/26	0d	Mon 4/27/26	Mon 4/27/26	0d
151	**Level 2 North**	**81 days**	**81 days**	**0d**	**Mon 1/12/26**	**Mon 1/12/26**	**0d**	**Mon 5/4/26**	**Mon 5/4/26**	**0d**
152	Overhead MEP Rough In	20 days	20 days	0d	Mon 1/12/26	Mon 1/12/26	0d	Fri 2/6/26	Fri 2/6/26	0d
153	Low Voltage Bulk Cabling	10 days	10 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Wed 3/4/26	Wed 3/4/26	0d
154	Slab Demo and Coring - Level 2 North	3 days	3 days	0d	Mon 2/2/26	Mon 2/2/26	0d	Wed 2/4/26	Wed 2/4/26	0d
155	Walls - Studs and Track	4 days	4 days	0d	Tue 2/3/26	Tue 2/3/26	0d	Fri 2/6/26	Fri 2/6/26	0d
156	Underslab MEP	3 days	3 days	0d	Thu 2/5/26	Thu 2/5/26	0d	Mon 2/9/26	Mon 2/9/26	0d
157	Fire Alarm Rough-in	2 days	2 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Fri 2/20/26	Fri 2/20/26	0d
158	MEP Rough-in Walls	10 days	10 days	0d	Tue 2/17/26	Tue 2/17/26	0d	Mon 3/2/26	Mon 3/2/26	0d
159	MEP Rough-in Inspection	1 day	1 day	0d	Tue 3/3/26	Tue 3/3/26	0d	Tue 3/3/26	Tue 3/3/26	0d
160	Single Side Drywall	7 days	7 days	0d	Thu 2/19/26	Thu 2/19/26	0d	Fri 2/27/26	Fri 2/27/26	0d
161	Second Side Drywall - Level 2 North	7 days	7 days	0d	Wed 3/4/26	Wed 3/4/26	0d	Thu 3/12/26	Thu 3/12/26	0d
162	Wall Tape and Bed	6 days	6 days	0d	Wed 4/1/26	Wed 4/1/26	0d	Wed 4/8/26	Wed 4/8/26	0d
163	Grid Install Rework	5 days	5 days	0d	Thu 4/2/26	Thu 4/2/26	0d	Wed 4/8/26	Wed 4/8/26	0d
164	Light Fixture Install (Regular) and Ceiling MEP Finishes	8 days	8 days	0d	Tue 4/7/26	Tue 4/7/26	0d	Thu 4/16/26	Thu 4/16/26	0d
165	Ceiling Cover Inspection	1 day	1 day	0d	Fri 4/17/26	Fri 4/17/26	0d	Fri 4/17/26	Fri 4/17/26	0d
166	Ceiling Tile Installation - Level 2 North	5 days	5 days	0d	Mon 4/20/26	Mon 4/20/26	0d	Fri 4/24/26	Fri 4/24/26	0d
167	Restroom Renovations	10 days	10 days	0d	Wed 4/1/26	Thu 3/26/26	4d	Wed 4/15/26	Thu 4/9/26	4d
168	Carpet and Tile Prep and Install	10 days	10 days	0d	Wed 4/15/26	Thu 4/9/26	4d	Tue 4/28/26	Wed 4/22/26	4d
169	Painting	10 days	10 days	0d	Thu 4/9/26	Thu 4/9/26	0d	Wed 4/22/26	Wed 4/22/26	0d
170	MEP Trimout - Level 2 North	8 days	8 days	0d	Thu 4/23/26	Thu 4/23/26	0d	Mon 5/4/26	Mon 5/4/26	0d
171	Millwork Install	5 days	5 days	0d	Tue 4/21/26	Tue 4/21/26	0d	Mon 4/27/26	Mon 4/27/26	0d
172	Inspections and Commissioning	8 days	8 days	0d	Fri 5/22/26	Tue 5/26/26	-2d	Wed 6/3/26	Thu 6/4/26	-1d
173	Punch Walk and Corrections	5 days	5 days	0d	Thu 5/14/26	Fri 5/15/26	-1d	Wed 5/20/26	Thu 5/21/26	-1d
174	Final Clean	6 days	6 days	0d	Fri 5/22/26	Tue 5/26/26	-2d	Mon 6/1/26	Tue 6/2/26	-1d
175	**Install of Owner Provided Equipment/Vendors**	**59 days**	**60 days**	**-1d**	**Mon 3/2/26**	**Mon 3/2/26**	**0d**	**Thu 5/21/26**	**Fri 5/22/26**	**-1d**
176	Confirm Weather For RTU Replacements	1 day	1 day	0d	Mon 3/2/26	Mon 3/2/26	0d	Mon 3/2/26	Mon 3/2/26	0d
177	RTU Replacement	3 days	3 days	0d	Thu 3/5/26	Thu 3/5/26	0d	Mon 3/9/26	Mon 3/9/26	0d
178	VAV Replacements - Level 1 South (Round 1)	5 days	5 days	0d	Thu 3/5/26	Thu 3/5/26	0d	Wed 3/11/26	Wed 3/11/26	0d
179	VAV Replacements - Level 1 South (Round 2)	3 days	3 days	0d	Mon 4/6/26	Mon 4/6/26	0d	Wed 4/8/26	Wed 4/8/26	0d
180	VAV Replacements - Level 1 North (Round 1)	5 days	5 days	0d	Thu 3/5/26	Thu 3/5/26	0d	Wed 3/11/26	Wed 3/11/26	0d
181	VAV Replacements - Level 1 North (Round 2)	3 days	3 days	0d	Thu 4/9/26	Thu 4/9/26	0d	Mon 4/13/26	Mon 4/13/26	0d
182	VAV Replacements - Level 2 South (Round 1)	5 days	5 days	0d	Thu 3/12/26	Thu 3/12/26	0d	Wed 3/18/26	Wed 3/18/26	0d
183	VAV Replacements - Level 2 South (Round 2)	3 days	3 days	0d	Tue 4/14/26	Tue 4/14/26	0d	Thu 4/16/26	Thu 4/16/26	0d
184	VAV Replacements - Level 2 North (Round 1)	5 days	5 days	0d	Thu 3/19/26	Thu 3/19/26	0d	Wed 3/25/26	Wed 3/25/26	0d
185	VAV Replacements - Level 2 North	3 days	3 days	0d	Fri 4/17/26	Fri 4/17/26	0d	Tue 4/21/26	Tue 4/21/26	0d
186	AV Equipment Rough-in (By Others)	10 days	10 days	0d	Thu 4/9/26	Thu 4/9/26	0d	Wed 4/22/26	Wed 4/22/26	0d
187	AV Equipment Installation and Trim (By Others)	6 days	6 days	0d	Thu 5/14/26	Fri 5/15/26	-1d	Thu 5/21/26	Fri 5/22/26	-1d
188	Security Systems Equipment Rough-in (By Others)	12 days	12 days	0d	Thu 4/9/26	Thu 4/9/26	0d	Fri 4/24/26	Fri 4/24/26	0d
189	Security Systems Equipment Installation and Trim (By Others)	5 days	5 days	0d	Thu 5/14/26	Fri 5/15/26	-1d	Wed 5/20/26	Thu 5/21/26	-1d
190	Furniture Systems Installation (By Others)	18 days	10 days	8d	Mon 4/20/26	Fri 5/1/26	-9d	Wed 5/13/26	Thu 5/14/26	-1d
191	Move in	1 day	1 day	0d	Thu 6/4/26	Wed 6/3/26	1d	Thu 6/4/26	Wed 6/3/26	1d
