Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

Public Storage Dashboard

Data Date: 12/9/2025

Type	Project	Region	Responsible
Construction	Mesa, AZ	West Coast	Josh Pait

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
1/12/2026	5/12/2026	-120 Baseline 0 Previous	Remaining Work Compression: -38% — Normal

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
Foundation Complete		4/21/2025	4/21/2025	0	0	Pour Slab on grade South 8"	On Track – Gaining
Structure Top Out		10/6/2025	10/6/2025	0	0	Roof Structural @ platforms & Screens	On Track – Gaining
Weather Tight		11/12/2025	11/12/2025	0	0	Roof Insulation cover board & Membrane	On Track – Gaining
Permanent Power		1/23/2026	1/23/2026	0	0	City Of Mesa Work Scope Power to Building	On Track – Gaining
Elevator Complete		3/25/2026	3/25/2026	0	0	Elevator inspection scheduling and approval	On Track – Gaining
Hardscape/Landscape Complete		3/23/2026	3/23/2026	0	0	Landscape	On Track – Gaining
Contract Completion	1/12/2026	5/12/2026	5/12/2026	-120	0	Building Final	Delayed – Gaining

Baseline Variance

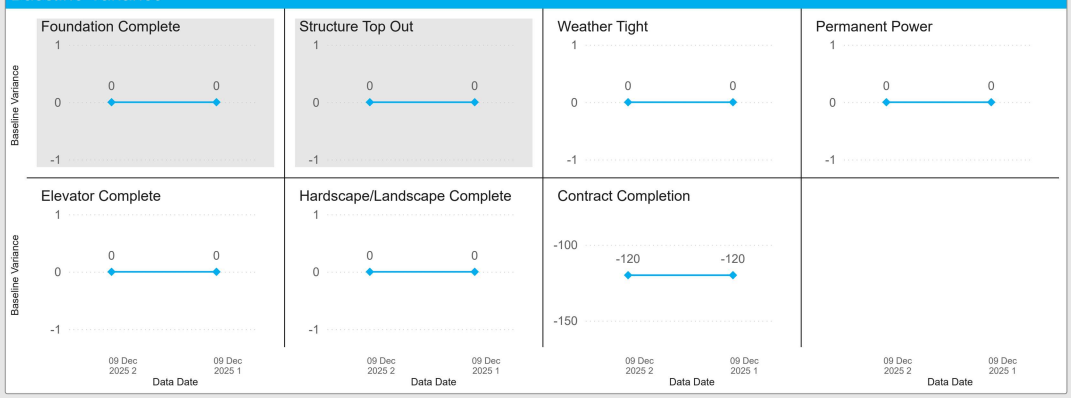

Schedule Performance Summary

Summary

This schedule is experiencing acute reliability and execution risks. Key weaknesses include uncontrolled logic changes, poor schedule quality, persistent finish slippage, and a lack of effective schedule-driven execution. Immediate leadership focus is needed to stabilize planning practices, restore data integrity, and address the root causes of project delay and poor schedule adherence.

Schedule Validation Score: 75.00 — ALERT

The SV Score is well below industry standards, indicating significant issues with logic, constraints, or data integrity in the schedule. This reduces confidence in the project's critical path and forecast accuracy. Immediate schedule quality review and correction are recommended.

Schedule Change Index: 100.00% — ALERT

Extremely high change activity signals major instability. Such volatility undermines planning reliability and increases risk of execution confusion. Immediate investigation into the source of excessive schedule changes is advised.

Finish Variance: 80.00% — ALERT

The project's forecasted finish date is slipping significantly, with an 80% variance, indicating severe delays versus the original plan. This reflects possible critical path delays or cumulative slippages.

Execution Score: 0.00% — ALERT

Execution performance is critical, with no alignment observed between planned and actual activity starts/finishes. This points to a breakdown in schedule use for managing work and requires urgent corrective action

Remaining Work Compression: -38% — Normal

Schedule Compression occurs when planned tasks are pushed into later periods of the project. The compression is mea… by calculating the number of construction days in a period (5 tasks in progress concurrently would equal 5 construction days per day) and comparing it to previous periods to determine if the number of construction days has increased - more work per period is required.

Powered By STELIC INSIGHT • ACTION • IMPACT
