ID	Unique ID	Task Name	Duration	Start	Finish	Predecessors
1	**1**	**Public Storage - 1061 Cudahy Place San Diego CA**	**20 days**	**Tue 25/05/27**	**Mon 25/06/23**	
2	325	Notice to Proceed	0 days	Tue 25/05/27	Tue 25/05/27	
3	180	Mobilization	5 days	Tue 25/05/27	Mon 25/06/02	2
4	630	Switchgear Submittal Approval	15 days	Tue 25/06/03	Mon 25/06/23	3
5	631	Chamber System Submittal Approval	15 days	Tue 25/06/03	Mon 25/06/23	3
6	**363**	**Public Storage Overall 88,386 Sq Ft**	**250 days**	**Tue 25/06/03**	**Tue 26/06/02**	
7	**327**	**Surface Demo & Grading**	**34 days**	**Tue 25/06/03**	**Tue 25/07/22**	
8	362	Erosion Control & Remove Owners Fencing	3 days	Tue 25/06/03	Thu 25/06/05	3
9	564	Pre Con Meeting	1 day	Fri 25/06/06	Fri 25/06/06	8
10	516	Demo Existing Bldg/Slabs,Tank slabs, Retaining walls Etc.	15 days	Mon 25/06/09	Fri 25/06/27	8;9
11	330	Site Survey, Boundry & Building Pad	1 day	Fri 25/06/27	Fri 25/06/27	10FS-1 day
12	161	Pre Grading Meeting	1 day	Fri 25/06/27	Fri 25/06/27	11SS
13	563	Install Shoring Wall NE corner of Site	12 days	Mon 25/06/30	Thu 25/07/17	12
14	331	Over-Ex & Recompact Bldg Pad & Site areas	12 days	Mon 25/06/30	Thu 25/07/17	12
15	13	**Certify Pad / Pad Delivery Date**	3 days	Fri 25/07/18	Tue 25/07/22	14;13
16	398	Building Permit Due	0 days	Tue 25/07/22	Tue 25/07/22	15
17	**522**	**Site Improvements - Structures & Utilities**	**20 days**	**Fri 25/07/18**	**Thu 25/08/14**	
18	567	Install Private Storm Drain & Chamber System	15 days	Fri 25/07/18	Thu 25/08/07	13;14;5
19	558	Install Offsite Fire Tie In & Lateral	5 days	Fri 25/07/18	Thu 25/07/24	18SS
20	559	Install Site Sewer line to Bldg.	5 days	Fri 25/07/18	Thu 25/07/24	19SS
21	557	Install Private Domestic Water	4 days	Fri 25/07/25	Wed 25/07/30	20
22	534	Install Dry Utility Ducts & Structures	5 days	Thu 25/07/31	Wed 25/08/06	21
23	527	Install Drainage Structures & Backfill	5 days	Fri 25/08/08	Thu 25/08/14	18
24	**618**	**Early AC Paving Option**	**18 days**	**Fri 25/08/15**	**Wed 25/09/10**	
25	528	Survey & Grade for Curb Cuts	2 days	Fri 25/08/15	Mon 25/08/18	23
26	529	UG Electric Site Lts, Gate Motors etc.	3 days	Tue 25/08/19	Thu 25/08/21	25
27	530	Irrigation Sleeves	3 days	Tue 25/08/19	Thu 25/08/21	25
28	570	Form & Pour Curb & Gutter onsite	3 days	Fri 25/08/22	Tue 25/08/26	27;26
29	569	Grade & Pour Site Walks Bollards & Gate Tracks	7 days	Wed 25/08/27	Fri 25/09/05	27;28
30	568	Agg Base import & "Early" AC Paving option	3 days	Mon 25/09/08	Wed 25/09/10	29
31	**15**	**Building Shell Construction**	**198 days**	**Wed 25/07/23**	**Wed 26/05/06**	
32	16	Underslab Plumbing & Electrical	8 days	Wed 25/07/23	Fri 25/08/01	15
33	332	Elevator Pits Excavate, Waterproofing, Form & Pour	10 days	Wed 25/07/23	Tue 25/08/05	32SS
34	517	Drill & Set Jack Casings	5 days	Wed 25/08/06	Tue 25/08/12	33
35	388	Bldg. Wall Ftgs. & CMU to FF	8 days	Mon 25/07/28	Wed 25/08/06	32FS-5 days
36	213	Fine Grade Slab Base materials & Reinforce Slab on grade	5 days	Fri 25/08/08	Thu 25/08/14	35;18
37	333	Pour Slab on Grade 8"	3 days	Fri 25/08/15	Tue 25/08/19	36;34
38	365	CMU walls/Ledgers to 18'	24 days	Wed 25/08/20	Tue 25/09/23	37
39	366	Shearwalls/Beams & Deck for 2nd floor	25 days	Wed 25/09/17	Tue 25/10/21	38FS-5 days
40	380	Reinforce & Pour 2nd floor Deck	6 days	Fri 25/10/17	Fri 25/10/24	39FS-3 days
41	384	Deck cure	5 days	Mon 25/10/27	Fri 25/10/31	40
42	370	CMU Walls/Ledgers to 29' (3rd floor)	15 days	Mon 25/11/03	Fri 25/11/21	41
43	371	Shearwalls/Beams & Deck for 3rd floor	21 days	Wed 25/11/19	Fri 25/12/19	42FS-3 days
44	372	Reinforce & Pour3rd floor Deck	6 days	Wed 25/12/17	Wed 25/12/24	43FS-3 days
45	385	Deck Cure	5 days	Mon 25/12/29	Tue 26/01/06	44
46	565	CMU Walls/Roof Ledgers to Top Out	15 days	Wed 26/01/07	Tue 26/01/27	45
47	377	Shearwalls/Beams & Roof Deck	18 days	Fri 26/01/23	Wed 26/02/18	46FS-3 days
48	399	Roof Structural @ platforms & Screens	5 days	Thu 26/02/19	Wed 26/02/25	47
49	212	Install roof accessories/Curbs, drains etc.	7 days	Thu 26/02/19	Fri 26/02/27	47
50	61	Roof Insulation Cover Board & Membrane	15 days	Mon 26/03/02	Fri 26/03/20	49
51	62	Set Rooftop Equipment	3 days	Mon 26/03/23	Wed 26/03/25	50;48
52	64	Elevator Construction Car #1	15 days	Thu 26/02/26	Wed 26/03/18	47;50FS-17 days
53	65	Elevator Construction Car #2	15 days	Thu 26/03/19	Wed 26/04/08	52
54	194	State Elevator inspection scheduling and approval	20 days	Thu 26/04/09	Wed 26/05/06	53;78
55	**602**	**Building Interior**	**122 days**	**Fri 25/10/17**	**Wed 26/04/15**	
56	603	Layout & Install Hangars from 2nd fl deck	3 days	Fri 25/10/17	Tue 25/10/21	40SS
57	604	Overhead M,P,E & Fire 1st fl	15 days	Wed 25/10/22	Tue 25/11/11	56
58	605	Hallway System & Doors 1st floor	15 days	Wed 25/11/05	Tue 25/11/25	57FS-5 days
59	606	Finish Mech. & Electrical 1st Fl	3 days	Wed 25/11/26	Tue 25/12/02	58
60	607	Layout & Install Overhead Hangars from 3rd fl deck	3 days	Mon 25/12/29	Wed 25/12/31	58;44
61	608	Overhead M,P,E & Fire 2nd Fl	15 days	Mon 26/01/05	Fri 26/01/23	59FS-2 days;60
62	609	Hallway System & Doors 2nd Floor	15 days	Mon 26/01/19	Fri 26/02/06	61FS-5 days
63	610	Finish Mech. & Electrical 2nd Fl	3 days	Mon 26/02/09	Wed 26/02/11	62
64	611	Install HM Doors & Hardware	9 days	Thu 26/02/12	Wed 26/02/25	63
65	612	Layout & Install Overhead Hangars from Roof deck	5 days	Thu 26/02/19	Wed 26/02/25	47
66	613	Overhead M,P,E & Fire 3rd Fl	15 days	Thu 26/02/26	Wed 26/03/18	63;65
67	614	Hallway System & Doors 3rd Floor	15 days	Thu 26/03/12	Wed 26/04/01	64;66FS-5 days
68	615	Electrical Room 100% Complete	15 days	Thu 26/03/19	Wed 26/04/08	66;74
69	616	Finish Painting in Storage areas	5 days	Mon 26/03/23	Fri 26/03/27	50
70	617	Final Clean up & Seal floors	10 days	Thu 26/04/02	Wed 26/04/15	67
71	**619**	**Switchgear, City Power & Building Energize**	**197 days**	**Tue 25/06/24**	**Wed 26/04/08**	
72	620	Switchgear Order & Lead Time	150 days	Tue 25/06/24	Fri 26/01/30	3;4
73	626	Install Dry Utility Ducts & Structures	5 days	Mon 26/02/02	Fri 26/02/06	72
74	621	Switchgear Delivery & Install	4 days	Mon 26/02/02	Thu 26/02/05	72
75	622	Single line Electrical & Grounding	5 days	Fri 26/02/06	Thu 26/02/12	72;74
76	623	SDG&E Utility Release for Equipment & Cabling	3 days	Fri 26/02/13	Wed 26/02/18	75;73
77	624	SDG&E Utility Scheduling & Lead time	30 days	Thu 26/02/19	Wed 26/04/01	76
78	625	Set Transformer, Cabling, & Energize	5 days	Thu 26/04/02	Wed 26/04/08	77
79	**573**	**Site Improvements - Structures & Utilities**	**38 days**	**Wed 26/01/28**	**Mon 26/03/23**	
80	574	Install Private Storm Drain & Chamber System	15 days	Wed 26/01/28	Wed 26/02/18	46
81	575	Install Offsite Fire Tie In & Lateral	5 days	Wed 26/01/28	Tue 26/02/03	80SS
82	576	Install Site Sewer line to Bldg.	5 days	Wed 26/02/04	Tue 26/02/10	81
83	577	Install Private Domestic Water	4 days	Wed 26/02/11	Tue 26/02/17	82
84	579	Install Drainage Structures & Backfill	5 days	Thu 26/02/19	Wed 26/02/25	80;83
85	580	Survey & Grade for Curb Cuts	2 days	Thu 26/02/26	Fri 26/02/27	84
86	581	UG Electric Site Lts, Gate Motors etc.	3 days	Mon 26/03/02	Wed 26/03/04	85
87	582	Irrigation Sleeves	3 days	Mon 26/03/02	Wed 26/03/04	85
88	583	Form & Pour Curb & Gutter onsite	3 days	Thu 26/03/05	Mon 26/03/09	87
89	584	Grade & Pour Site Walks Bollards & Gate Tracks	7 days	Tue 26/03/10	Wed 26/03/18	87;88
90	585	Agg Base import & AC Paving	3 days	Thu 26/03/19	Mon 26/03/23	89
91	**588**	**Offsite improvements**	**24 days**	**Tue 26/03/24**	**Fri 26/04/24**	
92	589	Demo & Grading	4 days	Tue 26/03/24	Fri 26/03/27	90
93	590	Offsite Concrete & Driveways	4 days	Mon 26/03/30	Thu 26/04/02	92
94	591	Offsite AC Patching & Paving	4 days	Fri 26/04/03	Wed 26/04/08	93
95	592	Offsite Striping	3 days	Thu 26/04/09	Mon 26/04/13	94
96	627	Final Public Works Inspections	2 days	Tue 26/04/14	Wed 26/04/15	95
97	628	Final Planning & Zoning Inspection	2 days	Thu 26/04/16	Fri 26/04/17	96
98	629	Owner Civil Punch list walkthrough & Completion	5 days	Mon 26/04/20	Fri 26/04/24	97;69
99	**536**	**Building Exterior, Tower & Office Finishes**	**67 days**	**Wed 26/01/28**	**Fri 26/05/01**	
100	537	Install Scaffolding at Office Tower	1 day	Wed 26/01/28	Wed 26/01/28	46
101	538	Exterior Metal Frame/Sheathing & Waterproofing	5 days	Thu 26/01/29	Wed 26/02/04	100
102	539	Install Storefront System @ Displays	5 days	Thu 26/02/05	Wed 26/02/11	101
103	540	EIFS	5 days	Thu 26/02/12	Thu 26/02/19	102
104	566	Exterior Painting & Coatings @ CMU Walls	10 days	Thu 26/02/05	Thu 26/02/19	101
105	541	Install Metal Panel Systems @ Tower Framing	5 days	Fri 26/02/20	Thu 26/02/26	103;104

2023 Qtr 1 Jan Feb Ma

Task		Rolled Up Milestone		Duration-only	
Split		Rolled Up Progress		Manual Summary Rollup	
Milestone		External Tasks		Manual Summary	
Summary		External Milestone		Start-only	
Project Summary		Inactive Task		Finish-only	
Group By Summary		Inactive Milestone		Deadline	
Rolled Up Task		Inactive Summary		Critical Task	
Rolled Up Critical Task		Manual Task		Progress	

ID		Unique ID	Task Name	Duration	Start	Finish	Predecessors
106		542	Install Steel Canopies	5 days	Fri 26/02/27	Thu 26/03/05	105
107		543	Exterior Breakmetal, flashings, Sealants, & Painting	5 days	Fri 26/03/06	Thu 26/03/12	103;105;106
108		544	Remove Scaffolding	1 day	Fri 26/03/13	Fri 26/03/13	107
109		596	Office Framing	6 days	Fri 26/03/06	Fri 26/03/13	106
110		597	Office M/E/P Rough in	6 days	Mon 26/03/16	Mon 26/03/23	109;108
111		598	Office Drywall	10 days	Tue 26/03/24	Mon 26/04/06	110;107
112		599	Suspended Ceilings & Rough in	6 days	Tue 26/04/07	Tue 26/04/14	111
113		600	Office Fixtures & Finishes	6 days	Wed 26/04/15	Wed 26/04/22	111;112
114		500	Final Electrical Inspection	3 days	Thu 26/04/23	Mon 26/04/27	51;113;68;75;78
115		501	Final Mechanical Inspections	3 days	Tue 26/04/28	Thu 26/04/30	114
116		502	**Office Completion Date, (Possible TCO 1st floor)**	1 day	Fri 26/05/01	Fri 26/05/01	104;115
117		**141**	**Accumulative Building Inspections & C of O**	**18 days**	**Thu 26/05/07**	**Tue 26/06/02**	
118		561	Rain/Weather Delays	10 days	Thu 26/05/07	Wed 26/05/20	116;54
119		234	Life Safety & Final Inspections	4 days	Thu 26/05/21	Wed 26/05/27	54;116;118
120		235	Building Final Inspection	2 days	Thu 26/05/28	Fri 26/05/29	119;95;97;98
121		308	Substantial Completion Date	0 days	Fri 26/05/29	Fri 26/05/29	120
122		236	Certificate Of Occupancy	2 days	Mon 26/06/01	Tue 26/06/02	**121**
123		305	**Open Date**	0 days	Tue 26/06/02	Tue 26/06/02	122;70
124		309	Final Completion Date	0 days	Tue 26/06/02	Tue 26/06/02	123

2023 Qtr 1
Jan Feb Ma

Task	Rolled Up Milestone	Duration-only	
Split	Rolled Up Progress	Manual Summary Rollup	
Milestone	External Tasks	Manual Summary	
Summary	External Milestone	Start-only	
Project Summary	Inactive Task	Finish-only	
Group By Summary	Inactive Milestone	Deadline	
Rolled Up Task	Inactive Summary	Critical Task	
Rolled Up Critical Task	Manual Task	Progress	

	2023 Qtr 2			2023 Qtr 3			2023 Qtr 4			2024 Qtr 1			2024 Qtr 2
Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr

Task		Rolled Up Milestone		Duration-only	
Split		Rolled Up Progress		Manual Summary Rollup	
Milestone		External Tasks		Manual Summary	
Summary		External Milestone		Start-only	
Project Summary		Inactive Task		Finish-only	
Group By Summary		Inactive Milestone		Deadline	
Rolled Up Task		Inactive Summary		Critical Task	
Rolled Up Critical Task		Manual Task		Progress	

	2023 Qtr 2			2023 Qtr 3			2023 Qtr 4			2024 Qtr 1			2024 Qtr 2
Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr

Task		Rolled Up Milestone		Duration-only	
Split		Rolled Up Progress		Manual Summary Rollup	
Milestone		External Tasks		Manual Summary	
Summary		External Milestone		Start-only	
Project Summary		Inactive Task		Finish-only	
Group By Summary		Inactive Milestone		Deadline	
Rolled Up Task		Inactive Summary		Critical Task	
Rolled Up Critical Task		Manual Task		Progress	





Task		Rolled Up Milestone		Duration-only	
Split		Rolled Up Progress		Manual Summary Rollup	
Milestone		External Tasks		Manual Summary	
Summary		External Milestone		Start-only	
Project Summary		Inactive Task		Finish-only	
Group By Summary		Inactive Milestone		Deadline	
Rolled Up Task		Inactive Summary		Critical Task	
Rolled Up Critical Task		Manual Task		Progress	

2024 Qtr 2			2024 Qtr 3			2024 Qtr 4			2025 Qtr 1			2025 Qtr 2	
Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May

Task		Rolled Up Milestone		Duration-only	
Split		Rolled Up Progress		Manual Summary Rollup	
Milestone		External Tasks		Manual Summary	
Summary		External Milestone		Start-only	
Project Summary		Inactive Task		Finish-only	
Group By Summary		Inactive Milestone		Deadline	
Rolled Up Task		Inactive Summary		Critical Task	
Rolled Up Critical Task		Manual Task		Progress	

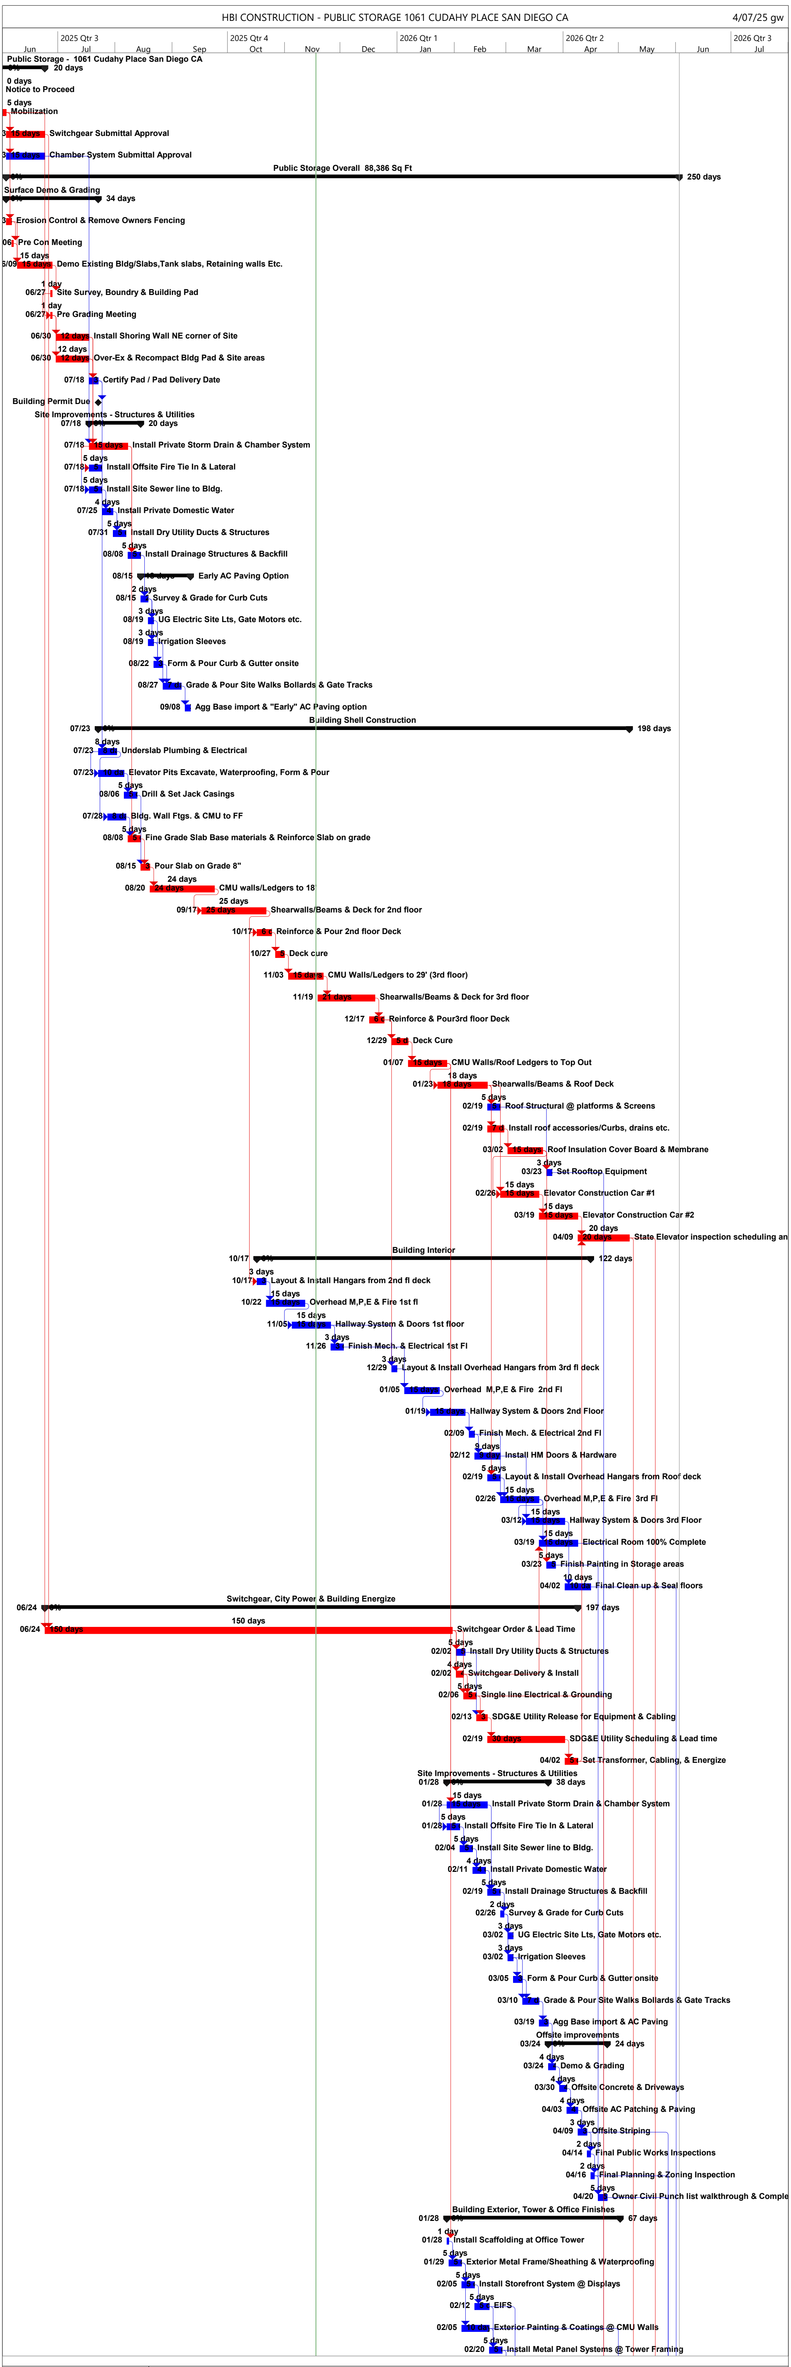

Task	Rolled Up Milestone	Duration-only	
Split	Rolled Up Progress	Manual Summary Rollup	
Milestone	External Tasks	Manual Summary	
Summary	External Milestone	Start-only	
Project Summary	Inactive Task	Finish-only	
Group By Summary	Inactive Milestone	Deadline	
Rolled Up Task	Inactive Summary	Critical Task	
Rolled Up Critical Task	Manual Task	Progress	

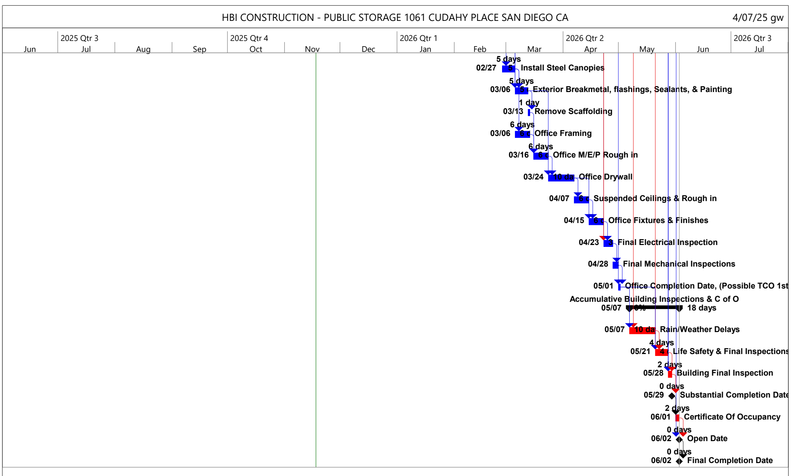

Task		Rolled Up Milestone		Duration-only	
Split		Rolled Up Progress		Manual Summary Rollup	
Milestone		External Tasks		Manual Summary	
Summary		External Milestone		Start-only	
Project Summary		Inactive Task		Finish-only	
Group By Summary		Inactive Milestone		Deadline	
Rolled Up Task		Inactive Summary		Critical Task	
Rolled Up Critical Task		Manual Task		Progress	
