HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
1	**Public Storage - 1061 Cudahy Place San Diego CA**	**156d**	**Tue 25/05/27**	**Mon 26/01/12**
2	Notice to Proceed	0d	Tue 25/05/27	Tue 25/05/27
3	**Demolition Permit Delay (Estimated)**	**96d**	**Tue 25/05/27**	**Fri 25/10/10**
4	SDGE Removal of Transformer	1d	Mon 25/10/06	Mon 25/10/06
5	Mobilization	5d	Mon 25/10/06	Fri 25/10/10
6	Switchgear Submittal Approval (30 week Lead Time)	15d	Mon 25/09/22	Fri 25/10/10
7	CO #4 - ADS Detension System	40d	Wed 25/07/16	Wed 25/09/10
8	Chamber System Submittal Approval	20d	Mon 25/10/27	Fri 25/11/21
9	ADS Detention System Lead Time	30d	Mon 25/11/24	Mon 26/01/12
10	**Public Storage Overall 88,386 Sq Ft**	**264d**	**Wed 25/10/08**	**Fri 26/10/23**
11	**Surface Demo & Grading**	**48d**	**Wed 25/10/08**	**Tue 25/12/16**
12	Erosion Control & Remove Owners Fencing	3d	Wed 25/10/08	Fri 25/10/10
13	Received Traffic Control Plans City Stamped	1d	Tue 25/10/21	Tue 25/10/21
14	Mock Pre-Con Meeting with City	1d	Wed 25/10/22	Wed 25/10/22
15	**Submitted Application for Traffic Control Permit DELAY**	**20d**	**Thu 25/10/23**	**Wed 25/11/19**
16	**City List of Items to resolve before Pre-Con Meeting can happen DELAY**	**1d**	**Thu 25/11/20**	**Thu 25/11/20**
17	Pre Con Meeting	1d	Fri 25/11/21	Fri 25/11/21
18	Demo Existing Bldg/Slabs,Tank slabs, Retaining walls Etc.	10d	Mon 25/10/13	Fri 25/10/24
19	Site Survey, Boundry & Building Pad	1d	Fri 25/10/24	Fri 25/10/24
20	Pre Grading Meeting	1d	Fri 25/10/24	Fri 25/10/24
21	Install Shoring Wall NE corner of Site	13d	Fri 25/11/21	Thu 25/12/11
22	Over-Ex & Recompact Bldg Pad & Site areas	12d	Fri 25/11/21	Wed 25/12/10
23	Certify Pad / Pad Delivery Date	3d	Fri 25/12/12	Tue 25/12/16
24	Building Permit Due	0d	Tue 25/12/16	Tue 25/12/16
25	**Site Improvements - Structures & Utilities**	**20d**	**Tue 26/01/13**	**Mon 26/02/09**
26	Install Private Storm Drain & Chamber System	15d	Tue 26/01/13	Mon 26/02/02
27	Install Offsite Fire Tie In & Lateral	5d	Tue 26/01/13	Mon 26/01/19
28	Install Site Sewer line to Bldg.	5d	Tue 26/01/13	Mon 26/01/19
29	Install Private Domestic Water	4d	Tue 26/01/20	Fri 26/01/23

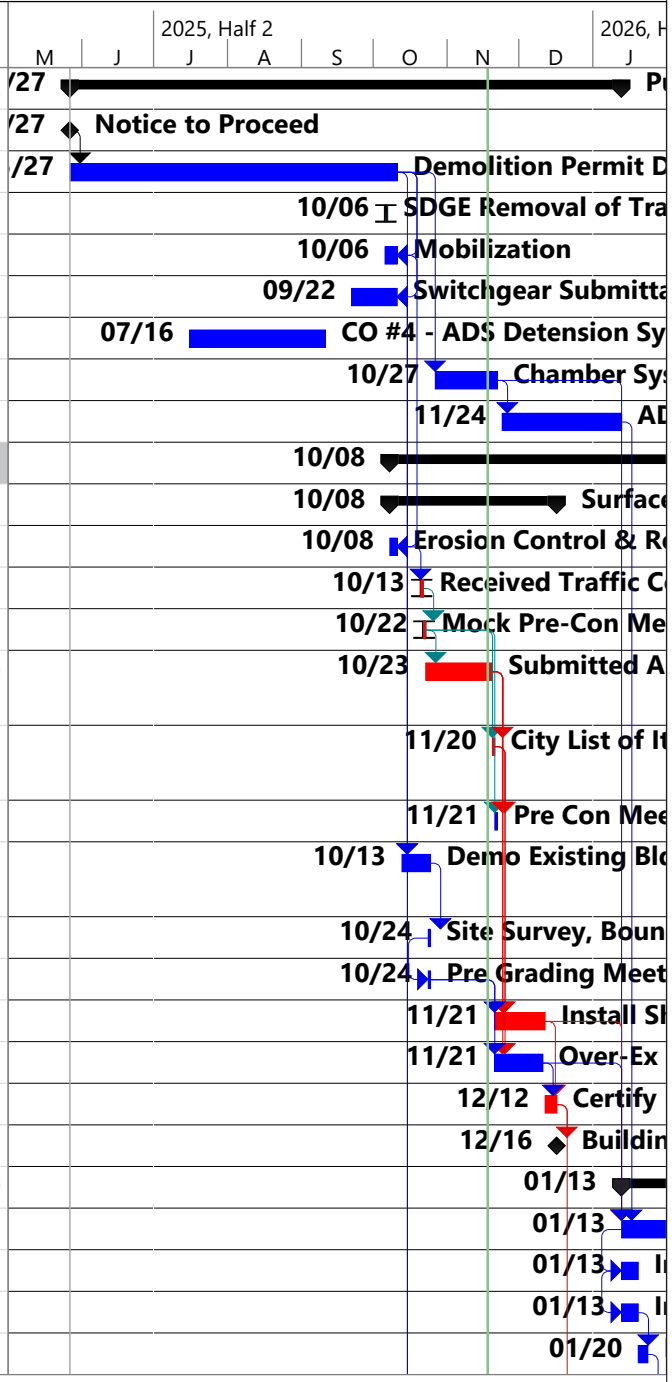

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
30	Install Dry Utility Ducts & Structures	5d	Mon 26/01/26	Fri 26/01/30
31	Install Drainage Structures & Backfill	5d	Tue 26/02/03	Mon 26/02/09
32	**Early AC Paving Option**	**18d**	**Tue 26/02/10**	**Fri 26/03/06**
33	Survey & Grade for Curb Cuts	2d	Tue 26/02/10	Wed 26/02/11
34	UG Electric Site Lts, Gate Motors etc.	3d	Thu 26/02/12	Tue 26/02/17
35	Irrigation Sleeves	3d	Thu 26/02/12	Tue 26/02/17
36	Form & Pour Curb & Gutter onsite	3d	Wed 26/02/18	Fri 26/02/20
37	Grade & Pour Site Walks Bollards & Gate Tracks	7d	Mon 26/02/23	Tue 26/03/03
38	Agg Base import & "Early" AC Paving option	3d	Wed 26/03/04	Fri 26/03/06
39	**Building Shell Construction**	**198d**	**Wed 25/12/17**	**Tue 26/09/29**
40	Underslab Plumbing & Electrical	8d	Wed 25/12/17	Tue 25/12/30
41	Elevator Pits Excavate, Waterproofing, Form & Pour	10d	Wed 25/12/17	Mon 26/01/05
42	Drill & Set Jack Casings	5d	Tue 26/01/06	Mon 26/01/12
43	Bldg. Wall Ftgs.	13d	Mon 25/12/22	Tue 26/01/13
44	CMU Stem Wall 8" AFF	10d	Mon 26/01/12	Fri 26/01/23
45	Fine Grade Slab Base materials	5d	Wed 26/01/21	Tue 26/01/27
46	Reinforce Slab on grade	3d	Wed 26/01/28	Fri 26/01/30
47	**Inspection**	**1d**	**Mon 26/02/02**	**Mon 26/02/02**
48	Pour Slab on Grade 8"	1d	Tue 26/02/03	Tue 26/02/03
49	CMU walls/Ledgers to 18' (exterior scaffold)	22d	Mon 26/01/26	Wed 26/02/25
50	CMU walls/Ledgers to 18' (interior scaffold)	15d	Wed 26/02/04	Wed 26/02/25
51	Shearwalls/Beams for 1st floor (Janus + 3 Wks / GBC / Abl	25d	Wed 26/02/11	Wed 26/03/18
52	Deck (Able)	3d	Thu 26/03/19	Mon 26/03/23
53	Reinforce 2nd floor Deck	3d	Tue 26/03/24	Thu 26/03/26
54	**Inspection**	**1d**	**Fri 26/03/27**	**Fri 26/03/27**
55	Pour 2nd floor Deck	1d	Mon 26/03/30	Mon 26/03/30
56	Deck cure	4d	Tue 26/03/31	Fri 26/04/03
57	CMU Walls/Ledgers to 29' (3rd floor - interior scaffold)	15d	Mon 26/04/06	Fri 26/04/24
58	CMU Walls/Ledgers to 29' (3rd floor - exterior scaffold)	47d	Thu 26/02/26	Fri 26/05/01
59	Shearwalls/Beams for 2nd Floor (Janus + 3 Wks / GBC / Ab	29d	Tue 26/04/07	Fri 26/05/15
60	Deck for 3rd floor (Able)	3d	Mon 26/05/18	Wed 26/05/20

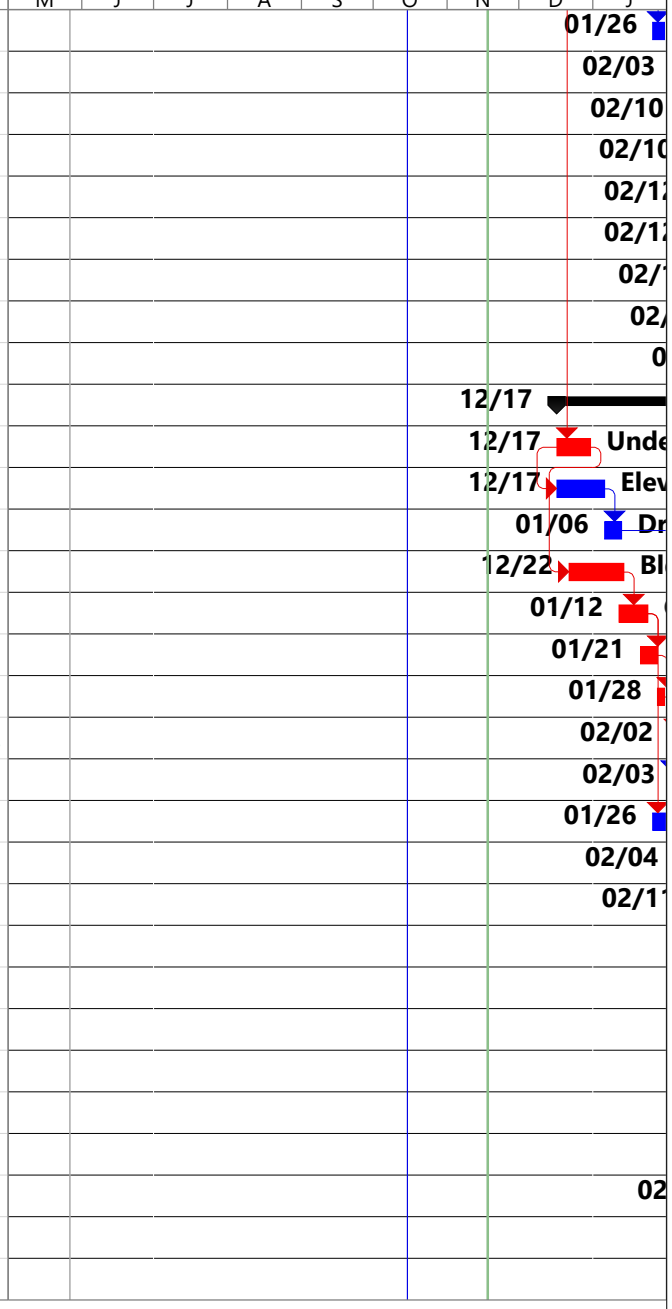

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
61	Reinforce for 3rd floor Deck	3d	Thu 26/05/21	Tue 26/05/26
62	**Inspection**	**1d**	**Wed 26/05/27**	**Wed 26/05/27**
63	Pour 3rd floor Deck	1d	Thu 26/05/28	Thu 26/05/28
64	Deck Cure	4d	Fri 26/05/29	Wed 26/06/03
65	CMU Walls/Roof Ledgers to Top Out (interior scaffold)	15d	Thu 26/06/04	Wed 26/06/24
66	CMU Walls/Roof Ledgers to Top Out (exterior scaffold)	42d	Mon 26/05/04	Wed 26/07/01
67	Shearwalls/Beams for 3rd floor (Janus + 3 Wks / GBC / Abl	29d	Fri 26/06/05	Thu 26/07/16
68	Roof Deck (Able)	3d	Fri 26/07/17	Tue 26/07/21
69	Roof Structural @ platforms & Screens	5d	Wed 26/07/22	Tue 26/07/28
70	Install roof accessories/Curbs, drains etc.	5d	Fri 26/07/17	Thu 26/07/23
71	Roof Insulation Cover Board & Membrane	15d	Fri 26/07/24	Thu 26/08/13
72	Set Rooftop Equipment	3d	Fri 26/08/14	Tue 26/08/18
73	Elevator Construction Car #1	15d	Wed 26/07/22	Tue 26/08/11
74	Elevator Construction Car #2	15d	Wed 26/08/12	Tue 26/09/01
75	State Elevator inspection scheduling and approval	20d	Wed 26/09/02	Tue 26/09/29
76	**Building Interior**	**121d**	**Tue 26/03/24**	**Thu 26/09/10**
77	Layout & Install Hangars from 2nd fl deck	3d	Tue 26/03/24	Thu 26/03/26
78	Overhead M,P,E & Fire 1st fl	15d	Fri 26/03/27	Thu 26/04/16
79	Hallway System & Doors 1st floor	15d	Fri 26/04/10	Thu 26/04/30
80	Finish Mech. & Electrical 1st Fl	3d	Fri 26/05/01	Tue 26/05/05
81	Layout & Install Overhead Hangars from 3rd fl deck	3d	Wed 26/05/27	Fri 26/05/29
82	Overhead M,P,E & Fire 2nd Fl	15d	Mon 26/06/01	Fri 26/06/19
83	Hallway System & Doors 2nd Floor	15d	Mon 26/06/15	Mon 26/07/06
84	Finish Mech. & Electrical 2nd Fl	3d	Tue 26/07/07	Thu 26/07/09
85	Install HM Doors & Hardware	9d	Fri 26/07/10	Wed 26/07/22
86	Layout & Install Overhead Hangars from Roof deck	5d	Fri 26/07/17	Thu 26/07/23
87	Overhead M,P,E & Fire 3rd Fl	15d	Fri 26/07/24	Thu 26/08/13
88	Hallway System & Doors 3rd Floor	15d	Fri 26/08/07	Thu 26/08/27
89	Electrical Room 100% Complete	15d	Fri 26/08/14	Thu 26/09/03
90	Finish Painting in Storage areas	5d	Fri 26/08/14	Thu 26/08/20
91	Final Clean up & Seal floors	10d	Fri 26/08/28	Thu 26/09/10

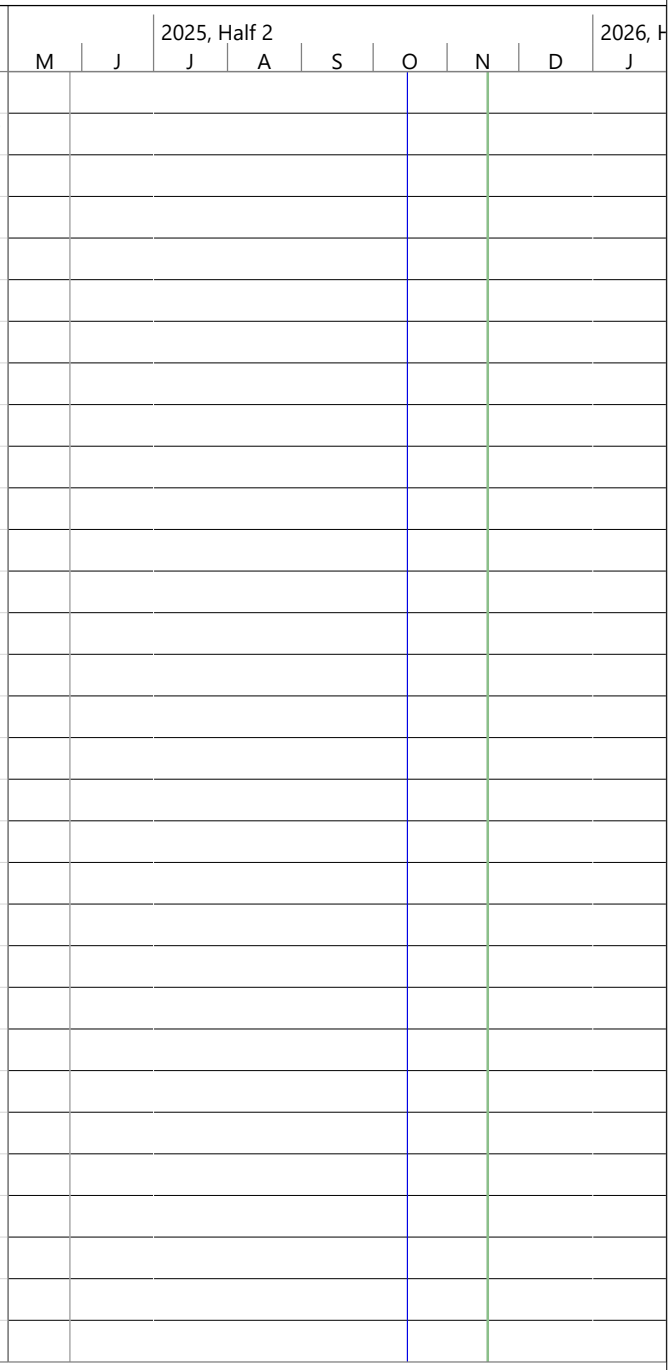

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
92	**Switchgear, City Power & Building Energize**	**197d**	**Mon 25/10/13**	**Mon 26/07/27**
93	Switchgear Order & Lead Time	150d	Mon 25/10/13	Tue 26/05/19
94	Install Dry Utility Ducts & Structures	5d	Wed 26/05/20	Wed 26/05/27
95	Switchgear Delivery & Install	4d	Wed 26/05/20	Tue 26/05/26
96	Single line Electrical & Grounding	5d	Wed 26/05/27	Tue 26/06/02
97	SDG&E Utility Release for Equipment & Cabling	3d	Wed 26/06/03	Fri 26/06/05
98	SDG&E Utility Scheduling & Lead time	30d	Mon 26/06/08	Mon 26/07/20
99	Set Transformer, Cabling, & Energize	5d	Tue 26/07/21	Mon 26/07/27
100	**Site Improvements - Structures & Utilities**	**38d**	**Thu 26/06/25**	**Tue 26/08/18**
101	Install Private Storm Drain & Chamber System	15d	Thu 26/06/25	Thu 26/07/16
102	Install Offsite Fire Tie In & Lateral	5d	Thu 26/06/25	Wed 26/07/01
103	Install Site Sewer line to Bldg.	5d	Thu 26/07/02	Thu 26/07/09
104	Install Private Domestic Water	4d	Fri 26/07/10	Wed 26/07/15
105	Install Drainage Structures & Backfill	5d	Fri 26/07/17	Thu 26/07/23
106	Survey & Grade for Curb Cuts	2d	Fri 26/07/24	Mon 26/07/27
107	UG Electric Site Lts, Gate Motors etc.	3d	Tue 26/07/28	Thu 26/07/30
108	Irrigation Sleeves	3d	Tue 26/07/28	Thu 26/07/30
109	Form & Pour Curb & Gutter onsite	3d	Fri 26/07/31	Tue 26/08/04
110	Grade & Pour Site Walks Bollards & Gate Tracks	7d	Wed 26/08/05	Thu 26/08/13
111	Agg Base import & AC Paving	3d	Fri 26/08/14	Tue 26/08/18
112	**Offsite improvements**	**24d**	**Wed 26/08/19**	**Mon 26/09/21**
113	Demo & Grading	4d	Wed 26/08/19	Mon 26/08/24
114	Offsite Concrete & Driveways	4d	Tue 26/08/25	Fri 26/08/28
115	Offsite AC Patching & Paving	4d	Mon 26/08/31	Thu 26/09/03
116	Offsite Striping	3d	Fri 26/09/04	Tue 26/09/08
117	Final Public Works Inspections	2d	Wed 26/09/09	Thu 26/09/10
118	Final Planning & Zoning Inspection	2d	Fri 26/09/11	Mon 26/09/14
119	Owner Civil Punch list walkthrough & Completion	5d	Tue 26/09/15	Mon 26/09/21
120	**Building Exterior, Tower & Office Finishes**	**67d**	**Thu 26/06/25**	**Mon 26/09/28**
121	Install Scaffolding at Office Tower	1d	Thu 26/06/25	Thu 26/06/25
122	Exterior Metal Frame/Sheathing & Waterproofing	5d	Fri 26/06/26	Thu 26/07/02



UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
123	Install Storefront System @ Displays	5d	Mon 26/07/06	Fri 26/07/10
124	EIFS	5d	Mon 26/07/13	Fri 26/07/17
125	Exterior Painting & Coatings @ CMU Walls	10d	Mon 26/07/06	Fri 26/07/17
126	Install Metal Panel Systems @ Tower Framing	5d	Mon 26/07/20	Fri 26/07/24
127	Install Steel Canopies	5d	Mon 26/07/27	Fri 26/07/31
128	Exterior Breakmetal, flashings, Sealants, & Painting	5d	Mon 26/08/03	Fri 26/08/07
129	Remove Scaffolding	1d	Mon 26/08/10	Mon 26/08/10
130	Office Framing	6d	Mon 26/08/03	Mon 26/08/10
131	Office M/E/P Rough in	6d	Tue 26/08/11	Tue 26/08/18
132	Office Drywall	10d	Wed 26/08/19	Tue 26/09/01
133	Suspended Ceilings & Rough in	6d	Wed 26/09/02	Wed 26/09/09
134	Office Fixtures & Finishes	6d	Thu 26/09/10	Thu 26/09/17
135	Final Electrical Inspection	3d	Fri 26/09/18	Tue 26/09/22
136	Final Mechanical Inspections	3d	Wed 26/09/23	Fri 26/09/25
137	Office Completion Date, (Possible TCO 1st floor)	1d	Mon 26/09/28	Mon 26/09/28
138	**Accumulative Building Inspections & C of O**	**18d**	**Wed 26/09/30**	**Fri 26/10/23**
139	Rain/Weather Delays	10d	Wed 26/09/30	Tue 26/10/13
140	Life Safety & Final Inspections	4d	Wed 26/10/14	Mon 26/10/19
141	Building Final Inspection	2d	Tue 26/10/20	Wed 26/10/21
142	Substantial Completion Date	0d	Wed 26/10/21	Wed 26/10/21
143	Certificate Of Occupancy	2d	Thu 26/10/22	Fri 26/10/23
144	Open Date	0d	Fri 26/10/23	Fri 26/10/23
145	Final Completion Date	0d	Fri 26/10/23	Fri 26/10/23



UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
1	**Public Storage - 1061 Cudahy Place San Diego CA**	**156d**	**Tue 25/05/27**	**Mon 26/01/12**
2	Notice to Proceed	0d	Tue 25/05/27	Tue 25/05/27
3	**Demolition Permit Delay (Estimated)**	**96d**	**Tue 25/05/27**	**Fri 25/10/10**
4	SDGE Removal of Transformer	1d	Mon 25/10/06	Mon 25/10/06
5	Mobilization	5d	Mon 25/10/06	Fri 25/10/10
6	Switchgear Submittal Approval (30 week Lead Time)	15d	Mon 25/09/22	Fri 25/10/10
7	CO #4 - ADS Detension System	40d	Wed 25/07/16	Wed 25/09/10
8	Chamber System Submittal Approval	20d	Mon 25/10/27	Fri 25/11/21
9	ADS Detention System Lead Time	30d	Mon 25/11/24	Mon 26/01/12
10	**Public Storage Overall 88,386 Sq Ft**	**264d**	**Wed 25/10/08**	**Fri 26/10/23**
11	**Surface Demo & Grading**	**48d**	**Wed 25/10/08**	**Tue 25/12/16**
12	Erosion Control & Remove Owners Fencing	3d	Wed 25/10/08	Fri 25/10/10
13	Received Traffic Control Plans City Stamped	1d	Tue 25/10/21	Tue 25/10/21
14	Mock Pre-Con Meeting with City	1d	Wed 25/10/22	Wed 25/10/22
15	**Submitted Application for Traffic Control Permit DELAY**	**20d**	**Thu 25/10/23**	**Wed 25/11/19**
16	**City List of Items to resolve before Pre-Con Meeting can happen DELAY**	**1d**	**Thu 25/11/20**	**Thu 25/11/20**
17	Pre Con Meeting	1d	Fri 25/11/21	Fri 25/11/21
18	Demo Existing Bldg/Slabs,Tank slabs, Retaining walls Etc.	10d	Mon 25/10/13	Fri 25/10/24
19	Site Survey, Boundry & Building Pad	1d	Fri 25/10/24	Fri 25/10/24
20	Pre Grading Meeting	1d	Fri 25/10/24	Fri 25/10/24
21	Install Shoring Wall NE corner of Site	13d	Fri 25/11/21	Thu 25/12/11
22	Over-Ex & Recompact Bldg Pad & Site areas	12d	Fri 25/11/21	Wed 25/12/10
23	Certify Pad / Pad Delivery Date	3d	Fri 25/12/12	Tue 25/12/16
24	Building Permit Due	0d	Tue 25/12/16	Tue 25/12/16
25	**Site Improvements - Structures & Utilities**	**20d**	**Tue 26/01/13**	**Mon 26/02/09**
26	Install Private Storm Drain & Chamber System	15d	Tue 26/01/13	Mon 26/02/02
27	Install Offsite Fire Tie In & Lateral	5d	Tue 26/01/13	Mon 26/01/19
28	Install Site Sewer line to Bldg.	5d	Tue 26/01/13	Mon 26/01/19
29	Install Private Domestic Water	4d	Tue 26/01/20	Fri 26/01/23

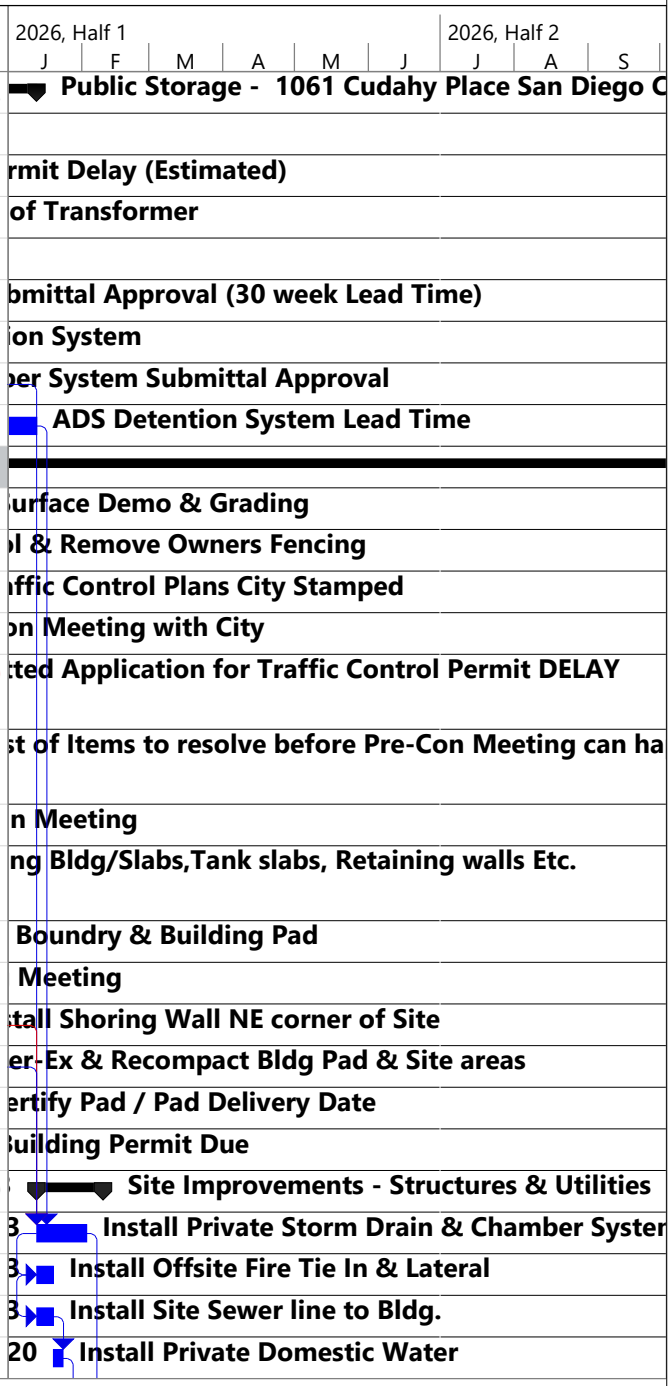

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
30	Install Dry Utility Ducts & Structures	5d	Mon 26/01/26	Fri 26/01/30
31	Install Drainage Structures & Backfill	5d	Tue 26/02/03	Mon 26/02/09
32	**Early AC Paving Option**	**18d**	**Tue 26/02/10**	**Fri 26/03/06**
33	Survey & Grade for Curb Cuts	2d	Tue 26/02/10	Wed 26/02/11
34	UG Electric Site Lts, Gate Motors etc.	3d	Thu 26/02/12	Tue 26/02/17
35	Irrigation Sleeves	3d	Thu 26/02/12	Tue 26/02/17
36	Form & Pour Curb & Gutter onsite	3d	Wed 26/02/18	Fri 26/02/20
37	Grade & Pour Site Walks Bollards & Gate Tracks	7d	Mon 26/02/23	Tue 26/03/03
38	Agg Base import & "Early" AC Paving option	3d	Wed 26/03/04	Fri 26/03/06
39	**Building Shell Construction**	**198d**	**Wed 25/12/17**	**Tue 26/09/29**
40	Underslab Plumbing & Electrical	8d	Wed 25/12/17	Tue 25/12/30
41	Elevator Pits Excavate, Waterproofing, Form & Pour	10d	Wed 25/12/17	Mon 26/01/05
42	Drill & Set Jack Casings	5d	Tue 26/01/06	Mon 26/01/12
43	Bldg. Wall Ftgs.	13d	Mon 25/12/22	Tue 26/01/13
44	CMU Stem Wall 8" AFF	10d	Mon 26/01/12	Fri 26/01/23
45	Fine Grade Slab Base materials	5d	Wed 26/01/21	Tue 26/01/27
46	Reinforce Slab on grade	3d	Wed 26/01/28	Fri 26/01/30
47	**Inspection**	**1d**	**Mon 26/02/02**	**Mon 26/02/02**
48	Pour Slab on Grade 8"	1d	Tue 26/02/03	Tue 26/02/03
49	CMU walls/Ledgers to 18' (exterior scaffold)	22d	Mon 26/01/26	Wed 26/02/25
50	CMU walls/Ledgers to 18' (interior scaffold)	15d	Wed 26/02/04	Wed 26/02/25
51	Shearwalls/Beams for 1st floor (Janus + 3 Wks / GBC / Able	25d	Wed 26/02/11	Wed 26/03/18
52	Deck (Able)	3d	Thu 26/03/19	Mon 26/03/23
53	Reinforce 2nd floor Deck	3d	Tue 26/03/24	Thu 26/03/26
54	**Inspection**	**1d**	**Fri 26/03/27**	**Fri 26/03/27**
55	Pour 2nd floor Deck	1d	Mon 26/03/30	Mon 26/03/30
56	Deck cure	4d	Tue 26/03/31	Fri 26/04/03
57	CMU Walls/Ledgers to 29' (3rd floor - interior scaffold)	15d	Mon 26/04/06	Fri 26/04/24
58	CMU Walls/Ledgers to 29' (3rd floor - exterior scaffold)	47d	Thu 26/02/26	Fri 26/05/01
59	Shearwalls/Beams for 2nd Floor (Janus + 3 Wks / GBC / Ab	29d	Tue 26/04/07	Fri 26/05/15
60	Deck for 3rd floor (Able)	3d	Mon 26/05/18	Wed 26/05/20

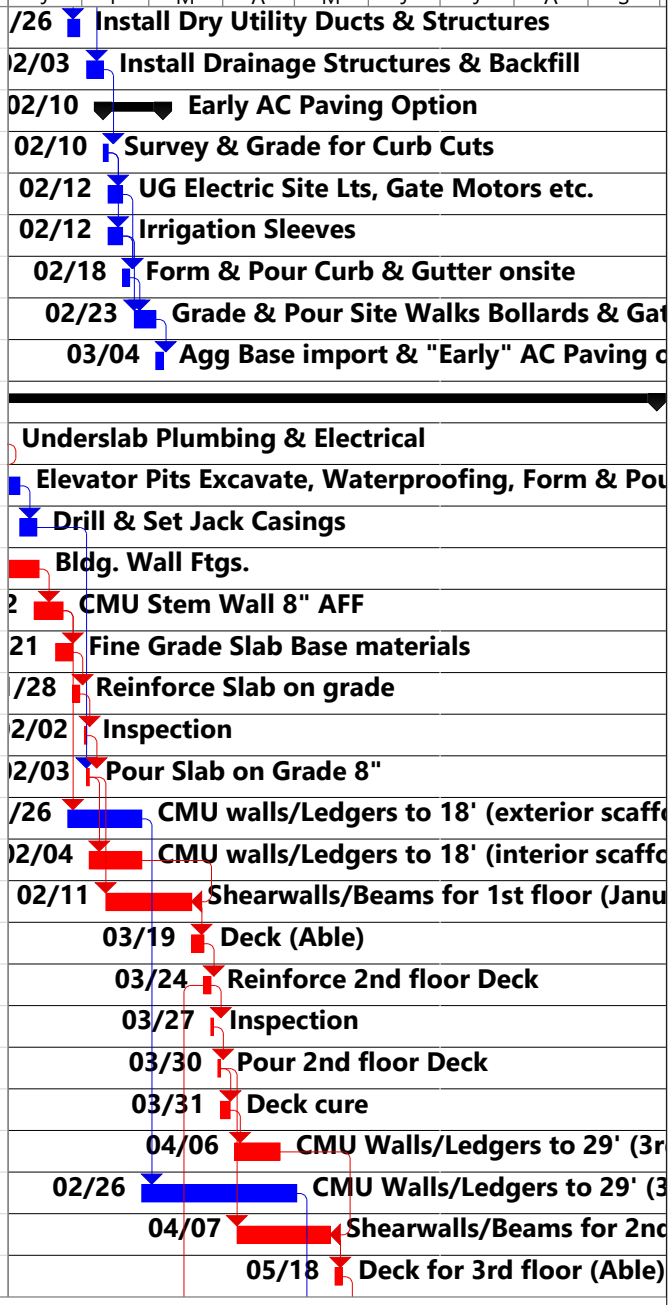

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
61	Reinforce for 3rd floor Deck	3d	Thu 26/05/21	Tue 26/05/26
62	**Inspection**	**1d**	**Wed 26/05/27**	**Wed 26/05/27**
63	Pour 3rd floor Deck	1d	Thu 26/05/28	Thu 26/05/28
64	Deck Cure	4d	Fri 26/05/29	Wed 26/06/03
65	CMU Walls/Roof Ledgers to Top Out (interior scaffold)	15d	Thu 26/06/04	Wed 26/06/24
66	CMU Walls/Roof Ledgers to Top Out (exterior scaffold)	42d	Mon 26/05/04	Wed 26/07/01
67	Shearwalls/Beams for 3rd floor (Janus + 3 Wks / GBC / Abl	29d	Fri 26/06/05	Thu 26/07/16
68	Roof Deck (Able)	3d	Fri 26/07/17	Tue 26/07/21
69	Roof Structural @ platforms & Screens	5d	Wed 26/07/22	Tue 26/07/28
70	Install roof accessories/Curbs, drains etc.	5d	Fri 26/07/17	Thu 26/07/23
71	Roof Insulation Cover Board & Membrane	15d	Fri 26/07/24	Thu 26/08/13
72	Set Rooftop Equipment	3d	Fri 26/08/14	Tue 26/08/18
73	Elevator Construction Car #1	15d	Wed 26/07/22	Tue 26/08/11
74	Elevator Construction Car #2	15d	Wed 26/08/12	Tue 26/09/01
75	State Elevator inspection scheduling and approval	20d	Wed 26/09/02	Tue 26/09/29
76	**Building Interior**	**121d**	**Tue 26/03/24**	**Thu 26/09/10**
77	Layout & Install Hangars from 2nd fl deck	3d	Tue 26/03/24	Thu 26/03/26
78	Overhead M,P,E & Fire 1st fl	15d	Fri 26/03/27	Thu 26/04/16
79	Hallway System & Doors 1st floor	15d	Fri 26/04/10	Thu 26/04/30
80	Finish Mech. & Electrical 1st Fl	3d	Fri 26/05/01	Tue 26/05/05
81	Layout & Install Overhead Hangars from 3rd fl deck	3d	Wed 26/05/27	Fri 26/05/29
82	Overhead M,P,E & Fire 2nd Fl	15d	Mon 26/06/01	Fri 26/06/19
83	Hallway System & Doors 2nd Floor	15d	Mon 26/06/15	Mon 26/07/06
84	Finish Mech. & Electrical 2nd Fl	3d	Tue 26/07/07	Thu 26/07/09
85	Install HM Doors & Hardware	9d	Fri 26/07/10	Wed 26/07/22
86	Layout & Install Overhead Hangars from Roof deck	5d	Fri 26/07/17	Thu 26/07/23
87	Overhead M,P,E & Fire 3rd Fl	15d	Fri 26/07/24	Thu 26/08/13
88	Hallway System & Doors 3rd Floor	15d	Fri 26/08/07	Thu 26/08/27
89	Electrical Room 100% Complete	15d	Fri 26/08/14	Thu 26/09/03
90	Finish Painting in Storage areas	5d	Fri 26/08/14	Thu 26/08/20
91	Final Clean up & Seal floors	10d	Fri 26/08/28	Thu 26/09/10

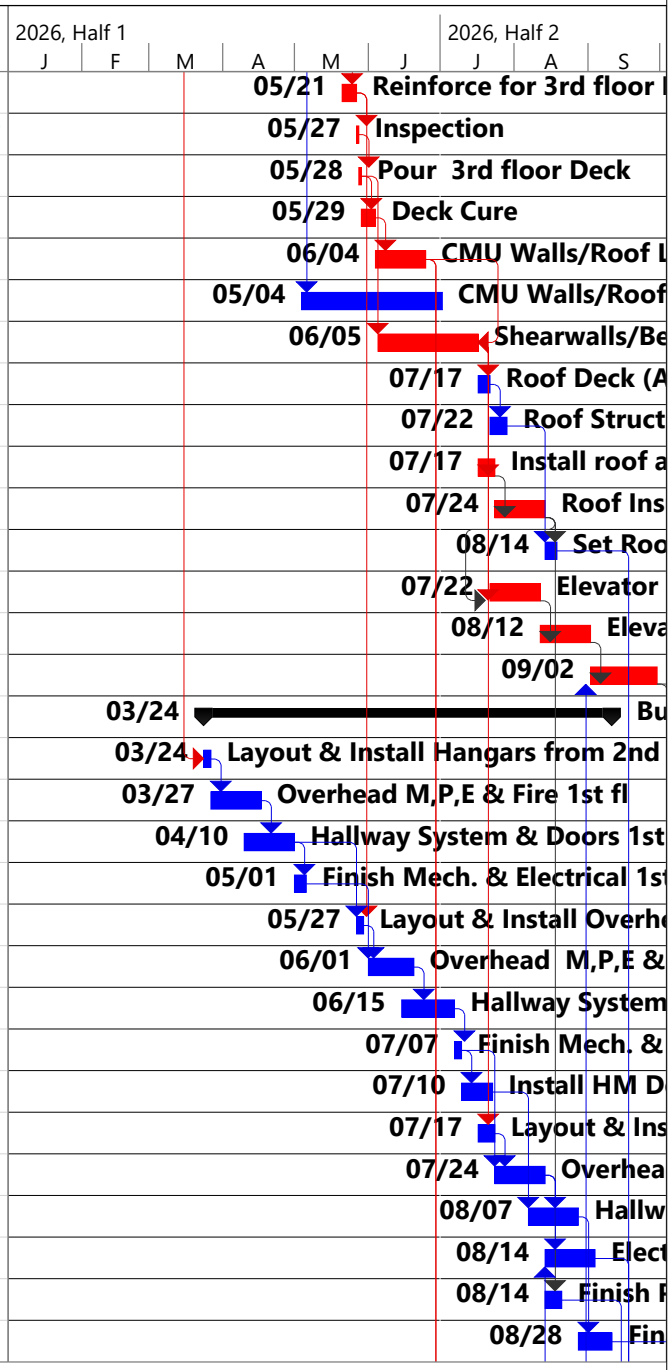

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
92	**Switchgear, City Power & Building Energize**	**197d**	**Mon 25/10/13**	**Mon 26/07/27**
93	Switchgear Order & Lead Time	150d	Mon 25/10/13	Tue 26/05/19
94	Install Dry Utility Ducts & Structures	5d	Wed 26/05/20	Wed 26/05/27
95	Switchgear Delivery & Install	4d	Wed 26/05/20	Tue 26/05/26
96	Single line Electrical & Grounding	5d	Wed 26/05/27	Tue 26/06/02
97	SDG&E Utility Release for Equipment & Cabling	3d	Wed 26/06/03	Fri 26/06/05
98	SDG&E Utility Scheduling & Lead time	30d	Mon 26/06/08	Mon 26/07/20
99	Set Transformer, Cabling, & Energize	5d	Tue 26/07/21	Mon 26/07/27
100	**Site Improvements - Structures & Utilities**	**38d**	**Thu 26/06/25**	**Tue 26/08/18**
101	Install Private Storm Drain & Chamber System	15d	Thu 26/06/25	Thu 26/07/16
102	Install Offsite Fire Tie In & Lateral	5d	Thu 26/06/25	Wed 26/07/01
103	Install Site Sewer line to Bldg.	5d	Thu 26/07/02	Thu 26/07/09
104	Install Private Domestic Water	4d	Fri 26/07/10	Wed 26/07/15
105	Install Drainage Structures & Backfill	5d	Fri 26/07/17	Thu 26/07/23
106	Survey & Grade for Curb Cuts	2d	Fri 26/07/24	Mon 26/07/27
107	UG Electric Site Lts, Gate Motors etc.	3d	Tue 26/07/28	Thu 26/07/30
108	Irrigation Sleeves	3d	Tue 26/07/28	Thu 26/07/30
109	Form & Pour Curb & Gutter onsite	3d	Fri 26/07/31	Tue 26/08/04
110	Grade & Pour Site Walks Bollards & Gate Tracks	7d	Wed 26/08/05	Thu 26/08/13
111	Agg Base import & AC Paving	3d	Fri 26/08/14	Tue 26/08/18
112	**Offsite improvements**	**24d**	**Wed 26/08/19**	**Mon 26/09/21**
113	Demo & Grading	4d	Wed 26/08/19	Mon 26/08/24
114	Offsite Concrete & Driveways	4d	Tue 26/08/25	Fri 26/08/28
115	Offsite AC Patching & Paving	4d	Mon 26/08/31	Thu 26/09/03
116	Offsite Striping	3d	Fri 26/09/04	Tue 26/09/08
117	Final Public Works Inspections	2d	Wed 26/09/09	Thu 26/09/10
118	Final Planning & Zoning Inspection	2d	Fri 26/09/11	Mon 26/09/14
119	Owner Civil Punch list walkthrough & Completion	5d	Tue 26/09/15	Mon 26/09/21
120	**Building Exterior, Tower & Office Finishes**	**67d**	**Thu 26/06/25**	**Mon 26/09/28**
121	Install Scaffolding at Office Tower	1d	Thu 26/06/25	Thu 26/06/25
122	Exterior Metal Frame/Sheathing & Waterproofing	5d	Fri 26/06/26	Thu 26/07/02

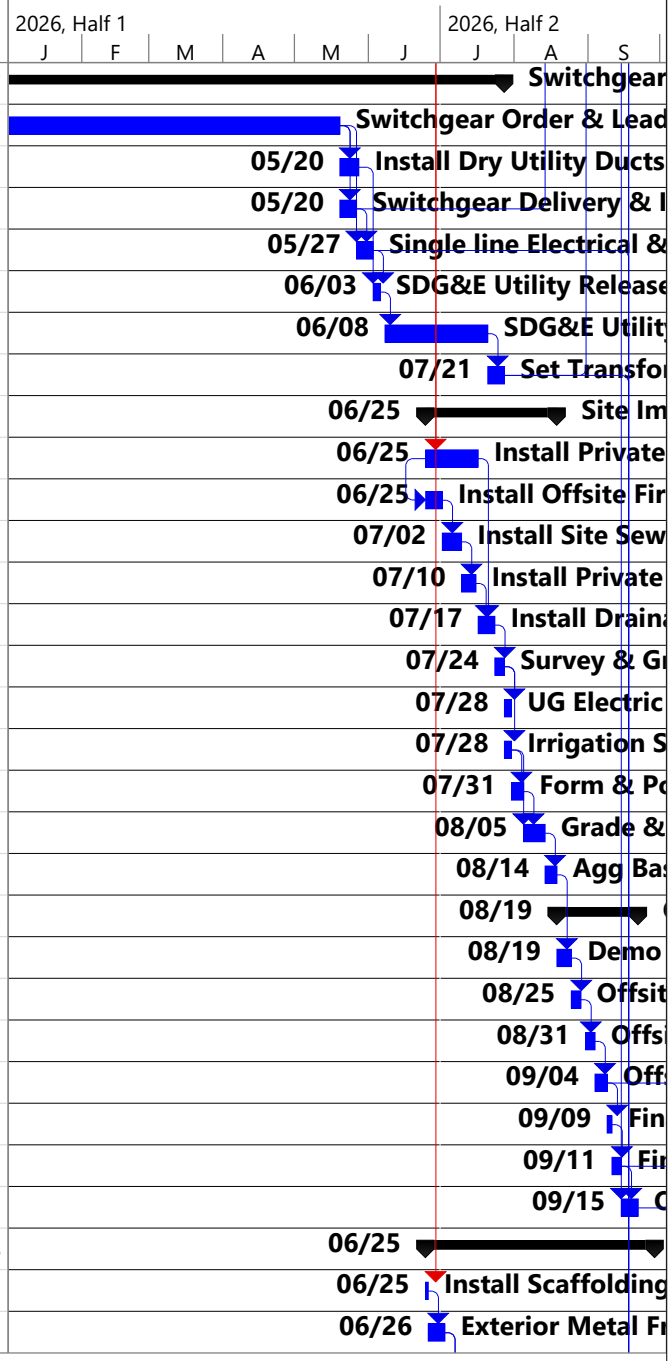

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
123	Install Storefront System @ Displays	5d	Mon 26/07/06	Fri 26/07/10
124	EIFS	5d	Mon 26/07/13	Fri 26/07/17
125	Exterior Painting & Coatings @ CMU Walls	10d	Mon 26/07/06	Fri 26/07/17
126	Install Metal Panel Systems @ Tower Framing	5d	Mon 26/07/20	Fri 26/07/24
127	Install Steel Canopies	5d	Mon 26/07/27	Fri 26/07/31
128	Exterior Breakmetal, flashings, Sealants, & Painting	5d	Mon 26/08/03	Fri 26/08/07
129	Remove Scaffolding	1d	Mon 26/08/10	Mon 26/08/10
130	Office Framing	6d	Mon 26/08/03	Mon 26/08/10
131	Office M/E/P Rough in	6d	Tue 26/08/11	Tue 26/08/18
132	Office Drywall	10d	Wed 26/08/19	Tue 26/09/01
133	Suspended Ceilings & Rough in	6d	Wed 26/09/02	Wed 26/09/09
134	Office Fixtures & Finishes	6d	Thu 26/09/10	Thu 26/09/17
135	Final Electrical Inspection	3d	Fri 26/09/18	Tue 26/09/22
136	Final Mechanical Inspections	3d	Wed 26/09/23	Fri 26/09/25
137	Office Completion Date, (Possible TCO 1st floor)	1d	Mon 26/09/28	Mon 26/09/28
138	**Accumulative Building Inspections & C of O**	**18d**	**Wed 26/09/30**	**Fri 26/10/23**
139	Rain/Weather Delays	10d	Wed 26/09/30	Tue 26/10/13
140	Life Safety & Final Inspections	4d	Wed 26/10/14	Mon 26/10/19
141	Building Final Inspection	2d	Tue 26/10/20	Wed 26/10/21
142	Substantial Completion Date	0d	Wed 26/10/21	Wed 26/10/21
143	Certificate Of Occupancy	2d	Thu 26/10/22	Fri 26/10/23
144	Open Date	0d	Fri 26/10/23	Fri 26/10/23
145	Final Completion Date	0d	Fri 26/10/23	Fri 26/10/23

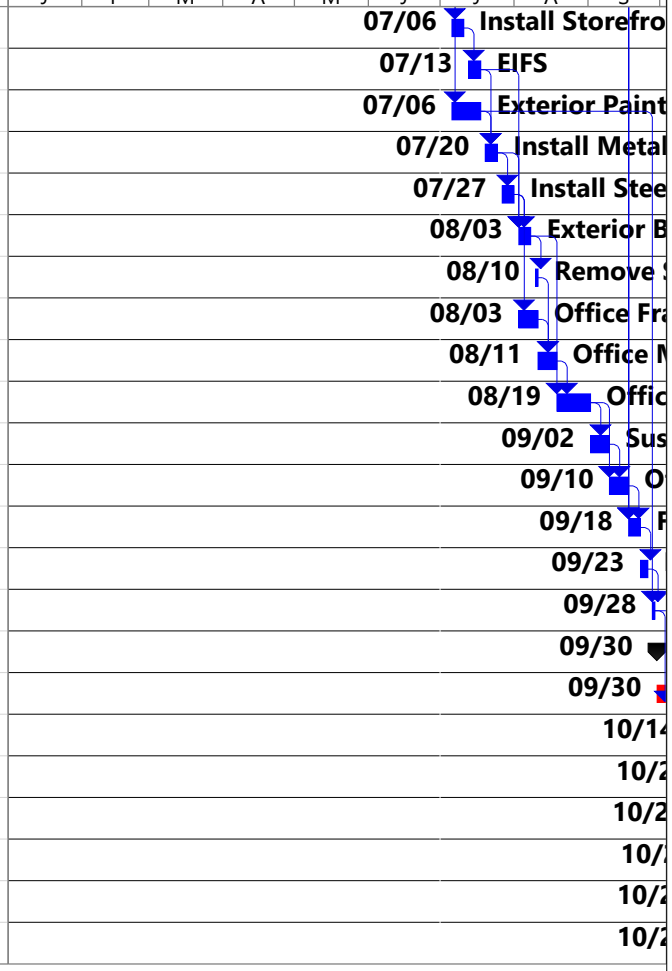

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
1	**Public Storage - 1061 Cudahy Place San Diego CA**	**156d**	**Tue 25/05/27**	**Mon 26/01/12**
2	Notice to Proceed	0d	Tue 25/05/27	Tue 25/05/27
3	**Demolition Permit Delay (Estimated)**	**96d**	**Tue 25/05/27**	**Fri 25/10/10**
4	SDGE Removal of Transformer	1d	Mon 25/10/06	Mon 25/10/06
5	Mobilization	5d	Mon 25/10/06	Fri 25/10/10
6	Switchgear Submittal Approval (30 week Lead Time)	15d	Mon 25/09/22	Fri 25/10/10
7	CO #4 - ADS Detension System	40d	Wed 25/07/16	Wed 25/09/10
8	Chamber System Submittal Approval	20d	Mon 25/10/27	Fri 25/11/21
9	ADS Detention System Lead Time	30d	Mon 25/11/24	Mon 26/01/12
10	**Public Storage Overall 88,386 Sq Ft**	**264d**	**Wed 25/10/08**	**Fri 26/10/23**
11	**Surface Demo & Grading**	**48d**	**Wed 25/10/08**	**Tue 25/12/16**
12	Erosion Control & Remove Owners Fencing	3d	Wed 25/10/08	Fri 25/10/10
13	Received Traffic Control Plans City Stamped	1d	Tue 25/10/21	Tue 25/10/21
14	Mock Pre-Con Meeting with City	1d	Wed 25/10/22	Wed 25/10/22
15	**Submitted Application for Traffic Control Permit DELAY**	**20d**	**Thu 25/10/23**	**Wed 25/11/19**
16	**City List of Items to resolve before Pre-Con Meeting can happen DELAY**	**1d**	**Thu 25/11/20**	**Thu 25/11/20**
17	Pre Con Meeting	1d	Fri 25/11/21	Fri 25/11/21
18	Demo Existing Bldg/Slabs,Tank slabs, Retaining walls Etc.	10d	Mon 25/10/13	Fri 25/10/24
19	Site Survey, Boundry & Building Pad	1d	Fri 25/10/24	Fri 25/10/24
20	Pre Grading Meeting	1d	Fri 25/10/24	Fri 25/10/24
21	Install Shoring Wall NE corner of Site	13d	Fri 25/11/21	Thu 25/12/11
22	Over-Ex & Recompact Bldg Pad & Site areas	12d	Fri 25/11/21	Wed 25/12/10
23	Certify Pad / Pad Delivery Date	3d	Fri 25/12/12	Tue 25/12/16
24	Building Permit Due	0d	Tue 25/12/16	Tue 25/12/16
25	**Site Improvements - Structures & Utilities**	**20d**	**Tue 26/01/13**	**Mon 26/02/09**
26	Install Private Storm Drain & Chamber System	15d	Tue 26/01/13	Mon 26/02/02
27	Install Offsite Fire Tie In & Lateral	5d	Tue 26/01/13	Mon 26/01/19
28	Install Site Sewer line to Bldg.	5d	Tue 26/01/13	Mon 26/01/19
29	Install Private Domestic Water	4d	Tue 26/01/20	Fri 26/01/23

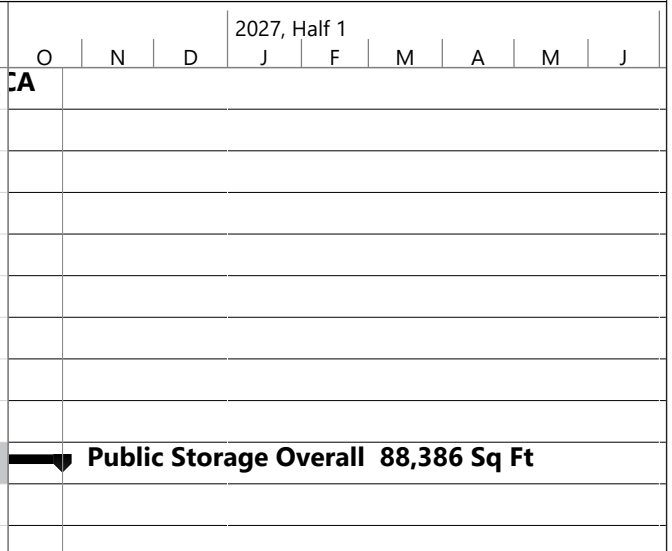

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
30	Install Dry Utility Ducts & Structures	5d	Mon 26/01/26	Fri 26/01/30
31	Install Drainage Structures & Backfill	5d	Tue 26/02/03	Mon 26/02/09
32	**Early AC Paving Option**	**18d**	**Tue 26/02/10**	**Fri 26/03/06**
33	Survey & Grade for Curb Cuts	2d	Tue 26/02/10	Wed 26/02/11
34	UG Electric Site Lts, Gate Motors etc.	3d	Thu 26/02/12	Tue 26/02/17
35	Irrigation Sleeves	3d	Thu 26/02/12	Tue 26/02/17
36	Form & Pour Curb & Gutter onsite	3d	Wed 26/02/18	Fri 26/02/20
37	Grade & Pour Site Walks Bollards & Gate Tracks	7d	Mon 26/02/23	Tue 26/03/03
38	Agg Base import & "Early" AC Paving option	3d	Wed 26/03/04	Fri 26/03/06
39	**Building Shell Construction**	**198d**	**Wed 25/12/17**	**Tue 26/09/29**
40	Underslab Plumbing & Electrical	8d	Wed 25/12/17	Tue 25/12/30
41	Elevator Pits Excavate, Waterproofing, Form & Pour	10d	Wed 25/12/17	Mon 26/01/05
42	Drill & Set Jack Casings	5d	Tue 26/01/06	Mon 26/01/12
43	Bldg. Wall Ftgs.	13d	Mon 25/12/22	Tue 26/01/13
44	CMU Stem Wall 8" AFF	10d	Mon 26/01/12	Fri 26/01/23
45	Fine Grade Slab Base materials	5d	Wed 26/01/21	Tue 26/01/27
46	Reinforce Slab on grade	3d	Wed 26/01/28	Fri 26/01/30
47	**Inspection**	**1d**	**Mon 26/02/02**	**Mon 26/02/02**
48	Pour Slab on Grade 8"	1d	Tue 26/02/03	Tue 26/02/03
49	CMU walls/Ledgers to 18' (exterior scaffold)	22d	Mon 26/01/26	Wed 26/02/25
50	CMU walls/Ledgers to 18' (interior scaffold)	15d	Wed 26/02/04	Wed 26/02/25
51	Shearwalls/Beams for 1st floor (Janus + 3 Wks / GBC / Able	25d	Wed 26/02/11	Wed 26/03/18
52	Deck (Able)	3d	Thu 26/03/19	Mon 26/03/23
53	Reinforce 2nd floor Deck	3d	Tue 26/03/24	Thu 26/03/26
54	**Inspection**	**1d**	**Fri 26/03/27**	**Fri 26/03/27**
55	Pour 2nd floor Deck	1d	Mon 26/03/30	Mon 26/03/30
56	Deck cure	4d	Tue 26/03/31	Fri 26/04/03
57	CMU Walls/Ledgers to 29' (3rd floor - interior scaffold)	15d	Mon 26/04/06	Fri 26/04/24
58	CMU Walls/Ledgers to 29' (3rd floor - exterior scaffold)	47d	Thu 26/02/26	Fri 26/05/01
59	Shearwalls/Beams for 2nd Floor (Janus + 3 Wks / GBC / Ab	29d	Tue 26/04/07	Fri 26/05/15
60	Deck for 3rd floor (Able)	3d	Mon 26/05/18	Wed 26/05/20

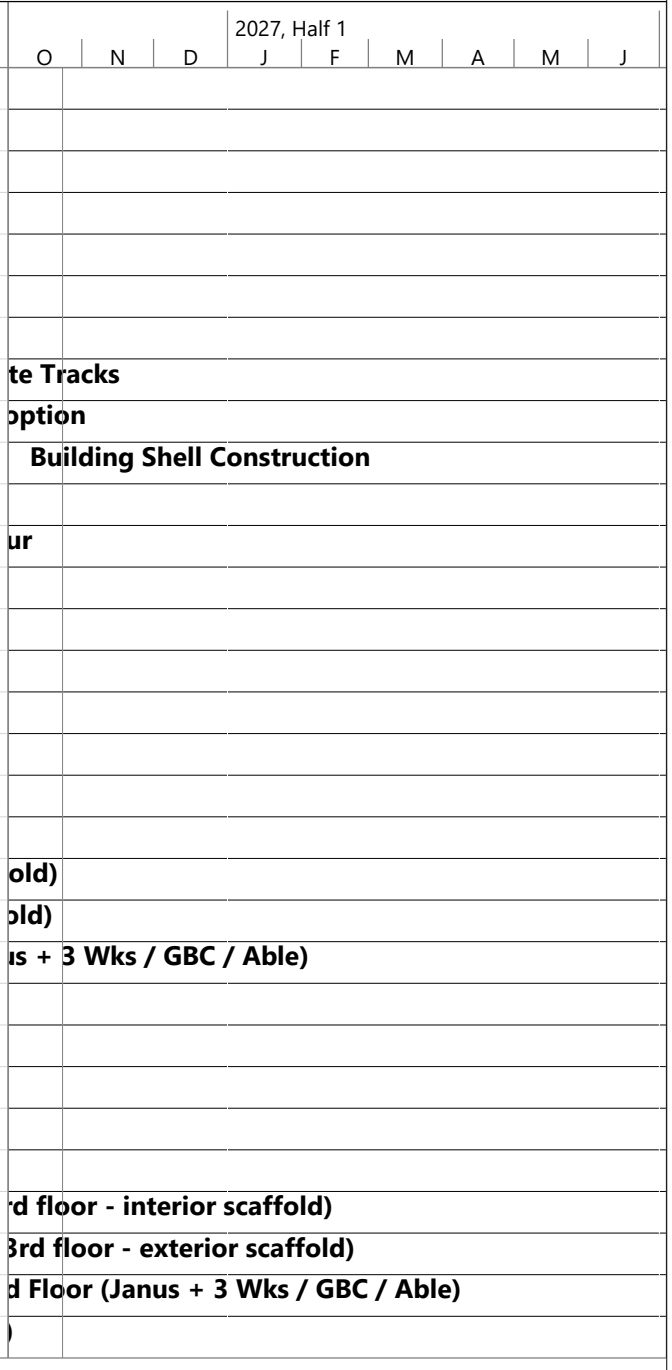

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
61	Reinforce for 3rd floor Deck	3d	Thu 26/05/21	Tue 26/05/26
62	**Inspection**	**1d**	**Wed 26/05/27**	**Wed 26/05/27**
63	Pour 3rd floor Deck	1d	Thu 26/05/28	Thu 26/05/28
64	Deck Cure	4d	Fri 26/05/29	Wed 26/06/03
65	CMU Walls/Roof Ledgers to Top Out (interior scaffold)	15d	Thu 26/06/04	Wed 26/06/24
66	CMU Walls/Roof Ledgers to Top Out (exterior scaffold)	42d	Mon 26/05/04	Wed 26/07/01
67	Shearwalls/Beams for 3rd floor (Janus + 3 Wks / GBC / Abl	29d	Fri 26/06/05	Thu 26/07/16
68	Roof Deck (Able)	3d	Fri 26/07/17	Tue 26/07/21
69	Roof Structural @ platforms & Screens	5d	Wed 26/07/22	Tue 26/07/28
70	Install roof accessories/Curbs, drains etc.	5d	Fri 26/07/17	Thu 26/07/23
71	Roof Insulation Cover Board & Membrane	15d	Fri 26/07/24	Thu 26/08/13
72	Set Rooftop Equipment	3d	Fri 26/08/14	Tue 26/08/18
73	Elevator Construction Car #1	15d	Wed 26/07/22	Tue 26/08/11
74	Elevator Construction Car #2	15d	Wed 26/08/12	Tue 26/09/01
75	State Elevator inspection scheduling and approval	20d	Wed 26/09/02	Tue 26/09/29
76	**Building Interior**	**121d**	**Tue 26/03/24**	**Thu 26/09/10**
77	Layout & Install Hangars from 2nd fl deck	3d	Tue 26/03/24	Thu 26/03/26
78	Overhead M,P,E & Fire 1st fl	15d	Fri 26/03/27	Thu 26/04/16
79	Hallway System & Doors 1st floor	15d	Fri 26/04/10	Thu 26/04/30
80	Finish Mech. & Electrical 1st Fl	3d	Fri 26/05/01	Tue 26/05/05
81	Layout & Install Overhead Hangars from 3rd fl deck	3d	Wed 26/05/27	Fri 26/05/29
82	Overhead M,P,E & Fire 2nd Fl	15d	Mon 26/06/01	Fri 26/06/19
83	Hallway System & Doors 2nd Floor	15d	Mon 26/06/15	Mon 26/07/06
84	Finish Mech. & Electrical 2nd Fl	3d	Tue 26/07/07	Thu 26/07/09
85	Install HM Doors & Hardware	9d	Fri 26/07/10	Wed 26/07/22
86	Layout & Install Overhead Hangars from Roof deck	5d	Fri 26/07/17	Thu 26/07/23
87	Overhead M,P,E & Fire 3rd Fl	15d	Fri 26/07/24	Thu 26/08/13
88	Hallway System & Doors 3rd Floor	15d	Fri 26/08/07	Thu 26/08/27
89	Electrical Room 100% Complete	15d	Fri 26/08/14	Thu 26/09/03
90	Finish Painting in Storage areas	5d	Fri 26/08/14	Thu 26/08/20
91	Final Clean up & Seal floors	10d	Fri 26/08/28	Thu 26/09/10

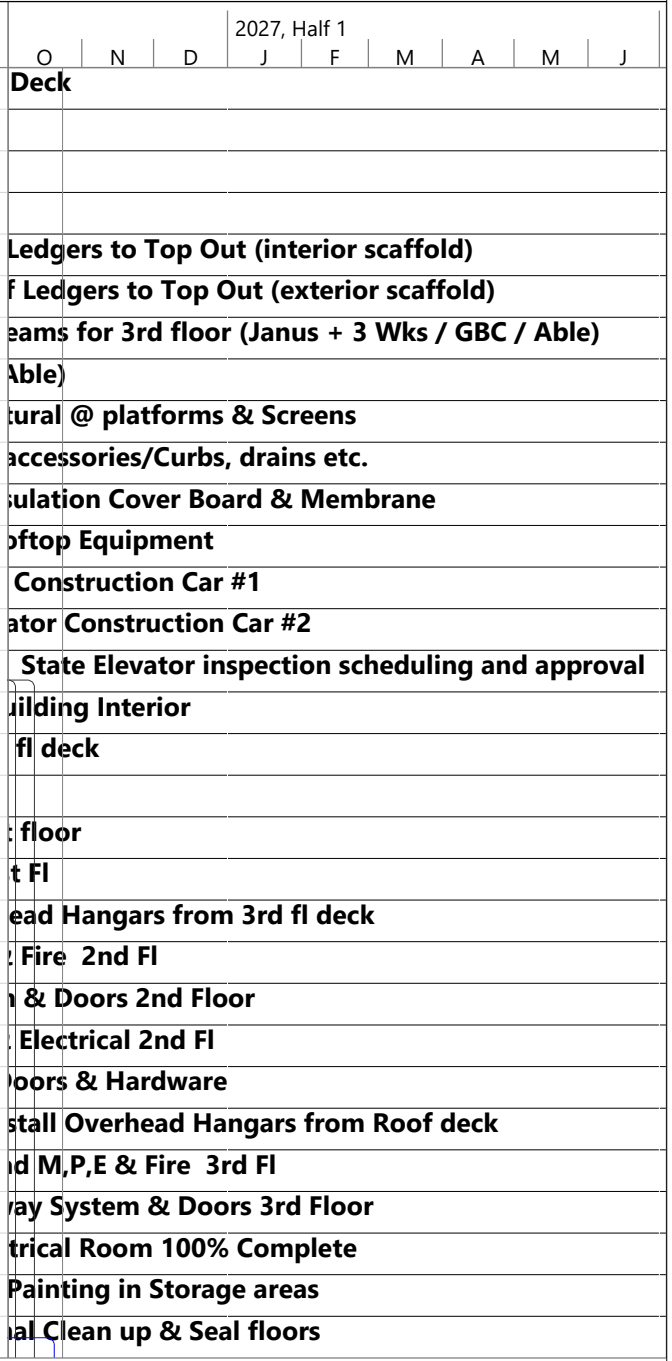

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
92	**Switchgear, City Power & Building Energize**	**197d**	**Mon 25/10/13**	**Mon 26/07/27**
93	Switchgear Order & Lead Time	150d	Mon 25/10/13	Tue 26/05/19
94	Install Dry Utility Ducts & Structures	5d	Wed 26/05/20	Wed 26/05/27
95	Switchgear Delivery & Install	4d	Wed 26/05/20	Tue 26/05/26
96	Single line Electrical & Grounding	5d	Wed 26/05/27	Tue 26/06/02
97	SDG&E Utility Release for Equipment & Cabling	3d	Wed 26/06/03	Fri 26/06/05
98	SDG&E Utility Scheduling & Lead time	30d	Mon 26/06/08	Mon 26/07/20
99	Set Transformer, Cabling, & Energize	5d	Tue 26/07/21	Mon 26/07/27
100	**Site Improvements - Structures & Utilities**	**38d**	**Thu 26/06/25**	**Tue 26/08/18**
101	Install Private Storm Drain & Chamber System	15d	Thu 26/06/25	Thu 26/07/16
102	Install Offsite Fire Tie In & Lateral	5d	Thu 26/06/25	Wed 26/07/01
103	Install Site Sewer line to Bldg.	5d	Thu 26/07/02	Thu 26/07/09
104	Install Private Domestic Water	4d	Fri 26/07/10	Wed 26/07/15
105	Install Drainage Structures & Backfill	5d	Fri 26/07/17	Thu 26/07/23
106	Survey & Grade for Curb Cuts	2d	Fri 26/07/24	Mon 26/07/27
107	UG Electric Site Lts, Gate Motors etc.	3d	Tue 26/07/28	Thu 26/07/30
108	Irrigation Sleeves	3d	Tue 26/07/28	Thu 26/07/30
109	Form & Pour Curb & Gutter onsite	3d	Fri 26/07/31	Tue 26/08/04
110	Grade & Pour Site Walks Bollards & Gate Tracks	7d	Wed 26/08/05	Thu 26/08/13
111	Agg Base import & AC Paving	3d	Fri 26/08/14	Tue 26/08/18
112	**Offsite improvements**	**24d**	**Wed 26/08/19**	**Mon 26/09/21**
113	Demo & Grading	4d	Wed 26/08/19	Mon 26/08/24
114	Offsite Concrete & Driveways	4d	Tue 26/08/25	Fri 26/08/28
115	Offsite AC Patching & Paving	4d	Mon 26/08/31	Thu 26/09/03
116	Offsite Striping	3d	Fri 26/09/04	Tue 26/09/08
117	Final Public Works Inspections	2d	Wed 26/09/09	Thu 26/09/10
118	Final Planning & Zoning Inspection	2d	Fri 26/09/11	Mon 26/09/14
119	Owner Civil Punch list walkthrough & Completion	5d	Tue 26/09/15	Mon 26/09/21
120	**Building Exterior, Tower & Office Finishes**	**67d**	**Thu 26/06/25**	**Mon 26/09/28**
121	Install Scaffolding at Office Tower	1d	Thu 26/06/25	Thu 26/06/25
122	Exterior Metal Frame/Sheathing & Waterproofing	5d	Fri 26/06/26	Thu 26/07/02

UPDATED: 9/11/25

HBI CONSTRUCTION - PUBLIC STORAGE - 1061 CUDAHY PLACE, SAN DIEGO CA

ID	Task Name	Duration	Start	Finish
123	Install Storefront System @ Displays	5d	Mon 26/07/06	Fri 26/07/10
124	EIFS	5d	Mon 26/07/13	Fri 26/07/17
125	Exterior Painting & Coatings @ CMU Walls	10d	Mon 26/07/06	Fri 26/07/17
126	Install Metal Panel Systems @ Tower Framing	5d	Mon 26/07/20	Fri 26/07/24
127	Install Steel Canopies	5d	Mon 26/07/27	Fri 26/07/31
128	Exterior Breakmetal, flashings, Sealants, & Painting	5d	Mon 26/08/03	Fri 26/08/07
129	Remove Scaffolding	1d	Mon 26/08/10	Mon 26/08/10
130	Office Framing	6d	Mon 26/08/03	Mon 26/08/10
131	Office M/E/P Rough in	6d	Tue 26/08/11	Tue 26/08/18
132	Office Drywall	10d	Wed 26/08/19	Tue 26/09/01
133	Suspended Ceilings & Rough in	6d	Wed 26/09/02	Wed 26/09/09
134	Office Fixtures & Finishes	6d	Thu 26/09/10	Thu 26/09/17
135	Final Electrical Inspection	3d	Fri 26/09/18	Tue 26/09/22
136	Final Mechanical Inspections	3d	Wed 26/09/23	Fri 26/09/25
137	Office Completion Date, (Possible TCO 1st floor)	1d	Mon 26/09/28	Mon 26/09/28
138	**Accumulative Building Inspections & C of O**	**18d**	**Wed 26/09/30**	**Fri 26/10/23**
139	Rain/Weather Delays	10d	Wed 26/09/30	Tue 26/10/13
140	Life Safety & Final Inspections	4d	Wed 26/10/14	Mon 26/10/19
141	Building Final Inspection	2d	Tue 26/10/20	Wed 26/10/21
142	Substantial Completion Date	0d	Wed 26/10/21	Wed 26/10/21
143	Certificate Of Occupancy	2d	Thu 26/10/22	Fri 26/10/23
144	Open Date	0d	Fri 26/10/23	Fri 26/10/23
145	Final Completion Date	0d	Fri 26/10/23	Fri 26/10/23

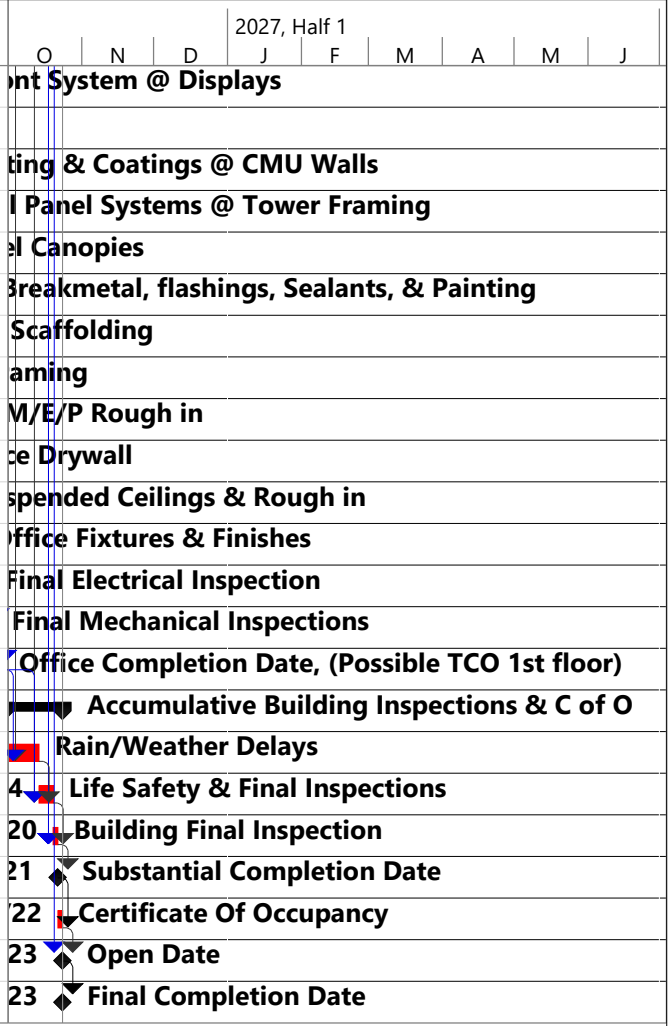

UPDATED: 9/11/25
