Landing Page | Risk | Schedule Performance Report | Calendar View | Schedule

Public Storage Dashboard

Data Date: 12/1/2025

Type	Project	Region	Responsible
Construction	San Diego, CA	West Coast	Josh Pait

Baseline Completion Date	Current Completion Date	Schedule Variance	Schedule Compression
5/29/2026	10/30/2026	-154 Baseline -9 Previous	Remaining Work Compression: 27% — ALERT

Milestone Variance

Milestone	Baseline Milestone Date	Previous Milestone Date	Current Milestone Date	Current Baseline Variance	Delta from Last Month	Activity Name	Status Indicator
NTP	5/27/2025	5/27/2025	5/27/2025	0	0	Notice To Proceed	On Track – Gaining
Foundation Complete	8/19/2025	2/3/2026	1/8/2026	-142	26	Pour Slab On Grade 8"	Delayed – Gaining
1st Floor Finishes Complete	12/2/2025	5/5/2026	4/16/2026	-135	19	Finish Mech. & Electrical 1St Fl	Delayed – Gaining
2nd Floor Finishes Complete	2/11/2026	7/9/2026	6/22/2026	-131	17	Finish Mech. & Electrical 2Nd Fl	Delayed – Gaining
Permanent Power	4/8/2026	7/27/2026	7/16/2026	-99	11	Set Transformer, Cabling, & Energize	Delayed – Gaining
Structure Top Out	3/13/2026	8/10/2026	7/23/2026	-132	18	Office Framing	Delayed – Gaining
3rd Floor Finishes Complete	3/18/2026	8/13/2026	7/31/2026	-135	13	Overhead M,P,E & Fire 3Rd Fl	Delayed – Gaining
Hardscape/Landscape Complete	3/23/2026	8/18/2026	7/31/2026	-130	18	Agg Base Import & Ac Paving	Delayed – Gaining
Elevator Complete	5/6/2026	9/29/2026	10/15/2026	-162	-16	State Elevator Inspection Scheduling And Approval	Delayed – Slipping
Contract Completion	5/29/2026	10/21/2026	10/30/2026	-154	-9	Substantial Completion Date	Delayed – Slipping

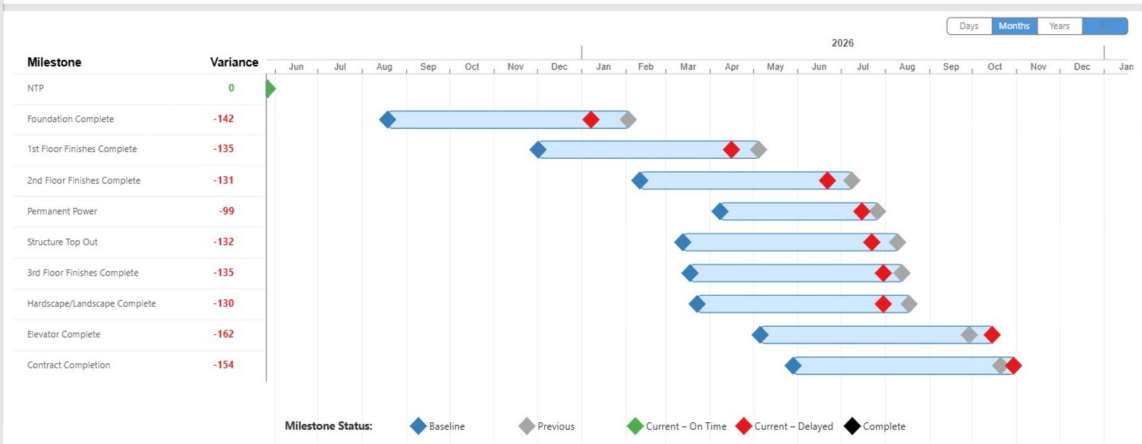

Baseline Variance

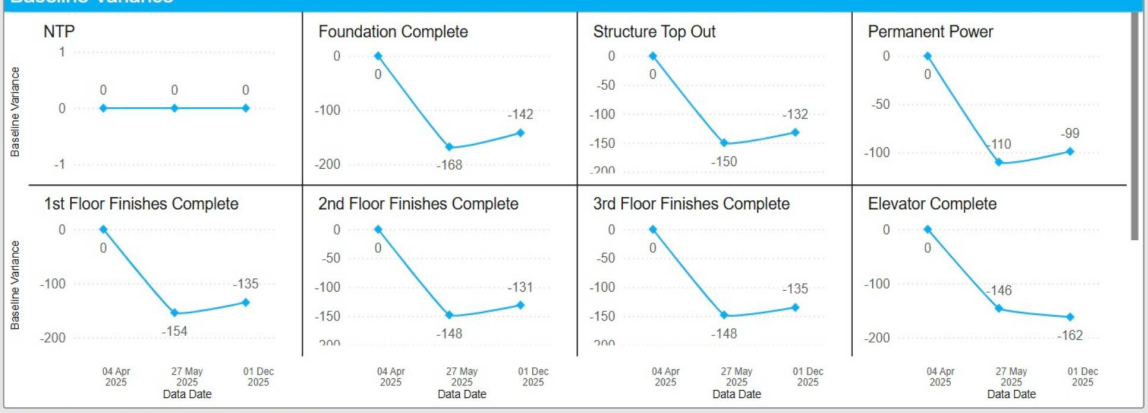

Schedule Performance Summary

Summary

The schedule is in a high-risk state across all major dimensions, with critical breakdowns in logic quality, schedule stability, execution strategy, and completion forecast. Immediate, comprehensive intervention is required to reassess project planning, validate logic, control changes, and reset achievable delivery targets, as the current schedule is not reliable for decision-making or stakeholder communication.

Schedule Validation Score: 62 — ALERT
The overall schedule quality is substantially below industry standards, indicating widespread technical soundness and logic flaws that undermine forecasting accuracy. Immediate schedule validation and correction are required.

Schedule Change Index: 100% — ALERT
An extremely high percentage of activities have experienced changes, reflecting severe instability and a lack of control in the planning process. Investigate root causes and implement stricter change controls.

Finish Variance: 269% — ALERT
The projected finish date has slipped drastically, far exceeding acceptable limits. This magnitude of delay signals critical schedule failure and imminent risk to project completion.

Remaining Work Compression: 27% — ALERT
Remaining activities have been compressed by 27%, indicating aggressive and potentially unachievable acceleration. This raises concerns regarding execution feasibility and increased risk of cascading delays.

Powered By STELIC INSIGHT • ACTION • IMPACT
