Public Storage
Davenport

ID		Task Mode	Task Name	Duration	Start	Actual Start	Finish	Actual Finish	Remaining Duration	Physical % Complete	Total Slack
0			**Overall Construction Schedule**	**343 days**	**Wed 7/9/25**	**Wed 7/9/25**	**Fri 10/30/26**	**NA**	**254.8 days**	**0%**	**0 days**
1	✓		**Contract Administration**	**40 days**	**Wed 7/9/25**	**Wed 7/9/25**	**Tue 9/2/25**	**Tue 9/2/25**	**0 days**	**0%**	**0 days**
2	✓		Notice to Proceed	34 days	Wed 7/9/25	Wed 7/9/25	Mon 8/25/25	Mon 8/25/25	0 days	100%	0 days
3	✓		Mobilization	1 day	Tue 8/26/25	Tue 8/26/25	Tue 9/2/25	Tue 9/2/25	0 days	100%	0 days
4			**Procurement**	**296 days**	**Thu 8/7/25**	**Thu 8/7/25**	**Thu 9/24/26**	**NA**	**209.82 days**	**0%**	**26 days**
302			**Pre-Installation Meetings**	**134 days**	**Tue 9/23/25**	**Tue 9/23/25**	**Fri 3/27/26**	**NA**	**122.83 days**	**0%**	**155 days**
317			**Sitework**	**145 days**	**Thu 7/24/25**	**Thu 7/24/25**	**Wed 2/11/26**	**NA**	**68.88 days**	**0%**	**154 days**
318	✓		Complete Erosion Control Install	4 days	Thu 7/24/25	Thu 7/24/25	Mon 9/8/25	Mon 9/8/25	0 days	100%	0 days
319	✓		Silt Fence Inspection	1 day	Tue 9/9/25	Tue 9/9/25	Tue 9/9/25	Tue 9/9/25	0 days	100%	0 days
320	✓		Clear and Grub	0 days	Wed 9/3/25	Wed 9/3/25	Thu 9/18/25	Thu 9/18/25	0 days	100%	0 days
321	✓		Install Temporary Fencing	1 day	Fri 10/3/25	Fri 10/3/25	Fri 10/3/25	Fri 10/3/25	0 days	100%	0 days
322	✓		Mass Grade Site	14 days	Tue 9/16/25	Tue 9/16/25	Wed 10/8/25	Wed 10/8/25	0 days	100%	0 days
323			Construct Retention Pond	3 days	Fri 10/10/25	Fri 10/10/25	Mon 2/2/26	NA	3 days	50%	122 days
324			Storm Sewer	6 days	Fri 11/14/25	Fri 11/14/25	Thu 2/5/26	NA	6 days	50%	158 days
325			Sanitary Sewer, Fire Line and domestic water	10 days	Fri 11/14/25	Fri 11/14/25	Wed 2/11/26	NA	10 days	50%	115 days
326	✓		Grade for building pad	1 day	Wed 10/1/25	Wed 10/1/25	Wed 10/8/25	Wed 10/8/25	0 days	100%	0 days
327	✓		**Building Pad Construction**	**43 days**	**Thu 10/9/25**	**Thu 10/9/25**	**Mon 12/8/25**	**Mon 12/8/25**	**0 days**	**0%**	**0 days**
328	✓		Survey and Form Perimeter Walls of Building	10 days	Thu 10/9/25	Thu 10/9/25	Wed 10/22/25	Wed 10/22/...	0 days	100%	0 days
329	✓		Concrete Footings for Columns	10 days	Tue 10/28/25	Tue 10/28/25	Fri 12/5/25	Fri 12/5/25	0 days	100%	0 days
330	✓		Excavation for Elevator Pits	0 days	Tue 10/28/25	Tue 10/28/25	Fri 11/7/25	Fri 11/7/25	0 days	100%	0 days
331	✓		Waterproofing of Below Elevator Pit Floors	3 days	Thu 11/6/25	Thu 11/6/25	Mon 11/10/25	Mon 11/10/...	0 days	100%	0 days
332	✓		Construct Concrete Elevator Pit Floors and Sump Pits	0 days	Thu 11/6/25	Thu 11/6/25	Fri 11/7/25	Fri 11/7/25	0 days	100%	0 days
333	✓		Form and Pour Elevator Pit Walls	2 days	Thu 11/6/25	Thu 11/6/25	Fri 11/7/25	Fri 11/7/25	0 days	100%	0 days
334	✓		Underslab Plumbing Rough	0 days	Tue 11/11/25	Tue 11/11/25	Fri 11/21/25	Fri 11/21/25	0 days	100%	0 days
335	✓		Fine Grade SOG-Place Stone	0 days	Thu 11/20/25	Thu 11/20/25	Mon 11/24/25	Mon 11/24/...	0 days	100%	0 days
336	✓		Underslab Electrical Rough	0 days	Thu 10/30/25	Thu 10/30/25	Fri 12/5/25	Fri 12/5/25	0 days	100%	0 days
337	✓		Vapor Barrier/Rebar for Slab on Grade	9 days	Tue 11/11/25	Tue 11/11/25	Fri 12/5/25	Fri 12/5/25	0 days	100%	0 days
338	✓		Pour First Half of Slab on Grade	0 days	Sat 11/22/25	Sat 11/22/25	Sat 11/22/25	Sat 11/22/25	0 days	100%	0 days
339	✓		Pour Second Half of Slab on Grade	0 days	Sat 12/6/25	Sat 12/6/25	Sat 12/6/25	Sat 12/6/25	0 days	100%	0 days
340	✓		Backfill Around Slab on Grade	1 day	Mon 12/8/25	Mon 12/8/25	Mon 12/8/25	Mon 12/8/25	0 days	100%	0 days
341			**Building Construction**	**172 days**	**Wed 12/10/25**	**Wed 12/10/25**	**Thu 8/6/26**	**NA**	**170.78 days**	**0%**	**20 days**
342	✓		Hollow metal frames to job site for CMU	0 days	Wed 12/10/25	Wed 12/10/25	Wed 12/10/25	Wed 12/10/...	0 days	100%	0 days
343	✓		Construct First Lift of Elevators/Stair Tower CMU	0 days	Thu 12/11/25	Thu 12/11/25	Fri 1/9/26	Fri 1/9/26	0 days	100%	0 days
344			Construct Exterior CMU Walls - SOG to 2nd Floor	10 days	Thu 12/11/25	Thu 12/11/25	Wed 2/11/26	NA	10 days	30%	0 days
345	✓		Install Hollow Metal Frames in CMU - 1st Floor	1 day	Wed 12/10/25	Wed 12/10/25	Wed 12/10/25	Wed 12/10/...	0 days	100%	0 days
346	✓		Grout First Lift of CMU at Elevators/Stair Towers	1 day	Wed 12/31/25	Wed 12/31/25	Wed 12/31/25	Wed 12/31/...	0 days	100%	0 days
347			Construct Second Lift of Elevators/Stair Tower CMU	8 days	Thu 1/15/26	Thu 1/15/26	Mon 2/9/26	NA	8 days	35%	5 days
348			Install Hollow Metal Frames in Stair Towers - 2nd Floor	1 day	Thu 1/29/26	NA	Thu 1/29/26	NA	1 day	0%	50 days
349			Grout Second Lift of CMU at Elevators/Stair Towers	2 days	Fri 1/30/26	NA	Mon 2/2/26	NA	2 days	0%	50 days
350			Construct Final Lift of Elevators/Stair Tower CMU	8 days	Tue 2/3/26	NA	Thu 2/12/26	NA	8 days	0%	50 days
351			Install Hollow Metal Frame in Stair Towers - 3rd Floor	1 day	Tue 2/3/26	NA	Tue 2/3/26	NA	1 day	0%	50 days
352			Grout Final Lift of CMU at Elevators/Stair Towers	2 days	Thu 3/12/26	NA	Fri 3/13/26	NA	2 days	0%	24 days
353			1st floor structure erection/decking	7 days	Wed 1/7/26	Wed 1/7/26	Fri 2/20/26	NA	7 days	75%	6 days
354			2nd floor SOD-Prep/wire install/Pour	7 days	Tue 1/20/26	Tue 1/20/26	Mon 2/9/26	NA	7 days	25%	0 days
355			2nd floor SOD-Pour Completed	0 days	Mon 2/9/26	NA	Mon 2/9/26	NA	0 days	0%	10 days
356			Construct Exterior CMU Walls - 2nd to 3rd floor	15 days	Thu 1/15/26	Thu 1/15/26	Mon 3/9/26	NA	15 days	0%	33 days

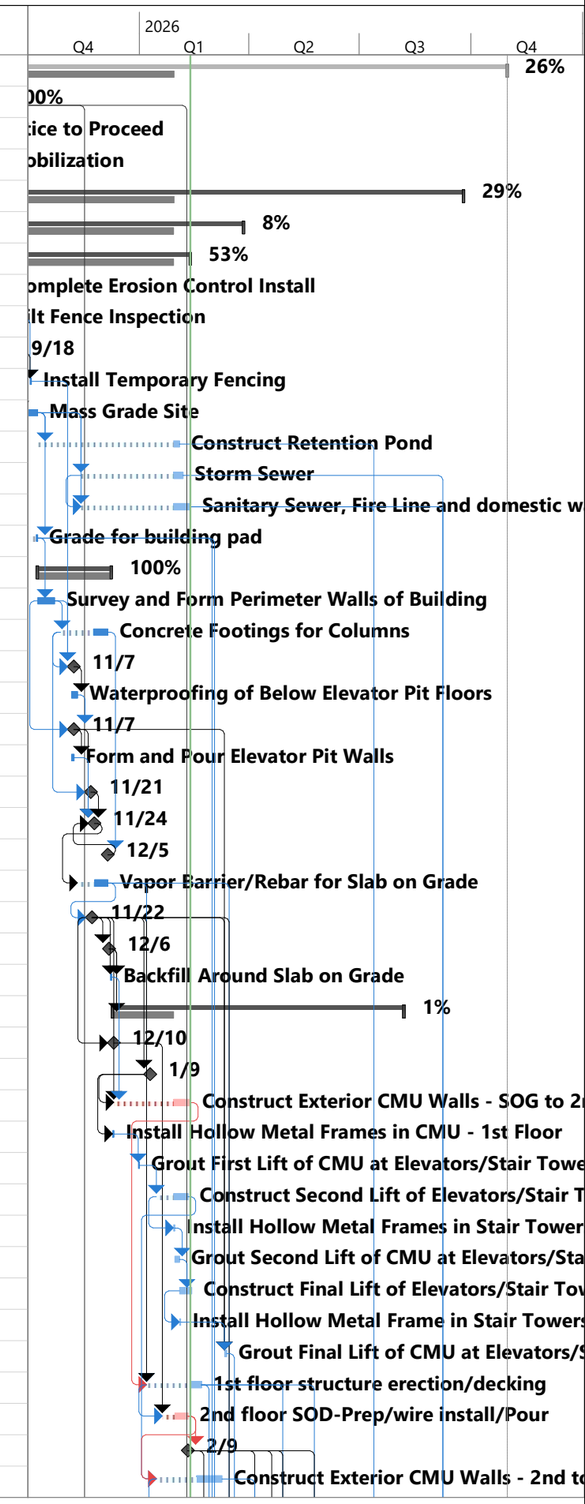

Public Storage
Davenport

ID	Task Mode	Task Name	Duration	Start	Actual Start	Finish	Actual Finish	Remaining Duration	Physical % Complete	Total Slack
357		2nd floor-structure erection	25 days	Mon 2/23/26	NA	Fri 3/27/26	NA	25 days	0%	6 days
358		3rd floor-SOD prep/wire install/Pour	7 days	Thu 3/26/26	NA	Fri 4/3/26	NA	7 days	0%	6 days
359		3rd floor-SOD Pour Completed	0 days	Fri 4/3/26	NA	Fri 4/3/26	NA	0 days	0%	6 days
360		Install stairs in stair towers	7 days	Mon 3/16/26	NA	Tue 3/24/26	NA	7 days	0%	24 days
361		Install Railings	8 days	Wed 3/25/26	NA	Fri 4/3/26	NA	8 days	0%	41 days
362		3rd Floor - Construct CMU walls from 3rd Floor to Roof	15 days	Mon 4/13/26	NA	Fri 5/1/26	NA	15 days	0%	6 days
363		3rd floor structure erection & Roof	25 days	Mon 4/20/26	NA	Fri 5/22/26	NA	25 days	0%	6 days
364		Install TPO Roofing	7 days	Mon 5/25/26	NA	Tue 6/2/26	NA	7 days	0%	6 days
365		Roofing Complete - Building Dry-In	0 days	Wed 6/3/26	NA	Wed 6/3/26	NA	0 days	0%	6 days
366		EIFS/Stucco	35 days	Mon 5/25/26	NA	Fri 7/10/26	NA	35 days	0%	8 days
367		Storefront Frames Install	10 days	Thu 6/4/26	NA	Wed 6/17/26	NA	10 days	0%	6 days
368		Storefront Glass Installed	10 days	Thu 7/2/26	NA	Wed 7/15/26	NA	10 days	0%	6 days
369		Stanley Sliding Door Install	1 day	Wed 6/3/26	NA	Wed 6/3/26	NA	1 day	0%	6 days
370		Canopies	8 days	Mon 6/22/26	NA	Wed 7/1/26	NA	8 days	0%	16 days
371		Install Metal Coping/Downspouts/Trim	6 days	Thu 7/16/26	NA	Thu 7/23/26	NA	6 days	0%	6 days
372		Exterior Building Caulking	5 days	Fri 7/24/26	NA	Thu 7/30/26	NA	5 days	0%	8 days
373		Exterior Building Punchlist	5 days	Fri 7/31/26	NA	Thu 8/6/26	NA	5 days	0%	8 days
374		Light gauge office framing	5 days	Mon 5/25/26	NA	Fri 5/29/26	NA	5 days	0%	11 days
375		Elevator #1 Install	20 days	Fri 6/5/26	NA	Thu 7/2/26	NA	20 days	0%	25 days
376		Elevator #2 install	20 days	Fri 7/3/26	NA	Thu 7/30/26	NA	20 days	0%	25 days
377		Building Façade Complete	0 days	Thu 7/23/26	NA	Thu 7/23/26	NA	0 days	0%	6 days
378		**Site Utlities/As-Builts**	**223 days**	**Mon 11/17/25**	**Mon 11/17/25**	**Wed 9/23/26**	**NA**	**223 days**	**0%**	**6 days**
379		Electrical Gear Procurement	20 days	Mon 11/17/25	Mon 11/17/25	Wed 2/25/26	NA	20 days	75%	80 days
380		Install Secondary Power from Building to Transfomer	0 days	Mon 12/22/25	Mon 12/22/25	Mon 12/22/25	Mon 12/22/...	0 days	100%	0 days
381		Survey for Transformer Pad	1 day	Thu 1/29/26	NA	Thu 1/29/26	NA	1 day	0%	70 days
382		Grade for Transformer Pad	2 days	Fri 1/30/26	NA	Mon 2/2/26	NA	2 days	0%	70 days
383		Construct or Set Transformer Pad	4 days	Tue 2/3/26	NA	Fri 2/6/26	NA	4 days	0%	70 days
384		Order Transformer from Duke Energy	15 days	Mon 2/9/26	NA	Fri 2/27/26	NA	15 days	0%	70 days
385		Set Transformer	2 days	Mon 3/2/26	NA	Tue 3/3/26	NA	2 days	0%	70 days
386		Install Primary Power Conduits and Transformer - Duke Energy	10 days	Wed 3/4/26	NA	Tue 3/17/26	NA	10 days	0%	70 days
387		Permanent Power to Building	10 days	Wed 3/18/26	NA	Tue 3/31/26	NA	10 days	0%	70 days
388		As-Built Drawings for Sanitary and Storm	12 days	Tue 9/8/26	NA	Wed 9/23/26	NA	12 days	0%	6 days
389		**Rough-ins and Finishes**	**134 days**	**Mon 4/6/26**	**NA**	**Thu 10/8/26**	**NA**	**134 days**	**0%**	**0 days**
390		Office Buildout	40 days	Thu 7/2/26	NA	Wed 8/26/26	NA	40 days	0%	0 days
391		1st Floor HVAC Rough In	15 days	Mon 4/6/26	NA	Fri 4/24/26	NA	15 days	0%	14 days
392		3rd Floor Electrical/Fire Alarm Rough In	15 days	Thu 6/25/26	NA	Wed 7/15/26	NA	15 days	0%	7 days
393		Power to elevator machine rooms	2 days	Wed 6/3/26	NA	Thu 6/4/26	NA	2 days	0%	25 days
394		Install Gear in Electrical Room	10 days	Wed 6/3/26	NA	Tue 6/16/26	NA	10 days	0%	11 days
395		3rd Floor HVAC Trim/Line Sets	10 days	Thu 6/25/26	NA	Wed 7/8/26	NA	10 days	0%	12 days
396		Install Aluminum Wainscot at Elevator Lobbies	5 days	Thu 8/13/26	NA	Wed 8/19/26	NA	5 days	0%	9 days
397		1st Floor HVAC Trim/Line Set	10 days	Wed 5/20/26	NA	Tue 6/2/26	NA	10 days	0%	14 days
398		1st Floor Electrical Trim/FA/Hang Lights	7 days	Mon 7/6/26	NA	Tue 7/14/26	NA	7 days	0%	24 days
399		2nd Floor HVAC Rough In	15 days	Mon 5/25/26	NA	Fri 6/12/26	NA	15 days	0%	11 days
400		2nd Floor HVAC Trim/Line Sets	10 days	Wed 6/17/26	NA	Tue 6/30/26	NA	10 days	0%	14 days
401		3rd Floor Electrical Trim/FA/Hang Lights	7 days	Thu 8/13/26	NA	Fri 8/21/26	NA	7 days	0%	7 days
402		Initial BDA System Requirement Testing	1 day	Thu 8/13/26	NA	Thu 8/13/26	NA	1 day	0%	19 days

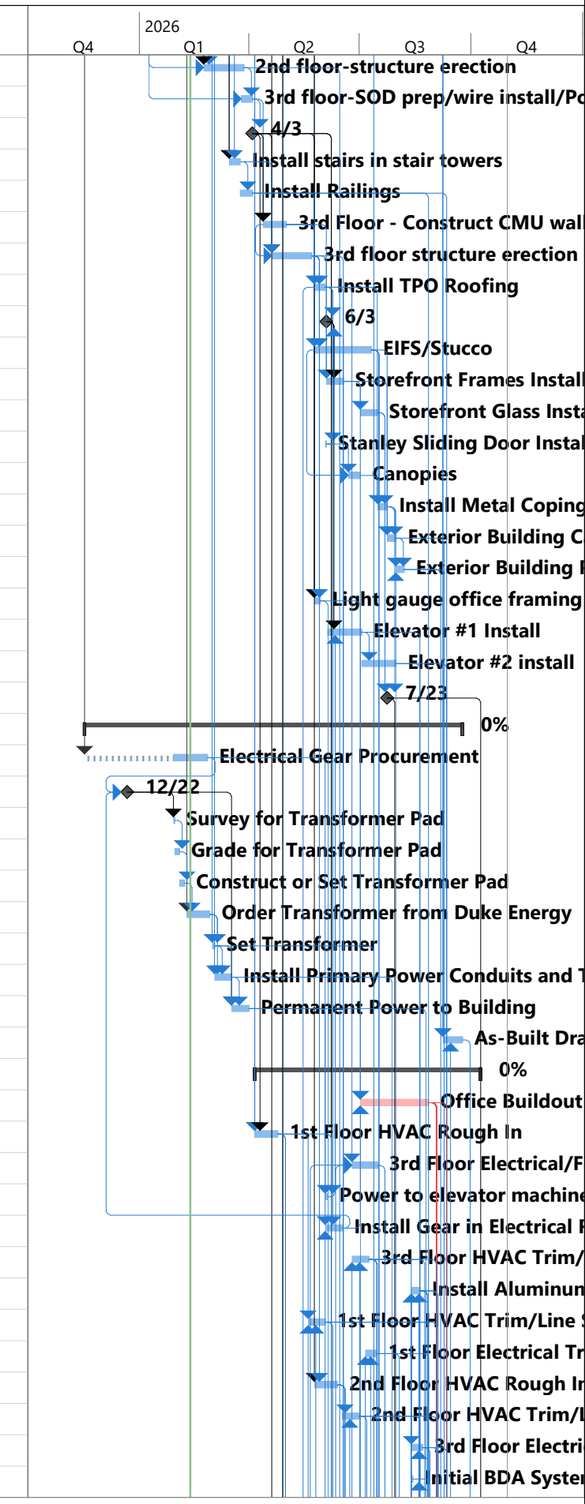

Public Storage
Davenport
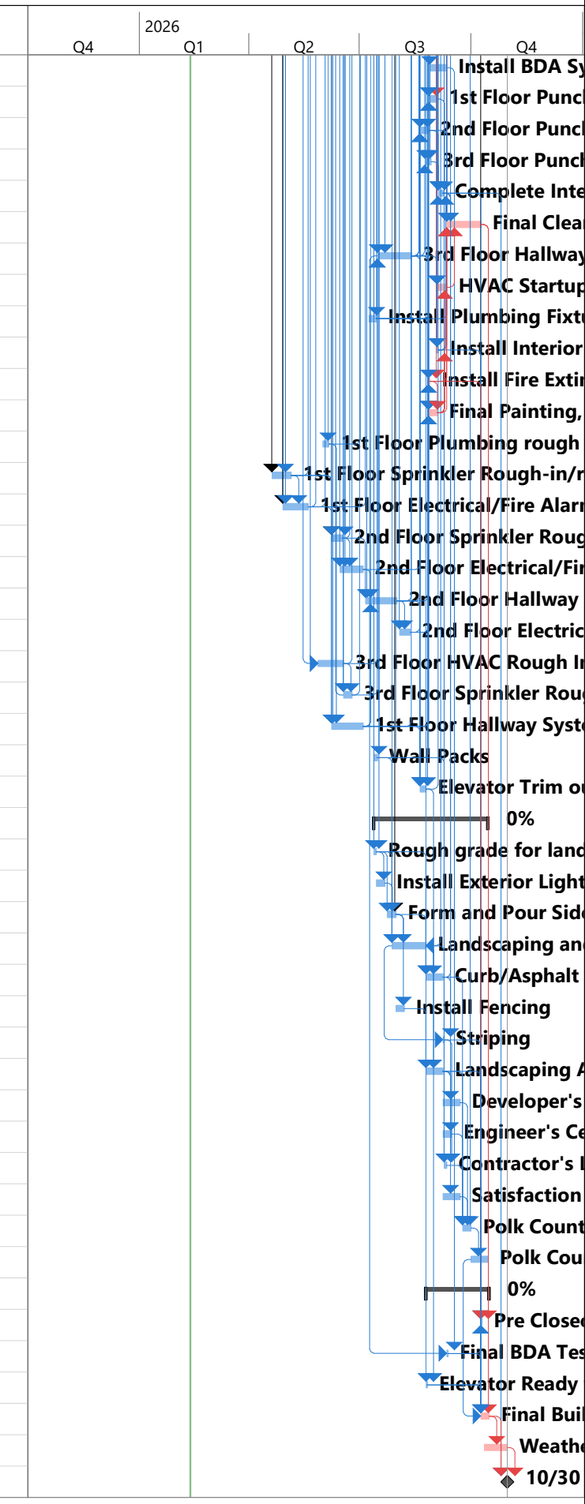
ID	Task Mode	Task Name	Duration	Start	Actual Start	Finish	Actual Finish	Remaining Duration	Physical % Complete	Total Slack
403		Install BDA System	10 days	Fri 8/28/26	NA	Thu 9/10/26	NA	10 days	0%	19 days
404		1st Floor Punchlist Repairs	5 days	Thu 8/27/26	NA	Wed 9/2/26	NA	5 days	0%	4 days
405		2nd Floor Punchlist Repairs	5 days	Thu 8/20/26	NA	Wed 8/26/26	NA	5 days	0%	9 days
406		3rd Floor Punchlist Repairs	5 days	Mon 8/24/26	NA	Fri 8/28/26	NA	5 days	0%	7 days
407		Complete Interior Punchlist Work - All Floors	2 days	Fri 9/4/26	NA	Mon 9/7/26	NA	2 days	0%	3 days
408		Final Clean/Floor Sealer	20 days	Fri 9/11/26	NA	Thu 10/8/26	NA	20 days	0%	0 days
409		3rd Floor Hallway System-by Janus	20 days	Thu 7/16/26	NA	Wed 8/12/26	NA	20 days	0%	7 days
410		HVAC Startup	6 days	Thu 9/3/26	NA	Thu 9/10/26	NA	6 days	0%	0 days
411		Install Plumbing Fixtures and Water Heaters	4 days	Thu 7/9/26	NA	Tue 7/14/26	NA	4 days	0%	30 days
412		Install Interior Signage	1 day	Thu 9/3/26	NA	Thu 9/3/26	NA	1 day	0%	3 days
413		Install Fire Extinguishers and Cabinets	1 day	Thu 8/27/26	NA	Thu 8/27/26	NA	1 day	0%	0 days
414		Final Painting, Stairs/Railings/Doors	5 days	Thu 8/27/26	NA	Wed 9/2/26	NA	5 days	0%	0 days
415		1st Floor Plumbing rough walls	5 days	Mon 6/1/26	NA	Fri 6/5/26	NA	5 days	0%	11 days
416		1st Floor Sprinkler Rough-in/riser room-1st floor	12 days	Mon 4/20/26	NA	Tue 5/5/26	NA	12 days	0%	14 days
417		1st Floor Electrical/Fire Alarm Rough In	15 days	Wed 4/29/26	NA	Tue 5/19/26	NA	15 days	0%	14 days
418		2nd Floor Sprinkler Rough-in	7 days	Mon 6/8/26	NA	Tue 6/16/26	NA	7 days	0%	14 days
419		2nd Floor Electrical/Fire Alarm Rough In	15 days	Mon 6/15/26	NA	Fri 7/3/26	NA	15 days	0%	11 days
420		2nd Floor Hallway System - by Janus	20 days	Mon 7/6/26	NA	Fri 7/31/26	NA	20 days	0%	11 days
421		2nd Floor Electrical Trim/FA/Hang Light-2nd Floor	7 days	Mon 8/3/26	NA	Tue 8/11/26	NA	7 days	0%	11 days
422		3rd Floor HVAC Rough In	15 days	Thu 5/28/26	NA	Wed 6/17/26	NA	15 days	0%	7 days
423		3rd Floor Sprinkler Rough-in	5 days	Thu 6/18/26	NA	Wed 6/24/26	NA	5 days	0%	7 days
424		1st Floor Hallway System- by Janus	20 days	Mon 6/8/26	NA	Fri 7/3/26	NA	20 days	0%	11 days
425		Wall Packs	3 days	Mon 7/13/26	NA	Wed 7/15/26	NA	3 days	0%	14 days
426		Elevator Trim out by Subs	3 days	Thu 8/20/26	NA	Mon 8/24/26	NA	3 days	0%	11 days
427		**Finsh Sitework - Dumpster/Sidewalks/Paving/Landscaping**	**68 days**	**Mon 7/13/26**	**NA**	**Wed 10/14/26**	**NA**	**68 days**	**0%**	**6 days**
428		Rough grade for landscaping	2 days	Mon 7/13/26	NA	Tue 7/14/26	NA	2 days	0%	8 days
429		Install Exterior Lighting in Parking Area	5 days	Wed 7/15/26	NA	Tue 7/21/26	NA	5 days	0%	8 days
430		Form and Pour Sidewalks	5 days	Fri 7/24/26	NA	Thu 7/30/26	NA	5 days	0%	6 days
431		Landscaping and Irrigation Installation	20 days	Tue 7/28/26	NA	Mon 8/24/26	NA	20 days	0%	6 days
432		Curb/Asphalt Paving	10 days	Tue 8/25/26	NA	Mon 9/7/26	NA	10 days	0%	6 days
433		Install Fencing	5 days	Fri 7/31/26	NA	Thu 8/6/26	NA	5 days	0%	20 days
434		Striping	1 day	Tue 9/8/26	NA	Tue 9/8/26	NA	1 day	0%	15 days
435		Landscaping As-Built Drawings	10 days	Tue 8/25/26	NA	Mon 9/7/26	NA	10 days	0%	8 days
436		Developer's Letter of Dedication	10 days	Tue 9/8/26	NA	Mon 9/21/26	NA	10 days	0%	8 days
437		Engineer's Certificate of Completion	5 days	Tue 9/8/26	NA	Mon 9/14/26	NA	5 days	0%	13 days
438		Contractor's Letter of Completion	2 days	Wed 9/9/26	NA	Thu 9/10/26	NA	2 days	0%	15 days
439		Satisfaction Letter/Email from FDOT and City for Infrastructure	10 days	Tue 9/8/26	NA	Mon 9/21/26	NA	10 days	0%	8 days
440		Polk County Final Walkthrough Request	5 days	Thu 9/24/26	NA	Wed 9/30/26	NA	5 days	0%	6 days
441		Polk County Approval of Site	10 days	Thu 10/1/26	NA	Wed 10/14/26	NA	10 days	0%	6 days
442		**Final Building Sign-Offs**	**38 days**	**Tue 8/25/26**	**NA**	**Thu 10/15/26**	**NA**	**38 days**	**0%**	**11 days**
443		Pre Closeout Meeting with AHJ	1 day	Fri 10/9/26	NA	Fri 10/9/26	NA	1 day	0%	15 days
444		Final BDA Test	1 day	Fri 9/11/26	NA	Fri 9/11/26	NA	1 day	0%	19 days
445		Elevator Ready for State Inspection	1 day	Tue 8/25/26	NA	Tue 8/25/26	NA	1 day	0%	32 days
446		Final Building Inspections	5 days	Fri 10/9/26	NA	Thu 10/15/26	NA	5 days	0%	0 days
447		Weather Days per Contract (20 Calendar Days)	15 days	Mon 10/12/26	NA	Fri 10/30/26	NA	15 days	0%	0 days
448		Substantial Completion	0 days	Fri 10/30/26	NA	Fri 10/30/26	NA	0 days	0%	0 days
